



# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects

Data Date: 05/18/2023

Report Date: 05/31/2023

### DESCRIPTION/TEAM

### SCOPE

### PHOTO

**Project Title:** Headquarters R&R

Project Number: 11206  
 BCC District: 03  
 Delivery Method: Construction Management  
 Category: S06-Sheriff - FDO  
 Status: Construction  
 Designer: Leo Daly  
 Contractor: Kast Construction  
 Project Manager: Terri Wolfe

The project consists of the exterior hardening of the entire building consisting of new exterior walls, impact resistant doors and windows, roof replacement and structural tie-ins as well as the R&R of all major building systems and interior renovation of approx. 75% of the building. As part of the project, the Board has also approved the temp. relocation of employees occupying approx. 70% of the space to ensure continuity of operations during the construction, reduce the overall duration of the project and therefore total project cost. This project is funded in:  
 FY 2017 IST \$1,600,000, FY 2019 IST \$11,047,000  
 FY 2020 IST \$10,835,000  
 FY 2021 IST \$17,620,000  
 FY 2022 IST \$6,577,994



### SCHEDULE SUMMARY

	Original	Actual
Project Start	3/14/2016	3/14/2016
Design Start	5/9/2017	5/9/2017
Construction Start	1/31/2019	3/22/2021
Substantial Completion	8/23/2022	
Project Completion	3/24/2023	

### PARTICIPATION


#### Consultant

SBE 24.71%  
 Local 100%  
 WBE N/A  
 MBE N/A


#### Contractor

SBE 12.75%  
 Local 100%  
 WBE N/A  
 MBE N/A

### FUNDING

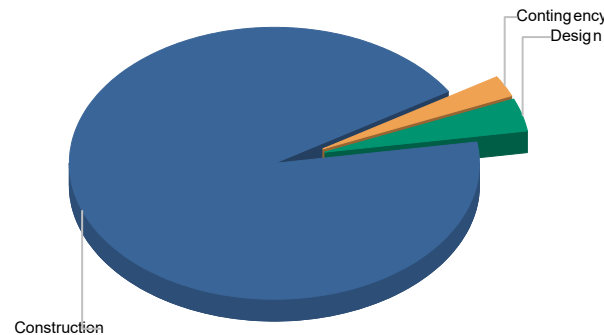

Current Budget

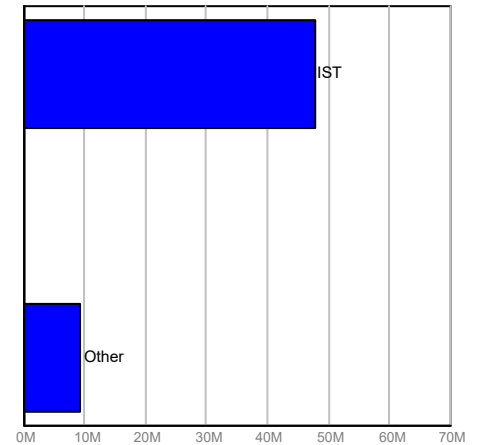

Fund Source

### FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$2,274,200	\$3,187,474	140.16%	\$2,824,200
Construction	\$53,355,994	\$46,292,974	86.76%	\$38,388,071
Furniture, Fixtures & Equipment	\$0	\$199,340	0.00%	\$199,174
Other	\$0	\$116,675	0.00%	\$116,675
Contingency	\$1,418,800	\$0	0.00%	\$0
<b>TOTAL</b>	<b>\$57,048,994</b>	<b>\$49,796,463</b>	<b>87.29%</b>	<b>\$41,528,119</b>

### NOTES

All 3 levels continue to progress. The current floor sections being punched out are the 2nd Floor, Section 4, and 3rd Floor (final walk). The punch-out process is approx. 85% complete. The 1st and 3rd Floor other than reception is 100% punched out. A stocking permit should be in place, and site ready for owner furniture in late- July 2023. Exterior work punch-out has begun. The new exterior camera wiring, parking lot sealing, final roof inspection, and civil/ landscape final inspection is still pending but will begin shortly. Interior work includes final finishes and MEP trim on all levels, all 5 new elevators are complete, other than some final building electrical connections. Expected completion is late July 2023. Owner acceptance and turnover are expected in late July 2023.



# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects


Data Date: 05/18/2023

Report Date: 05/31/2023

DESCRIPTION/TEAM	SCOPE	PHOTO
<p><b>Project Title: Ocean Inlet Park and Marina Renovation</b></p> <p>Project Number: 13367            BCC District: 04            Delivery Method: Hard Bid            Category: P08-Public Building Repair Replacement &amp; Expans            Status: Construction            Designer: Alan Gerwig &amp; Associates, Inc.            Contractor: Poseidon            Project Manager: Rich Avery</p>	<p>The project consists of the replacement of marina components as well as new components including bulkhead wall, floating docks, floating finger docks, fixed dock, boat lifts, floating wave attenuator, landscaping, and replacement of the current Marina/Restroom and concession buildings. The project will be constructed in two phases. Phase one will consist of marina bulkhead, dock reconstruction and wave attenuator construction. The remaining scope to be completed during phase 2.</p> <p>Total available funding for this project consists of \$2,500,000 FY18 IST funds, \$2,500,000 FY20 Find Grant funds, and \$3,200,000 FY23 IST funds.</p>	

SCHEDULE SUMMARY		
	Original	Actual
Phase I Start	2/5/2018	2/4/2018
Design Start	10/22/2018	10/22/2018
Construction Start	12/3/2019	11/1/2021
Substantial Completion	11/1/2022	

PARTICIPATION	
<b>Consultant</b>	
SBE	82.50%
Local	100%
WBE	N/A
MBE	N/A
<b>Contractor</b>	
SBE	92.67
Local	92.67
WBE	TBD
MBE	TBD

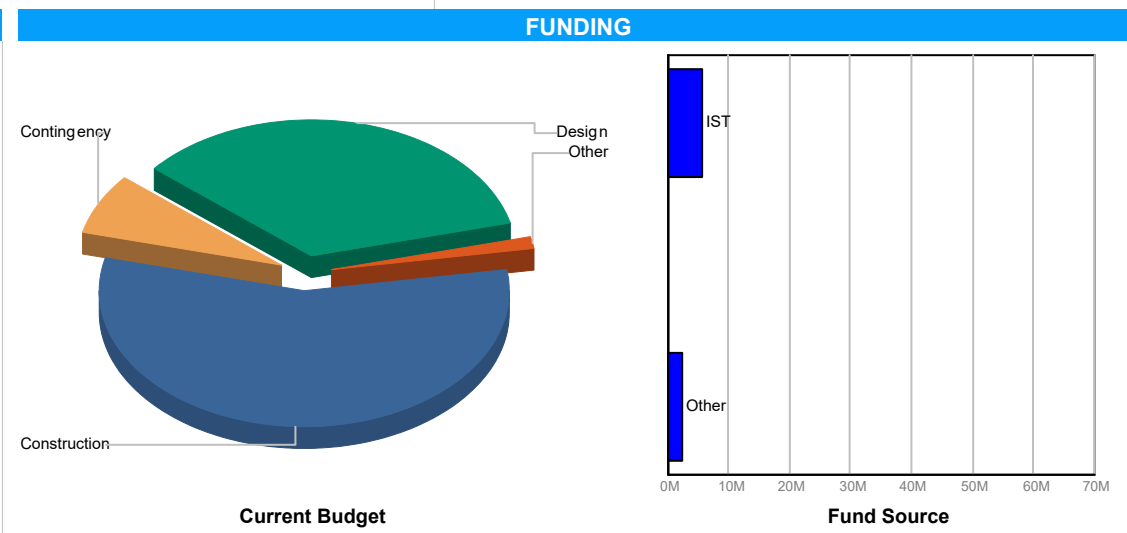

FINANCIAL SUMMARY				
	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$2,877,200	\$330,314	11.48%	\$308,448
Construction	\$4,614,300	\$1,426,249	30.91%	\$1,060,055
Other	\$108,500	\$94,843	87.41%	\$94,843
Contingency	\$600,000	\$0	0.00%	\$0
<b>TOTAL</b>	<b>\$8,200,000</b>	<b>\$1,851,406</b>	<b>22.58%</b>	<b>\$1,463,346</b>

**NOTES**

North sea wall: Fixed dock installation continues. Upland plaza restoration is pending. South sea wall: Sheet panel is installed, concrete cladding of panel is pending. Construction of wall cap is approximately 50% complete. The remaining cap is being formed.



# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects

Data Date: 05/18/2023

Report Date: 05/31/2023

### DESCRIPTION/TEAM

### SCOPE

### PHOTO

**Project Title:** Evidence Building

Project Number: 14218  
 BCC District: 03  
 Delivery Method: Construction Management  
 Category: S06-Sheriff - FDO  
 Status: Construction  
 Designer: Leo Daly  
 Contractor: Pirtle Construction  
 Project Manager: Jeffrey Halverson

The project consists of a new 2-story Evidence Storage/Crime Scene/Crime Lab Facility (Approximately 87,000 GSF) and a 12,000 GSF metal building for impound vehicle storage. The main facility will house property seized by the Sheriff's Office, Administrative Offices, Evidence Processing via the crime scene investigation unit and the crime lab. Monitored cameras, motion detectors, and restricted access with electronic logging will be provided. The facility will accommodate secure vehicle garage bays that can store large vehicles (i.e. 56' long trailers) holding evidence for investigation or transport. Site Development (16 Acres) to include user parking (public, booking officers & staff), a fenced/gated impound lot (350 surface spaces) and a limited area of covered parking.



Palm Beach County Sheriff's Office Forensic Facility



### SCHEDULE SUMMARY

	Original	Actual
Project Start	3/30/2016	12/21/2016
Design Start	6/28/2017	6/28/2017
Construction Start	7/5/2018	4/29/2019
Substantial Completion	11/5/2019	10/30/2020
Project Completion	11/26/2019	

### PARTICIPATION

#### Consultant

SBE 33.21%

Local 78.96%

WBE N/A

MBE N/A

#### Contractor


SBE 21.60%

Local 55%


WBE N/A

MBE N/A

### FUNDING

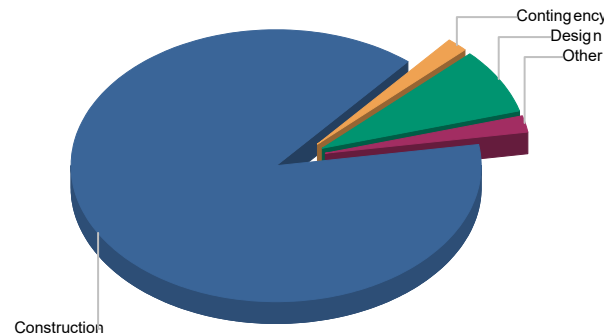

Current Budget

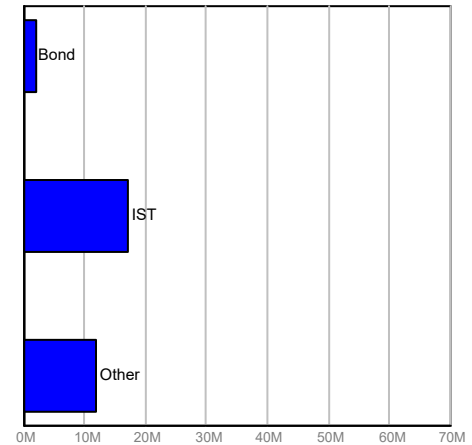

Fund Source

### FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$2,461,526	\$2,370,540	96.30%	\$2,039,277
Construction	\$27,729,163	\$28,414,988	102.47%	\$20,078,750
Furniture, Fixtures & Equipment	\$0	\$0	0.00%	\$0
Other	\$602,158	\$199,506	33.13%	\$199,506
Contingency	\$492,268	\$3,672	0.75%	\$3,672
<b>TOTAL</b>	<b>\$31,285,116</b>	<b>\$30,988,707</b>	<b>99.05%</b>	<b>\$22,321,205</b>

### NOTES

The dehumidification system is operating and being monitored. Electrical work remains to be completed and tested. Work associated with the Preserve Area Management Plan remains to be completed in late June. Awaiting response from CM on Field Bulletin 80 that was issued on 12/22 with the price for processing the Garage HVAC upgrade, Hazards Storage room conversion, and other small items.



# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects

Data Date: 05/18/2023

Report Date: 05/31/2023

### DESCRIPTION/TEAM

### SCOPE

### PHOTO

**Project Title:** CR 880 Canal Bank Stabilization

Project Number: 1448  
 BCC District: 06  
 Delivery Method: Bid Contract Award  
 Category: C02-CR 880 Canal Bank Stabilization  
 Status: Construction  
 Designer: Wantman Group  
 Contractor: Dickerson Florida, Inc.  
 Project Manager: Holly Knight

This project will repair, restore, and stabilize the embankment along a portion of County Road 880. The South Florida Water Management District's L-13 Canal parallels and is very close to County Road 880. The embankment area for County Road 880 to the canal is minimal. The undermining of the County Road 880 embankment continues due to storm events and increased South Florida Water Management District pumping and has progressively deteriorated. Repair of the embankment is necessary to prevent the eventual collapse of County Road 880 and to ensure the integrity of County Road 880 and provide a safe roadway for the public.  
 IST Funds: FY17 \$1,000,000 FY18 \$2,000,000 FY24 \$2,000,000.



### SCHEDULE SUMMARY

	Original	Actual
Construction Notice to Proceed	6/5/2017	6/5/2017
Phase III Construction Complete	11/2/2017	10/20/2017
Phase IV-Construction Notice to Proceed	6/1/2018	7/9/2018
Phase IV-Construction Complete	12/1/2018	3/27/2019
Phase V-Construction Notice to Proceed	6/1/2019	7/1/2019
Phase V-Construction Complete	12/1/2019	11/20/2019

### PARTICIPATION



#### Consultant

SBE 15%  
 Local 100%  
 WBE 0%  
 MBE 0%

#### Contractor

SBE 23.4%  
 Local 23.4%  
 WBE 0%  
 MBE 0%

### FUNDING

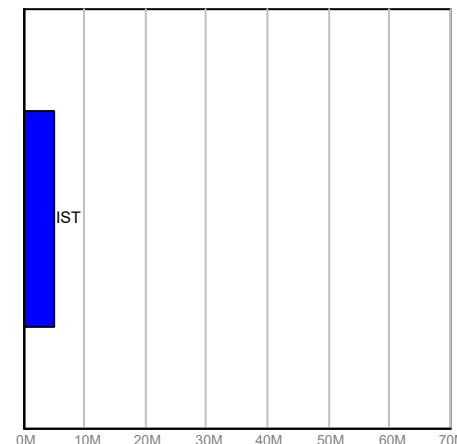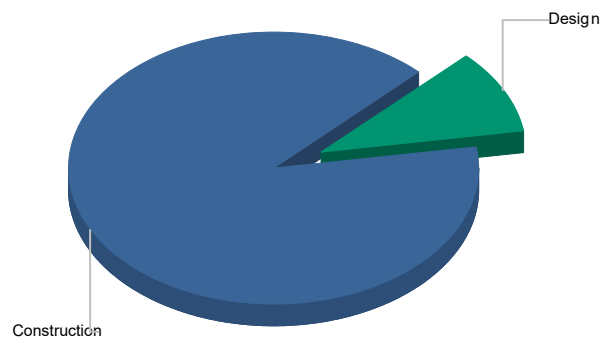

Current Budget

Fund Source

### FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$500,000	\$75,698	15.14%	\$75,698
Construction	\$4,500,000	\$2,537,336	56.39%	\$2,311,606
Contingency	\$0	\$0	0.00%	\$0
<b>TOTAL</b>	<b>\$5,000,000</b>	<b>\$2,613,034</b>	<b>52.26%</b>	<b>\$2,387,304</b>

### NOTES

Phases I and II (constructing adjacent locations) were completed in FY 2015 and FY 2016 using non-IST funding. Phase III construction is funded at \$1,000,000 in FY 2017. Construction for Phases IV & V are funded at \$2,000,000 in FY 2018. Construction is complete for Phases III, IV and V. Project will recommence upon arrival of FY 2024 funding.



# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects

Data Date: 05/18/2023

Report Date: 05/31/2023

### DESCRIPTION/TEAM

### SCOPE

### PHOTO

**Project Title:** 6th Ave. So. over Lake Osborne (LWDD E-4 Canal)(S Br/ East bound) (934307)

Project Number: 1464

BCC District: 03

Delivery Method: Design CCNA

Category: B08-Bridge Replacements

Status: Construction

Designer: Stantec

Contractor: Ranger

Project Manager: Will Carey

This project will replace an existing bridge that was built over 50 years ago. The new bridge will improve traffic safety (lane widths, bike lanes and barrier walls), improve roadway drainage, and enhance pedestrian sidewalk safety. The new bridge will also provide greater vertical clearance.



### SCHEDULE SUMMARY

	Original	Actual
Design Contract Notice to Proceed	7/17/2018	7/17/2018
Design Completion	12/1/2020	2/14/2021
Construction Bid Date	3/1/2021	5/4/2021
Construction Start	12/1/2021	2/14/2022
Construction Complete	9/1/2023	

### PARTICIPATION

#### Consultant

SBE 25%

Local 100%

WBE 0%

MBE 0%

#### Contractor


SBE 11%

Local 100%

WBE 0%

MBE 0%

### FUNDING

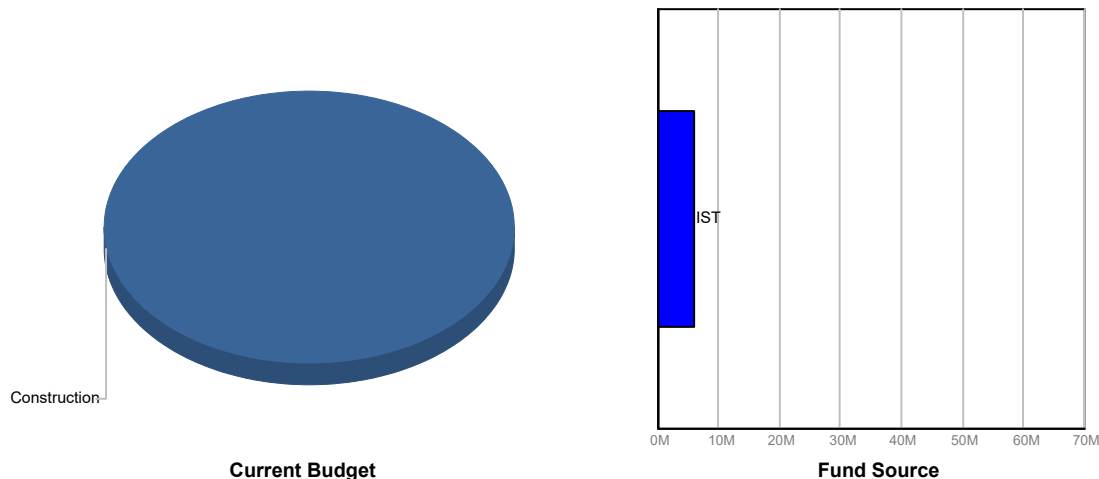

### FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Construction	\$6,000,000	\$5,598,585	93.31%	\$1,776,432
<b>TOTAL</b>	<b>\$6,000,000</b>	<b>\$5,598,585</b>	<b>93.31%</b>	<b>\$1,776,432</b>

### NOTES

This project is funded with 5-Year Road Program (RP) funding and IST funding. Design (using RP funds) is complete. The project was bid on 5/4/21 - with apparent low bid of \$ 11.1m The IST partially funds the construction of the project at \$6m in FY 2020. Construction is ongoing (40% complete).



# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects

Data Date: 05/18/2023

Report Date: 05/31/2023

### DESCRIPTION/TEAM

### SCOPE

### PHOTO

**Project Title:** CR 880 (Old SR 80) Over C-51 Canal (930940)  
**Project Number:** 1480  
**BCC District:** 06  
**Delivery Method:** Design CCNA  
**Category:** B08-Bridge Replacements  
**Status:** Design  
**Designer:** Alan Gerwig & Assoc.  
**Contractor:** TBD (Bid)  
**Project Manager:** Maroun Azzi

This project will replace an existing bridge that was built over 80 years ago. The new bridge will improve traffic safety (lane widths and vehicle barrier walls). The current bridge is weight restricted.



### SCHEDULE SUMMARY

	Original	Actual
Design Contract Notice to Proceed	11/9/2018	11/9/2018
Design Completion	12/1/2023	
Construction Bid Date	4/1/2024	
Construction Start	9/1/2024	
Construction Complete	6/1/2026	

### PARTICIPATION


**Consultant**

- SBE 94.3%
- Local 100%
- WBE 0%
- MBE 0%

**Contractor**

- SBE TBD
- Local TBD
- WBE TBD
- MBE TBD

### FUNDING

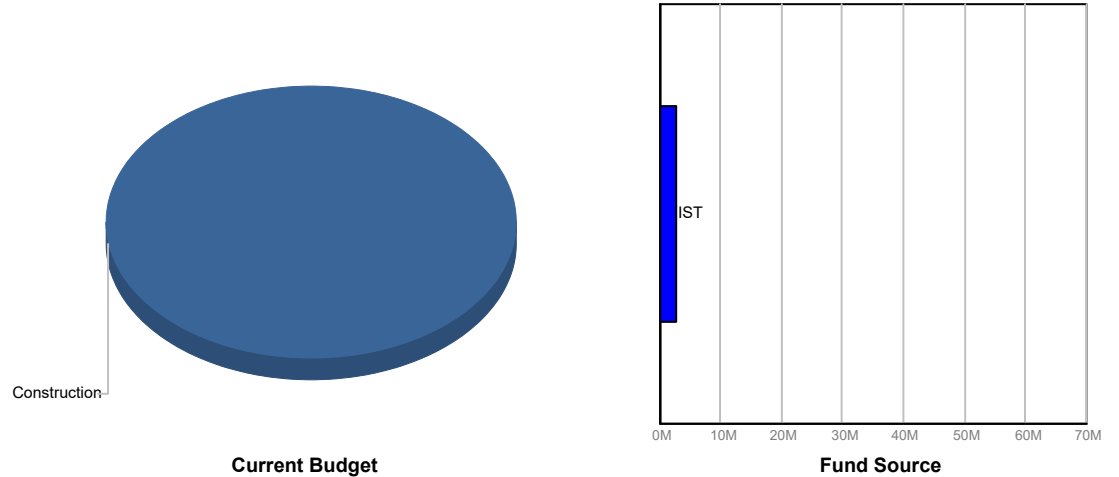

### FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Construction	\$2,700,000	\$13,710	0.51%	\$13,710
<b>TOTAL</b>	<b>\$2,700,000</b>	<b>\$13,710</b>	<b>0.51%</b>	<b>\$13,710</b>

### NOTES

This project is funded with 5-Year Road Program (RP) funding and IST funding. Design (using 5-Year RP funds) is ongoing (80% complete). The construction of the project is currently estimated at \$5.8m. The IST partially funds the construction of the project at \$2.7m in FY 2019. The project is currently scheduled to begin construction in FY24. The scheduled dates have been revised to depict design and permitting delays.



# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects

Data Date: 05/18/2023

Report Date: 05/31/2023

### DESCRIPTION/TEAM

### SCOPE

### PHOTO

**Project Title: Main Detention Center Electronics**

Project Number: 15218  
 BCC District: 03  
 Delivery Method: Construction Management  
 Category: S06-Sheriff - FDO  
 Status: Construction  
 Designer: Leo A. Daly  
 Contractor: Hedrick Brothers Construction  
 Project Manager: Jeffrey Halverson

Phase II - Electronics for the South, East, and West Towers at the Main Detention Center, which have continually operated since the early 1980's. These systems include door controls, intercom, nurse's call system, CCTV, upgrade of EST3 software for fire alarm and new infrastructure for the future expansion of the CCTV system.  
 Main Detention Center Electronics (B594) IST Funding  
 FY 2017 IST \$5,600,000  
 FY 2018 IST \$4,700,000  
 The total Electronics budget is \$11,235,851 of which \$1,021,161 is funded through Ad Valorem.



### SCHEDULE SUMMARY

	Original	Actual
Project Start	7/9/2015	6/9/2015
Design Start	6/21/2016	6/21/2016
Construction Start	3/19/2018	5/17/2018
Substantial Completion	3/15/2022	8/10/2020
Project Completion	6/30/2022	

### PARTICIPATION



**Consultant**

- SBE 22.60%
- Local 67%
- WBE N/A
- MBE N/A

**Contractor**

- SBE 76.79%
- Local 80%
- WBE N/A
- MBE N/A

### FUNDING

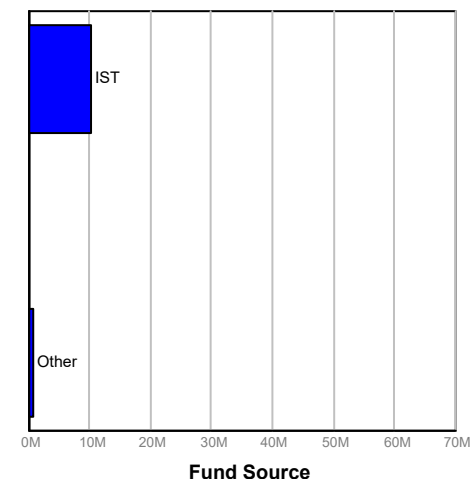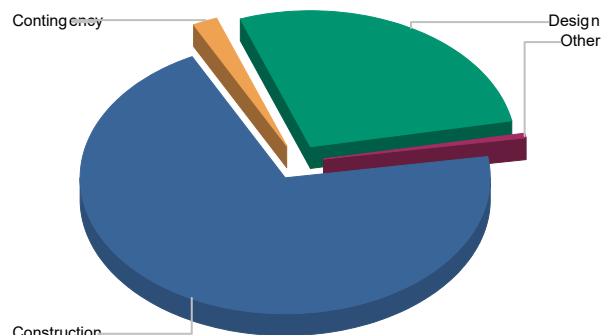

### FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$3,096,507	\$3,053,730	98.62%	\$2,933,781
Construction	\$7,868,421	\$7,204,857	91.57%	\$7,166,663
Furniture, Fixtures & Equipment	\$0	\$0	0.00%	\$0
Other	\$55,740	\$62,260	111.70%	\$62,260
Contingency	\$215,183	\$0	0.00%	\$0
<b>TOTAL</b>	<b>\$11,235,851</b>	<b>\$10,320,847</b>	<b>91.86%</b>	<b>\$10,162,704</b>

### NOTES

Phase II financial reconciliation final will be a scheduled agenda item for the BCC meeting on August 22, 2023.



# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects


Data Date: 05/18/2023

Report Date: 05/31/2023

DESCRIPTION/TEAM	SCOPE	PHOTO
<p><b>Project Title:</b> Palm Beach Lakes Blvd over FEC R/R</p> <p>Project Number: 1532            BCC District: 07            Delivery Method: Design CCNA            Category: B04-Bridge Modifications            Status: Design            Designer: HNTB            Contractor: TBD            Project Manager: Maroun Azzi</p>	<p>This project will rehabilitate an existing bridge that was built over 50 years ago. The project will improve traffic safety (lane widths, pedestrian barrier, railings) and may involve other improvements such as shoulders, bike lanes, and sidewalks.</p> <p>FY 2017 IST \$1,500,000            FY 2021 IST \$4,500,000            FY 2025 IST \$8,300,000</p>	

SCHEDULE SUMMARY		
	Original	Actual
Project Start	9/30/2017	9/30/2017
Consultant Procurement Finish	9/3/2019	12/1/2019
Study Start	4/7/2020	4/7/2020
Design Complete	4/1/2026	
Permit Application	6/1/2024	
Permit Issued	12/25/2025	
Construction Start	1/1/2027	
Construction Complete	1/1/2029	
Study Complete	5/1/2022	4/1/2022
Design Start	4/1/2023	5/10/2023

PARTICIPATION	
<b>Consultant</b>	
SBE	36.5%
Local	96%
WBE	TBD
MBE	TBD
<b>Contractor</b>	
SBE	TBD
Local	TBD
WBE	TBD
MBE	TBD

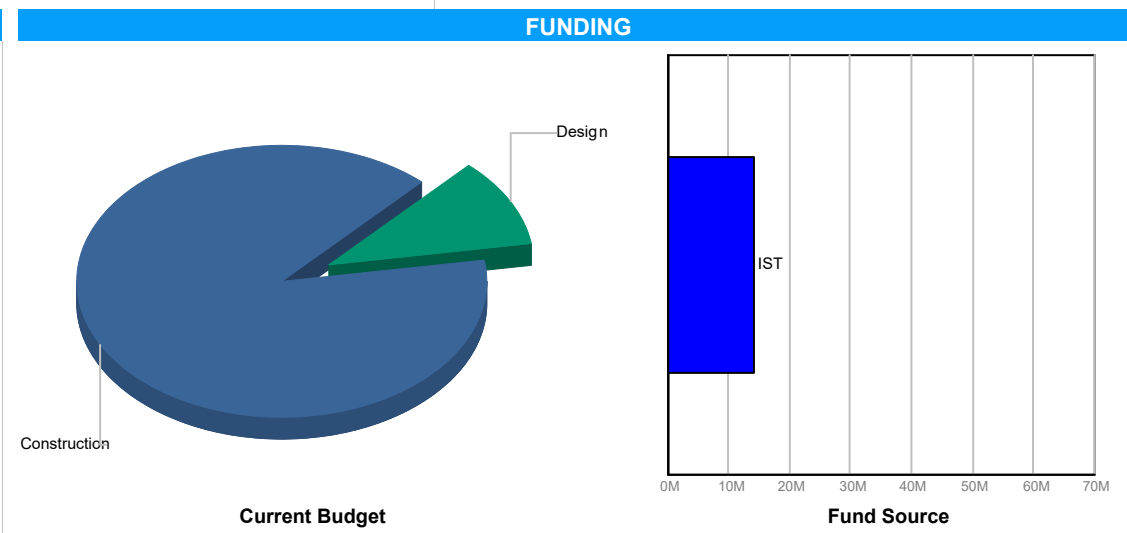

FINANCIAL SUMMARY				
	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$1,500,000	\$1,501,024	100.07%	\$314,716
Construction	\$12,800,000	\$689	0.01%	\$689
Other	\$0	\$15,327	0.00%	\$15,327
Contingency	\$0	\$0	0.00%	\$0
<b>TOTAL</b>	<b>\$14,300,000</b>	<b>\$1,517,040</b>	<b>10.61%</b>	<b>\$330,732</b>

**NOTES**

Initial coordination has been completed with stakeholders including the City of West Palm Beach and the Community Redevelopment Agency to determine scope and design parameters for the rehabilitation of the bridge superstructure. Design is ongoing (0% complete). The scheduled dates have been revised to depict coordination, planning, and scope delays.





# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects

Data Date: 05/18/2023

Report Date: 05/31/2023

### DESCRIPTION/TEAM

### SCOPE

### PHOTO

**Project Title:** Sections of Jog Road  
**Project Number:** 1537  
**BCC District:** Multiple  
**Delivery Method:** Annual Striping Contract  
**Category:** S16-Striping  
**Status:** Construction  
**Designer:** N/A  
**Contractor:** Oglesby  
**Project Manager:** Larry Kelly

This project consists of restriping sections of Jog Road.  
 FY 2017 \$350,000  
 FY 2021 \$150,000  
 FY 2022 \$100,000  
 FY 2023 \$100,000  
 FY 2024 \$200,000  
 FY 2026 \$200,000



### SCHEDULE SUMMARY

### PARTICIPATION

### FUNDING


	Original	Actual
Summit to Gun Club Complete	9/20/2017	9/20/2017
PGA to Hood Complete	10/31/2017	10/31/2017
10th Avenue N. to Summit Complete	1/22/2018	1/22/2018
Wallis to Roebuck Complete	3/7/2018	3/7/2018
Gateway to S. of Hypoluxo Complete	12/17/2018	10/18/2018
Glades to NW 55th St.	3/19/2019	3/19/2019
Hood to Donald Ross	12/2/2020	12/12/2020
N. Oriole to Lake Ida	4/3/2021	3/9/2021
Beeline to Northlake	5/11/2023	5/11/2023

#### Consultant


SBE N/A  
 Local N/A  
 WBE N/A  
 MBE N/A

#### Contractor

SBE 61%  
 Local 61%  
 WBE 0%  
 MBE 0%

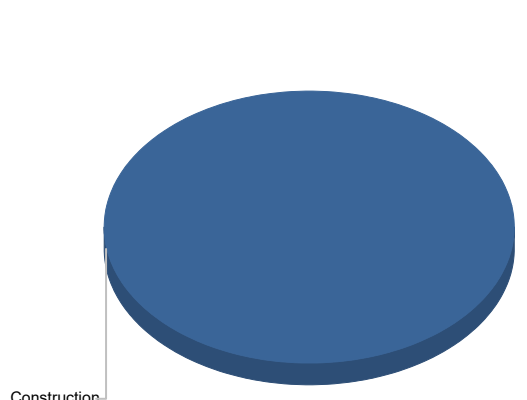

Current Budget

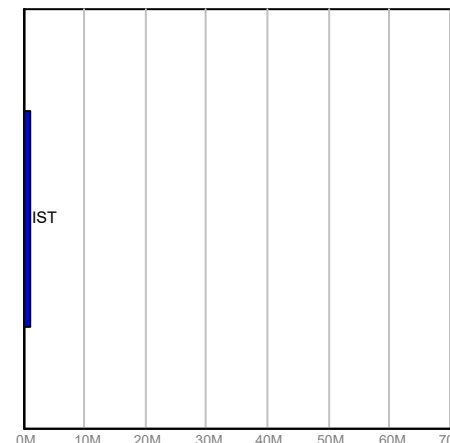

Fund Source

### FINANCIAL SUMMARY

### NOTES

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$0	\$0	0.00%	\$0
Construction	\$1,100,000	\$498,564	45.32%	\$367,829
Contingency	\$0	\$0	0.00%	\$0
<b>TOTAL</b>	<b>\$1,100,000</b>	<b>\$498,564</b>	<b>45.32%</b>	<b>\$367,829</b>

Jog Road is a North-South major County thoroughfare. This project consists of re-striping sections of Jog Road. Restriping continues on an as needed basis.



# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects

Data Date: 05/18/2023

Report Date: 05/31/2023

### DESCRIPTION/TEAM

### SCOPE

### PHOTO

**Project Title:** CR 880

Resurfacing approximately 2.5 miles (5 lane miles) of a portion of County Road 880 from Main Street to S.R. 80 each year.

Project Number: 1539  
 BCC District: 06  
 Delivery Method: Annual Construction Contract  
 Category: R04-Resurfacing  
 Status: Construction  
 Designer: N/A  
 Contractor: Community  
 Project Manager: Darren Prainito



### SCHEDULE SUMMARY

	Original	Actual
FY 2017 Construction Complete	12/22/2017	12/22/2017
FY 2018 Construction Complete	12/7/2018	11/30/2018
FY 2019 Construction Complete	12/31/2019	11/1/2019
FY 2020 Construction Complete	12/18/2020	12/3/2020
FY 2021 Construction Complete	12/17/2021	10/5/2021
FY 2022 Construction Complete	12/16/2022	7/14/2022
FY 2023 Construction Complete	12/15/2023	

### PARTICIPATION



#### Consultant

SBE N/A  
 Local N/A  
 WBE N/A  
 MBE N/A

#### Contractor

SBE 8.7%  
 Local 95.8%  
 WBE 0%  
 MBE 0%

### FUNDING

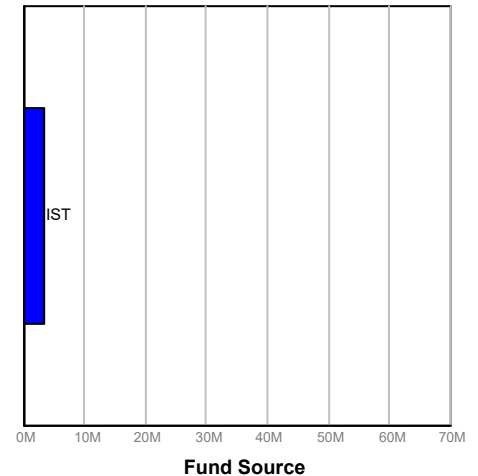

### FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$0	\$2,328	0.00%	\$2,328
Construction	\$3,300,000	\$1,320,999	40.03%	\$1,320,999
Contingency	\$0	\$0	0.00%	\$0
<b>TOTAL</b>	<b>\$3,300,000</b>	<b>\$1,323,327</b>	<b>40.10%</b>	<b>\$1,323,327</b>

### NOTES

County Road 880 is approximately 19 miles in length. This project entails resurfacing a portion of County Road 880 each year. Construction complete for FY2017 thru 2022.



# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects

Data Date: 05/18/2023

Report Date: 05/31/2023

### DESCRIPTION/TEAM

### SCOPE

### PHOTO

**Project Title:** Brown's Farms Road

Resurfacing approximately 2 miles (4 lane miles) of a portion of Brown's Farm Road from CR 880 to South Terminus each year.

Project Number: 1540  
 BCC District: 06  
 Delivery Method: Annual Construction Contract  
 Category: R04-Resurfacing  
 Status: Construction  
 Designer: N/A  
 Contractor: Community  
 Project Manager: Darren Prainito



### SCHEDULE SUMMARY

	Original	Actual
FY 2017 Construction Complete	12/22/2017	12/22/2017
FY 2018 Construction Complete	12/1/2018	11/30/2018
FY 2019 Construction Complete	12/31/2019	11/1/2019
FY 2020 Construction Complete	12/18/2020	12/2/2020
FY2021 Construction Complete	12/17/2021	10/18/2021
FY 2022 Construction Complete	12/22/2022	7/19/2022
FY 2023 Construction Complete	12/19/2023	

### PARTICIPATION



#### Consultant

SBE N/A  
 Local N/A  
 WBE N/A  
 MBE N/A

#### Contractor

SBE 7.4%  
 Local 94.4%  
 WBE 0%  
 MBE 0%

### FUNDING

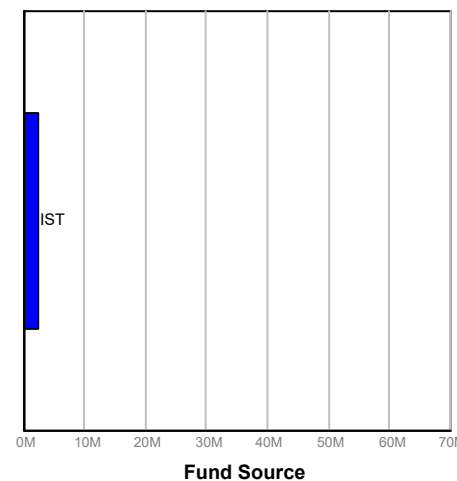

### FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$0	\$1,588	0.00%	\$1,588
Construction	\$2,300,000	\$1,157,401	50.32%	\$1,157,401
Contingency	\$0	\$0	0.00%	\$0
<b>TOTAL</b>	<b>\$2,300,000</b>	<b>\$1,158,989</b>	<b>50.39%</b>	<b>\$1,158,989</b>

### NOTES

Brown's Farm Road is approximately 14 miles in length. This project entails resurfacing a portion of Brown's Farm Road each year. Construction complete for FY2017 thru 2022.



# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects

Data Date: 05/18/2023

Report Date: 05/31/2023

### DESCRIPTION/TEAM

### SCOPE

### PHOTO

**Project Title:** Prosperity Farms Rd. over SFWMD C-17 Canal (934116)  
**Project Number:** 1555  
**BCC District:** 01  
**Delivery Method:** Design CCNA  
**Category:** B08-Bridge Replacements  
**Status:** Design  
**Designer:** Scalar  
**Contractor:** TBD - (bid)  
**Project Manager:** Will Carey

This project will replace an existing bridge that was built over 60 years ago. The new bridge will improve traffic safety (lane widths, bike lanes, parapets), improve roadway drainage, and enhance pedestrian sidewalk safety. Note the current bridge is weight restricted.  
 FY 2018 IST \$500,000  
 FY 2021 IST \$1,500,000  
 FY 2022 IST \$6,000,000



### SCHEDULE SUMMARY

	Original	Actual
Design Contract Notice to Proceed	11/19/2019	11/19/2019
Design Completion	4/1/2023	
Construction Bid Date	7/1/2023	
Construction Start	11/1/2023	
Construction Complete	12/1/2025	

### PARTICIPATION


#### Consultant

SBE 98%  
 Local 100%  
 WBE 0%  
 MBE 0%

#### Contractor

SBE TBD  
 Local TBD  
 WBE TBD  
 MBE TBD

### FUNDING

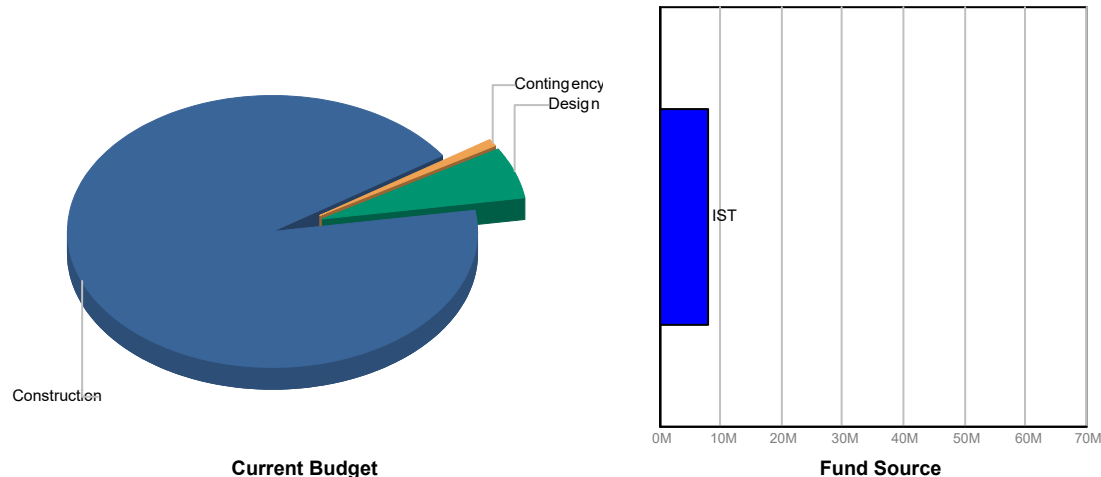

### FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$500,000	\$496,339	99.27%	\$422,436
Construction	\$7,450,000	\$10,810	0.15%	\$5,275
Contingency	\$50,000	\$8,365	16.73%	\$8,365
<b>TOTAL</b>	<b>\$8,000,000</b>	<b>\$515,514</b>	<b>6.44%</b>	<b>\$436,076</b>

### NOTES

Design is ongoing (90% complete).



# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects

Data Date: 05/18/2023

Report Date: 05/31/2023

### DESCRIPTION/TEAM

### SCOPE

### PHOTO

**Project Title:** Belvedere Rd over E-3 canal (934205 & 934206)  
**Project Number:** 1556  
**BCC District:** 02  
**Delivery Method:** Design CCNA  
**Category:** B08-Bridge Replacements  
**Status:** Design  
**Designer:** Stantec  
**Contractor:** TBD (bid)  
**Project Manager:** Maroun Azzi

This project will replace the existing bridges that were built over 40 years ago. The new bridge(s) will improve traffic safety (lane widths, bike lanes, parapets), update the guardrail system, improve roadway drainage, restore the slope protection, and enhance pedestrian sidewalk safety.  
 FY 2018 IST \$450,000  
 FY 2021 IST \$1,350,000  
 FY 2022 IST \$300,000



### SCHEDULE SUMMARY



	Original	Actual
Design Contract Notice to Proceed	10/22/2019	10/22/2019
Design Completion	12/1/2023	
Construction Bid Date	3/1/2024	
Construction Start	8/1/2024	
Construction Complete	3/1/2026	

### PARTICIPATION

**Consultant**  
 SBE 30%  
 Local 100%  
 WBE 0%  
 MBE 0%

**Contractor**  
 SBE TBD  
 Local TBD  
 WBE TBD  
 MBE TBD

### FUNDING

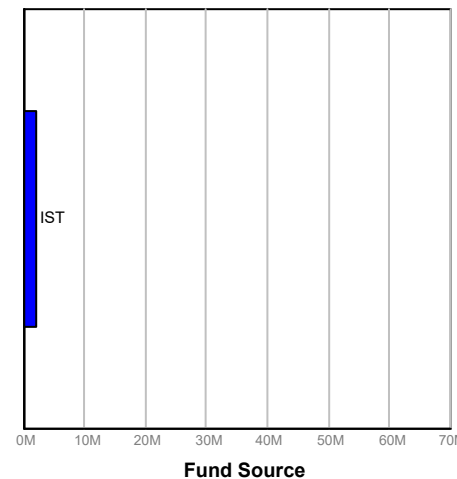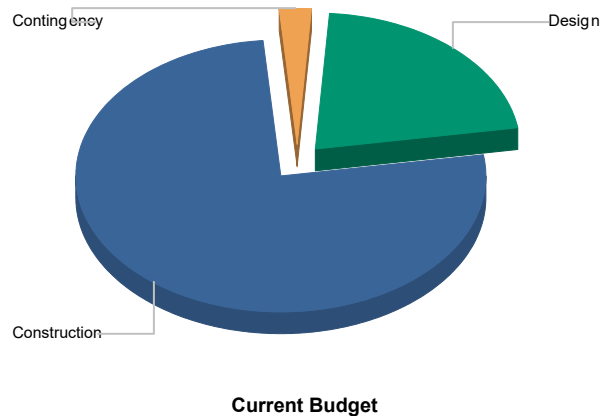

### FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$450,000	\$402,311	89.40%	\$282,540
Construction	\$1,600,000	\$5,770	0.36%	\$5,770
Contingency	\$50,000	\$0	0.00%	\$0
<b>TOTAL</b>	<b>\$2,100,000</b>	<b>\$408,081</b>	<b>19.43%</b>	<b>\$288,310</b>

### NOTES

Design is ongoing (75% complete).



# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects

Data Date: 05/18/2023

Report Date: 05/31/2023

### DESCRIPTION/TEAM

**Project Title:** Various other locations Countywide

Project Number: 1558  
 BCC District: Multiple  
 Delivery Method: Annual Construction Contract  
 Category: D02-Drainage (Pipe Replacements)  
 Status: Construction  
 Designer: N/A  
 Contractor: Hinterland  
 Project Manager: Darren Prainito

### SCOPE

This project will repair and/or replace existing pipe culverts and drainage structures along various roads and canals Countywide. These repairs are needed in order to properly drain and maintain the various roads and canals in a safe operating condition.

### PHOTO



### SCHEDULE SUMMARY

	Original	Actual
Jupiter Farms (133rd Rd. & 156th St.)	8/1/2018	3/12/2018
1069 Edgehill Road	8/15/2018	6/12/2018
Limestone Creek & Palm Garden St.	8/1/2018	7/17/2018
3261 Atlantic Road	8/15/2018	7/1/2018
Van Buren Road @ E-3 Canal	8/1/2018	6/15/2018
19506 Trails End Terrace	8/1/2018	5/11/2018
Jupiter Farms (4 locates)	10/15/2018	8/21/2018
6361 Wood Lake Rd./19650 Red Maple F	10/1/2018	10/1/2018
19598 Trails End Terrace	9/15/2018	8/20/2018
19582 Trails End Terrace	9/1/2018	9/1/2018
6558 Wood Lake Road	9/15/2018	9/14/2018
6126 Wood Lake Road	10/15/2018	12/12/2018
6528 Wood Lake Road	11/1/2018	12/12/2018

### PARTICIPATION


#### Consultant

SBE N/A  
 Local N/A  
 WBE N/A  
 MBE N/A

#### Contractor

SBE 100%  
 Local 100%  
 WBE 0%  
 MBE 0%

### FUNDING

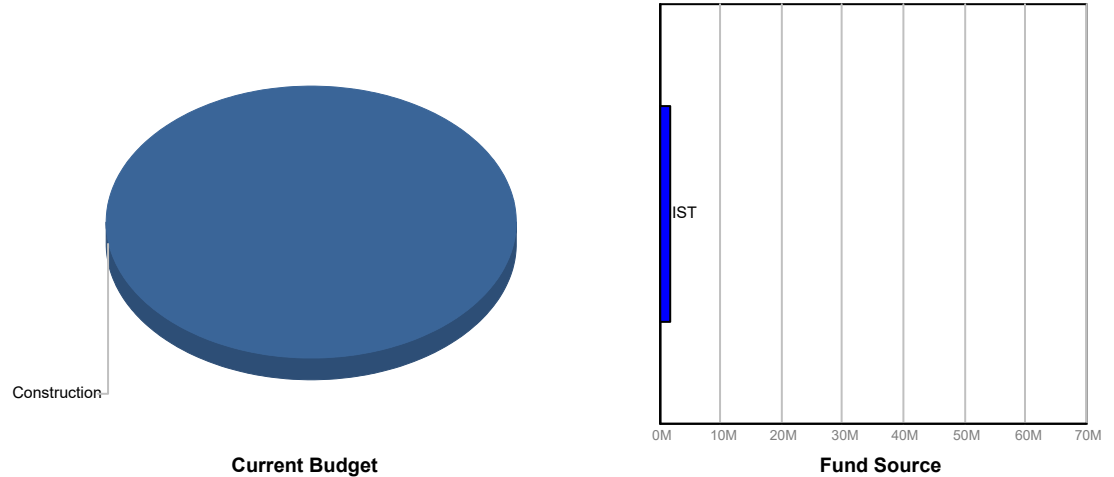

### FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Construction	\$1,700,000	\$1,033,762	60.81%	\$625,009
Contingency	\$0	\$0	0.00%	\$0
<b>TOTAL</b>	<b>\$1,700,000</b>	<b>\$1,033,762</b>	<b>60.81%</b>	<b>\$625,009</b>

### NOTES

This project is funded in:  
 FY 2018 \$500,000, FY 2021 \$500,000, FY 2022 \$200,000  
 FY 2023 \$200,000, FY 2024 \$200,000, FY 2025 \$100,000

The total project is estimated at \$1,700,000.



# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects

Data Date: 05/18/2023

Report Date: 05/31/2023

### DESCRIPTION/TEAM

**Project Title: Video Detection (80 +/- intersection)**

Project Number: 1580  
 BCC District: Multiple  
 Delivery Method: Annual Traffic Signals Contract  
 Category: S08-Signals and Signal Systems  
 Status: Construction  
 Designer: N/A  
 Contractor: Gerelco  
 Project Manager: Fattoush Jafar

### SCOPE

This project will replace the traffic detection at numerous signalized intersections from the existing inductive loop system to video detection. The video detection system is more reliable and easier to maintain.

### PHOTO



### SCHEDULE SUMMARY

	Original	Actual
Military Tr. & Garden Lake	8/1/2018	11/21/2018
Gateway & Renaissance Commons	9/1/2018	4/3/2019
Australian & Turnage	10/1/2018	1/7/2019
Woolbright & Hagen Ranch	11/1/2018	4/4/2019
Belvedere & Country Club Road	12/1/2018	4/4/2019
Palm Beach Lakes & Wellesley	1/1/2019	4/4/2019

### PARTICIPATION


#### Consultant

SBE N/A  
 Local N/A  
 WBE N/A  
 MBE N/A

#### Contractor

SBE 0%  
 Local 23%  
 WBE 0%  
 MBE 0%

### FUNDING

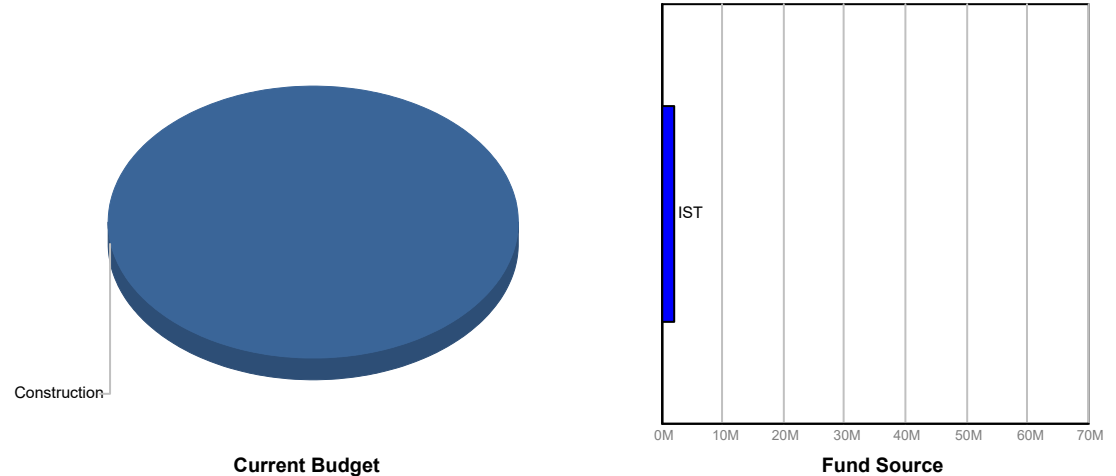

### FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Construction	\$2,200,000	\$199,136	9.05%	\$199,136
Contingency	\$0	\$0	0.00%	\$0
<b>TOTAL</b>	<b>\$2,200,000</b>	<b>\$199,136</b>	<b>9.05%</b>	<b>\$199,136</b>

### NOTES

Work has been completed at six intersections. This project is funded in:  
 FY 2018 \$200,000  
 FY 2023 \$300,000  
 FY 2024 \$800,000  
 FY 2026 \$900,000  
 The total project is estimated at \$2,200,000.



# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects

Data Date: 05/18/2023

Report Date: 05/31/2023

### DESCRIPTION/TEAM

### SCOPE

### PHOTO

**Project Title:** FY 2018 Street Lighting LED Replacements - Countywide  
**Project Number:** 1581  
**BCC District:** CW  
**Delivery Method:** Florida Power and Light  
**Category:** S14-Street Lighting  
**Status:** Construction  
**Designer:** Florida Power and Light  
**Contractor:** Florida Power and Light  
**Project Manager:** May Cheng

These projects will replace the high pressure sodium street lights with LED lights. Many of the street lights along County roads are owned and maintained by Florida Power and Light (FPL) with the County paying all the operation and maintenance costs (including power). FPL will be responsible for the final design and installation to convert the street lighting to the newer LED technology, and the County will reimburse FPL all applicable conversion costs. The result will provide a cost savings, better quality illumination, and a more desirable environmental light source.



### SCHEDULE SUMMARY

	Original	Actual
Gun Club Road/Bosque to Congress	8/16/2019	8/16/2019
Congress/Okeechobee to Belvedere	8/16/2019	8/16/2019
10th Avenue North/Haverhill to Kirk	12/11/2019	12/11/2019
Community/Haverhill to Military	8/16/2019	8/16/2019
Haverhill Road/WPB City to Haverhill City		
Glades Road/State Road 7 to Boca Rio		
Boynton Beach Boulevard/Turnpike to Kn		
Jog Road/Belvedere to State Road 80	7/28/2021	7/28/2021
Forest Hill/Turnpike to Pinehurst & Jog to		
Haverhill/State Road 80 to Lake Worth		
Congress/Lantana to Hypoluxo & Gun Cl	9/14/2021	9/14/2021
Gateway/Military to Windward	8/1/2019	8/1/2019
Belvedere Road/RPB City to Haverhill Cit		

### PARTICIPATION


#### Consultant

SBE N/A  
 Local N/A  
 WBE N/A  
 MBE N/A


#### Contractor

SBE N/A  
 Local N/A  
 WBE N/A  
 MBE N/A

### FUNDING

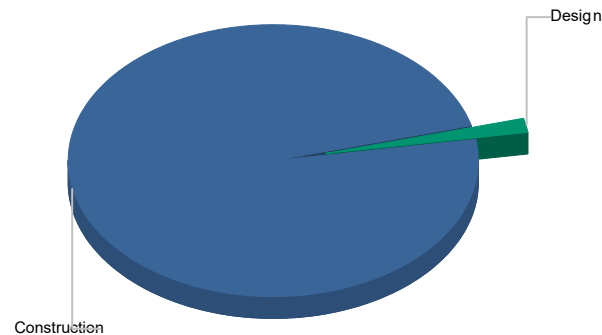

Current Budget

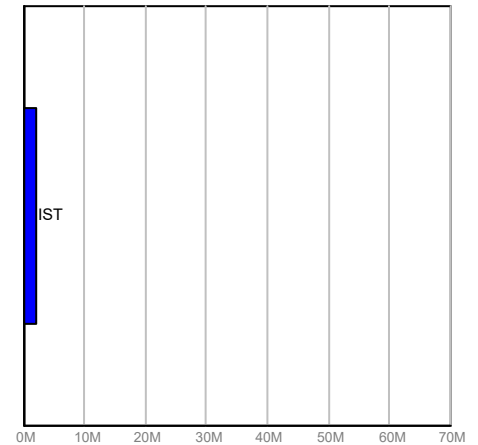

Fund Source

### FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$30,000	\$26,175	87.25%	\$26,175
Construction	\$1,920,000	\$1,799,372	93.72%	\$598,540
Contingency	\$0	\$0	0.00%	\$0
<b>TOTAL</b>	<b>\$1,950,000</b>	<b>\$1,825,546</b>	<b>93.62%</b>	<b>\$624,714</b>

### NOTES

There are 16 street lighting projects (road segments) funded (\$1,950,000) for conversion in FY 2018. All 16 projects have been forwarded to FPL requesting final design and installation. As of 12/1/22, eight projects have been completed, and the street lighting along a portion of the Hypoluxo Road project has also been converted.






# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects


Data Date: 05/18/2023

Report Date: 05/31/2023

DESCRIPTION/TEAM	SCOPE	PHOTO
<p><b>Project Title:</b> Courthouse Electronics System R&amp;R/Command Center</p> <p>Project Number: 16208</p> <p>BCC District: 07</p> <p>Delivery Method: Construction Management</p> <p>Category: J02-Judicial</p> <p>Status: Construction</p> <p>Designer: TLC Engineering</p> <p>Contractor: Hedrick Brothers Construction Co., Inc.</p> <p>Project Manager: Rich Avery</p>	<p>Security Systems replacement at the Main County Courthouse including the Security Management System, Access Control System, CCTV system, Duress System, Intercom, Elevator Override, and Fire Alarm. The Project will also include addressing the emergency egress procedures for the facility, as well as build-out for the expansion of the 4th floor Command Center.</p> <p>Total IST, and Ad Valorem funding for this project is \$16,514,475; Total IST funds are \$12,999,700, which are comprised of FY17 IST funds of \$1,300,000 and FY18 IST funds of \$8,699,700 and FY 19 IST funds of \$3,000,000. Ad Valorem funds are \$3,449,845</p>	

SCHEDULE SUMMARY		
	Original	Actual
Project Start	2/19/2016	2/19/2016
Design Start	2/15/2017	2/15/2017
Construction - Start	11/26/2018	1/7/2019
Substantial Completion	2/1/2021	
Project Completion	4/1/2021	

PARTICIPATION	
<b>Consultant</b>	
SBE	13.4%
Local	100%
WBE	N/A
MBE	N/A
<b>Contractor</b>	
SBE	25%
Local	100%
WBE	N/A
MBE	N/A

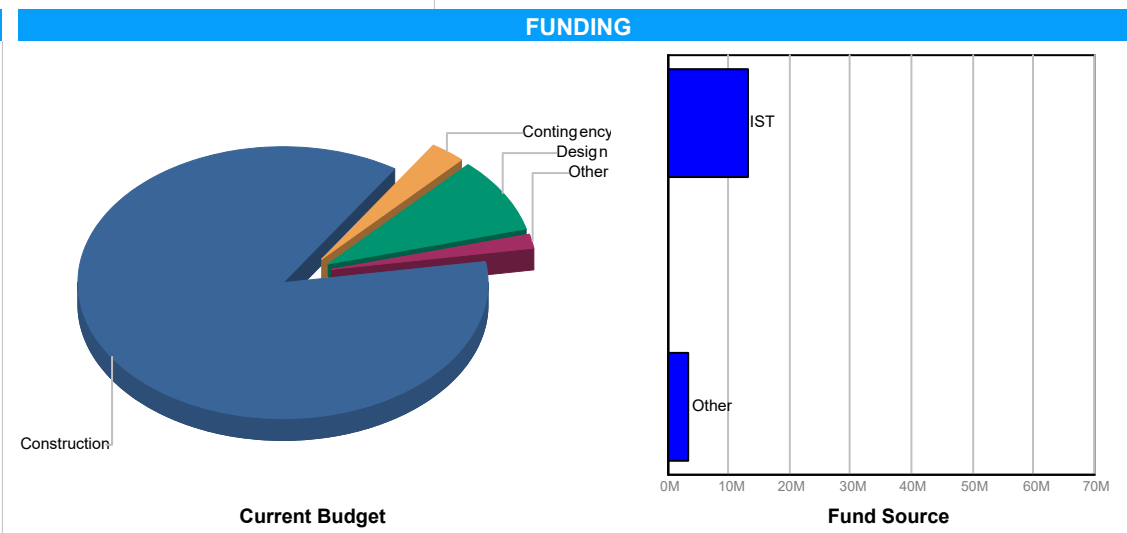

FINANCIAL SUMMARY				
	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$1,456,336	\$1,342,276	92.17%	\$949,157
Construction	\$14,307,700	\$14,282,398	99.82%	\$12,795,746
Furniture, Fixtures & Equipment	\$0	\$0	0.00%	\$0
Other	\$285,139	\$116,320	40.79%	\$116,320
Contingency	\$465,300	\$0	0.00%	\$0
<b>TOTAL</b>	<b>\$16,514,475</b>	<b>\$15,740,995</b>	<b>95.32%</b>	<b>\$13,861,224</b>

**NOTES**

Final substantial completion is pending confirmation of all punch list items being completed.



# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects

Data Date: 05/18/2023

Report Date: 05/31/2023

### DESCRIPTION/TEAM

**Project Title:** Jupiter Beach Rd. over Branch of ICWW

Project Number: 1657  
 BCC District: 01  
 Delivery Method: Design CCNA  
 Category: B08-Bridge Replacements  
 Status: Design  
 Designer: Alan Gerwig & Associates  
 Contractor: TBD  
 Project Manager: Maroun Azzi

### SCOPE

This project will replace an existing bridge that was built over 60 years ago. The project will improve traffic safety (lane widths, bike lanes, sidewalks, etc.) and improve drainage and embankment/slope protection.

### PHOTO



### SCHEDULE SUMMARY

	Original	Actual
Project Start	4/1/2022	4/13/2022
Consultant Procurement Finish	2/1/2023	1/10/2023
Design Start	5/1/2023	1/23/2023
Design Complete	12/1/2025	
Construction Start	6/1/2026	
Construction Complete	12/1/2027	

### PARTICIPATION


#### Consultant

SBE 90%  
 Local 100%  
 WBE 0%  
 MBE 0%


#### Contractor

SBE TBD  
 Local TBD  
 WBE TBD  
 MBE TBD

### FUNDING

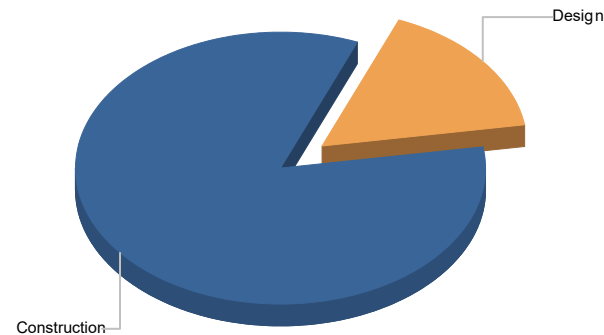

Current Budget

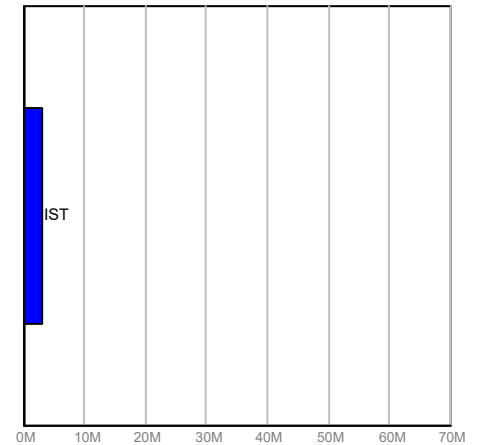

Fund Source

### FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$500,000	\$303,797	60.76%	\$9,251
Construction	\$2,529,000	\$924	0.04%	\$924
<b>TOTAL</b>	<b>\$3,029,000</b>	<b>\$304,721</b>	<b>10.06%</b>	<b>\$10,176</b>

### NOTES

The project is funded for design (\$500k) in FY22 and for construction (\$2.5m) in FY25. Design is ongoing (5% complete)



# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects

Data Date: 05/18/2023

Report Date: 05/31/2023

### DESCRIPTION/TEAM

### SCOPE

### PHOTO

**Project Title:** Australian Ave. from Banyan St. to 45th St.  
**Project Number:** 1658  
**BCC District:** 07  
**Delivery Method:** Design CCNA  
**Category:** D04-Drainage Improvements  
**Status:** Design  
**Designer:** HSQ  
**Contractor:** TBD (Bid)  
**Project Manager:** Maroun Azzi

The project will include drainage improvements (pipd drainage system) and a new paving surface for a wider 4-lane divided section with new pathways on both sides along Australian Avenue from Banyan Blvd. to 45th Street. The work scope may also include replacing the twin bridges over Clear Lake (possible culverts) and replacing the twin bridges over the Carver Canal.



### SCHEDULE SUMMARY

	Original	Actual
Design Start	3/1/2022	4/12/2022
Design Complete	6/1/2024	
Construction Bid Date	9/1/2024	
Construction Start	12/28/2024	
Construction Complete	12/28/2026	

### PARTICIPATION


**Consultant**

- SBE 90.4%
- Local 100%
- WBE 0.4%
- MBE 5.6%

**Contractor**

- SBE TBD
- Local TBD
- WBE TBD
- MBE TBD

### FUNDING

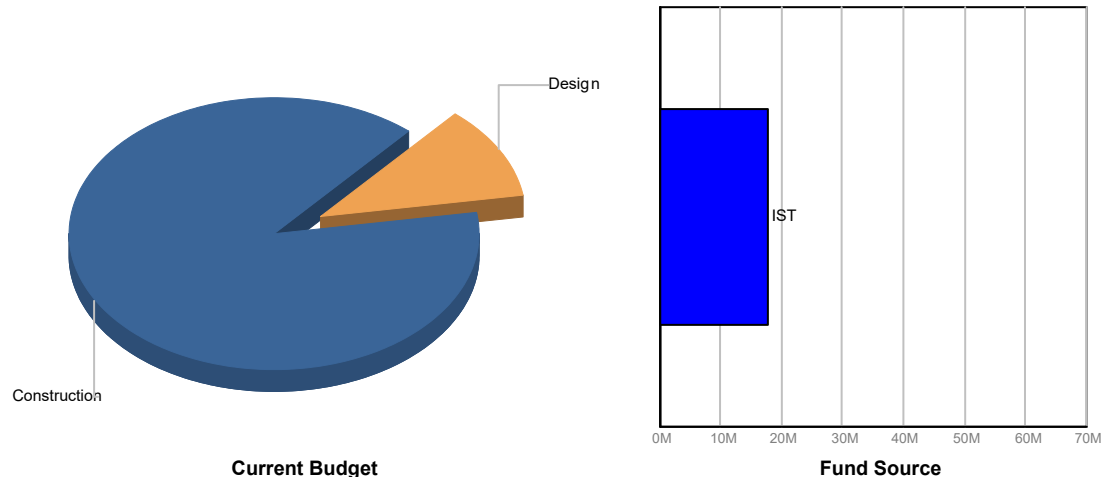

### FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$2,000,000	\$1,686,086	84.30%	\$422,843
Construction	\$15,800,000	\$170,041	1.08%	\$83,495
<b>TOTAL</b>	<b>\$17,800,000</b>	<b>\$1,856,127</b>	<b>10.43%</b>	<b>\$506,338</b>

### NOTES

Design is ongoing (50% complete). The project is funded for design (\$2m) in FY21 and for construction (\$15.8m) in FY24 and FY25. The total cost of the project is estimated at over \$30m. It is anticipated that a Florida Department of Environmental Protection (FDEP) Resiliency grant of \$13.4m will be received for the project.



# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects

Data Date: 05/18/2023

Report Date: 05/31/2023

### DESCRIPTION/TEAM

### SCOPE

### PHOTO

**Project Title:** Belvedere Rd canal piping & sidewalk addition (62nd Dr. N. to Haverhill park)

Project Number: 1661  
 BCC District: 02  
 Delivery Method: Design CCNA  
 Category: P04-Pathways  
 Status: Design  
 Designer: Keshavarz  
 Contractor: TBD (Bid)  
 Project Manager: Maroun Azzi

This project will add a new sidewalk (SW) on the south side of Belvedere Road from 62nd Dr. N. to the Haverhill park (just east of the E-3 Canal) - connecting to the existing south SW at the park's frontage. The SW may require the piping of Lake Worth Drainage District's (LWDD) L-3 Canal.  
 FY 2021 IST \$500,000  
 FY 2024 IST \$3,100,000



### SCHEDULE SUMMARY

	Original	Actual
Study Complete	4/20/2023	
Design Complete		
Construction Bid Date		
Construction Start		
Construction Complete		

### PARTICIPATION


#### Consultant

SBE 100%  
 Local 100%  
 WBE 0%  
 MBE 0%

#### Contractor

SBE TBD  
 Local TBD  
 WBE TBD  
 MBE TBD

### FUNDING

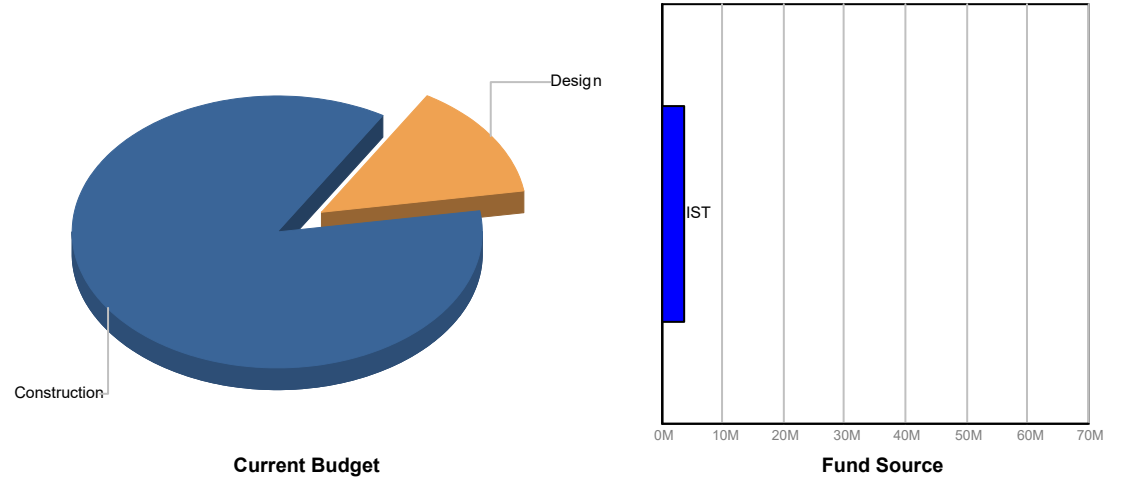

### FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$500,000	\$94,849	18.97%	\$64,099
Construction	\$3,100,000	\$86	0.00%	\$86
<b>TOTAL</b>	<b>\$3,600,000</b>	<b>\$94,935</b>	<b>2.64%</b>	<b>\$64,185</b>

### NOTES

The project is in the study phase to determine a more precise work scope. The project is funded for design (\$500k) in FY21 and for construction (\$3.1M) in FY24.



# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects

Data Date: 05/18/2023

Report Date: 05/31/2023

### DESCRIPTION/TEAM

### SCOPE

### PHOTO

**Project Title:** Seacrest Blvd from Gulfstream Blvd. to Hypoluxo Rd.  
**Project Number:** 1662  
**BCC District:** 07  
**Delivery Method:** Annual Construction Contract  
**Category:** R04-Resurfacing  
**Status:** Construction  
**Designer:** N/A  
**Contractor:** Ranger  
**Project Manager:** Thomas Coppini

Resurfacing 5.8 miles (25.3 lane miles) of Seacrest Boulevard from Gulfstream Boulevard to Hypoluxo Road.  
 FY 2021 IST \$2,400,000  
 FY 2022 IST \$300,000



### SCHEDULE SUMMARY

	Original	Actual
Drainage Repairs	11/1/2021	2/8/2022
Milling and Pavement Complete	2/1/2022	12/22/2021
ADA (Curb/Cut Ramps) Complete	4/1/2022	3/10/2023
Traffic Striping Complete	5/1/2022	2/15/2022
Traffic Loops Complete	7/1/2022	

### PARTICIPATION


#### Consultant

SBE N/A  
 Local N/A  
 WBE N/A  
 MBE N/A

#### Contractor

SBE 15%  
 Local 100%  
 WBE 0%  
 MBE 0%

### FUNDING

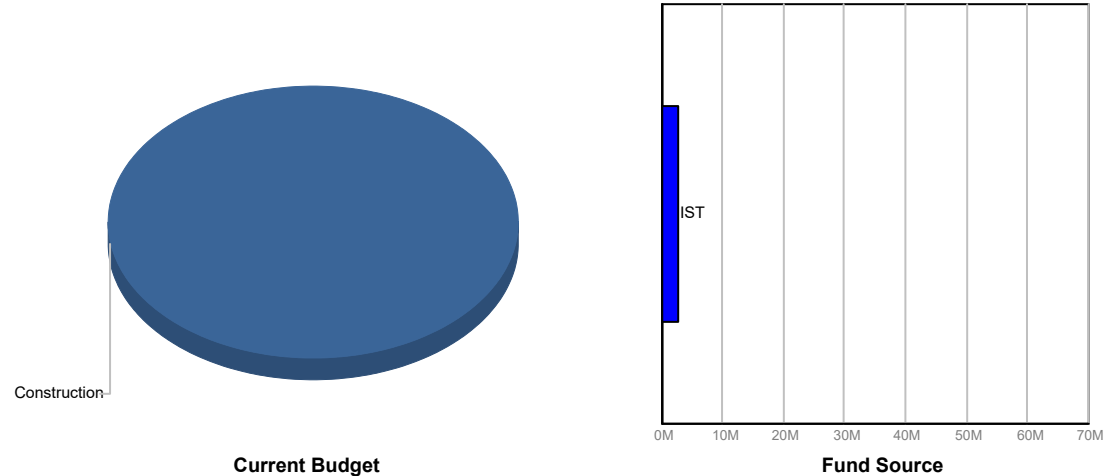

### FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Construction	\$2,700,000	\$2,087,646	77.32%	\$2,087,646
<b>TOTAL</b>	<b>\$2,700,000</b>	<b>\$2,087,646</b>	<b>77.32%</b>	<b>\$2,087,646</b>

### NOTES

Outstanding work includes replacing traffic loops.




# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects


Data Date: 05/18/2023

Report Date: 05/31/2023

DESCRIPTION/TEAM	SCOPE	PHOTO
<p><b>Project Title:</b> Congress Ave. from Palm Beach Lakes to 45th St.</p> <p>Project Number: 1664</p> <p>BCC District: 07</p> <p>Delivery Method: Annual Construction Contract</p> <p>Category: R04-Resurfacing</p> <p>Status: Construction</p> <p>Designer: N/A</p> <p>Contractor: Ranger</p> <p>Project Manager: Darren Prainito</p>	<p>Resurfacing 2.6 miles (11.4 lane miles) of Congress Avenue from Palm Beach Lakes Boulevard to 45th Street.</p> <p>FY2021 IST \$1,000,000</p> <p>FY2024 IST \$250,000</p>	

SCHEDULE SUMMARY		
	Original	Actual
Milling and Pavement Complete	12/1/2023	
ADA (Curb/Cut Ramps) Complete	2/14/2024	
Traffic Striping Complete	1/1/2024	
Traffic Loops Complete	4/1/2024	

PARTICIPATION	
<b>Consultant</b>	
SBE	N/A
Local	N/A
WBE	N/A
MBE	N/A
<b>Contractor</b>	
SBE	15%
Local	100%
WBE	0%
MBE	0%

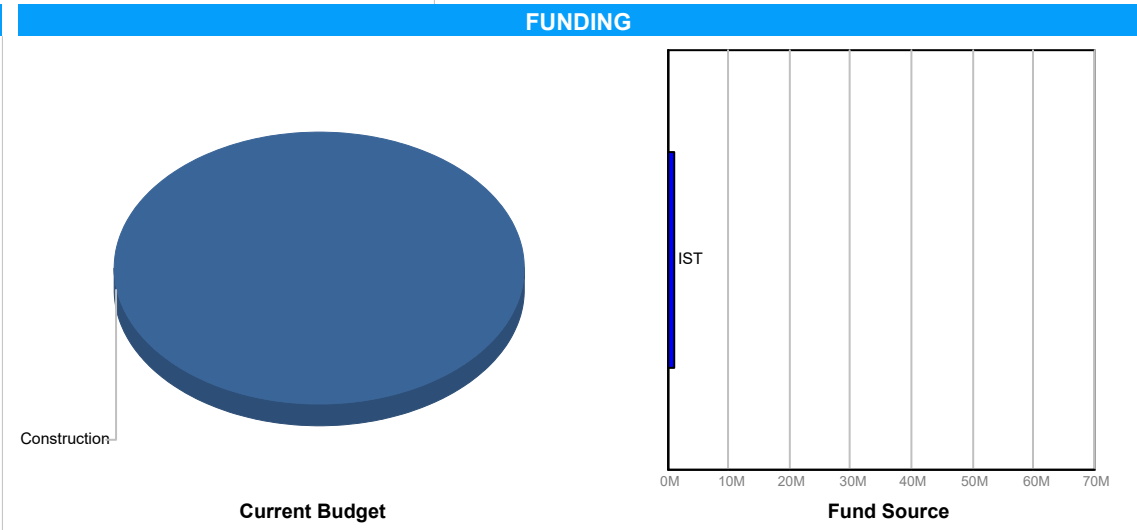

FINANCIAL SUMMARY				
	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Construction	\$1,250,000	\$1,675	0.13%	\$1,675
<b>TOTAL</b>	<b>\$1,250,000</b>	<b>\$1,675</b>	<b>0.13%</b>	<b>\$1,675</b>

**NOTES**

Outstanding work includes milling and paving, updating ADA ramps, restriping the road, and replacing traffic loops.



# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects

Data Date: 05/18/2023

Report Date: 05/31/2023

### DESCRIPTION/TEAM

### SCOPE

### PHOTO

**Project Title:** Belvedere Rd. Canal Piping

Project Number: 1690  
 BCC District: 02  
 Delivery Method: Design CCNA  
 Category: B02-Belvedere Rd. Canal Piping  
 Status: Design  
 Designer: Keith  
 Contractor: TBD (Bid)  
 Project Manager: Maroun Azzi

This project will pipe a portion of a drainage ditch that runs along Belvedere Road and Troy Boulevard - adjacent to Palm Beach International Airport. The embankment area for the ditch is small and difficult to maintain. The undermining of this area continues and compromises the integrity of the sidewalk and road. Piping of the ditch is necessary to properly protect the road and sidewalk.

FY2022 IST \$300,000  
 FY2024 IST \$1,100,000



### SCHEDULE SUMMARY

	Original	Actual
Study Complete	9/1/2023	
Design Complete		
Construction Bid Date		
Construction Start		
Construction Complete		

### PARTICIPATION


#### Consultant

SBE 50%  
 Local 100%  
 WBE 0%  
 MBE 0%

#### Contractor

SBE TBD  
 Local TBD  
 WBE TBD  
 MBE TBD

### FUNDING

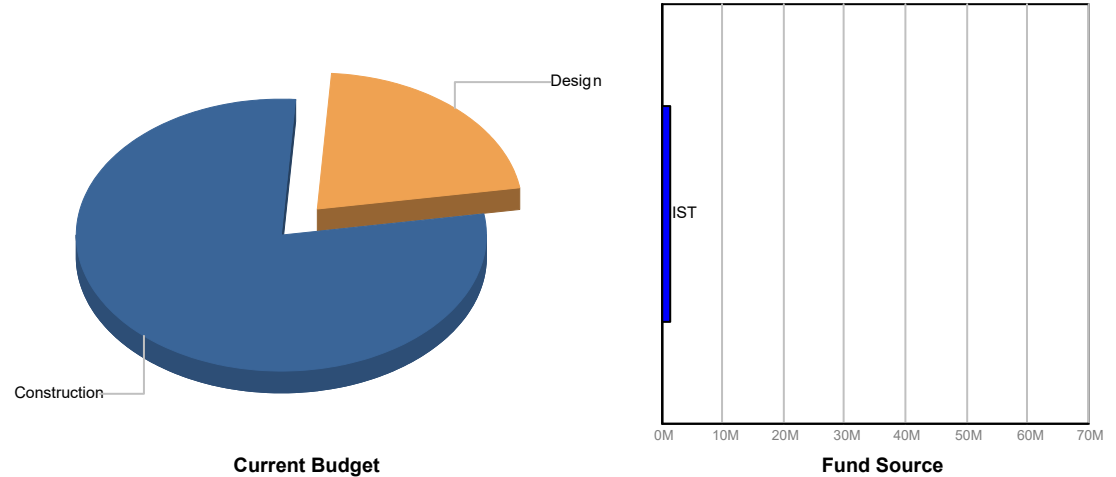

### FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$300,000	\$71,784	23.93%	\$3,519
Construction	\$1,100,000	\$0	0.00%	\$0
<b>TOTAL</b>	<b>\$1,400,000</b>	<b>\$71,784</b>	<b>5.13%</b>	<b>\$3,519</b>

### NOTES

The project is in the study phase to determine a more precise work scope. The project is funded for design (\$300k) in FY22 and for construction (\$1.1m) in FY24.



# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects

Data Date: 05/18/2023

Report Date: 05/31/2023

### DESCRIPTION/TEAM

### SCOPE

### PHOTO

**Project Title:** Summit Blvd. over C-51 Canal (934201)

This project will replace an existing bridge that was built over 50 years ago. The project will improve traffic safety (lane widths, bike lanes, sidewalks, etc.) and improve drainage and embankment/slope protection. The project will also add a left turn lane servicing the adjacent school on the NE quadrant.



Project Number: 1693  
 BCC District: 03  
 Delivery Method: Design CCNA  
 Category: B08-Bridge Replacements  
 Status: Design  
 Designer: Consor Engineers, LLC  
 Contractor: TBD  
 Project Manager: Maroun Azzi

### SCHEDULE SUMMARY

	Original	Actual
Project Start	3/1/2022	3/1/2022
Consultant Procurement Finish	12/1/2022	12/1/2022
Design Start	4/1/2023	3/14/2023
Design Complete	6/1/2026	
Permit Application	1/1/2025	
Permit Issued	6/1/2026	
Construction Start	12/1/2026	
Construction Complete	1/1/2029	

### PARTICIPATION

#### Consultant

SBE 40%

Local 100%

WBE 0%

MBE 0%

#### Contractor



SBE TBD

Local TBD

WBE TBD

MBE TBD

### FUNDING

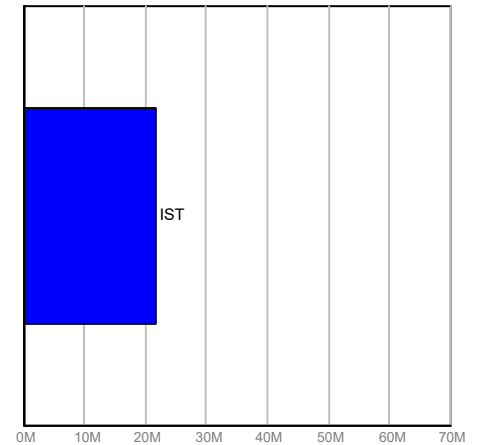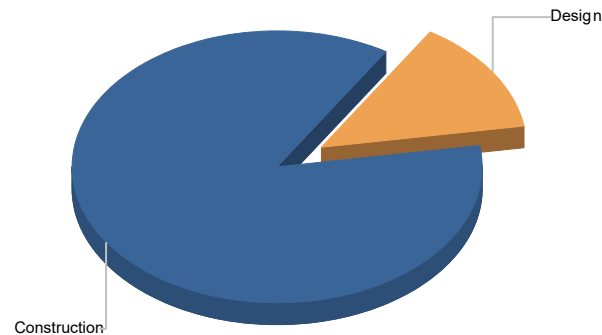

Current Budget

Fund Source

### FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$3,000,000	\$770,185	25.67%	\$12,941
Construction	\$18,863,000	\$0	0.00%	\$0
<b>TOTAL</b>	<b>\$21,863,000</b>	<b>\$770,185</b>	<b>3.52%</b>	<b>\$12,941</b>

### NOTES

The project is funded for design (\$3m) in FY22 and for construction (\$18.863m) in FY27. Design is ongoing (0% complete).





# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects

Data Date: 05/18/2023

Report Date: 05/31/2023

### DESCRIPTION/TEAM

### SCOPE

### PHOTO

**Project Title:** Seminole Colony east (Okeechobee/Military)  
**Project Number:** 1694  
**BCC District:** 07  
**Delivery Method:** Design CCNA  
**Category:** D04-Drainage Improvements  
**Status:** Design  
**Designer:** Masse Consulting Services  
**Contractor:** TBD  
**Project Manager:** Will Carey

The project will include drainage improvements along Seminole Colony East (Spafford Avenue, Scott Avenue, Indian Road, and Gardenia Street) just north of Okeechobee Boulevard.



### SCHEDULE SUMMARY


	Original	Actual
Design Start	4/1/2023	4/1/2023
Design Complete	12/1/2024	
Construction Bid Date	3/1/2025	
Construction Start	7/1/2025	
Construction Complete	7/1/2026	

### PARTICIPATION

**Consultant**  
 SBE 94.6%  
 Local 100%  
 WBE 0%  
 MBE 74.5%

**Contractor**  
 SBE TBD  
 Local TBD  
 WBE TBD  
 MBE TBD

### FUNDING

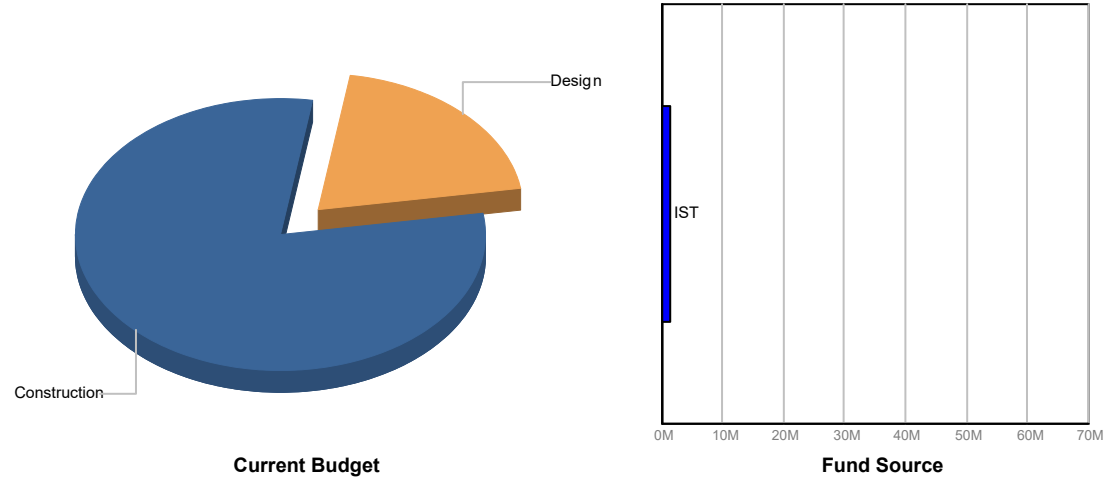

### FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$300,000	\$296,131	98.71%	\$2,581
Construction	\$1,200,000	\$258	0.02%	\$258
<b>TOTAL</b>	<b>\$1,500,000</b>	<b>\$296,389</b>	<b>19.76%</b>	<b>\$2,839</b>

### NOTES

Design is ongoing (0% complete). The project is funded for design (\$300k) in FY22 and for construction (\$1.2m) in FY24.



# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects

Data Date: 05/18/2023

Report Date: 05/31/2023

### DESCRIPTION/TEAM

### SCOPE

### PHOTO

**Project Title:** Palmetto Park Rd. from Glades Rd. to Crawford Blvd.  
**Project Number:** 1697  
**BCC District:** Multiple  
**Delivery Method:** Annual Construction Contract  
**Category:** R04-Resurfacing  
**Status:** Construction  
**Designer:** N/A  
**Contractor:** Ranger Construction Industries, Inc.  
**Project Manager:** Thomas Coppini

Resurfacing 10 miles (51.8 lane miles) of Palmetto Park Road from Glades Road to Crawford Boulevard (SW 3rd Ave.)

Note: There is a pending 5 Yr. Road Program project in FY22 to improve Palmetto Park Road from Military Trail to I-95 that will include resurfacing the existing pavement. There is also an ongoing 5 Yr. Road Program project to replace the bridge over the E-4 (El Rio) Canal (with scheduled completion date in 2023).  
 FY 2022 IST \$4,800,000



### SCHEDULE SUMMARY

	Original	Actual
Milling and Pavement Complete	9/1/2022	
ADA (Curb/Cut Ramps) Complete	12/1/2022	
Traffic Striping Complete	12/1/2022	
Traffic Loops Complete	3/1/2023	

### PARTICIPATION


#### Consultant

SBE N/A  
 Local N/A  
 WBE N/A  
 MBE N/A

#### Contractor

SBE 15%  
 Local 100%  
 WBE 0%  
 MBE 0%

### FUNDING

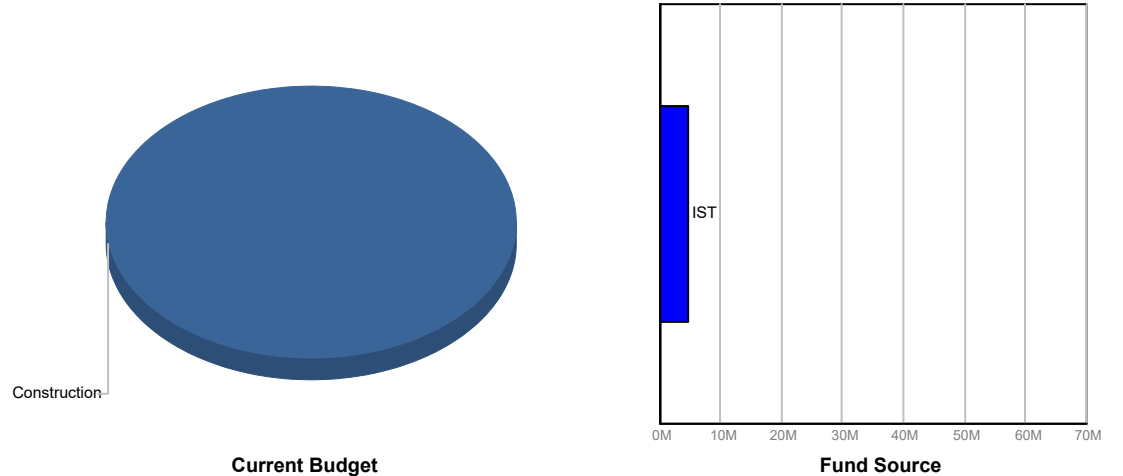

### FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Construction	\$4,800,000	\$4,794,434	99.88%	\$3,952,356
<b>TOTAL</b>	<b>\$4,800,000</b>	<b>\$4,794,434</b>	<b>99.88%</b>	<b>\$3,952,356</b>

### NOTES

Outstanding work includes milling and paving, updating ADA ramps, restriping the road, and replacing traffic loops.

Resurfacing and striping are complete for over 7 miles from Glades Road to Military Trail. Waiting on other projects along Palmetto to coordinate any additional repaving efforts.



# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects

Data Date: 05/18/2023

Report Date: 05/31/2023

### DESCRIPTION/TEAM

### SCOPE

### PHOTO

**Project Title:** Lake Lytal Aquatic Center Replace Public Aquatic Facility

Project Number: 17218

BCC District: 03

Delivery Method: Construction Management at Risk

Category: A02-Aquatic Facility Repair and Replacement

Status: Design

Designer: Harvard Jolly, Inc.

Contractor: Kauffman Lynn/ Hedrick Brothers

Project Manager: Mitchell Silverman

The project entails constructing a new multi-phase Aquatic Complex mainly on undeveloped land along Kirk Rd. within Lake Lytal Park. The existing Pool Facility is to be demolished once the new aquatic center is opened to the public. The major components of the new Aquatic Complex will be a 70 Meter competition pool with dive well, a family water play area, 6-lane warm-up pool, flow riders, slides and building amenities such as restrooms, lockers, concession stand.

FY 2017 IST - \$4,000,000  
 FY 2018 IST - \$2,000,000  
 FY 2023 IST - \$6,152,500



### SCHEDULE SUMMARY

	Original	Actual
Project Start	4/19/2018	4/19/2018
Design Start (Master Plan)	7/10/2018	7/10/2018
Design Start (Aquatic Center)	11/20/2018	5/1/2023
Construction Start	7/1/2019	
Substantial Completion	7/1/2020	
Project Completion	9/1/2020	

### PARTICIPATION

**Consultant**

SBE 30%

Local 100%

WBE N/A

MBE 0%

**Contractor**


SBE 24.66%

Local 0%

WBE 0%

MBE 0%

### FUNDING

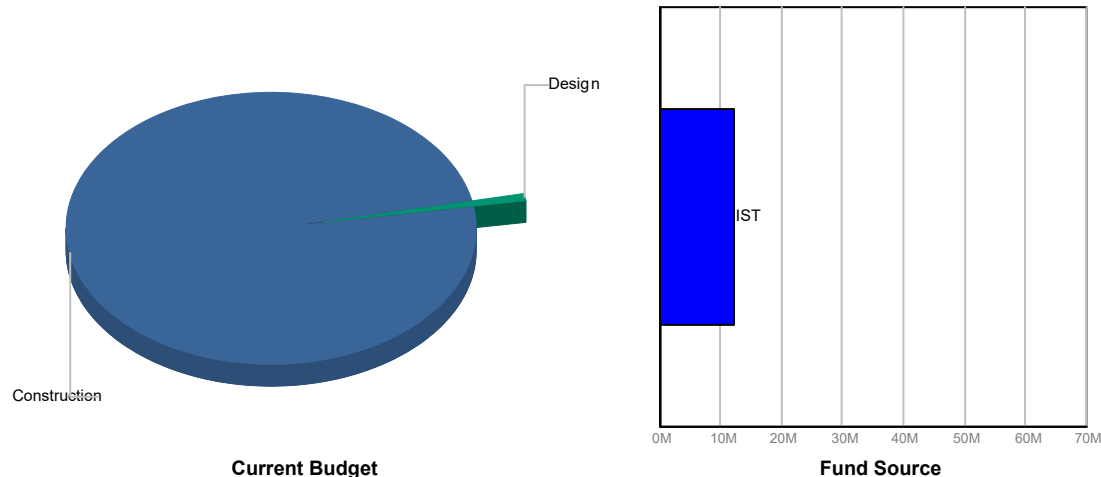

### FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$112,902	\$346,220	306.65%	\$300,908
Construction	\$12,039,598	\$1,024,073	8.51%	\$24,151
Furniture, Fixtures & Equipment	\$0	\$0	0.00%	\$0
Other	\$0	\$37,316	0.00%	\$37,316
Contingency	\$0	\$0	0.00%	\$0
<b>TOTAL</b>	<b>\$12,152,500</b>	<b>\$1,407,609</b>	<b>11.58%</b>	<b>\$362,375</b>

### NOTES

SFWMD permit modification is in progress. Phase 1: Tree barricade awaits permit. Phase 2: Civil/Site work awaits permit. Phase 3: Aquatic Center vertical construction. CM site mobilization will commence on August 1 in preparation for phase 2 Site Development. ERM permit approval is in process. The project is altering the FEMA flood zone and will need a flood map amendment via FEMA. PZB will issue a conditional permit. GMP is under review.




# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects


Data Date: 05/18/2023

Report Date: 05/31/2023

DESCRIPTION/TEAM	SCOPE	PHOTO
<p><b>Project Title:</b> Lantana Rd. from Hagen Ranch Rd. to I-95</p> <p>Project Number: 1731</p> <p>BCC District: Multiple</p> <p>Delivery Method: Annual Construction Contract</p> <p>Category: R04-Resurfacing</p> <p>Status: Design</p> <p>Designer: Mock, Roos &amp; Associates</p> <p>Contractor: TBD</p> <p>Project Manager: Darren Prainito</p>	<p>Resurfacing 5.5 miles (33 lane miles) of Lantana Road from Hagen Ranch Road to I-95.</p> <p>FY2022 IST \$3,280,000</p>	

SCHEDULE SUMMARY		
	Original	Actual
Drainage Repairs Complete	12/1/2023	
Milling and Pavement Complete	6/1/2024	
ADA (Curb/Cut Ramps) Complete	9/1/2024	
Traffic Striping Complete	8/1/2024	
Traffic Loops Complete	12/1/2024	

PARTICIPATION	
<b>Consultant</b>	
SBE	N/A
Local	N/A
WBE	N/A
MBE	N/A
<b>Contractor</b>	
SBE	15%
Local	100%
WBE	0%
MBE	0%

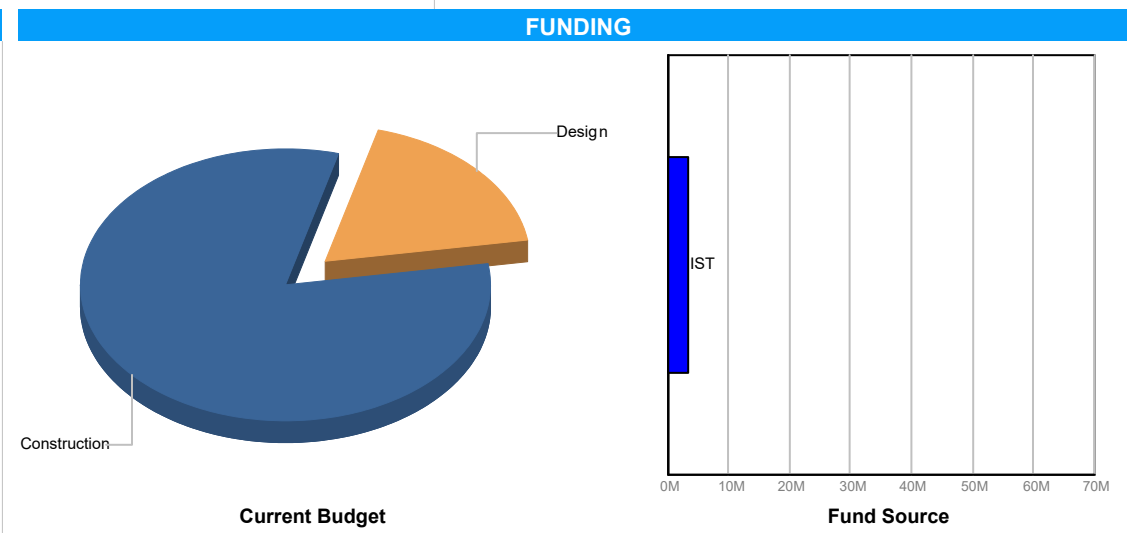

FINANCIAL SUMMARY				
	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$600,000	\$0	0.00%	\$0
Construction	\$2,680,000	\$6,070	0.23%	\$6,070
<b>TOTAL</b>	<b>\$3,280,000</b>	<b>\$6,070</b>	<b>0.19%</b>	<b>\$6,070</b>

**NOTES**

Drainage infrastructure study underway to determine scope of drainage repairs. Outstanding work includes drainage repairs, milling and paving, updating ADA ramps, restriping the road, and replacing traffic loops.



# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects

Data Date: 05/18/2023

Report Date: 05/31/2023

### DESCRIPTION/TEAM

### SCOPE

### PHOTO

**Project Title:** Military Trail from Palmetto to Clint Moore  
**Project Number:** 1780  
**BCC District:** 04  
**Delivery Method:** Annual Construction Contract  
**Category:** R04-Resurfacing  
**Status:** Construction  
**Designer:** N/A  
**Contractor:** Ranger  
**Project Manager:** Darren Prainito

Resurfacing 4.2 miles (25.2 lane miles) of Military Trail from Palmetto Park Road to Clint Moore Road.  
 FY2022 IST \$3,100,000



### SCHEDULE SUMMARY

	Original	Actual
Milling and Pavement Complete	4/1/2023	5/12/2023
ADA (Curb/Cut Ramps) Complete	8/1/2023	
Traffic Striping Complete	6/1/2023	
Traffic Loops Complete	10/1/2023	

### PARTICIPATION


#### Consultant

SBE N/A  
 Local N/A  
 WBE N/A  
 MBE N/A

#### Contractor

SBE 15%  
 Local 100%  
 WBE 0  
 MBE 0

### FUNDING

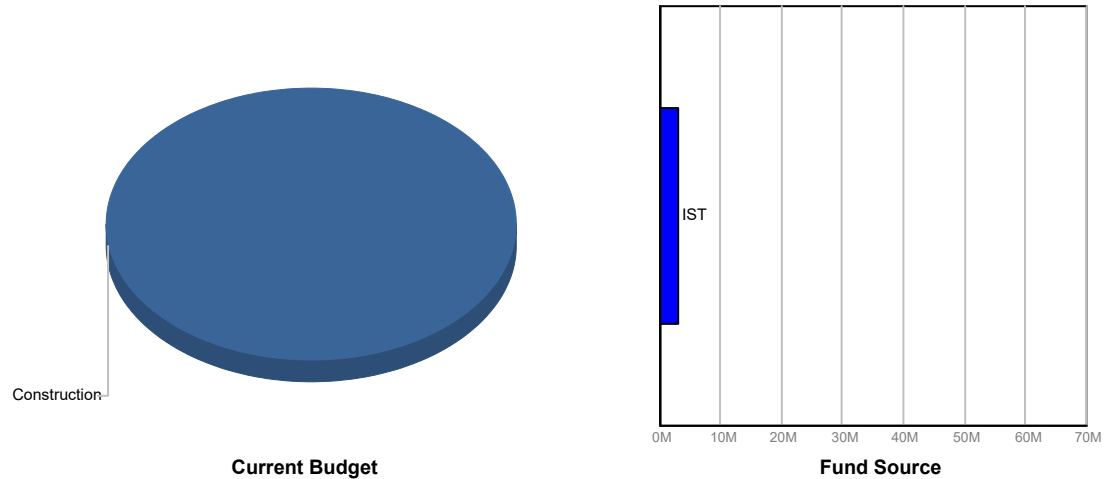

### FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Construction	\$3,100,000	\$2,556,737	82.48%	\$850,334
<b>TOTAL</b>	<b>\$3,100,000</b>	<b>\$2,556,737</b>	<b>82.48%</b>	<b>\$850,334</b>

### NOTES

Outstanding work includes milling and paving, updating ADA ramps, restriping the road, and replacing traffic loops.

This resurfacing project will be phased due to other ongoing work improvements within this Military Trail corridor. The scheduled dates have been revised to depict the delay due to coordination efforts .



# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects

Data Date: 05/18/2023

Report Date: 05/31/2023

### DESCRIPTION/TEAM

### SCOPE

### PHOTO

**Project Title:** Courthouse Buildout and Renovations

Improvement of approximately 100,000 square feet of unfinished interior space upon floors one, seven and eight of the Judge Daniel T.K. Hurley Courthouse in downtown West Palm Beach, as well as other incidental interior improvements. All improvements will implement the Palm Beach County Judicial Facilities Master Plan Update.  
 IST funding consists of:  
 \$8,000,000 in FY 2022,  
 \$24,500,000 in FY 2023  
 \$31,308,437 in FY 2023,  
 \$3,000,000 Impact Fees  
 Total of \$66,808,437.



Project Number: B592  
 BCC District: CW  
 Delivery Method: CMAR  
 Category: J02-Judicial  
 Status: Design  
 Designer: Leo A. Daly  
 Contractor: TBD  
 Project Manager: Rich Avery

### SCHEDULE SUMMARY

	Original	Actual
Design Contract Issued	6/7/2022	6/7/2022
Design Commencement	6/17/2022	6/17/2022
Design Completion	5/18/2023	

### PARTICIPATION



#### Consultant

SBE 25%  
 Local 100%  
 WBE 100%  
 MBE 100%

#### Contractor

SBE TBD  
 Local TBD  
 WBE TBD  
 MBE TBD

### FUNDING

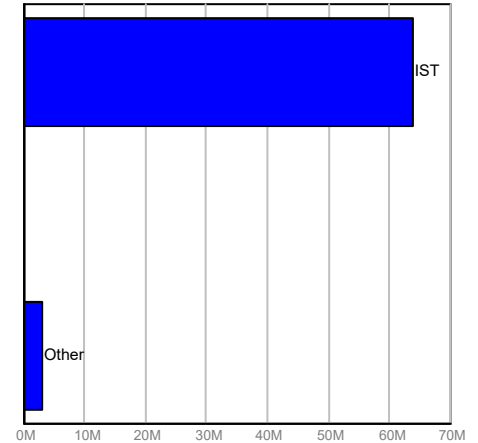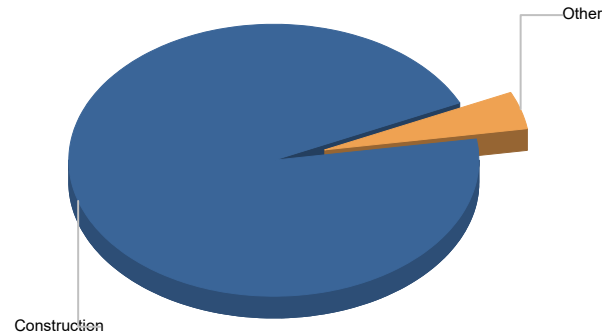

Current Budget

Fund Source

### FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Construction	\$63,808,437	\$0	0.00%	\$0
Other	\$3,000,000	\$1,771,846	59.06%	\$45,658
<b>TOTAL</b>	<b>\$66,808,437</b>	<b>\$1,771,846</b>	<b>2.65%</b>	<b>\$45,658</b>

### NOTES

The preconstruction services scope and fee continues to be negotiated with the Weitz Company. The conceptual floor plans for the 7th & 8th floors have been review by Court Administration. Schematic design has commenced and is ongoing.



# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects

Data Date: 05/18/2023

Report Date: 05/31/2023

### DESCRIPTION/TEAM

### SCOPE

### PHOTO

**Project Title:** Lake Worth West Substation

Provide dedicated office(s) within the HRC2 building (project-19220) for PBSO field personnel's use. Additional interior improvements include a multipurpose room for PBSO training purposes and HRC/community programming, as well as restrooms, circulation area, and other incidental improvements.



Project Number: B607  
 BCC District: Multiple  
 Delivery Method: Construction Manager at Risk  
 Category: S06-Sheriff - FDO  
 Status: Construction  
 Designer: Ohlson Lavoie Collaborative  
 Contractor: D Stephenson  
 Project Manager: Sunil Jagoo

FY 2019 IST \$1,213,460

### SCHEDULE SUMMARY

### PARTICIPATION

### FUNDING



Original	Actual
Please Refer to Central County Resource	

#### Consultant

SBE TBD  
 Local TBD  
 WBE TBD  
 MBE TBD

#### Contractor

SBE TBD  
 Local TBD  
 WBE TBD  
 MBE TBD

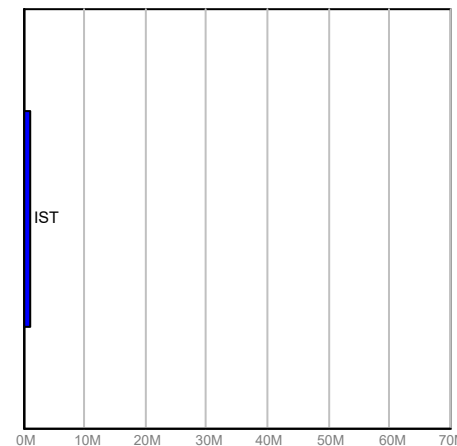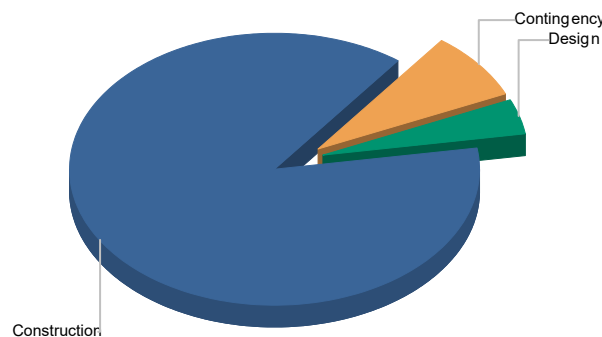

Current Budget

Fund Source

### FINANCIAL SUMMARY

### NOTES

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$50,000	\$2,227	4.45%	\$2,227
Construction	\$1,063,460	\$1,085,373	102.06%	\$1,085,374
Contingency	\$100,000	\$0	0.00%	\$0
<b>TOTAL</b>	<b>\$1,213,460</b>	<b>\$1,087,601</b>	<b>89.63%</b>	<b>\$1,087,601</b>

Please refer to the Central County Resource Center report for current status and material project updates.



# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects

Data Date: 05/18/2023

Report Date: 05/31/2023

### DESCRIPTION/TEAM

### SCOPE

### PHOTO

**Project Title:** PBSO District 1 Substation and Marine Unit  
**Project Number:** B665  
**BCC District:** 02  
**Delivery Method:** CMAR  
**Category:** S06-Sheriff - FDO  
**Status:** Permitting  
**Designer:** Song & Associates  
**Contractor:** Kaufman Lynn  
**Project Manager:** TBA

Construction of an approximately 28,000 square foot facility and site improvements to accommodate the relocation of PBSO District 1 from PBSO Headquarters as well as the relocation of the PBSO Marine Unit from the County's Cherry Road Complex property. The subject site is approximately 5.75 acres and located on the west side of Jog Road approximately 1,000 feet south of Belvedere Road.



### SCHEDULE SUMMARY

	Original	Actual
Submit DRO Application	8/3/2020	8/3/2020
Submit for Permits	3/18/2022	5/6/2022
Construction Complete	10/31/2023	
PBSO Turn Over	11/30/2023	

### PARTICIPATION


**Consultant**

- SBE 77.4%
- Local 100%
- WBE 77.4%
- MBE 77.4%

**Contractor**

- SBE 25%
- Local 100%
- WBE 0%
- MBE 0%

### FUNDING

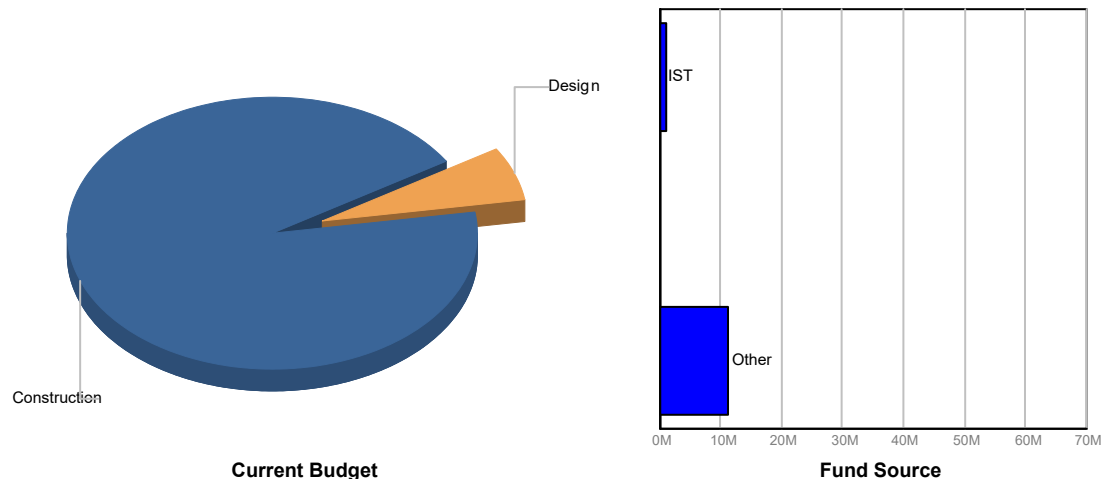

### FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$777,565	\$0	0.00%	\$0
Construction	\$11,525,435	\$951,148	8.25%	\$951,148
<b>TOTAL</b>	<b>\$12,303,000</b>	<b>\$951,148</b>	<b>7.73%</b>	<b>\$951,148</b>

### NOTES

Revisions toward receipt of the Building Permit have been submitted to the Building Division for review. Permits with other agencies having jurisdiction remain in progress. Kaufman Lynn is finalizing its Guaranteed Maximum Price (GMP) to support contract award by the BCC at an upcoming meeting. New PM TBD. IST funding in the amount of \$1M was allocated in FY2022, and we will be relied upon to support the project construction phase.





# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects

Data Date: 05/18/2023

Report Date: 05/31/2023

### DESCRIPTION/TEAM

### SCOPE

### PHOTO

**Project Title:** Housing Units for Homeless, Extremely Low Income, & Low Income  
**Project Number:** Q001  
**BCC District:** CW  
**Delivery Method:** TBD  
**Category:** H02-Housing  
**Status:** Varies  
**Designer:** Varies  
**Contractor:** Varies  
**Project Manager:** Varies

This project involves the delivery of housing units for use as temporary or longer term affordable housing for homeless and special populations.  
  
 This Project is funded in:  
 FY 2017 - FY 2026 for \$2,550,000 each year for a total of \$25,500,000.




### SCHEDULE SUMMARY

	Original	Actual
Project Start	9/1/2017	9/1/2017
Project Completion		

### PARTICIPATION

- Consultant**
- SBE VARIES
  - Local VARIES
  - WBE VARIES
  - MBE VARIES
- Contractor**
- SBE VARIES
  - Local VARIES
  - WBE VARIES
  - MBE VARIES

### FUNDING

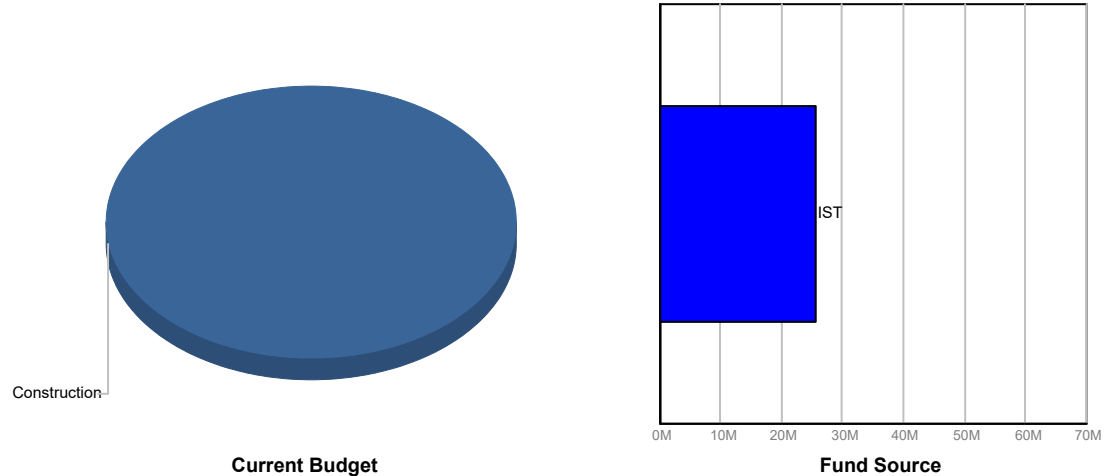

### FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$0	\$12,138	0.00%	\$12,138
Construction	\$25,500,000	\$9,132,606	35.81%	\$974,292
Furniture, Fixtures & Equipment	\$0	\$0	0.00%	\$0
Other	\$0	\$50,674	0.00%	\$50,674
Contingency	\$0	\$0	0.00%	\$0
<b>TOTAL</b>	<b>\$25,500,000</b>	<b>\$9,195,418</b>	<b>36.06%</b>	<b>\$1,037,105</b>

### NOTES

This Project will fund multiple projects over a 10-year period per the direction provided by BCC on September 26, 2017, and February 26, 2019. The Cottage Homes pilot project by the WPB Housing Authority (\$6,073,458.06) broke ground on January 19, 2023 and construction is ongoing. The BCC approved an allocation of \$1M toward the renovation of a non-congregate shelter in Pahokee on Sept. 15, 2020 (\$621,000 expended). A \$2.5M allocation to the Belle Glade Housing Authority for the improvement of 534 housing units in Belle Glade was approved by the BCC on November 1, 2022 and work is ongoing.



# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects

Data Date: 05/18/2023

Report Date: 05/31/2023

### DESCRIPTION/TEAM

### SCOPE

### PHOTO

**Project Title:** Countywide ADA Renovations

Project Number: Q002  
 BCC District: CW  
 Delivery Method: Annual Contract  
 Category: G02-General Government Facilities  
 Status: Construction  
 Designer: Colome' and Associates  
 Contractor: Varies  
 Project Manager: Varies

Renovate multiple public facility restrooms to meet ADA requirements. The following locations are planned for renovation:  
 Delray Health Clinic ADA Restrooms @ \$250K FY2017  
 Lantana Health Clinic ADA Restrooms @ \$275K FY2022  
 Lantana Health Clinic ADA Service Counter @ \$16K FY2022  
 Jupiter Health Clinic ADA Restrooms @ \$64K FY2022  
 West County Administration Building (aka Glades Office Building) ADA Improvements @ \$245K FY2022 and \$450K FY2023

This Project is funded in:  
 FY 2017 \$250,000 FY 2024 \$700,000  
 FY 2022 \$600,000 FY 2025 \$539,000  
 FY 2023 \$450,000




### SCHEDULE SUMMARY

	Original	Actual
Delray Health Start	7/27/2017	7/27/2017
Delray Health Finish	12/21/2018	10/24/2022
Lantana Health Start	7/7/2017	7/7/2017
Lantana Health Finish	4/8/2018	
Lantana Health (Counters) Start	11/24/2020	11/24/2020
Lantana Health (Counters) Finish		
Jupiter Health Start	12/22/2020	12/22/2020
Jupiter Health Finish		
West County Admin Start	6/22/2022	6/1/2023
West County Admin Finish		

### PARTICIPATION

- Consultant**
- SBE Varies
  - Local Varies
  - WBE Varies
  - MBE Varies
- Contractor**
- SBE Varies
  - Local Varies
  - WBE Varies
  - MBE Varies

### FUNDING

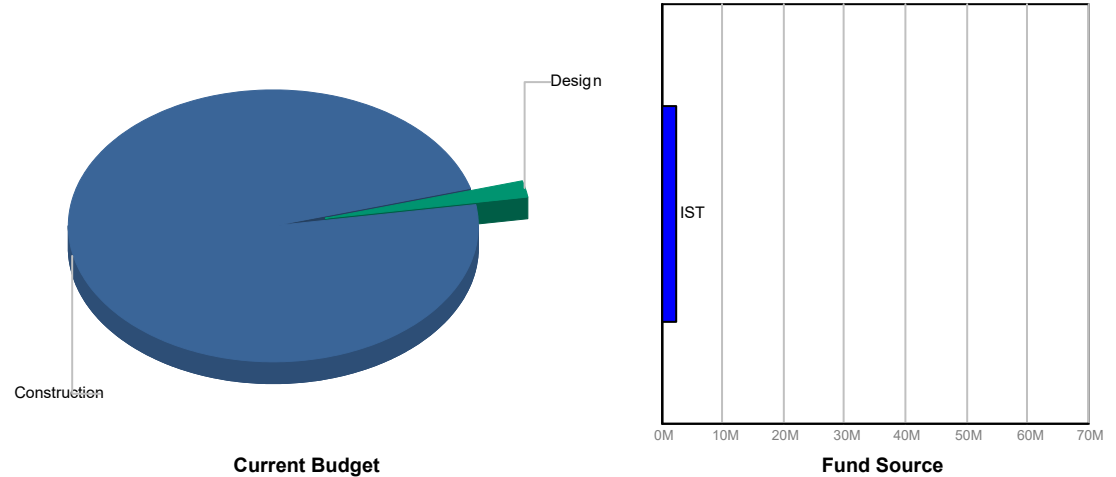

### FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$50,000	\$312,493	624.99%	\$52,926
Construction	\$2,489,000	\$800,632	32.17%	\$292,297
Furniture, Fixtures & Equipment	\$0	\$0	0.00%	\$0
Other	\$0	\$1,339	0.00%	\$1,339
Contingency	\$0	\$0	0.00%	\$0
<b>TOTAL</b>	<b>\$2,539,000</b>	<b>\$1,114,464</b>	<b>43.89%</b>	<b>\$346,562</b>

### NOTES

Delray Health; Closed. Lantana Health; Construction continues on Customer Service Counter, and the permit application is pending. Punch list site visit scheduled for mid June. First-floor restrooms at 90% completion. Second-floor restrooms are pending completion of the first floor. Updating supplement to allow for additional time. Jupiter Health; Project approved by BCC with NTP on 5/29 provided to Lebelo. Permit requirements are in process with the Town of Jupiter. West County Administration Building; A revised conceptual ROM estimate was received from Colome & Associates which indicates a construction value of over \$4M. Project will require an RFP for design and construction.





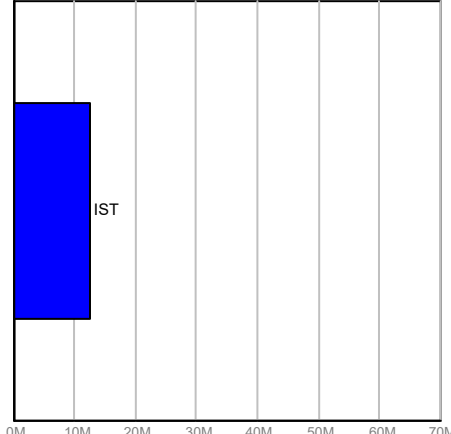
# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects

Data Date: 05/18/2023

Report Date: 05/31/2023

DESCRIPTION/TEAM	SCOPE	PHOTO
<p><b>Project Title: Vehicle Replacement</b></p> <p>Project Number: Q007            BCC District: Multiple            Delivery Method: Direct Purchase            Category: S04-Sheriff            Status: Construction            Designer: N/A            Contractor: N/A            Project Manager: Isami Ayala-Collazo</p>	<p>This project funds the replacement of PBSO public safety vehicles and related equipment (other than radios), tools and/or services.</p> <p>FY 18 Funds: \$3,650,513            FY 19 Funds: \$3,650,513            FY 20 Funds: \$3,650,514            FY 24 Funds: \$1,669,963</p>	

SCHEDULE SUMMARY	PARTICIPATION	FUNDING									
<table border="1"> <thead> <tr> <th></th> <th>Original</th> <th>Actual</th> </tr> </thead> <tbody> <tr> <td>1 Project Start</td> <td>10/1/2018</td> <td>5/1/2018</td> </tr> <tr> <td>2 Project Completion</td> <td>9/30/2024</td> <td></td> </tr> </tbody> </table>		Original	Actual	1 Project Start	10/1/2018	5/1/2018	2 Project Completion	9/30/2024		<p><b>Consultant</b></p> <ul style="list-style-type: none"> <li>SBE N/A</li> <li>Local N/A</li> <li>WBE N/A</li> <li>MBE N/A</li> </ul> <p><b>Contractor</b></p> <ul style="list-style-type: none"> <li>SBE N/A</li> <li>Local N/A</li> <li>WBE N/A</li> <li>MBE N/A</li> </ul>	<div style="display: flex; justify-content: space-around;"> <div style="text-align: center;">  <p>Furniture, Fixtures &amp; Equipment</p> <p><b>Current Budget</b></p> </div> <div style="text-align: center;">  <p><b>Fund Source</b></p> </div> </div>
	Original	Actual									
1 Project Start	10/1/2018	5/1/2018									
2 Project Completion	9/30/2024										

FINANCIAL SUMMARY				
	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Furniture, Fixtures & Equipment	\$12,621,503	\$10,951,540	86.77%	\$10,951,540
Other	\$0	\$0	0.00%	\$0
<b>TOTAL</b>	<b>\$12,621,503</b>	<b>\$10,951,540</b>	<b>86.77%</b>	<b>\$10,951,540</b>

**NOTES**

Prioritization, identification and cost of specific assets are determined by the Sheriff's Office with administration support being performed by FD&O through a Project Funding Agreement with the County.



# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects

Data Date: 05/18/2023

Report Date: 05/31/2023

### DESCRIPTION/TEAM

### SCOPE

### PHOTO

**Project Title:** Animal Care & Control

Project Number: Q008  
 BCC District: 02  
 Delivery Method: Construction Manager at Risk  
 Category: G02-General Government Facilities  
 Status: Design  
 Designer: PGAL  
 Contractor: Wharton-Smith  
 Project Manager: Rich Avery

The Animal Care & Control Renovation & Expansion project for the Belvedere Rd. campus includes: renovations to existing buildings for improved functionality; possible replacement of non-air conditioned kennel buildings with air-conditioned kennel buildings pending evaluation, pricing and approval; and the creation of new spaces necessary to facilitate current and future projected operational needs. The cost of the project includes cost-estimating services necessary in order to validate the project scope, which was derived jointly by FDO & the ACC Division via a needs assessment and programming document, as well as interim arrangements to sustain continuous operations during construction. Funding: FY 2019 IST \$6,000,000 FY 2020 IST \$7,000,000 FY 2025 IST \$35,289,104



### SCHEDULE SUMMARY

	Original	Actual
PROGRAMMING	10/1/2018	10/1/2018
Commence Design Comparative Study	7/24/2019	7/24/2019
Design Start	2/3/2020	12/2/2020
Construction Start	12/1/2020	
Substantial Completion	7/3/2023	

### PARTICIPATION


**Consultant**

SBE 20%  
 Local 100%  
 WBE N/A  
 MBE N/A

**Contractor**

SBE 13.04%  
 Local 13.04%  
 WBE 13.04%  
 MBE 13.04%

### FUNDING

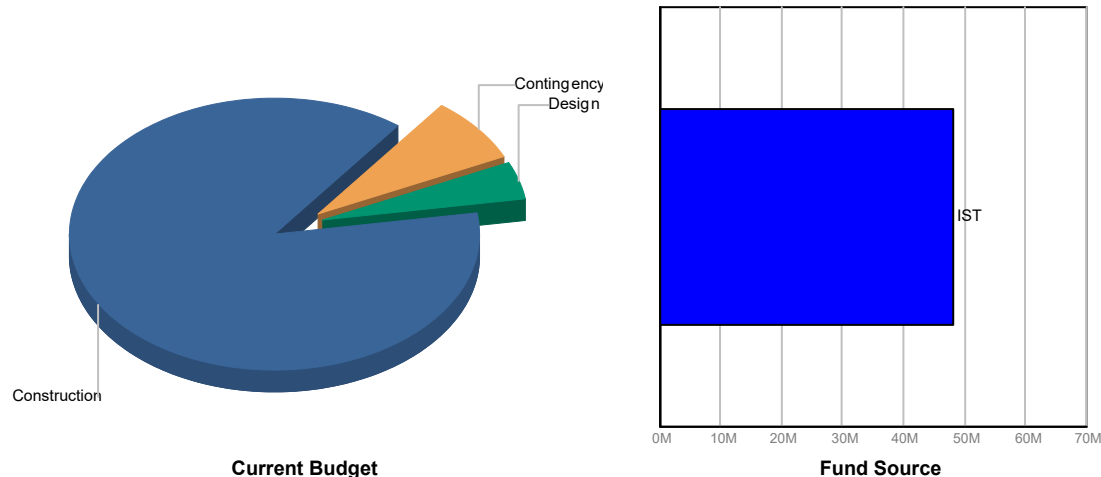

### FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$2,100,000	\$882,713	42.03%	\$876,943
Construction	\$42,409,104	\$625,369	1.47%	\$589,325
Contingency	\$3,780,000	\$0	0.00%	\$0
<b>TOTAL</b>	<b>\$48,289,104</b>	<b>\$1,508,082</b>	<b>3.12%</b>	<b>\$1,466,267</b>

### NOTES

The consultant completed a preliminary presentation to CID, which will be followed with a formal presentation to the Department Director on June 20th, 2023.



# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects

Data Date: 05/18/2023

Report Date: 05/31/2023

### DESCRIPTION/TEAM

**Project Title:** Central County Housing Resource Center  
**Project Number:** Q009  
**BCC District:** 03  
**Delivery Method:** Construction Manager at Risk  
**Category:** H02-Housing  
**Status:** Construction  
**Designer:** Ohlson Lavoie Collaborative  
**Contractor:** D Stephenson  
**Project Manager:** Sunil Jagoo

### SCOPE

The Homeless Resource Center 2 (HRC 2) is to provide an effective Crisis Response System that provides immediate and easy access to safe and decent temporary shelter to County residents that need it and aims to re-house people as quickly as possible while receiving wrap-around social services. The facility will compliment the County's existing Senator Philip D. Lewis Center in West Palm Beach and will consist of approximately 19,000 square feet to support 74 client beds, dining and service delivery/office areas, restrooms, laundry facilities, an intake lobby, and other incidental interior and exterior improvements. Co-located within the facility will be the improvements identified in the IST Project Plan titled PBSO Lake Worth West Substation. FY 2019 IST \$5,700,000 FY 2022 IST \$9,243,697

### PHOTO



### SCHEDULE SUMMARY

	Original	Actual
Program Development	11/1/2017	11/1/2017
Public Outreach	2/1/2019	2/1/2019
Design Team Solicitation	5/1/2019	9/30/2020
CM Solicitation	9/1/2019	11/26/2019
Schematic Design	11/11/2019	1/31/2020
Design Development	5/1/2020	9/28/2020
Construction Documents	10/1/2020	2/23/2021
Permitting	1/1/2021	11/1/2021
Construction Commencement	6/1/2021	5/10/2022
CO/Substantial Completion	9/1/2022	
Occupancy	10/3/2022	

### PARTICIPATION


**Consultant**

- SBE 0%
- Local 25%
- WBE 0%
- MBE 0%

**Contractor**

- SBE N/A
- Local 100%
- WBE 6.9%
- MBE 22.4%

### FUNDING

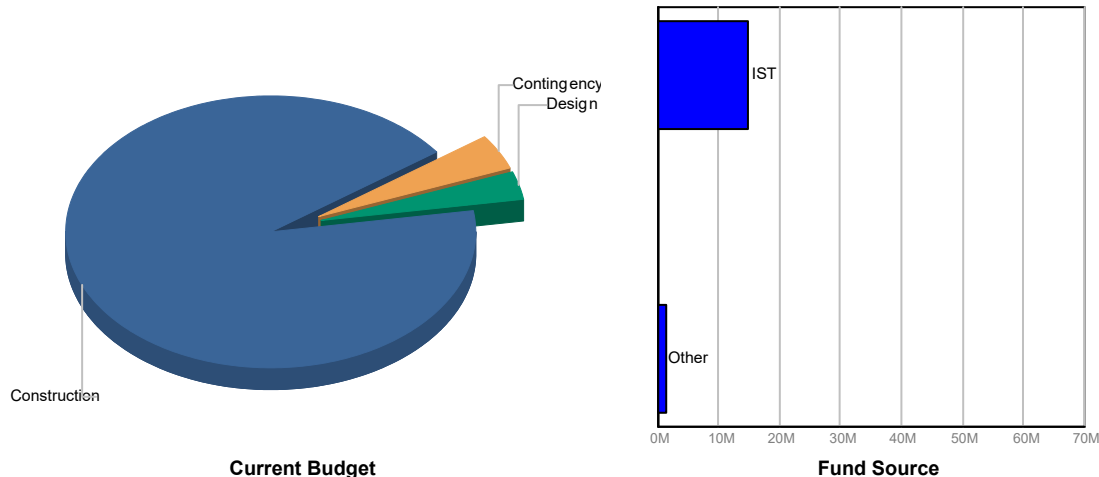

### FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$550,000	\$110,582	20.11%	\$108,581
Construction	\$15,118,540	\$12,732,542	84.22%	\$6,096,671
Contingency	\$700,000	\$0	0.00%	\$0
<b>TOTAL</b>	<b>\$16,368,540</b>	<b>\$12,843,125</b>	<b>78.46%</b>	<b>\$6,205,253</b>

### NOTES

Work within the interior is continuing, including all MEPs. First lift of Asphalt was installed. Concrete curbs are in the process of being formed, site fencing is being installed and landscaping is being installed. There was a potential delay noticed received which stated that the Main Electrical Distribution Panel (MDP) delivery date will be delayed from March 6th to June 16th 2023. Contractor is looking into alternatives at this time, and is preparing a revised schedule based on the projected delivery date.



# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects

Data Date: 05/18/2023

Report Date: 05/31/2023

### DESCRIPTION/TEAM

### SCOPE

### PHOTO

**Project Title:** South County Administrative Complex

Project Number: Q010  
 BCC District: 07  
 Delivery Method: Varies  
 Category: G02-General Government Facilities  
 Status: Design  
 Designer: Varies  
 Contractor: Varies  
 Project Manager: Eric McClellan

This project funds essential Renewal and Replacement (R&R) needs to sustain the continuous operation of this 40+ year old complex prior to its future redevelopment. As such there is no defined scope of work. Any funds remaining at such time that redevelopment is funded would be utilized toward professional design services for the redevelopment. Funding includes \$3M each in FY 2020 and FY 2021, for a total of \$6M.



### SCHEDULE SUMMARY

### PARTICIPATION

### FUNDING


Original	Actual
N/A. See notes for current activity.	

#### Consultant

- SBE Varies
- Local Varies
- WBE Varies
- MBE Varies


#### Contractor

- SBE Varies
- Local Varies
- WBE Varies
- MBE Varies



Construction

Current Budget

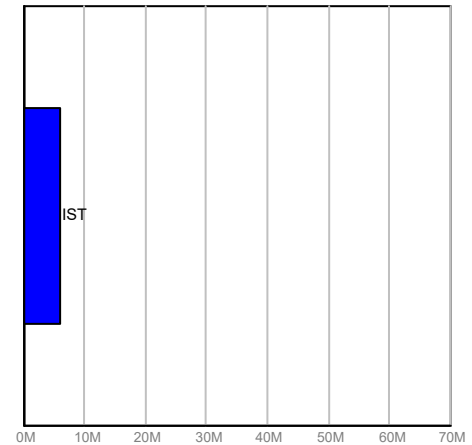

Fund Source

### FINANCIAL SUMMARY

### NOTES

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Construction	\$6,000,000	\$1,188,950	19.82%	\$338,323
Other	\$0	\$26,372	0.00%	\$20,898
<b>TOTAL</b>	<b>\$6,000,000</b>	<b>\$1,215,322</b>	<b>20.26%</b>	<b>\$359,222</b>

Paved vehicular surfaces throughout the complex are in need of R&R and work is approaching. Other work is also occurring on an as-needed basis to sustain operations. Zyscovich, LLC was competitively selected to provide professional master site planning, programming, investigation design, interior space planning, engineering, permitting and construction administration services for site redevelopment. The needs assessment interviews were recently completed, and results are being compiled for review and assessment by the project team.



# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects

Data Date: 05/18/2023

Report Date: 05/31/2023

### DESCRIPTION/TEAM

### SCOPE

### PHOTO

**Project Title:** Government Center  
Renewal/Replacement

Project Number: Q011

BCC District: 02

Delivery Method: Construction Manager at Risk

Category: G02-General Government Facilities

Status: Design

Designer: Netta Architects

Contractor: The Weitz Company LLC

Project Manager: Jeffrey Halverson

This project includes but is not limited to upgrades and replacement of select building finishes and systems including security, HVAC, plumbing, fire alarm, fire sprinkler, electrical, low voltage, lighting, flooring and paint. The scope of the project will additionally include a building conditions assessment, program evaluation study, interior space planning and layout improvements. The proposed renovations to the Robert Weisman Governmental Center are designed to increase the functionality of key areas within the facility and bring the building up to current County standards.

FY2022 IST \$8,000,000 FY2023 IST \$14,000,000 FY2024 IST \$10,000,000 FY2025 \$11,000,000  
FY2026 IST \$15,000,000 FY2027 IST \$11,500,000



### SCHEDULE SUMMARY

	Original	Actual
CM RFP Proposals Due	12/2/2021	12/2/2021
CM Shortlist Meeting	1/19/2022	3/15/2022
Design RFP Final Selection	11/8/2021	9/30/2021
Structural Assessment	1/31/2023	3/17/2023
Building Construction Assesment	6/1/2023	
Life Cycle Analysis	11/1/2023	

### PARTICIPATION

#### Consultant

SBE 33%

Local 100%

WBE 100%

MBE 100%

#### Contractor


SBE TBD

Local TBD


WBE TBD

MBE TBD

### FUNDING



Current Budget

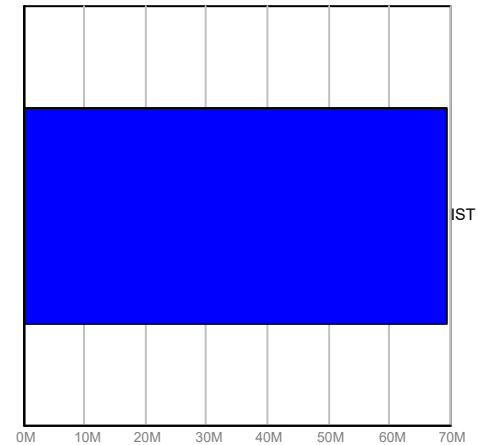

Fund Source

### FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Construction	\$69,500,000	\$269,866	0.39%	\$118,964
<b>TOTAL</b>	<b>\$69,500,000</b>	<b>\$269,866</b>	<b>0.39%</b>	<b>\$118,964</b>

### NOTES

A CSA to cover the professional services related to the Building Condition Assessment , the Life Cycle Cost Analysis, and the Programming is being prepared for the July 11 BCC meeting.



# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects

Data Date: 05/18/2023

Report Date: 05/31/2023

DESCRIPTION/TEAM	SCOPE	PHOTO
<p><b>Project Title:</b> In car cameras</p> <p>Project Number: Q016            BCC District: CW            Delivery Method: Direct Purchase            Category: S04-Sheriff            Status: Procurement            Designer: N/A            Contractor: N/A            Project Manager: Isami Ayala-Collazo</p>	<p>This project funds the purchase of PBSO, in-car and integrated body-worn cameras, and related devices and services.</p> <p>FY 23 Funds: \$10,951,540</p>	

SCHEDULE SUMMARY	PARTICIPATION	FUNDING						
<table border="1"> <thead> <tr> <th></th> <th>Original</th> <th>Actual</th> </tr> </thead> <tbody> <tr> <td>N/A</td> <td></td> <td></td> </tr> </tbody> </table>		Original	Actual	N/A			<p><b>Consultant</b></p> <ul style="list-style-type: none"> <li>SBE N/A</li> <li>Local N/A</li> <li>WBE N/A</li> <li>MBE N/A</li> </ul> <p><b>Contractor</b></p> <ul style="list-style-type: none"> <li>SBE N/A</li> <li>Local N/A</li> <li>WBE N/A</li> <li>MBE N/A</li> </ul>	
	Original	Actual						
N/A								

FINANCIAL SUMMARY				
	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Construction	\$0	\$0	0.00%	\$0
Other	\$10,951,540	\$0	0.00%	\$0
<b>TOTAL</b>	<b>\$10,951,540</b>	<b>\$0</b>	<b>0.00%</b>	<b>\$0</b>

**NOTES**

Prioritization, identification and cost of specific assets are determined by the Sheriff's Office with administration support being performed by FD&O through a Project Funding Agreement with the County.





# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects

Data Date: 05/18/2023

Report Date: 05/31/2023

### DESCRIPTION/TEAM


### SCOPE

### PHOTO

**Project Title:** 810 Datura Building Replacement

Project Number: Q018  
 BCC District: 07  
 Delivery Method: CMAR  
 Category: G02-General Government Facilities  
 Status: Design  
 Designer: Alfonso Hernandez Architect, LLC  
 Contractor: TBD  
 Project Manager: Mitch Silverman

This project relocates the Community Services Department from 810 Datura Street to the County's 45th Street Complex. The result will be a modern office building to replace the existing facility which is 50+ years old, providing adequate space for services and programs into the future.  
 FY 2023 - \$2,600,000  
 FY 2025 - \$5,000,000  
 FY 2026 - \$21,260,000

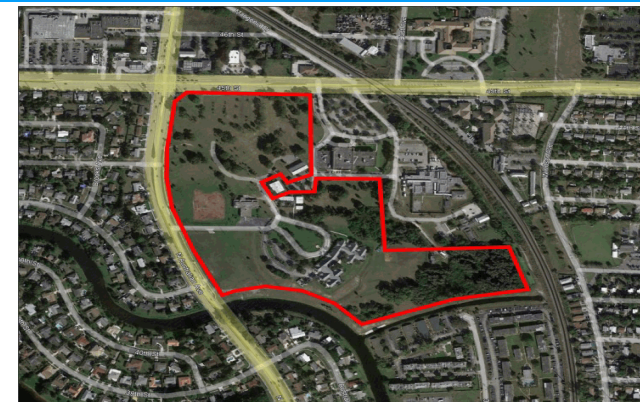

### SCHEDULE SUMMARY

### PARTICIPATION

### FUNDING


	Original	Actual
Project Start	10/1/2024	2/9/2022
Programming	5/15/2023	
Design		
Construction Commencement		
Construction Completion		

#### Consultant


SBE TBD  
 Local TBD  
 WBE TBD  
 MBE TBD

#### Contractor

SBE TBD  
 Local TBD  
 WBE TBD  
 MBE TBD

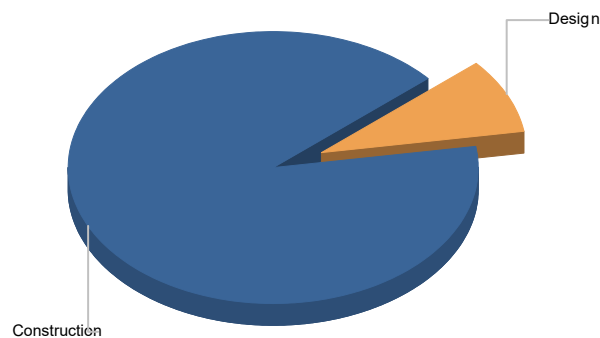

Current Budget

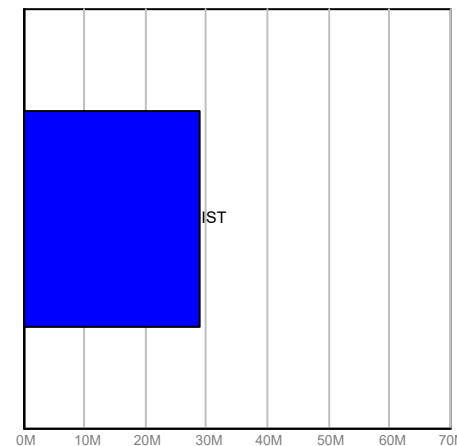

Fund Source

### FINANCIAL SUMMARY

### NOTES

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$2,600,000	\$0	0.00%	\$0
Construction	\$26,260,000	\$2,337,191	8.90%	\$23,589
<b>TOTAL</b>	<b>\$28,860,000</b>	<b>\$2,337,191</b>	<b>8.10%</b>	<b>\$23,589</b>

In response to a Development and Conveyance Agreement approved by the BCC on 8/23/2022 that commits the 810 Datura Street property to the University of Florida, design must immediately commence. Competitive Selection resulted in the recommendation of Alfonso Hernandez Architect, LLC. An advance of \$2.6M to commence design received BCC approval. Programming and survey work are now in progress. First draft of a conceptual master plan expected in late October.



# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects

Data Date: 05/18/2023

Report Date: 05/31/2023

### DESCRIPTION/TEAM

### SCOPE

### PHOTO

**Project Title:** Detention Center Facilities R/R (Phases 3-5)  
**Project Number:** Q019  
**BCC District:** 03  
**Delivery Method:** Construction Management  
**Category:** S06-Sheriff - FDO  
**Status:** Construction  
**Designer:** Leo A. Daly  
**Contractor:** Hedrick Brothers Construction  
**Project Manager:** Jeffrey Halverson

Phases 3-5 consist of the East Tower and West Tower which are located at the Main Detention Center. The West Detention Center is located in Belle Glade. The design for both towers and the West Detention Center will require repairing and replacing MEP, Fire Sprinkler System, Low Voltage Systems and interior finishes.  
 Detention Center Facilities R/R (Phases 3-5)  
 FY 2018 IST \$8,500,000  
 FY 2019 IST \$14,700,000  
 FY 2020 IST \$9,800,000  
 FY 2022 IST \$10,000,000



### SCHEDULE SUMMARY

	Original	Actual
East Tower Design Start	11/12/2018	7/11/2019
East Tower Construction Start-Phase 3	10/14/2019	11/18/2020
East Tower Substantial Completion	5/11/2022	12/11/2023
West Tower Design Start-Phase 4	3/8/2022	
West Tower Construction Start-Phase 4	1/2/2024	

### PARTICIPATION


#### Consultant

SBE 19.88%  
 Local 67%  
 WBE N/A  
 MBE N/A


#### Contractor

SBE 63%  
 Local 84%  
 WBE N/A  
 MBE N/A

### FUNDING

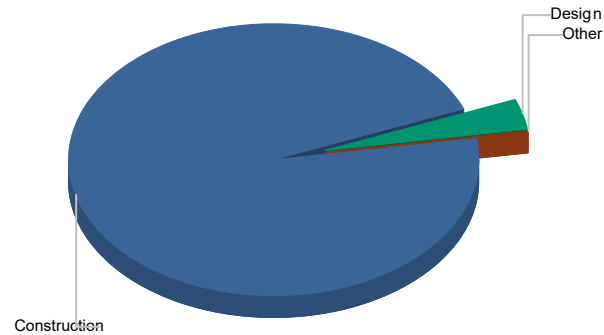

Current Budget

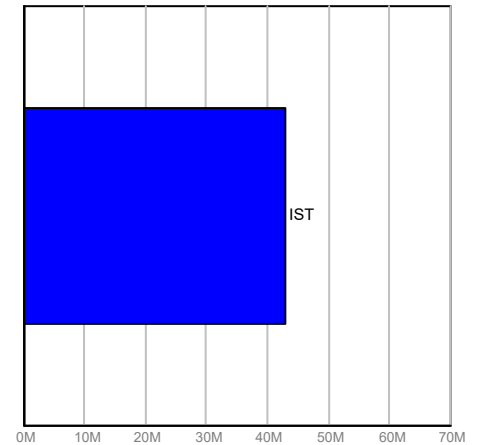

Fund Source

### FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$1,500,000	\$2,060,035	137.34%	\$1,420,940
Construction	\$41,475,692	\$24,789,697	59.77%	\$20,062,698
Other	\$24,308	\$1,328,794	5,466.49%	\$952,935
Contingency	\$0	\$0	0.00%	\$0
<b>TOTAL</b>	<b>\$43,000,000</b>	<b>\$28,178,526</b>	<b>65.53%</b>	<b>\$22,436,574</b>

### NOTES

Plans are still being completed for phase IV. Hold up due to some scope increase. GMP for phase IV will be prepared in January 2024.



# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects

Data Date: 05/18/2023

Report Date: 05/31/2023


### DESCRIPTION/TEAM

### SCOPE

### PHOTO

**Project Title:** West Boynton Park Athletic Field Renovations Sports Turf  
**Project Number:** T002  
**BCC District:** 02  
**Delivery Method:** TBD  
**Category:** A06-Athletic Field Renovations  
**Status:** Design  
**Designer:** Florida Transportation Engineering  
**Contractor:** TBD  
**Project Manager:** Stuart Patterson

Replacement of existing grass field turf with synthetic turf on multi-purpose field 1 & 2.  
**Funded:**  
 FY 2017 \$2,000,000  
 FY 2018 (\$1,011,658)  
 FY 2022 \$1,196,658

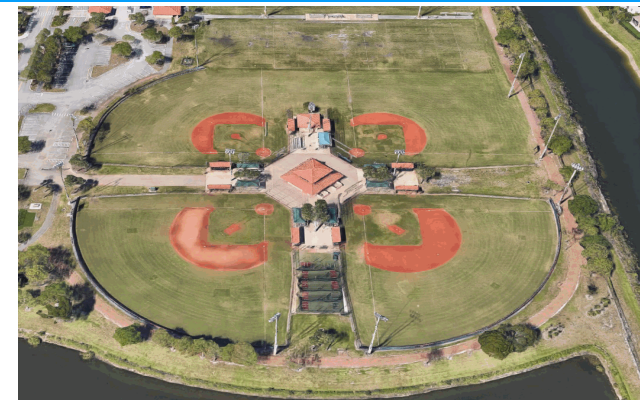

### SCHEDULE SUMMARY


	Original	Actual
Begin Existing Site Surveys	1/29/2020	1/29/2020
Complete Existing Site Surveys	6/30/2020	3/9/2020
Finalization of Existing Site Surveys	8/30/2020	10/16/2020
Design RFP Proposals Due	9/4/2020	9/10/2020
Design RFP Final Selection	10/29/2020	10/29/2020
Consultant Contract Issuance	12/14/2020	4/20/2021
Design Completion	12/31/2021	
Turf Supplier RFP Proposal Due	4/30/2022	

### PARTICIPATION

**Consultant**  
 SBE 25%  
 Local 25%  
 WBE 0%  
 MBE 6.13%

**Contractor**  
 SBE TBD  
 Local TBD  
 WBE TBD  
 MBE TBD

### FUNDING

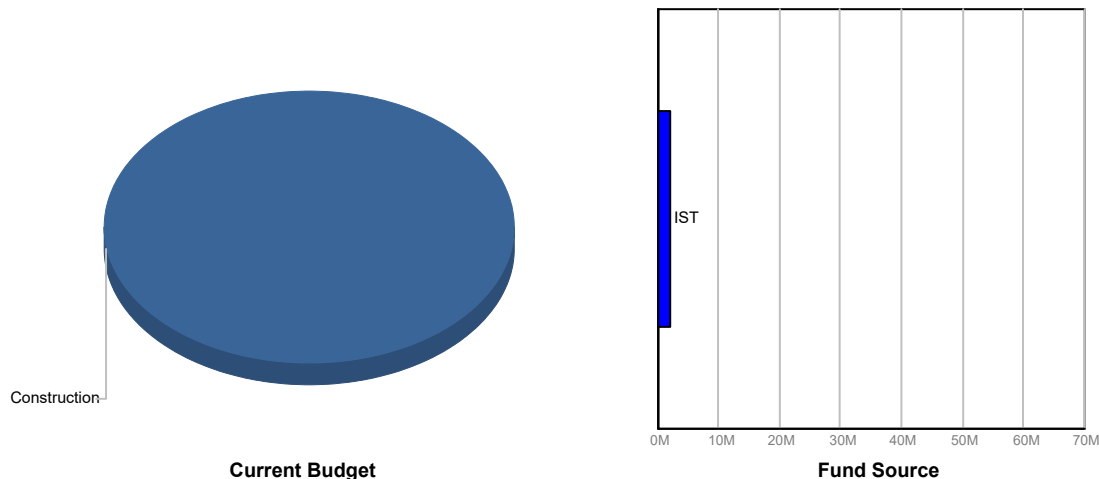

### FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$0	\$178,760	0.00%	\$69,686
Construction	\$2,185,000	\$19,185	0.88%	\$19,185
Furniture, Fixtures & Equipment	\$0	\$0	0.00%	\$0
Other	\$0	\$459	0.00%	\$459
Contingency	\$0	\$0	0.00%	\$0
<b>TOTAL</b>	<b>\$2,185,000</b>	<b>\$198,404</b>	<b>9.08%</b>	<b>\$89,330</b>

### NOTES

Due to the current and foreseeable issues with construction materials, turf design has been slowed, with a revised anticipated completion in Spring 2023. FDO Director recently declared that construction/CM RFP method will be addressed as a single, project specific contract to cover all (9) parks and associated fields. CM RFP pre-proposal meeting held 5/4/2023, and proposals are due 6/6/2023. Field design documents are to be 100% before CM award. Design & schedule meetings being held on 1st Wednesday of each month.



# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects

Data Date: 05/18/2023

Report Date: 05/31/2023

### DESCRIPTION/TEAM

### SCOPE

### PHOTO

**Project Title:** Buttonwood Park

Project Number: T003  
 BCC District: 03  
 Delivery Method: TBD  
 Category: A06-Athletic Field Renovations  
 Status: Design  
 Designer: Florida Transportation Engineering  
 Contractor: TBD  
 Project Manager: Stuart Patterson

Replacement of existing grass field turf with synthetic turf on multi-purpose field 2 & 3  
 Funded:  
 FY 2017 \$1,500,000  
 FY 2018 (\$1,488,342)  
 FY 2021 \$900,000  
 FY 2022 \$1,963,342



### SCHEDULE SUMMARY

	Original	Actual
Begin Existing Site Surveys	1/29/2020	1/29/2020
Complete Existing Site Surveys	8/30/2020	5/18/2021
Finalization of Existing Site Surveys	8/30/2020	8/23/2021
Design RFP Proposals Due	9/4/2020	9/10/2020
Consultant Contract Issuance	12/14/2020	4/20/2021
Design Completion	12/31/2021	
Turf Supplier RFP Proposal Due	4/30/2022	

### PARTICIPATION


**Consultant**

SBE 25%  
 Local 25%  
 WBE 0%  
 MBE 6.13%

**Contractor**

SBE TBD  
 Local TBD  
 WBE TBD  
 MBE TBD

### FUNDING

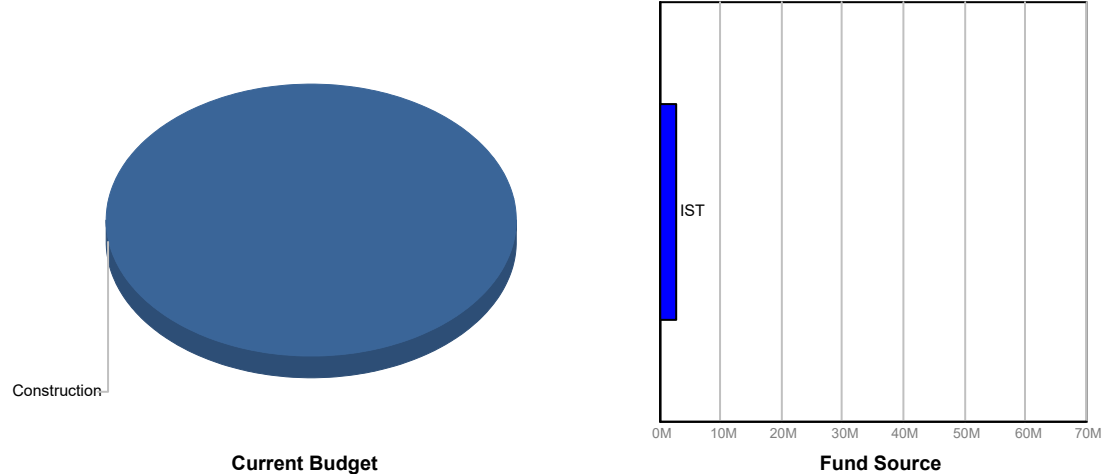

### FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$0	\$190,543	0.00%	\$78,293
Construction	\$2,875,000	\$39,492	1.37%	\$39,492
Furniture, Fixtures & Equipment	\$0	\$0	0.00%	\$0
Other	\$0	\$12,458	0.00%	\$12,458
Contingency	\$0	\$0	0.00%	\$0
<b>TOTAL</b>	<b>\$2,875,000</b>	<b>\$242,494</b>	<b>8.43%</b>	<b>\$130,243</b>

### NOTES

Due to the current and foreseeable issues with construction materials, turf design has been slowed, with a revised anticipated completion in Spring 2023. FDO Director recently declared that construction/CM RFP method will be addressed as a single, project specific contract to cover all (9) parks and associated fields. CM RFP pre-proposal meeting held 5/4/2023, and proposals are due 6/6/2023. Field design documents are to be 100% before CM award. Design & schedule meetings being held on 1st Wednesday of each month.




# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects


Data Date: 05/18/2023

Report Date: 05/31/2023

DESCRIPTION/TEAM	SCOPE	PHOTO
<p><b>Project Title: Community Park - New Development</b></p> <p>Project Number: T004            BCC District: Multiple            Delivery Method: Varies            Category: N02-New Park Development            Status: Varies            Designer: Varies            Contractor: Varies            Project Manager: Varies</p>	<p>Construction of neighborhood park facilities for underserved Countywide Community Revitalization Team (CCRT) areas.</p> <p>FY 2017 IST: \$1,000,000            FY 2021 IST: \$4,900,000            FY 2022 IST: (\$3,900,000)            FY 2024 IST: \$3,000,000</p>	

SCHEDULE SUMMARY	
Original	Actual
Varies by location. Work ongoing	

PARTICIPATION	
<b>Consultant</b>	
SBE	Varies
Local	Varies
WBE	Varies
MBE	Varies
<b>Contractor</b>	
SBE	Varies
Local	Varies
WBE	Varies
MBE	Varies

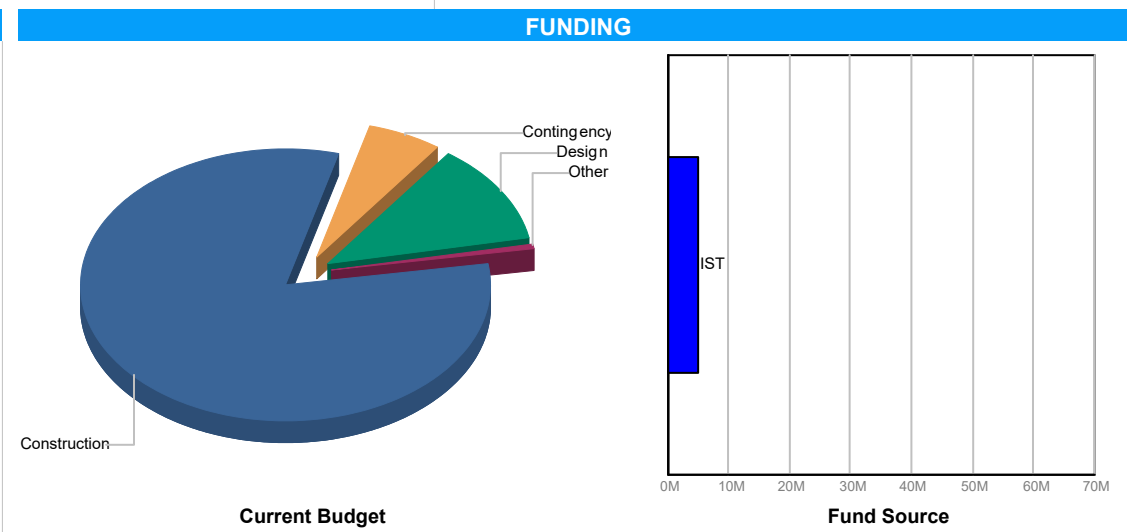

FINANCIAL SUMMARY				
	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$590,000	\$635,605	107.73%	\$323,317
Construction	\$4,082,035	\$142,687	3.50%	\$84,347
Furniture, Fixtures & Equipment	\$0	\$0	0.00%	\$0
Other	\$32,965	\$33,190	100.68%	\$33,190
Contingency	\$295,000	\$0	0.00%	\$0
<b>TOTAL</b>	<b>\$5,000,000</b>	<b>\$811,482</b>	<b>16.23%</b>	<b>\$440,854</b>

**NOTES**

Bridgeman; Construction of a .32 acre neighborhood park on a WUD parcel to serve the Belvedere Heights CCRT neighborhood within the Westgate CRA. Completed in 5/2020 with \$32,415 of IST funds.

Paulette Burdick; Construction of a +/- 4 acre community park within Cam Estates CCRT neighborhood. Schematic Design received, under review, and community outreach conducted 3/25/2023. Gramercy; Construction of a +/- 11,000 sq. ft. neighborhood center and passive park. 95% CD's (Permit and GMP) currently scheduled to be completed 6/29/2023. Project budget includes \$500 k of IST funds for design and permitting, with construction funding from a CDBG award.



# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects

Data Date: 05/18/2023

Report Date: 05/31/2023

### DESCRIPTION/TEAM

### SCOPE

### PHOTO

**Project Title:** FY2017 Sports Field Lighting Replacement  
**Project Number:** T006  
**BCC District:** Multiple  
**Delivery Method:** Sports Field Lighting Annual  
**Category:** S12-Sports Lighting Replacement  
**Status:** Construction  
**Designer:** JLRD Engineers  
**Contractor:** Grid One  
**Project Manager:** Mitch Silverman

Replacement of Sports Field Lighting at Bert Winters Park, Caloosa Park, Glades Pioneer Park, Juno South Park, Jupiter Farms Park, Okeeheliee Park, Pinewoods Park, (Burt Aaronson) South County Regional Park and Westgate Park.  
 IST FY 2017 funds: \$4,200,000.



### SCHEDULE SUMMARY

	Original	Actual
Project Start	6/29/2017	6/29/2017
Procurement (Light Fixture Vendor)	10/16/2018	10/16/2018
Procurement (Installation Contractor)	10/17/2018	5/9/2019
Final Completion	10/2/2020	11/2/2021
Bidding Package 1	11/6/2019	11/6/2019
Construction Start Package 1	2/3/2020	2/3/2020
Construction Completion Package 1	7/2/2020	8/24/2020
Bidding Package 2	2/13/2020	2/13/2020
Construction Start Package 2	5/11/2020	4/2/2020
Construction Completion Package 2	7/17/2020	4/2/2021
Bidding Package 3	3/26/2020	4/8/2022
Construction Start Package 3	6/15/2020	
Construction Completion Package 3		

### PARTICIPATION


**Consultant**

- SBE 100%
- Local 100%
- WBE N/A
- MBE N/A

**Contractor**

- SBE 0%
- Local 100%
- WBE 0%
- MBE 0%

### FUNDING

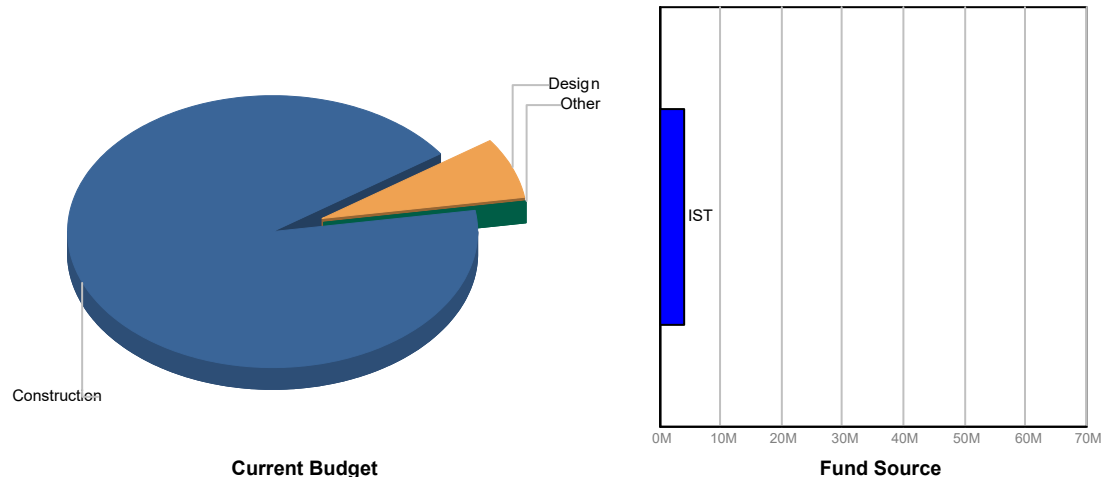

### FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$299,161	\$22,383	7.48%	\$22,383
Construction	\$3,900,000	\$4,037,033	103.51%	\$3,947,090
Other	\$839	\$2,952	351.65%	\$2,952
<b>TOTAL</b>	<b>\$4,200,000</b>	<b>\$4,062,368</b>	<b>96.72%</b>	<b>\$3,972,425</b>

### NOTES

Bert Winters Ballfield 2 is the only remaining park to be completed. RFP awarded to Grid One on 1/16/23; NTP issued to CM, and light fixtures are being installed.



# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects

Data Date: 05/18/2023

Report Date: 05/31/2023

### DESCRIPTION/TEAM

### SCOPE

### PHOTO

**Project Title:** FY2020 Sports Field Lighting Replacement  
**Project Number:** T010  
**BCC District:** Multiple  
**Delivery Method:** Sports Field Lighting Annual  
**Category:** S12-Sports Lighting Replacement  
**Status:** Construction  
**Designer:** JLRD Engineers  
**Contractor:** Various  
**Project Manager:** Mitch Silverman

Lake Lytal Athletic Courts, Haverhill Tennis & Racquetball Courts, BASCR Basketball Courts, Duncan Padgett Park Raquetball Courts  
 FY 2020 IST = \$1,300,000  
 FY 2021 IST = (\$100,000)  
 FY 2022 IST = (\$273,000)



### SCHEDULE SUMMARY

	Original	Actual
Project Start	6/29/2017	7/18/2019
Design Start	11/6/2020	11/6/2020
Design Completion	4/2/2021	4/2/2021
Final Completion	12/31/2022	
Bidding Package 1	6/14/2021	6/14/2021
Construction Start Package 1	2/14/2022	2/14/2022
Construction Completion Package 1		
Bidding Package 2	5/19/2022	
Construction Start Package 2		
Construction Completion Package 2		
Bidding Package 3		
Construction Start Package 3		
Construction Completion Package 3		

### PARTICIPATION


#### Consultant

SBE 100%  
 Local 100%  
 WBE N/A  
 MBE N/A

#### Contractor

SBE TBD  
 Local TBD  
 WBE TBD  
 MBE TBD

### FUNDING

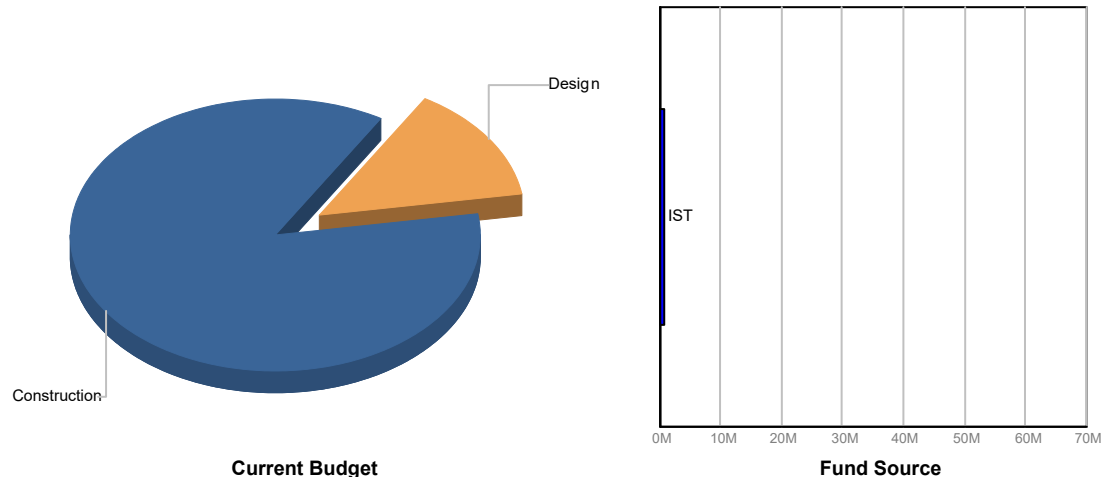

### FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$130,000	\$479,384	368.76%	\$471,599
Construction	\$797,000	\$340,984	42.78%	\$317,195
<b>TOTAL</b>	<b>\$927,000</b>	<b>\$820,368</b>	<b>88.50%</b>	<b>\$788,794</b>

### NOTES

Lake Lytal Racquetball: RFQ is in the queue for processing by CID for court construction(separate project). South County Basketball: Construction complete. Haverhill Tennis: Construction complete. Haverhill Racquetball- Design drawings under review by Parks; RFQ is in the queue for processing by CID for court construction(separate project). Duncan Padgett Picnic Area - Awaiting project approach from Parks to proceed.



# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects

Data Date: 05/18/2023

Report Date: 05/31/2023

### DESCRIPTION/TEAM

**Project Title:** FY2021 Sports Lighting Replacement

Project Number: T011  
 BCC District: Multiple  
 Delivery Method: Sports Field Lighting Annual  
 Category: S12-Sports Lighting Replacement  
 Status: Design  
 Designer: JLRD Engineers  
 Contractor: Various  
 Project Manager: Mitch Silverman

### SCOPE

Caloosa Park Athletic Courts, Seminole Palms BF 1-8 & MPF 9-11, BASCR Tennis Courts, Carlin Park Tennis Courts, Veterans Park Tennis & Bball Courts, Dyer Park Basketball Courts, Lake Lytal Tball.

FY 2021 IST \$4,050,000.  
 FY 2022 IST (\$301,000)

### PHOTO



### SCHEDULE SUMMARY

	Original	Actual
Project Start	6/29/2017	6/29/2017
Design Start	11/6/2020	11/6/2020
Design Completion	4/2/2021	4/2/2021
Final Completion	12/31/2022	
Bidding Package 1	6/14/2021	6/14/2021
Construction Start Package 1	4/11/2022	
Construction Completion Package 1		
Bidding Package 2	6/2/2022	6/2/2022
Construction Start Package 2		
Construction Completion Package 2		
Bidding Package 3		
Construction Start Package 2		
Construction Completion Package 3		

### PARTICIPATION


#### Consultant

SBE 100%  
 Local 100%  
 WBE N/A  
 MBE N/A


#### Contractor

SBE TBD  
 Local TBD  
 WBE TBD  
 MBE TBD

### FUNDING

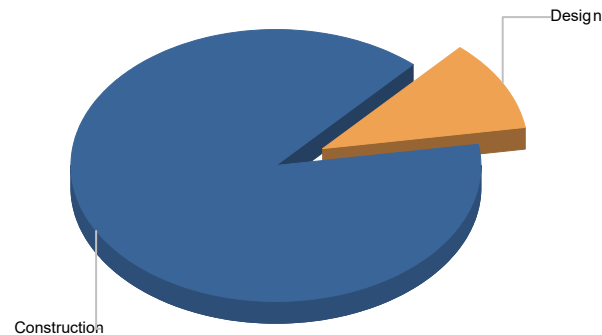

Current Budget

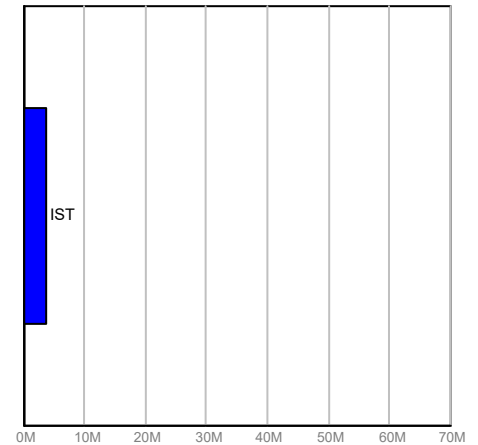

Fund Source

### FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$405,000	\$232,804	57.48%	\$109,930
Construction	\$3,326,949	\$2,328,567	69.99%	\$1,772,232
<b>TOTAL</b>	<b>\$3,731,949</b>	<b>\$2,561,371</b>	<b>68.63%</b>	<b>\$1,882,162</b>

### NOTES

Carlin Tennis - Project complete and closed. Lake Lytal Ballfield -Construction complete and closed  
 Seminole Palms Ballfield & MPF - Construction complete and currently in close-out. South County Tennis -Currently in construction. Caloosa Basketball & Tennis -NTP issued. Fixtures to be delivered by Musco 6/12/23. Construction schedule 06/19/23. Caloosa Racquetball- RFP awarded to Imperial. Dyer Basketball -Construction completed and in close-out. Veterans Memorial Tennis & Basketball - RFP awarded to Grid One and WO1 signature received from Grid One. Musco delivered fixtures on 2/27/2023. Construction is ongoing.






# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects


Data Date: 05/18/2023

Report Date: 05/31/2023

DESCRIPTION/TEAM	SCOPE	PHOTO
<p><b>Project Title:</b> FY2022 Sports Field Lighting Replacement</p> <p>Project Number: T012</p> <p>BCC District: Multiple</p> <p>Delivery Method: Sports Field Lighting Annual</p> <p>Category: S12-Sports Lighting Replacement</p> <p>Status: Construction</p> <p>Designer: JLRD</p> <p>Contractor: Davco</p> <p>Project Manager: Mitch Silverman</p>	<p>Replacement of Sports Field Lighting at Caloosa Park Ballfields 1-4.</p> <p>FY 2022 IST Funds = \$1,004,000</p>	

SCHEDULE SUMMARY		
	Original	Actual
Project Start	6/19/2023	

PARTICIPATION	
<b>Consultant</b>	
SBE	N/A
Local	N/A
WBE	N/A
MBE	N/A
<b>Contractor</b>	
SBE	3.60%
Local	100%
WBE	0%
MBE	0%

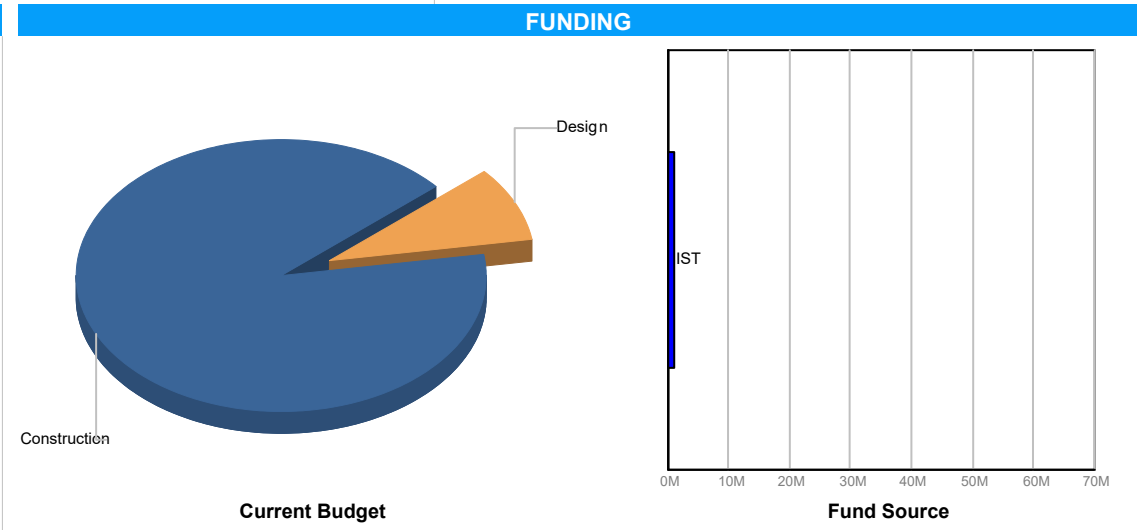

FINANCIAL SUMMARY				
	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$90,000	\$0	0.00%	\$0
Construction	\$914,000	\$1,858	0.20%	\$1,858
<b>TOTAL</b>	<b>\$1,004,000</b>	<b>\$1,858</b>	<b>0.19%</b>	<b>\$1,858</b>

**NOTES**

NTP issued and permit issued. Construction starts 06/19/23.



# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects

Data Date: 05/18/2023

Report Date: 05/31/2023

### DESCRIPTION/TEAM

**Project Title: Bert Winters Park Redevelopment**

Project Number: T041  
 BCC District: 01  
 Delivery Method: Annual Contract  
 Category: E02-Existing Park Redevelopment or Expansion  
 Status: Design  
 Designer: Architecture Green  
 Contractor: TBD  
 Project Manager: Sunil Jagoo

### SCOPE

Demolish former PBMI building, tennis courts, and playground. Remove lights and poles servicing Field 2. Renovate Baseball Field 1. Construct new regulation 220' x 360' multipurpose field. Construct new 30' x 60' rental pavilion. Construct new playground area. Renovate existing day use dock for public use. Construct new paved parking, curbing, landscaping, sidewalks and picnic areas. Install new underground infrastructure and site lighting.  
 FY 2019 IST \$200,000  
 FY 2021 IST \$1,500,000  
 \$200K FRDAP Phase II Redevelopment Grant (Construction)  
 \$220K FIND Phase II Planning, Design and Permitting Costs  
 \$1M FIND Phase II Redevelopment (Construction) – Application pending

### PHOTO




### SCHEDULE SUMMARY

	Original	Actual
Project Start	8/22/2019	8/22/2019
Asbestos Report Initiated	8/23/2019	8/23/2019
Asbestos Report Completion	10/1/2019	10/1/2019
Demolition Start	11/12/2019	4/16/2020
Demolition Completion	12/5/2019	8/17/2020
Design Completion	7/1/2020	11/16/2022
Permitting Start(Dock)	7/15/2020	11/30/2022
Permitting Completion(Dock)	12/31/2020	3/29/2023
Permitting Start(Site)		

### PARTICIPATION

**Consultant**  
 SBE 89.28%  
 Local 100%  
 WBE N/A  
 MBE N/A  
**Contractor**  
 SBE TBD  
 Local TBD  
 WBE TBD  
 MBE TBD

### FUNDING

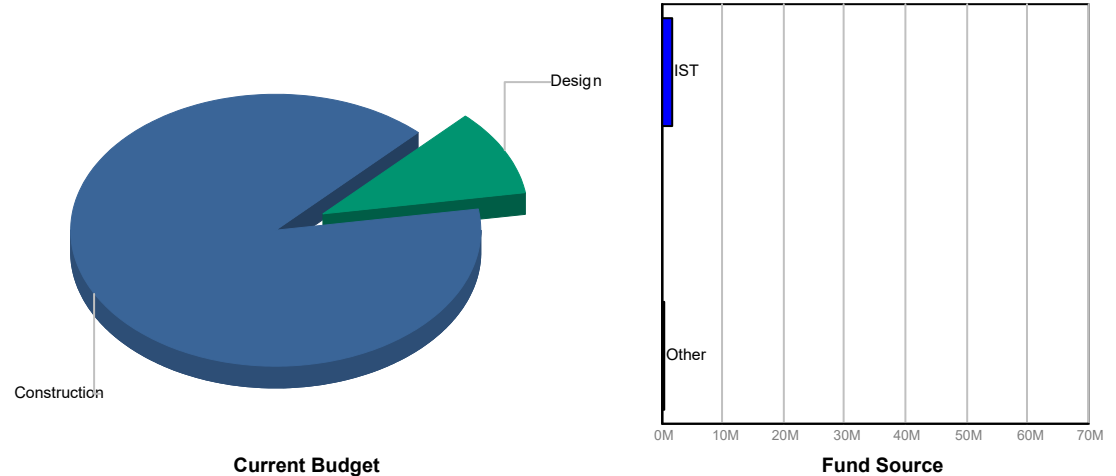

### FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$220,000	\$0	0.00%	\$0
Construction	\$1,900,000	\$815,117	42.90%	\$232,715
Other	\$0	\$10,958	0.00%	\$10,958
Contingency	\$0	\$270	0.00%	\$270
<b>TOTAL</b>	<b>\$2,120,000</b>	<b>\$826,345</b>	<b>38.98%</b>	<b>\$243,942</b>

### NOTES

Construction documents were split into two phases; the docks and the remainder of the site. 50% construction documents for the remainder of the improvements (not including the docks) were received and are under review now.



# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects

Data Date: 05/18/2023

Report Date: 05/31/2023

### DESCRIPTION/TEAM

### SCOPE

### PHOTO

**Project Title:** Aqua Crest Pool Facility Replacement

Project Number: T077  
 BCC District: 07  
 Delivery Method: CMR  
 Category: A02-Aquatic Facility Repair and Replacement  
 Status: Design  
 Designer: Ohlson Lavoie Collaborative  
 Contractor: TBD  
 Project Manager: Michael Jenner

The work consist of the design and renovation of the existing Aqua Crest pool facility. The scope includes but is not limited to: pool improvements such as leak detection, re-surface, lane marker replacement, filtration system replacement; pool deck renovations; demolition of wadding pool; new splash pad; relocation of ticketing booth, admin offices, guards room and weight's room; bathroom renovations; new shade structures and Marquee sign.  
 FY 2019 IST: \$6,000,000  
 FY 2022 IST: (\$5,000,000)  
 FY 2023 IST: \$11,152,500



### SCHEDULE SUMMARY

	Original	Actual
Pre-Scope meeting	2/20/2019	2/20/2019
Design Services Advertisement	6/17/2019	8/4/2019
Consultant BCC Approval	1/14/2020	
Design Start	1/21/2020	6/6/2023
Construction Start	3/9/2021	
Substantial Completion	3/8/2022	
Project Close-out	5/3/2022	

### PARTICIPATION


#### Consultant

SBE TBD  
 Local TBD  
 WBE N/A  
 MBE N/A


#### Contractor

SBE TBD  
 Local TBD  
 WBE TBD  
 MBE TBD

### FUNDING

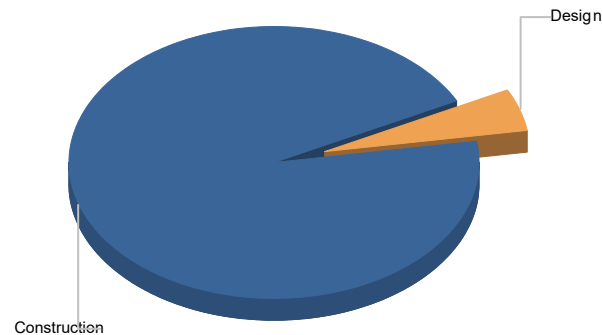

Current Budget

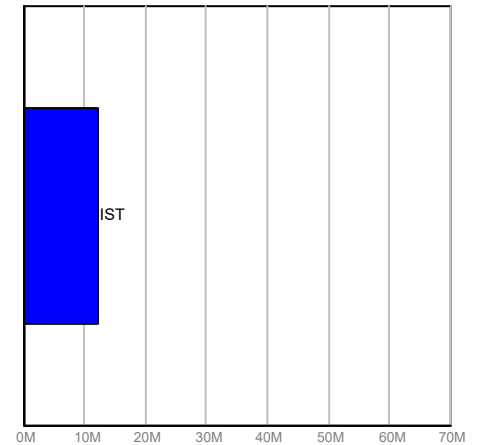

Fund Source

### FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$600,000	\$123,916	20.65%	\$106,650
Construction	\$11,552,500	\$18,260	0.16%	\$18,260
<b>TOTAL</b>	<b>\$12,152,500</b>	<b>\$142,177</b>	<b>1.17%</b>	<b>\$124,911</b>

### NOTES

The Design Consultant Kick-off Meeting was held with Parks, and the design consultant team (OLC) to discuss concepts, safety concerns, water quality, and probable construction cost estimates exceeding the budget. OLC was asked to develop their Fee Proposal based on DMS Curve(Fee Guide Calculator). Next design Coordination Meeting planned for end of June.



# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects

Data Date: 05/18/2023

Report Date: 05/31/2023

### DESCRIPTION/TEAM

### SCOPE

### PHOTO

**Project Title:** Dyer Park Athletic Field Renovation

Replacement of existing grass field turf with synthetic turf on multi-purpose field 3, 4, & 5 as well as additional damaged area.  
Funded: FY 2020 \$6,000,000



Project Number: T099  
 BCC District: 07  
 Delivery Method: Annual Contract  
 Category: A06-Athletic Field Renovations  
 Status: Design  
 Designer: Florida Transportation Engineering  
 Contractor: TBD  
 Project Manager: Stuart Patterson

### SCHEDULE SUMMARY

	Original	Actual
Begin Existing Site Surveys	1/29/2020	1/29/2020
Complete Existing Site Surveys	6/30/2020	5/29/2020
Finalization of Existing Site Surveys	8/30/2020	10/16/2020
Design RFP Proposals Due	9/4/2020	9/10/2020
Design RFP Final Selection	10/29/2020	10/29/2020
Consultant Contract Issuance	12/14/2020	4/20/2021
Design Completion	12/31/2021	
Turf Supplier RFP Proposal Due	4/30/2022	

### PARTICIPATION


**Consultant**

- SBE 25%
- Local 25%
- WBE 0%
- MBE 6.13%

**Contractor**

- SBE TBD
- Local TBD
- WBE TBD
- MBE TBD

### FUNDING

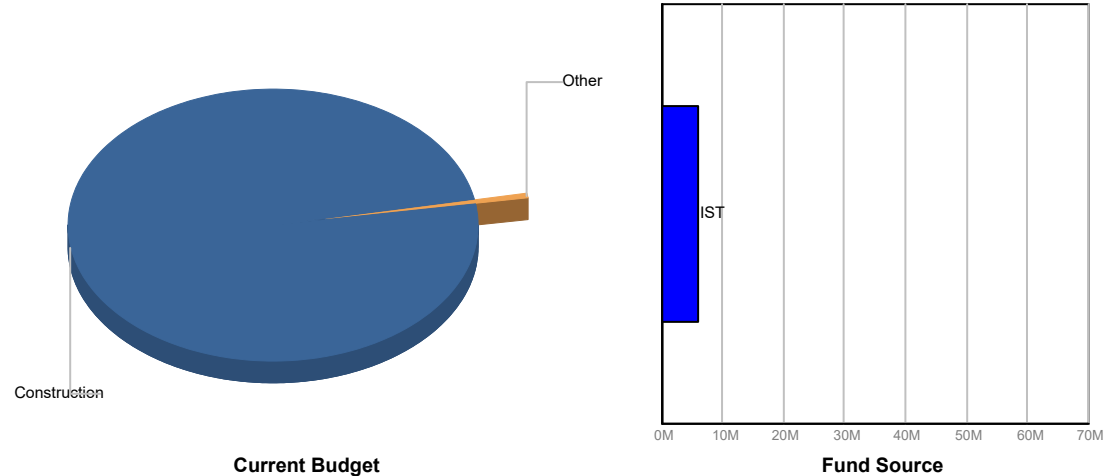

### FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Construction	\$5,970,000	\$249,155	4.17%	\$108,758
Other	\$30,000	\$151	0.50%	\$151
<b>TOTAL</b>	<b>\$6,000,000</b>	<b>\$249,306</b>	<b>4.16%</b>	<b>\$108,910</b>

### NOTES

Due to the current and foreseeable issues with construction materials, turf design has been slowed, with a revised anticipated completion in Spring 2023. FDO Director recently declared that construction/CM RFP method will be addressed as a single, project specific contract to cover all (9) parks and associated fields. CM RFP pre-proposal meeting held 5/4/2023, and proposals are due 6/6/2023. Field design documents are to be 100% before CM award. Design & schedule meetings being held on 1st Wednesday of each month.



# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects

Data Date: 05/18/2023

Report Date: 05/31/2023

### DESCRIPTION/TEAM

### SCOPE

### PHOTO

**Project Title:** Caloosa Park Athletic Field Renovation

Replacement of existing grass field turf with synthetic turf on multi-purpose field 1 & 3 as well as converted from multi-purpose field 4 converted from softball.  
Funded: FY 2020 \$4,000,000



Project Number: T100  
 BCC District: 04  
 Delivery Method: TBD  
 Category: A06-Athletic Field Renovations  
 Status: Design  
 Designer: Florida Transportation Engineering  
 Contractor: TBD  
 Project Manager: Stuart Patterson

### SCHEDULE SUMMARY

	Original	Actual
Begin Existing Site Surveys	1/29/2020	1/29/2020
Complete Existing Site Surveys	6/30/2020	3/30/2020
Finalization of Existing Site Surveys	8/30/2020	6/7/2020
Design RFP Proposals Due	9/4/2020	9/10/2020
Design RFP Final Selection	10/29/2020	10/29/2020
Consultant Contract Issuance	12/14/2020	4/20/2021
Design Completion	12/31/2021	
Turf Supplier RFP Proposal Due		

### PARTICIPATION


**Consultant**

- SBE 25%
- Local 25%
- WBE 0%
- MBE 6.13%

**Contractor**

- SBE TBD
- Local TBD
- WBE TBD
- MBE TBD

### FUNDING

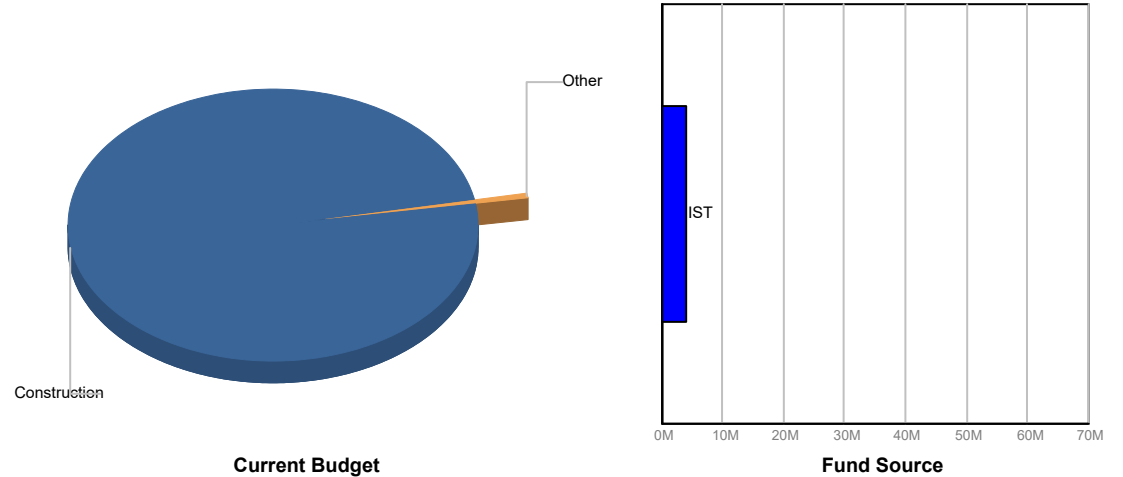

### FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Construction	\$3,980,000	\$230,856	5.80%	\$89,506
Other	\$20,000	\$12,604	63.02%	\$12,604
<b>TOTAL</b>	<b>\$4,000,000</b>	<b>\$243,460</b>	<b>6.09%</b>	<b>\$102,110</b>

### NOTES

Due to the current and foreseeable issues with construction materials, turf design has been slowed, with a revised anticipated completion in Spring 2023. FDO Director recently declared that construction/CM RFP method will be addressed as a single, project specific contract to cover all (9) parks and associated fields. CM RFP pre-proposal meeting held 5/4/2023, and proposals are due 6/6/2023. Field design documents are to be 100% before CM award. Design & schedule meetings being held on 1st Wednesday of each month.



# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects

Data Date: 05/18/2023

Report Date: 05/31/2023

### DESCRIPTION/TEAM

### SCOPE

### PHOTO

**Project Title:** JPP Athletic Field Renovation

Replacement of existing grass field turf with synthetic turf on the Miracle League Field as well as short field multi-purpose field, converted from softball 1.  
Funded: FY 2020 \$3,222,000



Project Number: T101  
 BCC District: 03  
 Delivery Method: TBD  
 Category: A06-Athletic Field Renovations  
 Status: Design  
 Designer: Florida Transportation Engineering  
 Contractor: TBD  
 Project Manager: Stuart Patterson

### SCHEDULE SUMMARY

	Original	Actual
Begin Existing Site Surveys	1/29/2020	1/29/2020
Complete Existing Site Surveys	6/30/2020	4/15/2020
Finalization of Existing Site Surveys	8/30/2020	10/15/2020
Design RFP Proposals Due	9/4/2020	9/10/2020
Design RFP Final Selection	10/29/2020	10/29/2020
Consultant Contract Issuance	12/14/2020	4/20/2021
Design Completion	12/31/2021	
Turf Supplier RFP Proposal Due	4/30/2022	

### PARTICIPATION


**Consultant**

- SBE 25%
- Local 25%
- WBE 0%
- MBE 6.13%

**Contractor**

- SBE TBD
- Local TBD
- WBE TBD
- MBE TBD

### FUNDING

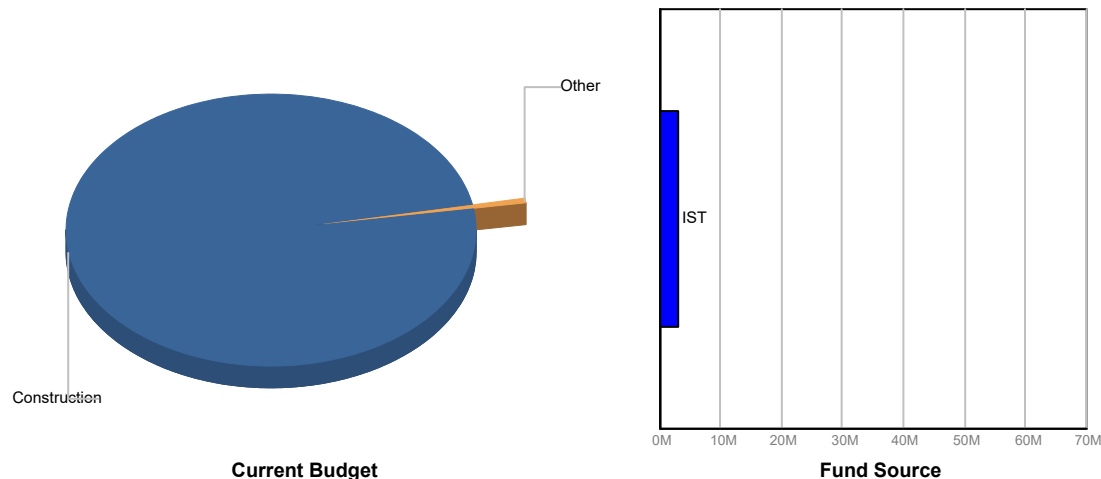

### FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Construction	\$3,204,000	\$199,280	6.22%	\$85,189
Other	\$16,000	\$80	0.50%	\$80
<b>TOTAL</b>	<b>\$3,220,000</b>	<b>\$199,359</b>	<b>6.19%</b>	<b>\$85,268</b>

### NOTES

Due to the current and foreseeable issues with construction materials, turf design has been slowed, with a revised anticipated completion in Spring 2023. FDO Director recently declared that construction/CM RFP method will be addressed as a single, project specific contract to cover all (9) parks and associated fields. CM RFP pre-proposal meeting held 5/4/2023, and proposals are due 6/6/2023. Field design documents are to be 100% before CM award. Design & schedule meetings being held on 1st Wednesday of each month.



# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects

Data Date: 05/18/2023

Report Date: 05/31/2023


### DESCRIPTION/TEAM

### SCOPE

### PHOTO

**Project Title:** Loggers Run Park Athletic Field Renovation  
**Project Number:** T102  
**BCC District:** 05  
**Delivery Method:** TBD  
**Category:** A06-Athletic Field Renovations  
**Status:** Design  
**Designer:** FTE  
**Contractor:** TBD  
**Project Manager:** Stuart Patterson

Replacement of existing grass field turf with synthetic turf on multi-purpose field 1 & 2.  
 FY 2020 IST \$3,200,000  
 FY 2022 IST (\$700,000)

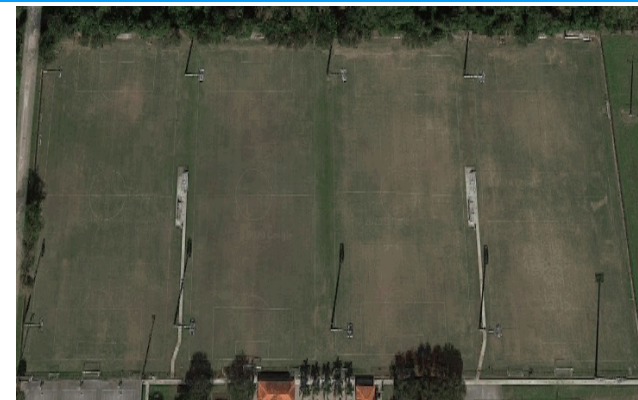

### SCHEDULE SUMMARY

	Original	Actual
Begin Existing Site Surveys	1/29/2020	1/29/2020
Complete Existing Site Surveys	6/30/2020	3/16/2020
Finalization of Existing Site Surveys	8/30/2020	10/16/2020
Design RFP Proposals Due	9/4/2020	9/10/2020
Design RFP Final Selection	10/29/2020	10/29/2020
Consultant Contract Issuance	12/14/2020	4/20/2021
Design Completion	12/31/2021	
Turf Supplier RFP Proposal Due	4/30/2022	

### PARTICIPATION


**Consultant**

- SBE 25%
- Local 25%
- WBE 0%
- MBE 6.13%

**Contractor**

- SBE TBD
- Local TBD
- WBE TBD
- MBE TBD

### FUNDING

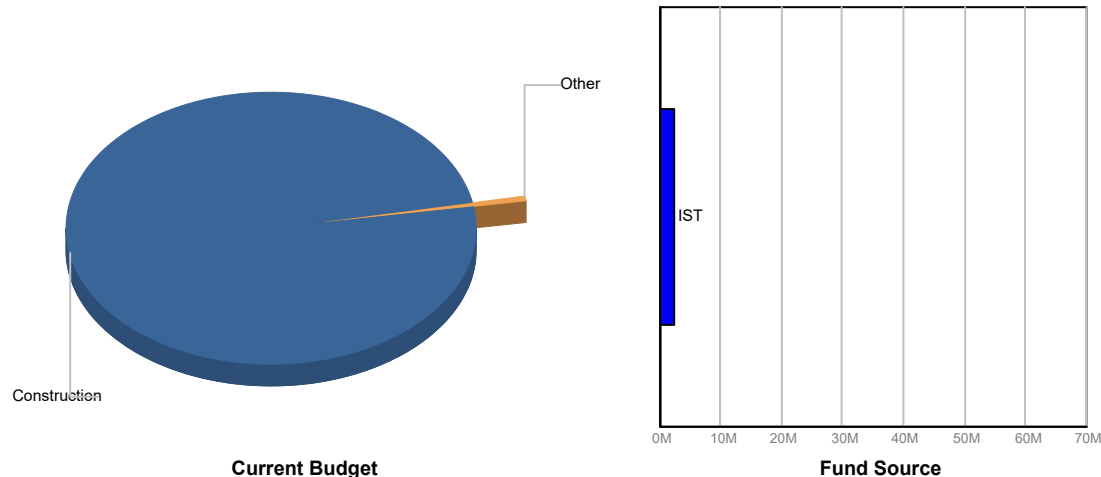

### FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Construction	\$2,484,000	\$182,953	7.37%	\$73,658
Other	\$16,000	\$15,621	97.63%	\$15,621
<b>TOTAL</b>	<b>\$2,500,000</b>	<b>\$198,574</b>	<b>7.94%</b>	<b>\$89,279</b>

### NOTES

Due to the current and foreseeable issues with construction materials, turf design has been slowed, with a revised anticipated completion in Spring 2023. FDO Director recently declared that construction/CM RFP method will be addressed as a single, project specific contract to cover all (9) parks and associated fields. CM RFP pre-proposal meeting held 5/4/2023, and proposals are due 6/6/2023. Field design documents are to be 100% before CM award. Design & schedule meetings being held on 1st Wednesday of each month.



# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects

Data Date: 05/18/2023

Report Date: 05/31/2023

### DESCRIPTION/TEAM

### SCOPE

### PHOTO

**Project Title:** Samuel Friedland District Park Expansion  
**Project Number:** T103  
**BCC District:** 06  
**Delivery Method:** TBD  
**Category:** A06-Athletic Field Renovations  
**Status:** Design  
**Designer:** Florida Transportation Engineering  
**Contractor:** TBD  
**Project Manager:** Stuart Patterson

Replacement of existing grass field turf with synthetic turf on multi-purpose field 9 & 10 as well as the open play field.  
 Funded: FY 2020 \$3,000,000



### SCHEDULE SUMMARY

	Original	Actual
Begin Existing Site Surveys	1/20/2020	1/29/2020
Complete Existing Site Surveys	6/30/2020	2/28/2020
Finalization of Existing Site Surveys	8/30/2020	10/16/2020
Design RFP Proposals Due	9/4/2020	9/10/2020
Design RFP Final Selection	10/29/2020	10/29/2020
Consultant Contract Issuance	12/14/2020	4/20/2021
Design Completion	12/31/2021	
Turf Supplier RFP Proposal Due	4/30/2022	

### PARTICIPATION


**Consultant**

- SBE 25%
- Local 25%
- WBE 0%
- MBE 6.13%

**Contractor**

- SBE TBD
- Local TBD
- WBE TBD
- MBE TBD

### FUNDING

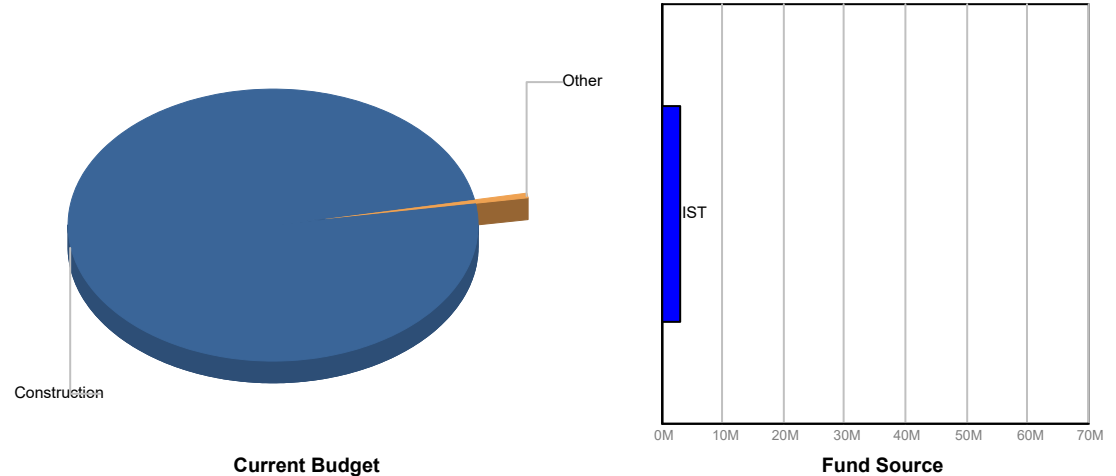

### FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Construction	\$2,985,000	\$184,116	6.17%	\$69,975
Other	\$15,000	\$10,559	70.40%	\$10,559
<b>TOTAL</b>	<b>\$3,000,000</b>	<b>\$194,676</b>	<b>6.49%</b>	<b>\$80,534</b>

### NOTES

Due to the current and foreseeable issues with construction materials, turf design has been slowed, with a revised anticipated completion in Spring 2023. FDO Director recently declared that construction/CM RFP method will be addressed as a single, project specific contract to cover all (9) parks and associated fields. CM RFP pre-proposal meeting held 5/4/2023, and proposals are due 6/6/2023. Field design documents are to be 100% before CM award. Design & schedule meetings being held on 1st Wednesday of each month.





# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects

Data Date: 05/18/2023

Report Date: 05/31/2023

### DESCRIPTION/TEAM

### SCOPE

### PHOTO

**Project Title:** Westgate Park Restroom and Athletic Field Renovation  
**Project Number:** T110  
**BCC District:** 07  
**Delivery Method:** TBD  
**Category:** E02-Existing Park Redevelopment or Expansion  
**Status:** Design  
**Designer:** Florida Transportation Engineering  
**Contractor:** TBD  
**Project Manager:** Stuart Patterson

Replacement of existing grass field turf with synthetic turf on multi-purpose field 1.  
**Funded:**  
 FY 2020 IST \$250,000  
 FY 2022 IST \$1,750,000



### SCHEDULE SUMMARY

	Original	Actual
Begin Existing Site Surveys	1/29/2020	1/29/2020
Complete Existing Site Surveys	6/30/2020	6/1/2021
Finalization of Existing Site Surveys	8/30/2020	8/25/2021
Design RFP Proposals Due	9/4/2020	9/10/2020
Design RFP Final Selection	10/29/2020	10/29/2020
Consultant Contract Issuance	12/14/2020	4/20/2021
Design Completion	12/31/2021	
Turf Supplier RFP Proposal Due	4/30/2022	

### PARTICIPATION


**Consultant**

- SBE 25%
- Local 25%
- WBE 0%
- MBE 6.13%

**Contractor**

- SBE TBD
- Local TBD
- WBE TBD
- MBE TBD

### FUNDING

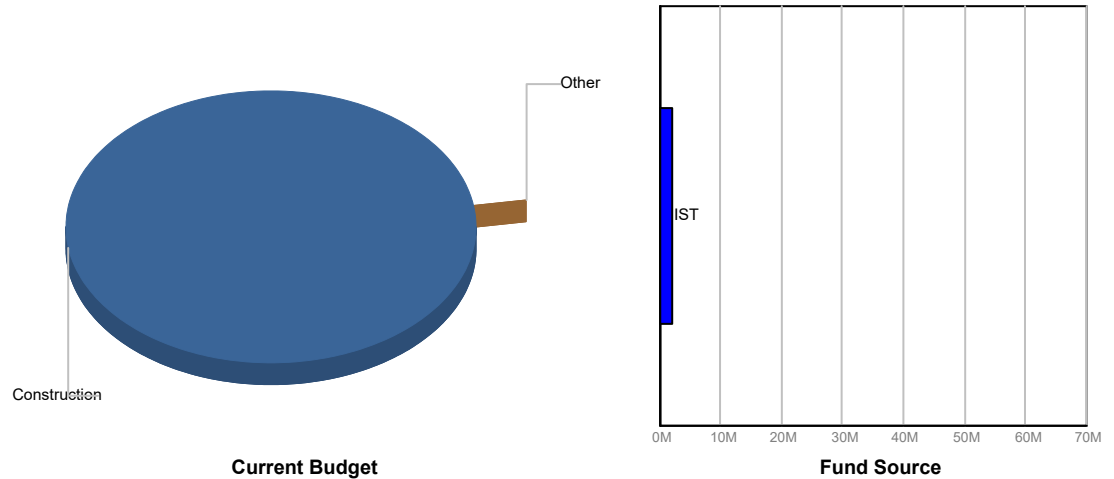

### FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Construction	\$1,998,750	\$163,792	8.19%	\$71,099
Other	\$1,250	\$0	0.00%	\$0
<b>TOTAL</b>	<b>\$2,000,000</b>	<b>\$163,792</b>	<b>8.19%</b>	<b>\$71,099</b>

### NOTES

Due to the current and foreseeable issues with construction materials, turf design has been slowed, with a revised anticipated completion in Spring 2023. FDO Director recently declared that construction/CM RFP method will be addressed as a single, project specific contract to cover all (9) parks and associated fields. CM RFP pre-proposal meeting held 5/4/2023, and proposals are due 6/6/2023. Field design documents are to be 100% before CM award. Design & schedule meetings being held on 1st Wednesday of each month.



# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects


Data Date: 05/18/2023

Report Date: 05/31/2023

DESCRIPTION/TEAM	SCOPE	PHOTO
<p><b>Project Title:</b> Dubois Park Var Historic Building Repair and Renovation</p> <p>Project Number: T111</p> <p>BCC District: 01</p> <p>Delivery Method: Annual Contract</p> <p>Category: P08-Public Building Repair Replacement &amp; Expans</p> <p>Status: Construction</p> <p>Designer: N/A</p> <p>Contractor: Robling Architecture Construction</p> <p>Project Manager: Ben Carroll</p>	<p>The project consists of relocating the Pineapple Packing House structure, wood framing repairs, roof replacement and new windows, doors, electrical and HVAC, as well as renovation to the Dubois House.</p> <p>IST FY 2020 - \$250,000</p> <p>IST FY 2021 - \$250,000</p> <p>IST FY 2022 - \$250,000</p> <p>IST FY 2023 - \$250,000</p> <p>IST FY 2024 - \$400,585</p> <p>IST FY 2025 - \$599,415</p>	

SCHEDULE SUMMARY		
	Original	Actual
Project Start	4/12/2021	4/12/2021
Project Completion	12/13/2021	

PARTICIPATION	
<b>Consultant</b>	
SBE	N/A
Local	N/A
WBE	N/A
MBE	N/A
<b>Contractor</b>	
SBE	10.46%
Local	100%
WBE	0%
MBE	0%

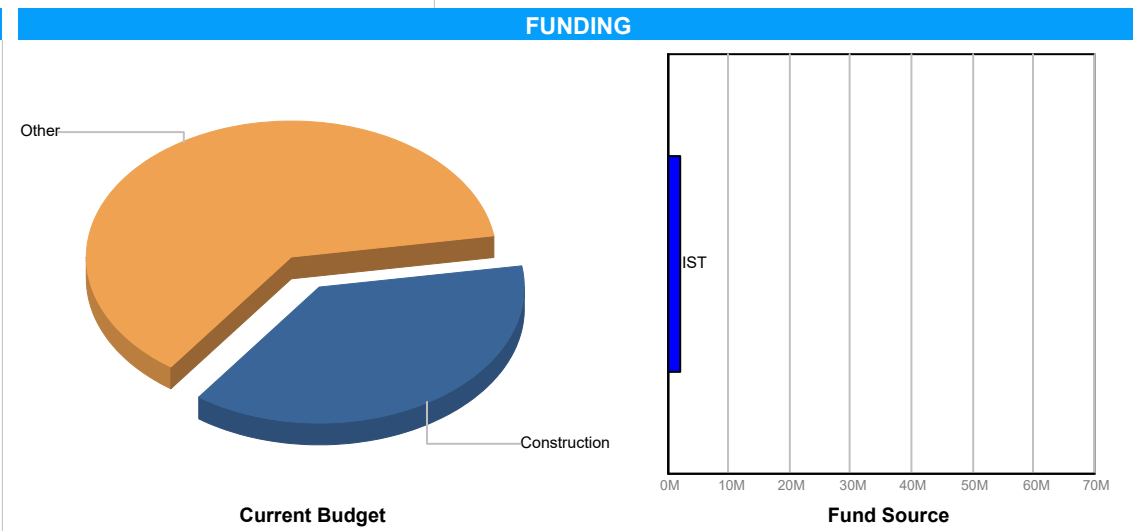

FINANCIAL SUMMARY				
	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Construction	\$748,750	\$291,844	38.98%	\$274,014
Other	\$1,251,250	\$6,524	0.52%	\$6,524
<b>TOTAL</b>	<b>\$2,000,000</b>	<b>\$298,368</b>	<b>14.92%</b>	<b>\$280,538</b>

**NOTES**

Pineapple House (\$400,000); Project substantially complete. Temporary fence removed. Sod installed. Landscape inspection failed due to an exposed HVAC condenser. Pioneer House; Parks to coordinate with State Preservation officer on ADA requirements. The entire area of DuBois Park is located within the Unincorporated Palm Beach County. Dubois House: Project commencement is anticipated in 2023.



# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects

Data Date: 05/18/2023

Report Date: 05/31/2023

### DESCRIPTION/TEAM

### SCOPE

### PHOTO

**Project Title:** Canyon's District Park New Park Development  
**Project Number:** T122  
**BCC District:** 05  
**Delivery Method:** Construction Manager at Risk  
**Category:** N02-New Park Development  
**Status:** Construction  
**Designer:** Architecture Green  
**Contractor:** Kaufman Lynn  
**Project Manager:** Stuart Patterson

The project consists of the construction of a 52 acre Park south of Boynton Beach Blvd, along the west side of Acme Dairy Rd. with the Canyon Lakes Communities bordering the south and west limits of the site. The park will be constructed in two phases. Phase I will need to be completed in order to transfer the multi-purpose activities that currently take place on two existing soccer fields located to the west of the park. Once transferred the old soccer fields site will become the site of the new Canyon District Library.



Impact Fees \$4,755,000  
 FY 2021 IST \$12,000,000  
 FY 2022 IST \$12,983,740

### SCHEDULE SUMMARY

	Original	Actual
GMP Approval-Phase I	1/14/2021	5/4/2021
Construction Start-Phase I	1/27/2021	1/4/2021
Construction Completion-Phase I	1/27/2022	10/31/2022
Project Completion-Phase II	3/27/2022	
Construction Start-Phase II	3/4/2024	

### PARTICIPATION


**Consultant**

- SBE 75.93%
- Local 100%
- WBE 21.41%
- MBE 0%

**Contractor**

- SBE 22.32%
- Local 100%
- WBE 22.32%
- MBE 22.32%

### FUNDING

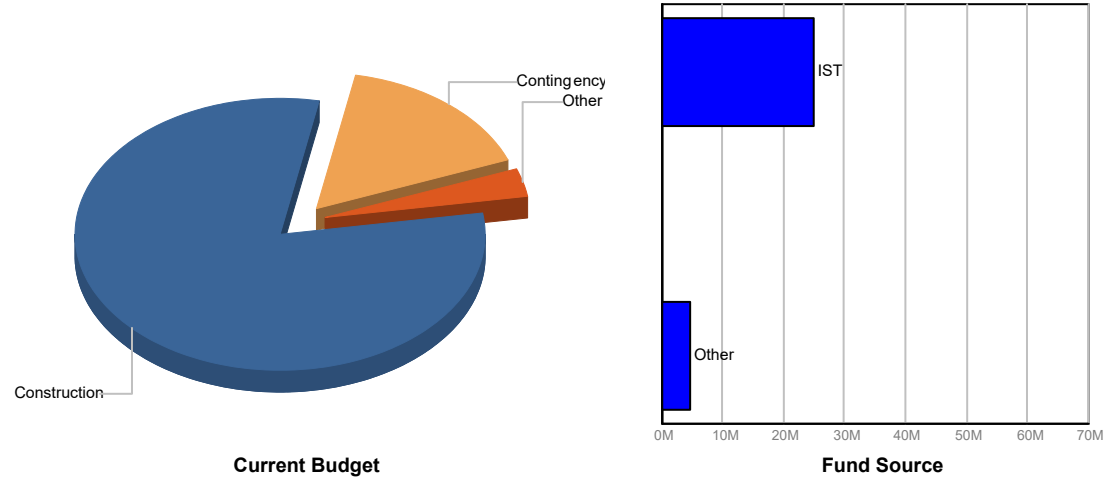

### FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$0	\$73,982	0.00%	\$150,569
Construction	\$23,983,740	\$11,068,961	46.15%	\$9,892,421
Other	\$1,000,000	\$1,140,827	114.08%	\$1,140,827
Contingency	\$4,755,000	\$0	0.00%	\$0
<b>TOTAL</b>	<b>\$29,738,740</b>	<b>\$12,283,770</b>	<b>41.31%</b>	<b>\$11,183,817</b>

### NOTES

Phases 1 & 1A currently in close-out. Phase 2 monthly design meetings ongoing. 50% CD's submittal scheduled for 7/5/2023; 95% construction/GMP documents submittal scheduled for 9/20/2023.



# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects

Data Date: 05/18/2023

Report Date: 05/31/2023

### DESCRIPTION/TEAM

### SCOPE

### PHOTO

**Project Title:** Okeehetee Park South Expansion

Project Number: T125  
 BCC District: 03  
 Delivery Method: Annual Contract  
 Category: E02-Existing Park Redevelopment or Expansion  
 Status: Construction  
 Designer: N/A  
 Contractor: RCP Shelters and Wynn & Sons  
 Project Manager: Bob Hamilton

Inclusion of new park amenities and accrual of funds for the development of a camping island, picnic island and RV park.  
 FY21: \$1,000,000  
 FY22: \$1,000,000  
 FY23: \$1,075,000



### SCHEDULE SUMMARY

	Original	Actual
Start Date	9/9/2021	9/9/2021
Completion Date	5/31/2022	

### PARTICIPATION


#### Consultant

SBE N/A  
 Local N/A  
 WBE N/A  
 MBE N/A


#### Contractor

SBE 100%  
 Local 100%  
 WBE 0%  
 MBE 0%

### FUNDING



Current Budget

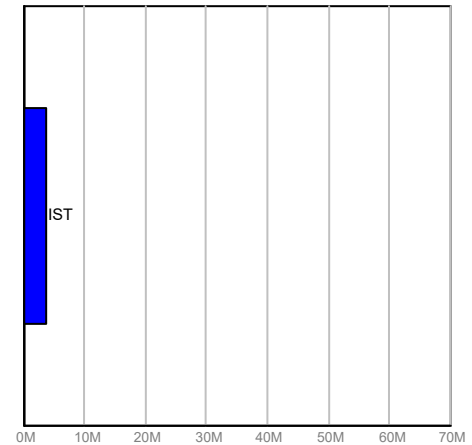

Fund Source

### FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Construction	\$3,705,000	\$56,818	1.53%	\$56,818
<b>TOTAL</b>	<b>\$3,705,000</b>	<b>\$56,818</b>	<b>1.53%</b>	<b>\$56,818</b>

### NOTES

Prior fund were expended for the construction of informational Kiosks.  
 No additional work orders have been processed to date.



# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects

Data Date: 05/18/2023

Report Date: 05/31/2023

### DESCRIPTION/TEAM

### SCOPE

### PHOTO

**Project Title:** Acreage Community Park Recreation Center  
**Project Number:** T156  
**BCC District:** 06  
**Delivery Method:** TBD  
**Category:** E02-Existing Park Redevelopment or Expansion  
**Status:** Design  
**Designer:** TBD  
**Contractor:** TBD  
**Project Manager:** ITID/Bob Hamilton

The project originally consisted of construction of a community/recreation center within Acreage Community Park. The project as now proposed consists of a synthetic turf multi-purpose field, state park, equestrian drop-off area and support infrastructure.



### SCHEDULE SUMMARY

	Original	Actual
Project Start	10/1/2021	4/1/2022

### PARTICIPATION



#### Consultant

- SBE TBD
- Local TBD
- WBE TBD
- MBE TBD

#### Contractor

- SBE TBD
- Local TBD
- WBE TBD
- MBE TBD

### FUNDING

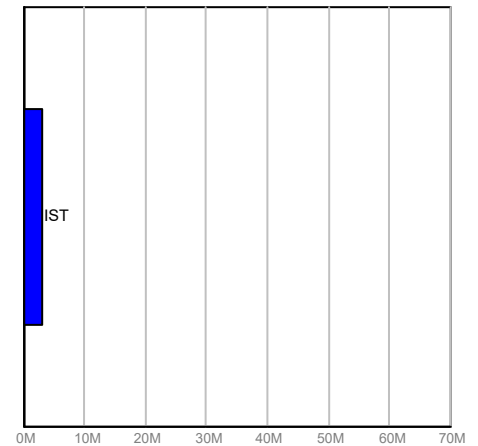

Current Budget

Fund Source

### FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Construction	\$3,000,000	\$0	0.00%	\$0
<b>TOTAL</b>	<b>\$3,000,000</b>	<b>\$0</b>	<b>0.00%</b>	<b>\$0</b>

### NOTES

ITID has requested to modify their scope to include a precast restroom instead of traditional CBS. Also requested that the synthetic turf multipurpose field be moved to a second field location. Request is under review by Parks and Rec.



# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects

Data Date: 05/18/2023

Report Date: 05/31/2023

### DESCRIPTION/TEAM

### SCOPE

### PHOTO

**Project Title:** Glades Pioneer Park Athletic Field Renovation  
**Project Number:** T175  
**BCC District:** 06  
**Delivery Method:** TBD  
**Category:** A06-Athletic Field Renovations  
**Status:** Design  
**Designer:** Florida Transportation Engineering  
**Contractor:** TBD  
**Project Manager:** Stuart Patterson

Athletic facility improvement to Glades Pioneer Park will allow for year-round use of football/soccer fields. High quality artificial surfacing will provide an excellent facility for youth and allow for minimal downtime for positive youth activities.  
**Funded:**  
 FY 2021 \$210,000  
 FY 2023 \$1,009,000



### SCHEDULE SUMMARY


	Original	Actual
Begin Existing Site Surveys	1/29/2020	1/29/2020
Complete Existing Site Surveys	6/30/2020	5/18/2020
Finalization of Existing Site Surveys	8/30/2020	9/18/2020
Design RFP Final Selection	10/29/2020	10/29/2020
Consultant Contract Issuance	12/14/2020	
Design Completion	12/31/2021	
Turf Supplier RFP Proposal Due	4/30/2022	

### PARTICIPATION

**Consultant**  
 SBE 25%  
 Local 25%  
 WBE 0%  
 MBE 6.13%

**Contractor**  
 SBE TBD  
 Local TBD  
 WBE TBD  
 MBE TBD

### FUNDING

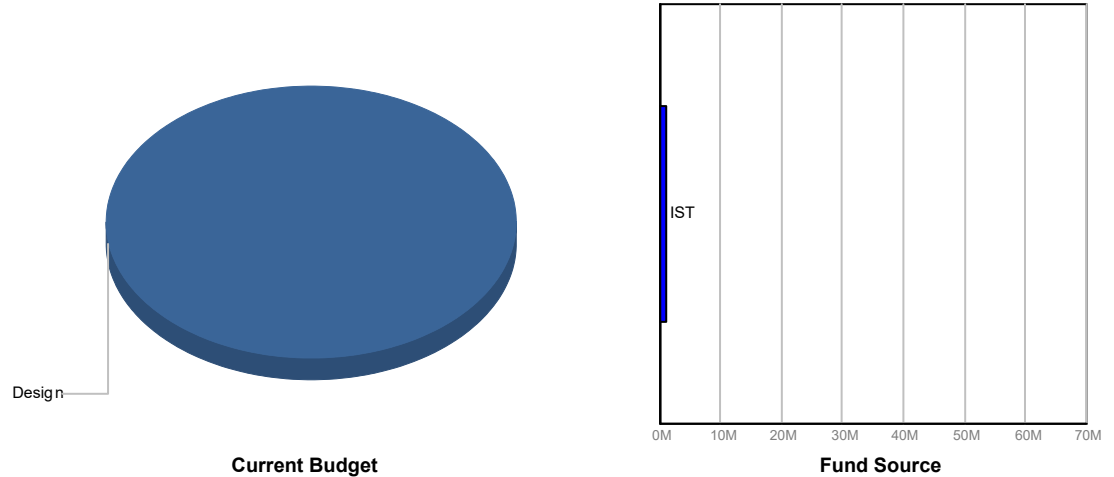

### FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$1,213,709	\$170,702	14.06%	\$79,748
<b>TOTAL</b>	<b>\$1,213,709</b>	<b>\$170,702</b>	<b>14.06%</b>	<b>\$79,748</b>

### NOTES

Due to the current and foreseeable issues with construction materials, turf design has been slowed, with a revised anticipated completion in Spring 2023. FDO Director recently declared that construction/CM RFP method will be addressed as a single, project specific contract to cover all (9) parks and associated fields. CM RFP pre-proposal meeting held 5/4/2023, and proposals are due 6/6/2023. Field design documents are to be 100% before CM award. Design & schedule meetings being held on 1st Wednesday of each month.



# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects

Data Date: 05/18/2023

Report Date: 05/31/2023

### DESCRIPTION/TEAM

### SCOPE

### PHOTO

**Project Title:** North County Pool Facility Repairs and Renovation  
**Project Number:** T176  
**BCC District:** 01  
**Delivery Method:** Annual Contract  
**Category:** A02-Aquatic Facility Repair and Replacement  
**Status:** Design  
**Designer:** TBD  
**Contractor:** TBD  
**Project Manager:** Mitch Silverman

Public aquatic facility overdue for large scale capital repair and renovation - renovations would include restroom/locker-room renovation, resurfacing and coping repairs, baby pool replacement with water feature and shade structures. We receive many public complaints about the structural design of and capital condition of the restrooms.  
  
 FY2023\$2,062,000.00



### SCHEDULE SUMMARY

### PARTICIPATION

### FUNDING



Original	Actual

#### Consultant

SBE TBD  
 Local TBD  
 WBE TBD  
 MBE TBD

#### Contractor

SBE TBD  
 Local TBD  
 WBE TBD  
 MBE TBD

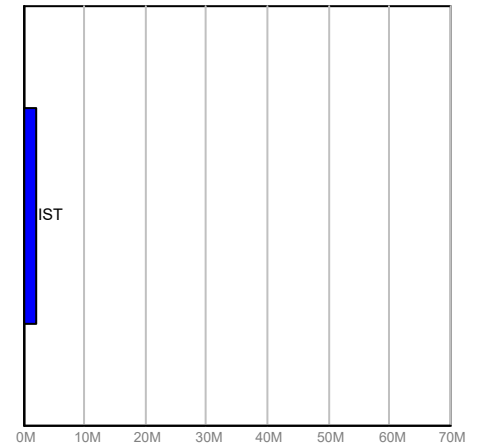

### FINANCIAL SUMMARY

### NOTES

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Construction	\$2,062,000	\$929	0.05%	\$929
<b>TOTAL</b>	<b>\$2,062,000</b>	<b>\$929</b>	<b>0.05%</b>	<b>\$929</b>

Pre-scope walk-through is scheduled for early June.



# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects

Data Date: 05/18/2023

Report Date: 05/31/2023

### DESCRIPTION/TEAM

### SCOPE

### PHOTO

**Project Title:** Coconut Cove Waterpark Facility Repairs and Renovation  
**Project Number:** T177  
**BCC District:** 05  
**Delivery Method:** Annual Contract  
**Category:** A02-Aquatic Facility Repair and Replacement  
**Status:** Design  
**Designer:** TBD  
**Contractor:** TBD  
**Project Manager:** Eric Chimienti

Repairs and renovations include replacement of play structure in zero depth playground, restroom refurbishment, replace old leaking concession tiki hut with a concession building, classroom and birthday party room renovation, replace old chairs/deck lounge chairs. Upgrades are necessary to maintain business operations and no loss in revenue.  
 FY2023\$1,449,000.00



### SCHEDULE SUMMARY

### PARTICIPATION

### FUNDING

Original	Actual


#### Consultant

SBE TBD  
 Local TBD  
 WBE TBD  
 MBE TBD


#### Contractor

SBE TBD  
 Local TBD  
 WBE TBD  
 MBE TBD

Construction



Current Budget

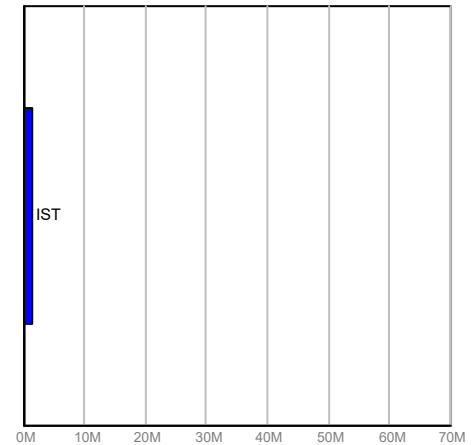

Fund Source

### FINANCIAL SUMMARY

### NOTES

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Construction	\$1,449,000	\$653	0.05%	\$653
<b>TOTAL</b>	<b>\$1,449,000</b>	<b>\$653</b>	<b>0.05%</b>	<b>\$653</b>

RFPA issued on 2/9/23, and PM assigned on 06/06/23.
