



Monthly Infrastructure Sales Tax Project Report

Small Cap Projects

Data Date: 04/16/2020

Report Date: 05/11/20

DESCRIPTION/TEAM	SCOPE/NOTES	SCHEDULE		
Project Title: Prairie Rd. over LWDD Lat. 8 Canal (PB934334) Project Number: 1504 BCC District: 03 Delivery Method: Design CCNA Category: B08-Bridge Replacements Status: Design Designer: Wantman Group Contractor: TBD (bid) Project Manager: Kristine Frazzell-Smith	Scope This project will replace an existing bridge that was built over 50 years ago. The new bridge will improve traffic safety (lane widths, bike lanes, parapets), update the guardrail system, improve roadway drainage, restore the slope protection, and enhance pedestrian sidewalk safety. Notes This project is funded for design (\$150k) in FY 2017 and construction (\$450k) in FY 2019.	Original	Actual	
		Design Contract Notice to Proceed	10/25/2016	10/25/2016
		Design Completion	10/1/2019	1/3/2020
		Construction Bid Date	1/1/2020	3/17/2020
		Construction Start	7/1/2020	
		Construction Complete	4/1/2021	

PARTICIPATION	FUNDING	FINANCIAL SUMMARY			
Consultant SBE 17.8% MBE 0% WBE 0% Local 100%		Project Budget	Committed	% Committed	Paid To Date
Contractor SBE TBD MBE TBD WBE TBD Local TBD		A	B	C=B/A	D
		\$600,000	\$175,766	29.29%	\$149,229

DESCRIPTION/TEAM	SCOPE/NOTES	SCHEDULE		
Project Title: Kudza Rd. over LWDD Lat. 8 Canal (934312) Project Number: 1520 BCC District: 02 Delivery Method: Design CCNA Category: B08-Bridge Replacements Status: Construction Designer: Wantman Group Contractor: FG Construction, LLC Project Manager: Kristine Frazzell-Smith	Scope This project will replace an existing bridge (built over 55 years ago) with a culvert. The project will improve traffic safety (lane widths, bike lanes), update the guardrail system, improve roadway drainage, restore the slope protection, and enhance pedestrian sidewalk safety. Notes This project is funded for design (\$150k) in FY 2017 and construction (\$550k) in FY 2019. Due to aging estimates and escalating construction costs, the project's budget was increased from \$700k to \$875k (BT 2020-0364).	Original	Actual	
		Design Contract Notice to Proceed	6/20/2017	6/20/2017
		Design Completion	9/1/2019	8/30/2019
		Construction Bid Date	12/1/2019	11/19/2019
		Construction Start	6/1/2020	
		Construction Complete	3/1/2021	

PARTICIPATION	FUNDING	FINANCIAL SUMMARY			
Consultant SBE 29.7% MBE 0% WBE 0% Local 100%		Project Budget	Committed	% Committed	Paid To Date
Contractor SBE 21.1% MBE TBD WBE TBD Local 21.1%		A	B	C=B/A	D
		\$875,000	\$138,058	15.78%	\$131,021



Monthly Infrastructure Sales Tax Project Report

Small Cap Projects

Data Date: 04/16/2020

Report Date: 05/11/20

DESCRIPTION/TEAM			SCOPE/NOTES			SCHEDULE																					
Project Title: Smith Sundy Rd. over LWDD Lat. 33 Canal Project Number: 1521 BCC District: 05 Delivery Method: Design CCNA Category: B04-Bridge Modifications Status: Design Designer: Wantman Group Contractor: TBD (bid) Project Manager: Kristine Frazell-Smith			Scope This project will replace an existing bridge that was built over 50 years ago. The new bridge will improve traffic safety (lane widths, bike lanes, parapets), update the guardrail system, improve roadway drainage, restore the slope protection, and enhance pedestrian sidewalk safety. Notes This project is funded for design (\$150k) in FY 2017 and construction (\$450K) in FY 2019.			<table border="1"> <thead> <tr> <th></th> <th>Original</th> <th>Actual</th> </tr> </thead> <tbody> <tr> <td>Design Contract Notice to Proceed</td> <td>3/13/2018</td> <td>3/21/2018</td> </tr> <tr> <td>Design Completion</td> <td>7/1/2020</td> <td></td> </tr> <tr> <td>Construction Bid Date</td> <td>10/1/2020</td> <td></td> </tr> <tr> <td>Construction Start</td> <td>3/1/2021</td> <td></td> </tr> <tr> <td>Construction Complete</td> <td>12/1/2021</td> <td></td> </tr> </tbody> </table>					Original	Actual	Design Contract Notice to Proceed	3/13/2018	3/21/2018	Design Completion	7/1/2020		Construction Bid Date	10/1/2020		Construction Start	3/1/2021		Construction Complete	12/1/2021	
	Original	Actual																									
Design Contract Notice to Proceed	3/13/2018	3/21/2018																									
Design Completion	7/1/2020																										
Construction Bid Date	10/1/2020																										
Construction Start	3/1/2021																										
Construction Complete	12/1/2021																										
PARTICIPATION			FUNDING			FINANCIAL SUMMARY																					
Consultant SBE 62.5% MBE 0% WBE 0% Local 100%						<table border="1"> <thead> <tr> <th>Project Budget</th> <th>Committed</th> <th>% Committed</th> <th>Paid To Date</th> </tr> <tr> <th>A</th> <th>B</th> <th>C=B/A</th> <th>D</th> </tr> </thead> <tbody> <tr> <td>\$600,000</td> <td>\$203,499</td> <td>33.92%</td> <td>\$131,679</td> </tr> </tbody> </table>				Project Budget	Committed	% Committed	Paid To Date	A	B	C=B/A	D	\$600,000	\$203,499	33.92%	\$131,679						
Project Budget	Committed	% Committed				Paid To Date																					
A	B	C=B/A	D																								
\$600,000	\$203,499	33.92%	\$131,679																								
Contractor SBE TBD MBE TBD WBE TBD Local TBD																											

DESCRIPTION/TEAM			SCOPE/NOTES			SCHEDULE															
Project Title: Sections of Military Trail Project Number: 1541 BCC District: CW Delivery Method: Annual Striping Contract Category: S16-Striping Status: Construction Designer: N/A Contractor: Oglesby/Southwide Project Manager: Larry Kelly			Scope This project consists of restriping sections of Military Trail. Notes The restriping construction scheduled for FY 2017 has been completed. The project is funded at \$200,000 in FY 2017 and FY 2021 and \$100,000 in FY 2022 thru FY 2026 for a total funding of \$900,000.			<table border="1"> <thead> <tr> <th></th> <th>Original</th> <th>Actual</th> </tr> </thead> <tbody> <tr> <td>Palmetto Park to Clint Moore Complete</td> <td>11/20/2017</td> <td>11/20/2017</td> </tr> <tr> <td>18th Street to Palmetto Park Complete</td> <td>12/18/2017</td> <td>12/18/2017</td> </tr> </tbody> </table>					Original	Actual	Palmetto Park to Clint Moore Complete	11/20/2017	11/20/2017	18th Street to Palmetto Park Complete	12/18/2017	12/18/2017			
	Original	Actual																			
Palmetto Park to Clint Moore Complete	11/20/2017	11/20/2017																			
18th Street to Palmetto Park Complete	12/18/2017	12/18/2017																			
PARTICIPATION			FUNDING			FINANCIAL SUMMARY															
Consultant SBE N/A MBE N/A WBE N/A Local N/A						<table border="1"> <thead> <tr> <th>Project Budget</th> <th>Committed</th> <th>% Committed</th> <th>Paid To Date</th> </tr> <tr> <th>A</th> <th>B</th> <th>C=B/A</th> <th>D</th> </tr> </thead> <tbody> <tr> <td>\$900,000</td> <td>\$136,687</td> <td>15.19%</td> <td>\$136,687</td> </tr> </tbody> </table>				Project Budget	Committed	% Committed	Paid To Date	A	B	C=B/A	D	\$900,000	\$136,687	15.19%	\$136,687
Project Budget	Committed	% Committed				Paid To Date															
A	B	C=B/A	D																		
\$900,000	\$136,687	15.19%	\$136,687																		
Contractor SBE 92% MBE 0% WBE 0% Local 92%																					



Monthly Infrastructure Sales Tax Project Report

Small Cap Projects

Data Date: 04/16/2020

Report Date: 05/11/20

DESCRIPTION/TEAM	SCOPE/NOTES	SCHEDULE	
<p>Project Title: Lake Osborne Dr. over Lake Bass Canal (PB934354)</p> <p>Project Number: 1542</p> <p>BCC District: 03</p> <p>Delivery Method: Design CCNA</p> <p>Category: B04-Bridge Modifications</p> <p>Status: Design</p> <p>Designer: Stantec</p> <p>Contractor: TBD (bid)</p> <p>Project Manager: Kristine Frazell-Smith</p>	<p>Scope</p> <p>This project will replace an existing bridge that was built over 60 years ago. The project will improve traffic safety (lane widths, bike lanes, parapets), update the guardrail system, improve roadway drainage, restore the slope protection, and enhance pedestrian sidewalk safety.</p> <p>Notes</p> <p>This project is funded for design (\$150k) in FY 2017 and construction (\$450k) in FY 2019.</p>	Original	Actual
		Design Contract NTP	8/2/2017 / 8/2/2017
		Study Start	8/2/2017 / 8/2/2017
		Study Complete	5/1/2018 / 5/1/2018
		Design Completion	12/1/2020
		Construction Bid Date	4/1/2021
		Construction Start	8/1/2021
		Construction Complete	12/1/2022

PARTICIPATION	FUNDING	FINANCIAL SUMMARY			
<p>Consultant</p> <p>SBE 28.9% MBE 27.7%</p> <p>WBE 0% Local 95%</p> <p>Contractor</p> <p>SBE TBD MBE TBD</p> <p>WBE TBD Local TBD</p>		Project Budget	Committed	% Committed	Paid To Date
		A	B	C=B/A	D
		\$600,000	\$321,570	53.59%	\$106,017

DESCRIPTION/TEAM	SCOPE/NOTES	SCHEDULE	
<p>Project Title: Sections of Congress Avenue</p> <p>Project Number: 1543</p> <p>BCC District: Multiple</p> <p>Delivery Method: Annual Striping Contract</p> <p>Category: S16-Striping</p> <p>Status: Construction</p> <p>Designer: N/A</p> <p>Contractor: Oglesby/Southwide</p> <p>Project Manager: Larry Kelly</p>	<p>Scope</p> <p>This project consists of restriping sections of Congress Avenue.</p> <p>Notes</p> <p>The restriping construction scheduled for FY 2017 has been completed. The project is funded at \$100,000 in FY 2017 and FY 2021 thru FY 2025 and \$200,000 in FY 2026 for a total funding of \$800,000.</p>	Original	Actual
		Palm Beach Lakes to 45th Street Comple	10/6/2017 / 10/6/2017
		Okeehobee to Palm Beach Lakes Complt	2/6/2018 / 2/6/2018
		Silver Beach to Water Tower	3/18/2019 / 3/18/2019

PARTICIPATION	FUNDING	FINANCIAL SUMMARY			
<p>Consultant</p> <p>SBE N/A MBE N/A</p> <p>WBE N/A Local N/A</p> <p>Contractor</p> <p>SBE 68% MBE 0%</p> <p>WBE 0% Local 68%</p>		Project Budget	Committed	% Committed	Paid To Date
		A	B	C=B/A	D
		\$800,000	\$67,559	8.44%	\$67,559



Monthly Infrastructure Sales Tax Project Report

Small Cap Projects

Data Date: 04/16/2020

Report Date: 05/11/20

DESCRIPTION/TEAM				SCOPE/NOTES				SCHEDULE															
Project Title: Sections of Gateway Blvd. Project Number: 1544 BCC District: 03 Delivery Method: Annual Striping Contract Category: S16-Striping Status: Construction Designer: N/A Contractor: Southwide Project Manager: Larry Kelly				Scope This project consists of restriping sections of Gateway Boulevard.				<table border="1"> <thead> <tr> <th></th> <th>Original</th> <th>Actual</th> </tr> </thead> <tbody> <tr> <td>Hagen Ranch Road to Jog Road Comple</td> <td>8/24/2017</td> <td>8/24/2017</td> </tr> <tr> <td>Military to Congress Complete</td> <td>1/22/2018</td> <td>1/22/2018</td> </tr> </tbody> </table>					Original	Actual	Hagen Ranch Road to Jog Road Comple	8/24/2017	8/24/2017	Military to Congress Complete	1/22/2018	1/22/2018			
	Original	Actual																					
Hagen Ranch Road to Jog Road Comple	8/24/2017	8/24/2017																					
Military to Congress Complete	1/22/2018	1/22/2018																					
				Notes The restriping construction scheduled for FY 2017 has been completed. The project is funded at \$100,000 in FY 2017 and FY 2025 for a total funding of \$200,000.																			
PARTICIPATION				FUNDING				FINANCIAL SUMMARY															
Consultant SBE N/A MBE N/A WBE N/A Local N/A								<table border="1"> <thead> <tr> <th>Project Budget</th> <th>Committed</th> <th>% Committed</th> <th>Paid To Date</th> </tr> <tr> <th>A</th> <th>B</th> <th>C=B/A</th> <th>D</th> </tr> </thead> <tbody> <tr> <td>\$200,000</td> <td>\$76,915</td> <td>38.46%</td> <td>\$76,915</td> </tr> </tbody> </table>				Project Budget	Committed	% Committed	Paid To Date	A	B	C=B/A	D	\$200,000	\$76,915	38.46%	\$76,915
Project Budget	Committed	% Committed	Paid To Date																				
A	B	C=B/A	D																				
\$200,000	\$76,915	38.46%	\$76,915																				
Contractor SBE 100% MBE 0% WBE 0% Local 100%																							

DESCRIPTION/TEAM				SCOPE/NOTES				SCHEDULE															
Project Title: Sections of Seacrest Blvd. Project Number: 1545 BCC District: 07 Delivery Method: Annual Striping Contract Category: S16-Striping Status: Construction Designer: N/A Contractor: Southwide Project Manager: Larry Kelly				Scope This project consists of restriping sections of Seacrest Boulevard.				<table border="1"> <thead> <tr> <th></th> <th>Original</th> <th>Actual</th> </tr> </thead> <tbody> <tr> <td>SW 26th to Boynton Beach Blvd. Comple</td> <td>9/6/2017</td> <td>9/6/2017</td> </tr> </tbody> </table>					Original	Actual	SW 26th to Boynton Beach Blvd. Comple	9/6/2017	9/6/2017						
	Original	Actual																					
SW 26th to Boynton Beach Blvd. Comple	9/6/2017	9/6/2017																					
				Notes The restriping construction scheduled for FY 2017 has been completed. The project is funded at \$50,000 in FY 2017, FY 2020, FY 2023 and FY 2025 for a total funding of \$200,000.																			
PARTICIPATION				FUNDING				FINANCIAL SUMMARY															
Consultant SBE N/A MBE N/A WBE N/A Local N/A								<table border="1"> <thead> <tr> <th>Project Budget</th> <th>Committed</th> <th>% Committed</th> <th>Paid To Date</th> </tr> <tr> <th>A</th> <th>B</th> <th>C=B/A</th> <th>D</th> </tr> </thead> <tbody> <tr> <td>\$200,000</td> <td>\$31,605</td> <td>15.80%</td> <td>\$31,605</td> </tr> </tbody> </table>				Project Budget	Committed	% Committed	Paid To Date	A	B	C=B/A	D	\$200,000	\$31,605	15.80%	\$31,605
Project Budget	Committed	% Committed	Paid To Date																				
A	B	C=B/A	D																				
\$200,000	\$31,605	15.80%	\$31,605																				
Contractor SBE 100% MBE 0 WBE 05 Local 100%																							



Monthly Infrastructure Sales Tax Project Report

Small Cap Projects

Data Date: 04/16/2020

Report Date: 05/11/20

DESCRIPTION/TEAM				SCOPE/NOTES				SCHEDULE															
Project Title: Sections of Old Dixie Hwy. Project Number: 1546 BCC District: 07 Delivery Method: Annual Striping Contract Category: S16-Striping Status: Construction Designer: N/A Contractor: Southwide Project Manager: Larry Kelly				Scope This project consists of restriping sections of Old Dixie Highway.				<table border="1"> <thead> <tr> <th></th> <th>Original</th> <th>Actual</th> </tr> </thead> <tbody> <tr> <td>Boca Raton city limits to Lindell Road Cor</td> <td>11/20/2017</td> <td>11/20/2017</td> </tr> <tr> <td>NE 2nd Street to Glades Road Complete</td> <td>11/20/2017</td> <td>11/20/2017</td> </tr> </tbody> </table>					Original	Actual	Boca Raton city limits to Lindell Road Cor	11/20/2017	11/20/2017	NE 2nd Street to Glades Road Complete	11/20/2017	11/20/2017			
	Original	Actual																					
Boca Raton city limits to Lindell Road Cor	11/20/2017	11/20/2017																					
NE 2nd Street to Glades Road Complete	11/20/2017	11/20/2017																					
				Notes The restriping construction scheduled for FY 2017 has been completed. The project is funded at \$50,000 in FY 2017, and \$100,000 in FY 2021 and FY 2023, and \$125,000 in FY 2026 for a total funding of \$375,000.																			
PARTICIPATION				FUNDING				FINANCIAL SUMMARY															
Consultant SBE N/A MBE N/A WBE N/A Local N/A								<table border="1"> <thead> <tr> <th>Project Budget</th> <th>Committed</th> <th>% Committed</th> <th>Paid To Date</th> </tr> <tr> <th>A</th> <th>B</th> <th>C=B/A</th> <th>D</th> </tr> </thead> <tbody> <tr> <td>\$375,000</td> <td>\$16,285</td> <td>4.34%</td> <td>\$16,285</td> </tr> </tbody> </table>				Project Budget	Committed	% Committed	Paid To Date	A	B	C=B/A	D	\$375,000	\$16,285	4.34%	\$16,285
Project Budget	Committed	% Committed	Paid To Date																				
A	B	C=B/A	D																				
\$375,000	\$16,285	4.34%	\$16,285																				
Contractor SBE 100% MBE 0% WBE 0% Local 100%																							

DESCRIPTION/TEAM				SCOPE/NOTES				SCHEDULE															
Project Title: Sections of Clint Moore Road Project Number: 1547 BCC District: Multiple Delivery Method: Annual Striping Contract Category: S16-Striping Status: Construction Designer: N/A Contractor: Southwide Project Manager: Larry Kelly				Scope This project consists of restriping sections of Clint Moore Road.				<table border="1"> <thead> <tr> <th></th> <th>Original</th> <th>Actual</th> </tr> </thead> <tbody> <tr> <td>Military to Congress Complete</td> <td>9/6/2017</td> <td>9/6/2017</td> </tr> </tbody> </table>					Original	Actual	Military to Congress Complete	9/6/2017	9/6/2017						
	Original	Actual																					
Military to Congress Complete	9/6/2017	9/6/2017																					
				Notes The restriping construction scheduled for FY 2017 has been completed. The project is funded at \$50,000 in FY 2017 and FY 2022, and \$100,000 in FY 2026 for a total funding of \$200,000.																			
PARTICIPATION				FUNDING				FINANCIAL SUMMARY															
Consultant SBE N/A MBE N/A WBE N/A Local N/A								<table border="1"> <thead> <tr> <th>Project Budget</th> <th>Committed</th> <th>% Committed</th> <th>Paid To Date</th> </tr> <tr> <th>A</th> <th>B</th> <th>C=B/A</th> <th>D</th> </tr> </thead> <tbody> <tr> <td>\$200,000</td> <td>\$34,182</td> <td>17.09%</td> <td>\$34,182</td> </tr> </tbody> </table>				Project Budget	Committed	% Committed	Paid To Date	A	B	C=B/A	D	\$200,000	\$34,182	17.09%	\$34,182
Project Budget	Committed	% Committed	Paid To Date																				
A	B	C=B/A	D																				
\$200,000	\$34,182	17.09%	\$34,182																				
Contractor SBE 100% MBE 0% WBE 0% Local 100%																							



Monthly Infrastructure Sales Tax Project Report

Small Cap Projects

Data Date: 04/16/2020

Report Date: 05/11/20

DESCRIPTION/TEAM	SCOPE/NOTES	SCHEDULE						
<p>Project Title: Sections of Hagen Ranch Road</p> <p>Project Number: 1548</p> <p>BCC District: Multiple</p> <p>Delivery Method: Annual Striping Contract</p> <p>Category: S16-Striping</p> <p>Status: Construction</p> <p>Designer: N/A</p> <p>Contractor: Southwide</p> <p>Project Manager: Larry Kelly</p>	<p>Scope</p> <p>This project consists of restriping sections of Hagen Ranch Road.</p> <p>Notes</p> <p>The restriping construction scheduled for FY 2017 has been completed. The project is funded at \$50,000 in FY 2017 and FY 2021, and \$100,000 in FY 2024, and \$75,000 in FY 2026 for a total funding of \$275,000.</p>	<table border="1"> <thead> <tr> <th></th> <th>Original</th> <th>Actual</th> </tr> </thead> <tbody> <tr> <td>Atlantic to Flavor Pict Complete</td> <td>7/31/2017</td> <td>7/11/2017</td> </tr> </tbody> </table>		Original	Actual	Atlantic to Flavor Pict Complete	7/31/2017	7/11/2017
	Original	Actual						
Atlantic to Flavor Pict Complete	7/31/2017	7/11/2017						

PARTICIPATION	FUNDING	FINANCIAL SUMMARY												
<p>Consultant</p> <p>SBE N/A MBE N/A</p> <p>WBE N/A Local N/A</p> <p>Contractor</p> <p>SBE 100% MBE 0%</p> <p>WBE 0% Local 100%</p>		<table border="1"> <thead> <tr> <th>Project Budget</th> <th>Committed</th> <th>% Committed</th> <th>Paid To Date</th> </tr> <tr> <th>A</th> <th>B</th> <th>C=B/A</th> <th>D</th> </tr> </thead> <tbody> <tr> <td>\$275,000</td> <td>\$49,596</td> <td>18.03%</td> <td>\$49,596</td> </tr> </tbody> </table>	Project Budget	Committed	% Committed	Paid To Date	A	B	C=B/A	D	\$275,000	\$49,596	18.03%	\$49,596
Project Budget	Committed	% Committed	Paid To Date											
A	B	C=B/A	D											
\$275,000	\$49,596	18.03%	\$49,596											

DESCRIPTION/TEAM	SCOPE/NOTES	SCHEDULE									
<p>Project Title: Sections of Palm Beach Lakes Blvd.</p> <p>Project Number: 1549</p> <p>BCC District: 07</p> <p>Delivery Method: Annual Striping Contract</p> <p>Category: S16-Striping</p> <p>Status: Construction</p> <p>Designer: N/A</p> <p>Contractor: Southwide</p> <p>Project Manager: Larry Kelly</p>	<p>Scope</p> <p>This project consists of restriping sections of Palm Beach Lakes Boulevard.</p> <p>Notes</p> <p>The restriping construction scheduled for FY 2017 has been completed. The project is funded at \$50,000 in FY 2017 and FY 2025 for a total funding of \$100,000.</p>	<table border="1"> <thead> <tr> <th></th> <th>Original</th> <th>Actual</th> </tr> </thead> <tbody> <tr> <td>Sapodilla to N. Dixie Complete</td> <td>8/23/2017</td> <td>8/23/2017</td> </tr> <tr> <td>Okeechobee to Robbins Complete</td> <td>8/24/2017</td> <td>8/24/2017</td> </tr> </tbody> </table>		Original	Actual	Sapodilla to N. Dixie Complete	8/23/2017	8/23/2017	Okeechobee to Robbins Complete	8/24/2017	8/24/2017
	Original	Actual									
Sapodilla to N. Dixie Complete	8/23/2017	8/23/2017									
Okeechobee to Robbins Complete	8/24/2017	8/24/2017									

PARTICIPATION	FUNDING	FINANCIAL SUMMARY												
<p>Consultant</p> <p>SBE N/A MBE N/A</p> <p>WBE N/A Local N/A</p> <p>Contractor</p> <p>SBE 100% MBE 0%</p> <p>WBE 0% Local 100%</p>		<table border="1"> <thead> <tr> <th>Project Budget</th> <th>Committed</th> <th>% Committed</th> <th>Paid To Date</th> </tr> <tr> <th>A</th> <th>B</th> <th>C=B/A</th> <th>D</th> </tr> </thead> <tbody> <tr> <td>\$100,000</td> <td>\$29,252</td> <td>29.25%</td> <td>\$29,252</td> </tr> </tbody> </table>	Project Budget	Committed	% Committed	Paid To Date	A	B	C=B/A	D	\$100,000	\$29,252	29.25%	\$29,252
Project Budget	Committed	% Committed	Paid To Date											
A	B	C=B/A	D											
\$100,000	\$29,252	29.25%	\$29,252											



Monthly Infrastructure Sales Tax Project Report

Small Cap Projects

Data Date: 04/16/2020

Report Date: 05/11/20

DESCRIPTION/TEAM	SCOPE/NOTES	SCHEDULE	
<p>Project Title: Wabasso Dr. over LWDD Lat. 2 Canal (934237)</p> <p>Project Number: 1557</p> <p>BCC District: 07</p> <p>Delivery Method: Design CCNA</p> <p>Category: B08-Bridge Replacements</p> <p>Status: Design</p> <p>Designer: Alan Gerwig & Associates</p> <p>Contractor: TBD (bid)</p> <p>Project Manager: Kristine Frazell-Smith</p>	<p>Scope</p> <p>This project will replace an existing bridge that was built over 50 years ago. The new bridge will improve traffic safety (lane widths, bike lanes, parapets), improve roadway drainage, and enhance pedestrian sidewalk safety.</p> <p>Notes</p> <p>This project is funded for design (\$150k) in FY 2018 and construction (\$550k) in FY 2021.</p>	Original	Actual
		Design Contract Notice to Proceed	7/10/2018 / 7/10/2018
		Design Completion	7/1/2020
		Construction Bid Date	10/1/2020
		Construction Start	3/1/2021
		Construction Complete	8/1/2021

PARTICIPATION	FUNDING	FINANCIAL SUMMARY			
<p>Consultant</p> <p>SBE 100% MBE 0%</p> <p>WBE 0% Local 100%</p> <p>Contractor</p> <p>SBE TBD MBE TBD</p> <p>WBE TBD Local TBD</p>	<p style="text-align: center;">Fund Source (x 100K)</p>	Project Budget	Committed	% Committed	Paid To Date
		A	B	C=B/A	D
		\$700,000	\$135,214	19.32%	\$47,028

DESCRIPTION/TEAM	SCOPE/NOTES	SCHEDULE	
<p>Project Title: Sections of Randolph Siding Rd.</p> <p>Project Number: 1559</p> <p>BCC District: 01</p> <p>Delivery Method: Annual Construction Contract</p> <p>Category: D02-Drainage (Pipe Replacements)</p> <p>Status: Construction</p> <p>Designer: N/A</p> <p>Contractor: Wynn and Sons</p> <p>Project Manager: Mark Kroeger</p>	<p>Scope</p> <p>This project will repair and/or replace existing pipe culverts and drainage structures along Randolph Siding Road. These repairs are needed in order to properly drain and maintain Randolph Siding Road in a safe operating condition.</p> <p>Notes</p> <p>This project is funded at \$300k in FY 2018 and FY 2021 for a total funding of \$600,000.</p>	Original	Actual
		110th to Jupiter Farms Road Complete	6/1/2018 / 5/10/2018
		@Alexander Run	5/1/2019 / 6/7/2019

PARTICIPATION	FUNDING	FINANCIAL SUMMARY			
<p>Consultant</p> <p>SBE N/A MBE N/A</p> <p>WBE N/A Local N/A</p> <p>Contractor</p> <p>SBE 100% MBE 0%</p> <p>WBE 0% Local 100%</p>	<p style="text-align: center;">Fund Source (x 100K)</p>	Project Budget	Committed	% Committed	Paid To Date
		A	B	C=B/A	D
		\$600,000	\$114,350	19.06%	\$92,775



Monthly Infrastructure Sales Tax Project Report

Small Cap Projects

Data Date: 04/16/2020

Report Date: 05/11/20

DESCRIPTION/TEAM	SCOPE/NOTES	SCHEDULE	
<p>Project Title: Hood Road from Briarlake Dr. to W. of Turnpike</p> <p>Project Number: 1561</p> <p>BCC District: 01</p> <p>Delivery Method: Design CCNA</p> <p>Category: P04-Pathways</p> <p>Status: Design</p> <p>Designer: Civil Design</p> <p>Contractor: TBD</p> <p>Project Manager: Sandra Ospina</p>	<p>Scope</p> <p>This project will add a new pathway on Hood Road from Briarlake Dr. to W. of Turnpike.</p> <p>Notes</p> <p>Design of the project is in progress. Project is delayed to avoid conflicts with pending development and associated construction.</p>	Original	Actual
		Design NTP Issued	4/11/2018
		Design Start	5/1/2018
		Design Complete	5/1/2020
		Construction Start	8/1/2020
		Construction Complete	11/1/2020

PARTICIPATION	FUNDING	FINANCIAL SUMMARY			
<p>Consultant</p> <p>SBE 100% MBE 0%</p> <p>WBE 0% Local 100%</p> <p>Contractor</p> <p>SBE TBD MBE TBD</p> <p>WBE TBD Local TBD</p>	<p style="text-align: center;">Fund Source (x 100K)</p>	Project Budget	Committed	% Committed	Paid To Date
		A	B	C=B/A	D
		\$200,000	\$66,583	33.29%	\$41,933

DESCRIPTION/TEAM	SCOPE/NOTES	SCHEDULE	
<p>Project Title: Boynton Beach Blvd. & Seacrest Blvd.</p> <p>Project Number: 1578</p> <p>BCC District: 07</p> <p>Delivery Method: Design CCNA</p> <p>Category: S08-Signals and Signal Systems</p> <p>Status: Design</p> <p>Designer: Wantman Group</p> <p>Contractor: TBD</p> <p>Project Manager: Fattouh Jafar</p>	<p>Scope</p> <p>This project will replace the existing span-wire signal system with a mast arm signal system.</p> <p>Notes</p> <p>Design of the project is in progress. Utility and right-of-way (ROW) issues still unresolved.</p>	Original	Actual
		Design NTP Issued	4/19/2019
		Design Complete	6/20/2020

PARTICIPATION	FUNDING	FINANCIAL SUMMARY			
<p>Consultant</p> <p>SBE 0% MBE 0%</p> <p>WBE 0% Local 100%</p> <p>Contractor</p> <p>SBE TBD MBE TBD</p> <p>WBE TBD Local TBD</p>	<p style="text-align: center;">Fund Source (x 100K)</p>	Project Budget	Committed	% Committed	Paid To Date
		A	B	C=B/A	D
		\$400,000	\$71,574	17.89%	\$14,463



Monthly Infrastructure Sales Tax Project Report

Small Cap Projects

Data Date: 04/16/2020

Report Date: 05/11/20

DESCRIPTION/TEAM	SCOPE/NOTES	SCHEDULE		
Project Title: Blue Heron Blvd. & Riviera FS # 2 Project Number: 1579 BCC District: 07 Delivery Method: Design CCNA Category: S08-Signals and Signal Systems Status: Design Designer: Simmons & White Contractor: TBD Project Manager: Fattoush Jafar	Scope This project will replace the existing span-wire signal system with a mast arm signal system. Notes Design of the project is on HOLD pending resolution of ROW acquisition.	Original	Actual	
		Design NTP Issued	3/28/2018	3/28/2018
		Design Complete	12/1/2020	

PARTICIPATION	FUNDING	FINANCIAL SUMMARY			
Consultant SBE 93.7% MBE 0% WBE 0% Local 100% Contractor SBE TBD MBE TBD WBE TBD Local TBD	<p style="text-align: center;">Fund Source (x 100K)</p>	Project Budget	Committed	% Committed	Paid To Date
		A	B	C=B/A	D
		\$400,000	\$45,640	11.41%	\$18,574

DESCRIPTION/TEAM	SCOPE/NOTES	SCHEDULE		
Project Title: Sections of Lyons Road Project Number: 1597 BCC District: Multiple Delivery Method: Annual Striping Contract Category: S16-Striping Status: Construction Designer: N/A Contractor: Oglesby/Southwide Project Manager: Larry Kelly	Scope This project consists of restriping sections of Lyons Road. Notes The restriping construction scheduled for FY2018 has been completed. The project is funded at \$200,000 in FY 2018, FY 2022, and FY 2025 for a total funding of \$600,000.	Original	Actual	
		Connector Road to Lantana Road	5/14/2018	5/7/2018
		Wendy Lane to Palm Beach Pantation Bl	3/20/2019	3/20/2019

PARTICIPATION	FUNDING	FINANCIAL SUMMARY			
Consultant SBE N/A MBE N/A WBE N/A Local N/A Contractor SBE 0% MBE 0% WBE 0% Local 0%	<p style="text-align: center;">Fund Source (x 100K)</p>	Project Budget	Committed	% Committed	Paid To Date
		A	B	C=B/A	D
		\$600,000	\$133,670	22.28%	\$133,670



Monthly Infrastructure Sales Tax Project Report

Small Cap Projects

Data Date: 04/16/2020

Report Date: 05/11/20

DESCRIPTION/TEAM	SCOPE/NOTES	SCHEDULE												
<p>Project Title: Sections of Haverhill Road</p> <p>Project Number: 1598</p> <p>BCC District: Multiple</p> <p>Delivery Method: Annual Striping Contract</p> <p>Category: S16-Striping</p> <p>Status: Construction</p> <p>Designer: N/A</p> <p>Contractor: Oglesby/Southwide</p> <p>Project Manager: Larry Kelly</p>	<p>Scope</p> <p>This project consists of restriping sections of Haverhill Road.</p> <p>Notes</p> <p>The project is funded at \$100,000 in FY 2018, FY 2021, FY 2023, and FY 2026 for a total funding of \$400,000.</p>	<table border="1"> <thead> <tr> <th></th> <th>Original</th> <th>Actual</th> </tr> </thead> <tbody> <tr> <td>Lantana Road to Hypoluxo Road</td> <td>5/14/2018</td> <td>5/2/2018</td> </tr> <tr> <td>10th Ave. N to Purdy Lane</td> <td>9/1/2019</td> <td>9/1/2019</td> </tr> <tr> <td>Caribbean to Beeline</td> <td>6/1/2020</td> <td></td> </tr> </tbody> </table>		Original	Actual	Lantana Road to Hypoluxo Road	5/14/2018	5/2/2018	10th Ave. N to Purdy Lane	9/1/2019	9/1/2019	Caribbean to Beeline	6/1/2020	
	Original	Actual												
Lantana Road to Hypoluxo Road	5/14/2018	5/2/2018												
10th Ave. N to Purdy Lane	9/1/2019	9/1/2019												
Caribbean to Beeline	6/1/2020													

PARTICIPATION	FUNDING	FINANCIAL SUMMARY												
<p>Consultant</p> <p>SBE N/A MBE N/A</p> <p>WBE N/A Local N/A</p> <p>Contractor</p> <p>SBE 45% MBE 0%</p> <p>WBE 0% Local 45%</p>		<table border="1"> <thead> <tr> <th>Project Budget</th> <th>Committed</th> <th>% Committed</th> <th>Paid To Date</th> </tr> <tr> <th>A</th> <th>B</th> <th>C=B/A</th> <th>D</th> </tr> </thead> <tbody> <tr> <td>\$400,000</td> <td>\$45,424</td> <td>11.36%</td> <td>\$45,424</td> </tr> </tbody> </table>	Project Budget	Committed	% Committed	Paid To Date	A	B	C=B/A	D	\$400,000	\$45,424	11.36%	\$45,424
Project Budget	Committed	% Committed	Paid To Date											
A	B	C=B/A	D											
\$400,000	\$45,424	11.36%	\$45,424											

DESCRIPTION/TEAM	SCOPE/NOTES	SCHEDULE						
<p>Project Title: Sections of Belvedere Road</p> <p>Project Number: 1599</p> <p>BCC District: Multiple</p> <p>Delivery Method: Annual Striping Contract</p> <p>Category: S16-Striping</p> <p>Status: Construction</p> <p>Designer: N/A</p> <p>Contractor: Oglesby/Southwide</p> <p>Project Manager: Larry Kelly</p>	<p>Scope</p> <p>This project consists of restriping sections of Belvedere Road.</p> <p>Notes</p> <p>The project is funded at \$100,000 in FY 2018, and \$50,000 in FY 2022 and FY 2025, and \$125,000 in FY 2024 for a total funding of \$325,000.</p>	<table border="1"> <thead> <tr> <th></th> <th>Original</th> <th>Actual</th> </tr> </thead> <tbody> <tr> <td>Haverhill Road to Drexel Road</td> <td>7/14/2018</td> <td>8/20/2018</td> </tr> </tbody> </table>		Original	Actual	Haverhill Road to Drexel Road	7/14/2018	8/20/2018
	Original	Actual						
Haverhill Road to Drexel Road	7/14/2018	8/20/2018						

PARTICIPATION	FUNDING	FINANCIAL SUMMARY												
<p>Consultant</p> <p>SBE N/A MBE N/A</p> <p>WBE N/A Local N/A</p> <p>Contractor</p> <p>SBE 100% MBE 0%</p> <p>WBE 0% Local 100%</p>		<table border="1"> <thead> <tr> <th>Project Budget</th> <th>Committed</th> <th>% Committed</th> <th>Paid To Date</th> </tr> <tr> <th>A</th> <th>B</th> <th>C=B/A</th> <th>D</th> </tr> </thead> <tbody> <tr> <td>\$325,000</td> <td>\$23,128</td> <td>7.12%</td> <td>\$23,128</td> </tr> </tbody> </table>	Project Budget	Committed	% Committed	Paid To Date	A	B	C=B/A	D	\$325,000	\$23,128	7.12%	\$23,128
Project Budget	Committed	% Committed	Paid To Date											
A	B	C=B/A	D											
\$325,000	\$23,128	7.12%	\$23,128											



Monthly Infrastructure Sales Tax Project Report

Small Cap Projects

Data Date: 04/16/2020

Report Date: 05/11/20

DESCRIPTION/TEAM	SCOPE/NOTES	SCHEDULE									
<p>Project Title: Sections of Yamato Road</p> <p>Project Number: 1603</p> <p>BCC District: Multiple</p> <p>Delivery Method: Annual Striping Contract</p> <p>Category: S16-Striping</p> <p>Status: Construction</p> <p>Designer: N/A</p> <p>Contractor: Oglesby/Southwide</p> <p>Project Manager: Larry Kelly</p>	<p>Scope</p> <p>This project consists of restriping sections of Yamato Road.</p> <p>Notes</p> <p>The restriping construction scheduled for FY 2018 has been completed. The project is funded at \$75,000 in FY 2018 and \$50,000 in FY 2020 and FY 2023 for a total funding of \$175,000.</p>	<table border="1"> <thead> <tr> <th></th> <th style="text-align: center;">Original</th> <th style="text-align: center;">Actual</th> </tr> </thead> <tbody> <tr> <td>Lyons Road to SR7</td> <td style="text-align: center;">8/1/2018</td> <td style="text-align: center;">11/1/2018</td> </tr> <tr> <td>Gatehouse Drive to Jog Road</td> <td style="text-align: center;">8/1/2018</td> <td style="text-align: center;">11/1/2018</td> </tr> </tbody> </table>		Original	Actual	Lyons Road to SR7	8/1/2018	11/1/2018	Gatehouse Drive to Jog Road	8/1/2018	11/1/2018
	Original	Actual									
Lyons Road to SR7	8/1/2018	11/1/2018									
Gatehouse Drive to Jog Road	8/1/2018	11/1/2018									

PARTICIPATION	FUNDING	FINANCIAL SUMMARY												
<p>Consultant</p> <p>SBE N/A MBE N/A</p> <p>WBE N/A Local N/A</p> <p>Contractor</p> <p>SBE 100% MBE 0%</p> <p>WBE 0% Local 100%</p>	<p style="text-align: center;">Fund Source (x 100K)</p>	<table border="1"> <thead> <tr> <th style="text-align: center;">Project Budget</th> <th style="text-align: center;">Committed</th> <th style="text-align: center;">% Committed</th> <th style="text-align: center;">Paid To Date</th> </tr> <tr> <th style="text-align: center;">A</th> <th style="text-align: center;">B</th> <th style="text-align: center;">C=B/A</th> <th style="text-align: center;">D</th> </tr> </thead> <tbody> <tr> <td style="text-align: center;">\$175,000</td> <td style="text-align: center;">\$73,517</td> <td style="text-align: center;">42.01%</td> <td style="text-align: center;">\$73,517</td> </tr> </tbody> </table>	Project Budget	Committed	% Committed	Paid To Date	A	B	C=B/A	D	\$175,000	\$73,517	42.01%	\$73,517
Project Budget	Committed	% Committed	Paid To Date											
A	B	C=B/A	D											
\$175,000	\$73,517	42.01%	\$73,517											

DESCRIPTION/TEAM	SCOPE/NOTES	SCHEDULE						
<p>Project Title: Sections of Indiantown Road Striping</p> <p>Project Number: 1604</p> <p>BCC District: 01</p> <p>Delivery Method: Annual Striping Contract</p> <p>Category: S16-Striping</p> <p>Status: Construction</p> <p>Designer: N/A</p> <p>Contractor: Oglesby/Southwide</p> <p>Project Manager: Larry Kelly</p>	<p>Scope</p> <p>This project consists of restriping sections of Indiantown Road.</p> <p>Notes</p> <p>The project is funded at \$75,000 in FY 2018, and \$100,000 in FY 2021, FY 2023, and FY 2025 for a total funding of \$375,000.</p>	<table border="1"> <thead> <tr> <th></th> <th style="text-align: center;">Original</th> <th style="text-align: center;">Actual</th> </tr> </thead> <tbody> <tr> <td>Beeline Highway to east for 1/2 mile</td> <td style="text-align: center;">7/14/2018</td> <td style="text-align: center;">1/9/2019</td> </tr> </tbody> </table>		Original	Actual	Beeline Highway to east for 1/2 mile	7/14/2018	1/9/2019
	Original	Actual						
Beeline Highway to east for 1/2 mile	7/14/2018	1/9/2019						

PARTICIPATION	FUNDING	FINANCIAL SUMMARY												
<p>Consultant</p> <p>SBE N/A MBE N/A</p> <p>WBE N/A Local N/A</p> <p>Contractor</p> <p>SBE 100% MBE 0%</p> <p>WBE 0% Local 100%</p>	<p style="text-align: center;">Fund Source (x 100K)</p>	<table border="1"> <thead> <tr> <th style="text-align: center;">Project Budget</th> <th style="text-align: center;">Committed</th> <th style="text-align: center;">% Committed</th> <th style="text-align: center;">Paid To Date</th> </tr> <tr> <th style="text-align: center;">A</th> <th style="text-align: center;">B</th> <th style="text-align: center;">C=B/A</th> <th style="text-align: center;">D</th> </tr> </thead> <tbody> <tr> <td style="text-align: center;">\$375,000</td> <td style="text-align: center;">\$5,535</td> <td style="text-align: center;">1.48%</td> <td style="text-align: center;">\$5,535</td> </tr> </tbody> </table>	Project Budget	Committed	% Committed	Paid To Date	A	B	C=B/A	D	\$375,000	\$5,535	1.48%	\$5,535
Project Budget	Committed	% Committed	Paid To Date											
A	B	C=B/A	D											
\$375,000	\$5,535	1.48%	\$5,535											



Monthly Infrastructure Sales Tax Project Report

Small Cap Projects

Data Date: 04/16/2020

Report Date: 05/11/20

DESCRIPTION/TEAM	SCOPE/NOTES	SCHEDULE		
<p>Project Title: Sections of Palmetto Park Road</p> <p>Project Number: 1605</p> <p>BCC District: 04</p> <p>Delivery Method: Annual Striping Contract</p> <p>Category: S16-Striping</p> <p>Status: Construction</p> <p>Designer: N/A</p> <p>Contractor: Oglesby/Southwide</p> <p>Project Manager: Larry Kelly</p>	<p>Scope</p> <p>This project consists of restriping sections of Palmetto Park Road.</p> <p>Notes</p> <p>The restriping construction scheduled for FY2018 has been completed. The project is funded at \$75,000 in FY 2018, and \$100,000 in FY 2021 and FY 2023 for a total funding of \$275,000.</p>	Original	Actual	
		CSX RR to Crawford Blvd.	5/14/2018	5/7/2018

PARTICIPATION	FUNDING	FINANCIAL SUMMARY			
<p>Consultant</p> <p>SBE N/A MBE N/A</p> <p>WBE N/A Local N/A</p> <p>Contractor</p> <p>SBE 0% MBE 0%</p> <p>WBE 0% Local 0%</p>		Project Budget	Committed	% Committed	Paid To Date
		A	B	C=B/A	D
		\$275,000	\$52,683	19.16%	\$52,683

DESCRIPTION/TEAM	SCOPE/NOTES	SCHEDULE		
<p>Project Title: Sections of Hypoluxo Road</p> <p>Project Number: 1606</p> <p>BCC District: Multiple</p> <p>Delivery Method: Annual Striping Contract</p> <p>Category: S16-Striping</p> <p>Status: Construction</p> <p>Designer: N/A</p> <p>Contractor: Oglesby/Southwide</p> <p>Project Manager: Larry Kelly</p>	<p>Scope</p> <p>This project consists of restriping sections of Hypoluxo Road.</p> <p>Notes</p> <p>The restriping construction scheduled for FY 2018 has been completed. The project is funded at \$75,000 in FY 2018, \$100,000 in FY 2021 and FY 2024 for a total funding of \$275,000.</p>	Original	Actual	
		Hagen Ranch Road to Jog Road	8/1/2018	10/19/2018
		Jog Road to Military Trail	9/1/2018	10/19/2018

PARTICIPATION	FUNDING	FINANCIAL SUMMARY			
<p>Consultant</p> <p>SBE N/A MBE N/A</p> <p>WBE N/A Local N/A</p> <p>Contractor</p> <p>SBE 100% MBE 0%</p> <p>WBE 0% Local 100%</p>		Project Budget	Committed	% Committed	Paid To Date
		A	B	C=B/A	D
		\$275,000	\$66,843	24.31%	\$66,843



Monthly Infrastructure Sales Tax Project Report

Small Cap Projects

Data Date: 04/16/2020

Report Date: 05/11/20

DESCRIPTION/TEAM	SCOPE/NOTES	SCHEDULE	
<p>Project Title: Sections of Australian Avenue</p> <p>Project Number: 1607</p> <p>BCC District: 07</p> <p>Delivery Method: Annual Striping Contract</p> <p>Category: S16-Striping</p> <p>Status: Construction</p> <p>Designer: N/A</p> <p>Contractor: Oglesby/Southwide</p> <p>Project Manager: Larry Kelly</p>	<p>Scope</p> <p>This project consists of restriping sections of Australian Avenue.</p> <p>Notes</p> <p>The project is funded at \$75,000 in FY 2018, \$125,000 in FY 2022 and FY 2026 for a total funding of \$325,000.</p>	Original	Actual
		Banyan Blvd. to Palm Beach Lake Blvd.	7/1/2018 1/29/2019

PARTICIPATION	FUNDING	FINANCIAL SUMMARY			
<p>Consultant</p> <p>SBE N/A MBE N/A</p> <p>WBE N/A Local N/A</p> <p>Contractor</p> <p>SBE 100% MBE 0%</p> <p>WBE 0% Local 100%</p>	<p style="text-align: center;">Fund Source (x 100K)</p>	Project Budget	Committed	% Committed	Paid To Date
		A	B	C=B/A	D
		\$325,000	\$13,540	4.17%	\$13,540

DESCRIPTION/TEAM	SCOPE/NOTES	SCHEDULE	
<p>Project Title: Sections of Okeechobee Blvd.</p> <p>Project Number: 1609</p> <p>BCC District: Multiple</p> <p>Delivery Method: Annual Striping Contract</p> <p>Category: S16-Striping</p> <p>Status: Construction</p> <p>Designer: N/A</p> <p>Contractor: Oglesby/Southwide</p> <p>Project Manager: Larry Kelly</p>	<p>Scope</p> <p>This project consists of restriping sections of Okeechobee Boulevard.</p> <p>Notes</p> <p>The restriping construction scheduled for FY 2018 has been completed. The project is funded at \$50,000 in FY 2018 and FY 2023, and \$100,000 in FY 2026 for a total funding of \$200,000.</p>	Original	Actual
		Royal Palm Beach Blvd to SR 7	5/14/2018 7/14/2018

PARTICIPATION	FUNDING	FINANCIAL SUMMARY			
<p>Consultant</p> <p>SBE N/A MBE N/A</p> <p>WBE N/A Local N/A</p> <p>Contractor</p> <p>SBE 100% MBE 0%</p> <p>WBE 0% Local 100%</p>	<p style="text-align: center;">Fund Source (x 100K)</p>	Project Budget	Committed	% Committed	Paid To Date
		A	B	C=B/A	D
		\$200,000	\$44,721	22.36%	\$44,721



Monthly Infrastructure Sales Tax Project Report

Small Cap Projects

Data Date: 04/16/2020

Report Date: 05/11/20

DESCRIPTION/TEAM	SCOPE/NOTES	SCHEDULE		
Project Title: Sections of 10th Avenue North Project Number: 1610 BCC District: Multiple Delivery Method: Annual Striping Contract Category: S16-Striping Status: Construction Designer: N/A Contractor: Oglesby/Southwide Project Manager: Larry Kelly	Scope This project consists of restriping sections of 10th Avenue North. Notes The restriping construction scheduled for FY2018 has been completed. The project is funded at \$50,000 in FY 2018 and FY 2023, and \$100,000 in FY 2026 for a total funding of \$200,000.	Original	Actual	
		Pinehurst Dr. to Jog Rd.	5/15/2018	8/9/2018

PARTICIPATION	FUNDING	FINANCIAL SUMMARY			
Consultant SBE N/A MBE N/A WBE NA Local N/A Contractor SBE 100% MBE 0% WBE 0% Local 100%	<p style="text-align: center;">Fund Source (x 100K)</p>	Project Budget	Committed	% Committed	Paid To Date
		A	B	C=B/A	D
		\$200,000	\$17,538	8.77%	\$17,538

DESCRIPTION/TEAM	SCOPE/NOTES	SCHEDULE		
Project Title: Sections of 45th Street Project Number: 1611 BCC District: 07 Delivery Method: Annual Striping Contract Category: S16-Striping Status: Construction Designer: N/A Contractor: Oglesby/Southwide Project Manager: Larry Kelly	Scope This project consists of restriping sections of 45th Street. Notes The restriping construction scheduled for FY2018 has been completed. The project is funded at \$50,000 in FY 2018 and FY 2023, and \$75,000 in FY 2026 for a total funding of \$175,000.	Original	Actual	
		Military Trail to I-95	7/1/2018	1/16/2019
		Greenwood Ave. to Broadway Blvd.	3/11/2019	3/18/2019

PARTICIPATION	FUNDING	FINANCIAL SUMMARY			
Consultant SBE N/A MBE N/A WBE N/A Local N/A Contractor SBE 100% MBE 0% WBE 0% Local 100%	<p style="text-align: center;">Fund Source (x 100K)</p>	Project Budget	Committed	% Committed	Paid To Date
		A	B	C=B/A	D
		\$175,000	\$33,067	18.90%	\$33,067



Monthly Infrastructure Sales Tax Project Report

Small Cap Projects

Data Date: 04/16/2020

Report Date: 05/11/20

DESCRIPTION/TEAM	SCOPE/NOTES	SCHEDULE	
<p>Project Title: Florida Mango Rd. over LWDD Lat. 8 Canal (PB934338)</p> <p>Project Number: 1613</p> <p>BCC District: 03</p> <p>Delivery Method: Design CCNA</p> <p>Category: B08-Bridge Replacements</p> <p>Status: Construction</p> <p>Designer: Alan Gerwig & Assoc.</p> <p>Contractor: TBD (bid)</p> <p>Project Manager: Kathleen Farrell</p>	<p>Scope</p> <p>This project will replace an existing bridge that was built over 50 years ago. The new bridge will improve traffic safety (lane widths, bike lanes, parapets), update the guardrail system, improve roadway drainage, improve the slope protection, and enhance pedestrian sidewalk safety.</p> <p>Notes</p> <p>The project is funded with 5-Year Road Program (RP) funding and IST funding. The project is under design (using RP funds). The const. of the project (incl. assoc. rdwy. improvements) is currently est. at \$1.9m. The IST partially funds the const. at \$700,000 in FY19. The project is currently scheduled to begin constr. in FY21.</p>	Original	Actual
		Design Contract Notice to Proceed	9/30/2015 / 9/30/2015
		Design Completion	7/1/2020
		Construction Bid Date	12/1/2020
		Construction Start	5/1/2021
		Construction Complete	12/1/2022

PARTICIPATION	FUNDING	FINANCIAL SUMMARY			
<p>Consultant</p> <p>SBE 100% MBE 0%</p> <p>WBE 0% Local 100%</p> <p>Contractor</p> <p>SBE TBD MBE TBD</p> <p>WBE TBD Local TBD</p>		Project Budget	Committed	% Committed	Paid To Date
		A	B	C=B/A	D
		\$700,000	\$0	0.00%	\$0

DESCRIPTION/TEAM	SCOPE/NOTES	SCHEDULE	
<p>Project Title: Congress Ave. over PBC Lat. 2 Canal (934251)</p> <p>Project Number: 1614</p> <p>BCC District: 02</p> <p>Delivery Method: Design CCNA</p> <p>Category: B08-Bridge Replacements</p> <p>Status: Design</p> <p>Designer: Stantec</p> <p>Contractor: TBD (bid)</p> <p>Project Manager: Kathleen Farrell</p>	<p>Scope</p> <p>This project will replace an existing bridge that was built over 50 years ago. The new bridge will improve traffic safety (lane widths, geometry, and parapets), improve roadway drainage, and enhance pedestrian sidewalk safety.</p> <p>Notes</p> <p>The project is funded for design (\$200k) in FY2019 and construction (\$600K) in FY2022.</p>	Original	Actual
		Design Construction Notice to Proceed	2/1/2020 / 1/15/2020
		Design Completion	6/1/2022
		Construction Bid Date	10/1/2022
		Construction Start	3/1/2023
		Construction Complete	10/1/2024

PARTICIPATION	FUNDING	FINANCIAL SUMMARY			
<p>Consultant</p> <p>SBE 31% MBE N/A</p> <p>WBE N/A Local 100%</p> <p>Contractor</p> <p>SBE TBD MBE TBD</p> <p>WBE TBD Local TBD</p>		Project Budget	Committed	% Committed	Paid To Date
		A	B	C=B/A	D
		\$800,000	\$15,996	2.00%	\$5,924



Monthly Infrastructure Sales Tax Project Report

Small Cap Projects

Data Date: 04/16/2020

Report Date: 05/11/20

DESCRIPTION/TEAM				SCOPE/NOTES				SCHEDULE																					
Project Title: Sam Senter Rd. over Ocean Canal (SFWMD Lat. 13 Canal) Project Number: 1615 BCC District: 06 Delivery Method: Design CCNA Category: B08-Bridge Replacements Status: Design Designer: TBD Contractor: TBD (bid) Project Manager: David Young				Scope This project will replace an existing bridge that was built over 50 years ago. The new bridge will improve traffic safety (lane widths, geometry, and parapets), improve roadway drainage and turning movements and enhance pedestrian sidewalk safety. Notes The project is funded with 5-Year Road Program (RP) funding and IST funding. The project is in the design selection process. The const. of project (incl. assoc. rdway improvements) is currently est. at \$2.5m. The IST partially funds design (\$150k) in FY19 and const. (\$450k) in FY22.				<table border="1"> <thead> <tr> <th></th> <th>Original</th> <th>Actual</th> </tr> </thead> <tbody> <tr> <td>Design Construction Notice to Proceed</td> <td>12/1/2020</td> <td></td> </tr> <tr> <td>Design Completion</td> <td>6/1/2023</td> <td></td> </tr> <tr> <td>Construction Bid Date</td> <td>10/1/2023</td> <td></td> </tr> <tr> <td>Construction Start</td> <td>3/1/2024</td> <td></td> </tr> <tr> <td>Construction Complete</td> <td>10/1/2025</td> <td></td> </tr> </tbody> </table>					Original	Actual	Design Construction Notice to Proceed	12/1/2020		Design Completion	6/1/2023		Construction Bid Date	10/1/2023		Construction Start	3/1/2024		Construction Complete	10/1/2025	
	Original	Actual																											
Design Construction Notice to Proceed	12/1/2020																												
Design Completion	6/1/2023																												
Construction Bid Date	10/1/2023																												
Construction Start	3/1/2024																												
Construction Complete	10/1/2025																												
PARTICIPATION				FUNDING				FINANCIAL SUMMARY																					
Consultant SBE TBD MBE TBD WBE TBD Local TBD				<p>Fund Source (x 100K)</p>				<table border="1"> <thead> <tr> <th>Project Budget</th> <th>Committed</th> <th>% Committed</th> <th>Paid To Date</th> </tr> <tr> <th>A</th> <th>B</th> <th>C=B/A</th> <th>D</th> </tr> </thead> <tbody> <tr> <td>\$600,000</td> <td>\$10,306</td> <td>1.72%</td> <td>\$10,306</td> </tr> </tbody> </table>				Project Budget	Committed	% Committed	Paid To Date	A	B	C=B/A	D	\$600,000	\$10,306	1.72%	\$10,306						
Project Budget	Committed	% Committed	Paid To Date																										
A	B	C=B/A	D																										
\$600,000	\$10,306	1.72%	\$10,306																										
Contractor SBE TBD MBE TBD WBE TBD Local TBD																													

DESCRIPTION/TEAM				SCOPE/NOTES				SCHEDULE																					
Project Title: Congress Ave. over LWDD Lat. 24 Canal (PB934479) Project Number: 1616 BCC District: 03 Delivery Method: Design CCNA Category: B08-Bridge Replacements Status: Design Designer: Stantec Contractor: TBD (bid) Project Manager: David Young				Scope This project will replace an existing bridge that was built over 50 years ago. The new bridge will improve traffic safety (lane widths, bike lanes, parapets), update the guardrail system, improve roadway drainage, restore the slope protection, and enhance pedestrian sidewalk safety. Notes The project is funded for design (\$150K) in FY2019 and construction (\$450K) in FY2022.				<table border="1"> <thead> <tr> <th></th> <th>Original</th> <th>Actual</th> </tr> </thead> <tbody> <tr> <td>Design Construction Notice to Proceed</td> <td>12/17/2019</td> <td>1/15/2020</td> </tr> <tr> <td>Design Completion</td> <td>3/1/2022</td> <td></td> </tr> <tr> <td>Construction Bid Date</td> <td>6/1/2022</td> <td></td> </tr> <tr> <td>Construction Start</td> <td>11/1/2022</td> <td></td> </tr> <tr> <td>Construction Complete</td> <td>6/1/2024</td> <td></td> </tr> </tbody> </table>					Original	Actual	Design Construction Notice to Proceed	12/17/2019	1/15/2020	Design Completion	3/1/2022		Construction Bid Date	6/1/2022		Construction Start	11/1/2022		Construction Complete	6/1/2024	
	Original	Actual																											
Design Construction Notice to Proceed	12/17/2019	1/15/2020																											
Design Completion	3/1/2022																												
Construction Bid Date	6/1/2022																												
Construction Start	11/1/2022																												
Construction Complete	6/1/2024																												
PARTICIPATION				FUNDING				FINANCIAL SUMMARY																					
Consultant SBE 30% MBE N/A WBE N/A Local 100%				<p>Fund Source (x 100K)</p>				<table border="1"> <thead> <tr> <th>Project Budget</th> <th>Committed</th> <th>% Committed</th> <th>Paid To Date</th> </tr> <tr> <th>A</th> <th>B</th> <th>C=B/A</th> <th>D</th> </tr> </thead> <tbody> <tr> <td>\$600,000</td> <td>\$127,790</td> <td>21.30%</td> <td>\$10,722</td> </tr> </tbody> </table>				Project Budget	Committed	% Committed	Paid To Date	A	B	C=B/A	D	\$600,000	\$127,790	21.30%	\$10,722						
Project Budget	Committed	% Committed	Paid To Date																										
A	B	C=B/A	D																										
\$600,000	\$127,790	21.30%	\$10,722																										
Contractor SBE TBD MBE TBD WBE TBD Local TBD																													



Monthly Infrastructure Sales Tax Project Report

Small Cap Projects

Data Date: 04/16/2020

Report Date: 05/11/20

DESCRIPTION/TEAM	SCOPE/NOTES	SCHEDULE															
<p>Project Title: A1A from US1 to Donald Ross</p> <p>Project Number: 1617</p> <p>BCC District: 01</p> <p>Delivery Method: Design CCNA</p> <p>Category: D04-Drainage Improvements</p> <p>Status: Design</p> <p>Designer: Baxter Woodman</p> <p>Contractor: TBD</p> <p>Project Manager: David Young</p>	<p>Scope</p> <p>The project involves addressing drainage issues within a couple of areas along A1A (US 1 to Donald Ross) to alleviate chronic or extended flooding. Drainage improvements may include upsizing existing pipes, adding a new system and/or outfall, and adding exfiltration trench.</p> <p>Notes</p> <p>The project is funded for design (\$100k) in FY19 and construction (\$400k) in FY21.</p>	<table border="1"> <thead> <tr> <th></th> <th>Original</th> <th>Actual</th> </tr> </thead> <tbody> <tr> <td>Design Contract Notice to Proceed</td> <td>4/28/2020</td> <td></td> </tr> <tr> <td>Design Completion</td> <td>2/1/2021</td> <td></td> </tr> <tr> <td>Construction Start</td> <td>5/1/2021</td> <td></td> </tr> <tr> <td>Construction Complete</td> <td>11/1/2021</td> <td></td> </tr> </tbody> </table>		Original	Actual	Design Contract Notice to Proceed	4/28/2020		Design Completion	2/1/2021		Construction Start	5/1/2021		Construction Complete	11/1/2021	
	Original	Actual															
Design Contract Notice to Proceed	4/28/2020																
Design Completion	2/1/2021																
Construction Start	5/1/2021																
Construction Complete	11/1/2021																

PARTICIPATION	FUNDING	FINANCIAL SUMMARY												
<p>Consultant</p> <p>SBE 27.8% MBE 0%</p> <p>WBE 0% Local 100%</p> <p>Contractor</p> <p>SBE TBD MBE TBD</p> <p>WBE TBD Local TBD</p>		<table border="1"> <thead> <tr> <th>Project Budget</th> <th>Committed</th> <th>% Committed</th> <th>Paid To Date</th> </tr> <tr> <th>A</th> <th>B</th> <th>C=B/A</th> <th>D</th> </tr> </thead> <tbody> <tr> <td>\$500,000</td> <td>\$1,676</td> <td>0.34%</td> <td>\$1,676</td> </tr> </tbody> </table>	Project Budget	Committed	% Committed	Paid To Date	A	B	C=B/A	D	\$500,000	\$1,676	0.34%	\$1,676
Project Budget	Committed	% Committed	Paid To Date											
A	B	C=B/A	D											
\$500,000	\$1,676	0.34%	\$1,676											

DESCRIPTION/TEAM	SCOPE/NOTES	SCHEDULE															
<p>Project Title: Jog Rd. from Summit Blvd to Gun Club Rd.</p> <p>Project Number: 1622</p> <p>BCC District: 02</p> <p>Delivery Method: Annual Construction Contract</p> <p>Category: R04-Resurfacing</p> <p>Status: Construction</p> <p>Designer: N/A</p> <p>Contractor: Ranger</p> <p>Project Manager: Mark Kroeger</p>	<p>Scope</p> <p>Resurfacing 0.8 miles (4.8 lane miles) of Jog Road from Summit Boulevard to Gun Club Road.</p> <p>Notes</p> <p>Work is complete. A Type 1 transfer to sweep the remaining balance of the project to reserves is forthcoming. Due to additional costs, the project's budget has increased from \$400k to \$480k (BT 2019-0895).</p>	<table border="1"> <thead> <tr> <th></th> <th>Original</th> <th>Actual</th> </tr> </thead> <tbody> <tr> <td>Milling and Pavement Complete</td> <td>4/1/2019</td> <td>4/24/2019</td> </tr> <tr> <td>ADA (Curb/Cut Ramps) Complete</td> <td>6/1/2019</td> <td>10/18/2019</td> </tr> <tr> <td>Traffic Striping Complete</td> <td>8/1/2019</td> <td>5/16/2019</td> </tr> <tr> <td>Traffic Loops Complete</td> <td>10/1/2019</td> <td>3/16/2020</td> </tr> </tbody> </table>		Original	Actual	Milling and Pavement Complete	4/1/2019	4/24/2019	ADA (Curb/Cut Ramps) Complete	6/1/2019	10/18/2019	Traffic Striping Complete	8/1/2019	5/16/2019	Traffic Loops Complete	10/1/2019	3/16/2020
	Original	Actual															
Milling and Pavement Complete	4/1/2019	4/24/2019															
ADA (Curb/Cut Ramps) Complete	6/1/2019	10/18/2019															
Traffic Striping Complete	8/1/2019	5/16/2019															
Traffic Loops Complete	10/1/2019	3/16/2020															

PARTICIPATION	FUNDING	FINANCIAL SUMMARY												
<p>Consultant</p> <p>SBE N/A MBE N/A</p> <p>WBE N/A Local N/A</p> <p>Contractor</p> <p>SBE 30% MBE 0%</p> <p>WBE 0% Local 100%</p>		<table border="1"> <thead> <tr> <th>Project Budget</th> <th>Committed</th> <th>% Committed</th> <th>Paid To Date</th> </tr> <tr> <th>A</th> <th>B</th> <th>C=B/A</th> <th>D</th> </tr> </thead> <tbody> <tr> <td>\$480,000</td> <td>\$426,805</td> <td>88.92%</td> <td>\$409,867</td> </tr> </tbody> </table>	Project Budget	Committed	% Committed	Paid To Date	A	B	C=B/A	D	\$480,000	\$426,805	88.92%	\$409,867
Project Budget	Committed	% Committed	Paid To Date											
A	B	C=B/A	D											
\$480,000	\$426,805	88.92%	\$409,867											



Monthly Infrastructure Sales Tax Project Report

Small Cap Projects

Data Date: 04/16/2020

Report Date: 05/11/20

DESCRIPTION/TEAM	SCOPE/NOTES	SCHEDULE															
<p>Project Title: Woolbright Rd. from Lawrence Rd. to Congress Ave.</p> <p>Project Number: 1624</p> <p>BCC District: 04</p> <p>Delivery Method: Annual Construction Contract</p> <p>Category: R04-Resurfacing</p> <p>Status: Construction</p> <p>Designer: N/A</p> <p>Contractor: Ranger</p> <p>Project Manager: Mark Kroeger</p>	<p>Scope</p> <p>Resurfacing 1 mile (4 lane miles) of Woolbright Road from Lawrence Road to Congress Avenue.</p> <p>Notes</p> <p>The project is funded with IST funding (\$200,000 in FY19) and with Capital Outlay funding. Work is complete. A type 1 transfer to sweep the remaining balance of the project to reserves is forthcoming.</p>	<table border="1"> <thead> <tr> <th></th> <th>Original</th> <th>Actual</th> </tr> </thead> <tbody> <tr> <td>Milling and Pavement Complete</td> <td>6/1/2019</td> <td>5/7/2019</td> </tr> <tr> <td>ADA (Curb/Cut Ramps) Complete</td> <td>8/1/2019</td> <td>10/24/2019</td> </tr> <tr> <td>Traffic Striping Complete</td> <td>10/1/2019</td> <td>7/15/2019</td> </tr> <tr> <td>Traffic Loops Complete</td> <td>12/1/2019</td> <td>1/15/2020</td> </tr> </tbody> </table>		Original	Actual	Milling and Pavement Complete	6/1/2019	5/7/2019	ADA (Curb/Cut Ramps) Complete	8/1/2019	10/24/2019	Traffic Striping Complete	10/1/2019	7/15/2019	Traffic Loops Complete	12/1/2019	1/15/2020
	Original	Actual															
Milling and Pavement Complete	6/1/2019	5/7/2019															
ADA (Curb/Cut Ramps) Complete	8/1/2019	10/24/2019															
Traffic Striping Complete	10/1/2019	7/15/2019															
Traffic Loops Complete	12/1/2019	1/15/2020															

PARTICIPATION	FUNDING	FINANCIAL SUMMARY												
<p>Consultant</p> <p>SBE N/A MBE N/A</p> <p>WBE N/A Local N/A</p> <p>Contractor</p> <p>SBE 27.2% MBE 0%</p> <p>WBE 0% Local 100%</p>		<table border="1"> <thead> <tr> <th>Project Budget</th> <th>Committed</th> <th>% Committed</th> <th>Paid To Date</th> </tr> <tr> <th>A</th> <th>B</th> <th>C=B/A</th> <th>D</th> </tr> </thead> <tbody> <tr> <td>\$200,000</td> <td>\$199,335</td> <td>99.67%</td> <td>\$199,335</td> </tr> </tbody> </table>	Project Budget	Committed	% Committed	Paid To Date	A	B	C=B/A	D	\$200,000	\$199,335	99.67%	\$199,335
Project Budget	Committed	% Committed	Paid To Date											
A	B	C=B/A	D											
\$200,000	\$199,335	99.67%	\$199,335											

DESCRIPTION/TEAM	SCOPE/NOTES	SCHEDULE																					
<p>Project Title: FY 2019 Street Lighting LED Replacements - Countywide</p> <p>Project Number: 1627</p> <p>BCC District: Multiple</p> <p>Delivery Method: Florida Power and Light</p> <p>Category: S14-Street Lighting</p> <p>Status: Design</p> <p>Designer: Florida Power and Light</p> <p>Contractor: Florida Power and Light</p> <p>Project Manager: May Cheng</p>	<p>Scope</p> <p>These projects replace the high pressure sodium lights with LED lights. Many of the street lights along County roads are owned and maintained by FPL with the County paying all the operation and maintenance costs. FPL will be responsible for final design and installation and the County will reimburse FPL.</p> <p>Notes</p> <p>There are six (6) street lighting projects (road segments) funded (\$820,000) for conversion in FY 2019.</p>	<table border="1"> <thead> <tr> <th></th> <th>Original</th> <th>Actual</th> </tr> </thead> <tbody> <tr> <td>Melaleuca Lane/Greenacres limits to Kir</td> <td></td> <td></td> </tr> <tr> <td>Linton/Military to Jog</td> <td></td> <td></td> </tr> <tr> <td>Jog Rd/SR80 to Forest Hill</td> <td></td> <td></td> </tr> <tr> <td>Jog Rd/Gateway to Woolbright</td> <td></td> <td></td> </tr> <tr> <td>Jog Rd/Lake Ida to Old Clint Moore</td> <td></td> <td></td> </tr> <tr> <td>Lantana Rd/Turnpike to High Ridge</td> <td></td> <td></td> </tr> </tbody> </table>		Original	Actual	Melaleuca Lane/Greenacres limits to Kir			Linton/Military to Jog			Jog Rd/SR80 to Forest Hill			Jog Rd/Gateway to Woolbright			Jog Rd/Lake Ida to Old Clint Moore			Lantana Rd/Turnpike to High Ridge		
	Original	Actual																					
Melaleuca Lane/Greenacres limits to Kir																							
Linton/Military to Jog																							
Jog Rd/SR80 to Forest Hill																							
Jog Rd/Gateway to Woolbright																							
Jog Rd/Lake Ida to Old Clint Moore																							
Lantana Rd/Turnpike to High Ridge																							

PARTICIPATION	FUNDING	FINANCIAL SUMMARY												
<p>Consultant</p> <p>SBE N/A MBE N/A</p> <p>WBE N/A Local N/A</p> <p>Contractor</p> <p>SBE N/A MBE N/A</p> <p>WBE N/A Local N/A</p>		<table border="1"> <thead> <tr> <th>Project Budget</th> <th>Committed</th> <th>% Committed</th> <th>Paid To Date</th> </tr> <tr> <th>A</th> <th>B</th> <th>C=B/A</th> <th>D</th> </tr> </thead> <tbody> <tr> <td>\$820,000</td> <td>\$4,251</td> <td>0.52%</td> <td>\$4,251</td> </tr> </tbody> </table>	Project Budget	Committed	% Committed	Paid To Date	A	B	C=B/A	D	\$820,000	\$4,251	0.52%	\$4,251
Project Budget	Committed	% Committed	Paid To Date											
A	B	C=B/A	D											
\$820,000	\$4,251	0.52%	\$4,251											



Monthly Infrastructure Sales Tax Project Report

Small Cap Projects

Data Date: 04/16/2020

Report Date: 05/11/20

DESCRIPTION/TEAM

SCOPE/NOTES

SCHEDULE

Project Title: Florida Mango Rd. over LWDD Lat. 9 Canal (PB934337)
Project Number: 1635
BCC District: BIAF
Delivery Method: Design CCNA
Category: B08-Bridge Replacements
Status: Design
Designer: Stanley Consultants
Contractor: TBD (bid)
Project Manager: Kathleen Farrell

Scope

This project will replace an existing bridge that was built over 50 years ago. The new bridge will improve traffic safety (lane widths, bike lanes, parapets), update the guardrail system, improve roadway drainage, improve the slope protection, and enhance pedestrian sidewalk safety.

Notes

The project is funded with 5-Year Road Program (RP) funding and IST funding. The project is under design (using RP funds). The const. of the project (incl. assoc. rdway. improvements) is currently est. at \$3.3m. The IST partially funds the const. at \$700,000 in FY 20. The project is currently scheduled to begin construction in FY22.

	Original	Actual
Design Contract Notice to Proceed	9/20/2016	9/20/2016
Design Completion	10/1/2020	
Construction Bid Date	2/1/2021	
Construction Start	10/1/2021	
Construction Complete	10/1/2023	

PARTICIPATION

FUNDING


FINANCIAL SUMMARY

Consultant

SBE	18%	MBE	N/A
WBE	N/A	Local	100%

Contractor

SBE	TBD	MBE	TBD
WBE	TBD	Local	TBD



Project Budget	Committed	% Committed	Paid To Date
A	B	C=B/A	D
\$700,000	\$0	0.00%	\$0

DESCRIPTION/TEAM

SCOPE/NOTES

SCHEDULE

Project Title: Lyons Rd from Hillsboro Canal to Boca Lago Blvd.
Project Number: 1637
BCC District: 05
Delivery Method: Annual Construction Contract
Category: R04-Resurfacing
Status: Construction
Designer: N/A
Contractor: Ranger
Project Manager: Mark Kroeger

Scope

Resurfacing 1.5 miles (6 lane miles) of Lyons Road from the Hillsboro Canal to Boca Lago Boulevard.

Notes

Outstanding work includes milling and paving, updating ADA ramps, restriping the road, and replacing traffic loops.

	Original	Actual
Milling and Pavement Complete	6/1/2020	
ADA (Curb/Cut Ramps) Complete	8/1/2020	
Traffic Striping Complete	9/1/2020	
Traffic Loops Complete	11/1/2020	

PARTICIPATION

FUNDING


FINANCIAL SUMMARY

Consultant

SBE	N/A	MBE	N/A
WBE	N/A	Local	N/A

Contractor

SBE	5%	MBE	0%
WBE	0%	Local	100%

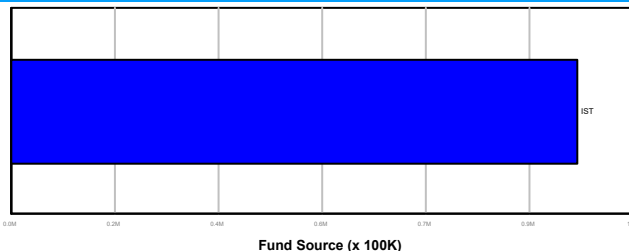

Project Budget	Committed	% Committed	Paid To Date
A	B	C=B/A	D
\$1,000,000	\$854,313	85.43%	\$313



Monthly Infrastructure Sales Tax Project Report

Small Cap Projects

Data Date: 04/16/2020

Report Date: 05/11/20

DESCRIPTION/TEAM	SCOPE/NOTES	SCHEDULE															
<p>Project Title: Lake Ida Rd from Congress Ave to Swinton Ave.</p> <p>Project Number: 1638</p> <p>BCC District: 04</p> <p>Delivery Method: Annual Construction Contract</p> <p>Category: R04-Resurfacing</p> <p>Status: Construction</p> <p>Designer: N/A</p> <p>Contractor: Ranger</p> <p>Project Manager: Mark Kroeger</p>	<p>Scope</p> <p>Resurfacing 1.3 miles (6 lane miles) of Lake Ida Road from Congress Avenue to Swinton Avenue.</p> <p>Notes</p> <p>Outstanding work includes milling and paving, updating ADA ramps, restriping the road, and replacing traffic loops.</p>	<table border="1"> <thead> <tr> <th></th> <th>Original</th> <th>Actual</th> </tr> </thead> <tbody> <tr> <td>Milling and Pavement Complete</td> <td>9/1/2020</td> <td></td> </tr> <tr> <td>Traffic Striping Complete</td> <td>12/1/2020</td> <td></td> </tr> <tr> <td>ADA (Curb/Cut Ramps) Complete</td> <td>1/1/2021</td> <td></td> </tr> <tr> <td>Traffic Loops Complete</td> <td>3/1/2021</td> <td></td> </tr> </tbody> </table>		Original	Actual	Milling and Pavement Complete	9/1/2020		Traffic Striping Complete	12/1/2020		ADA (Curb/Cut Ramps) Complete	1/1/2021		Traffic Loops Complete	3/1/2021	
	Original	Actual															
Milling and Pavement Complete	9/1/2020																
Traffic Striping Complete	12/1/2020																
ADA (Curb/Cut Ramps) Complete	1/1/2021																
Traffic Loops Complete	3/1/2021																

PARTICIPATION	FUNDING	FINANCIAL SUMMARY												
<p>Consultant</p> <p>SBE N/A MBE N/A</p> <p>WBE N/A Local N/A</p> <p>Contractor</p> <p>SBE 5% MBE 0%</p> <p>WBE 0% Local 100%</p>		<table border="1"> <thead> <tr> <th>Project Budget</th> <th>Committed</th> <th>% Committed</th> <th>Paid To Date</th> </tr> <tr> <th>A</th> <th>B</th> <th>C=B/A</th> <th>D</th> </tr> </thead> <tbody> <tr> <td>\$700,000</td> <td>\$25,719</td> <td>3.67%</td> <td>\$219</td> </tr> </tbody> </table>	Project Budget	Committed	% Committed	Paid To Date	A	B	C=B/A	D	\$700,000	\$25,719	3.67%	\$219
Project Budget	Committed	% Committed	Paid To Date											
A	B	C=B/A	D											
\$700,000	\$25,719	3.67%	\$219											

DESCRIPTION/TEAM	SCOPE/NOTES	SCHEDULE															
<p>Project Title: Okeechobee Blvd from Royal Palm Beach Blvd. to Wildc</p> <p>Project Number: 1639</p> <p>BCC District: 06</p> <p>Delivery Method: Annual Construction Contract</p> <p>Category: R04-Resurfacing</p> <p>Status: Construction</p> <p>Designer: N/A</p> <p>Contractor: Ranger</p> <p>Project Manager: Mark Kroeger</p>	<p>Scope</p> <p>Resurfacing 1.1 miles (6.6 lane miles) of Okeechobee Boulevard from Royal Palm Beach Boulevard to Wildcat Way.</p> <p>Notes</p> <p>Outstanding work includes updating ADA ramps, restriping the road, and replacing traffic loops.</p>	<table border="1"> <thead> <tr> <th></th> <th>Original</th> <th>Actual</th> </tr> </thead> <tbody> <tr> <td>Milling and Pavement Complete</td> <td>5/1/2020</td> <td>4/14/2020</td> </tr> <tr> <td>ADA (Curb/Cut Ramps) Complete</td> <td>7/1/2020</td> <td></td> </tr> <tr> <td>Traffic Striping Complete</td> <td>8/1/2020</td> <td></td> </tr> <tr> <td>Traffic Loops Complete</td> <td>10/1/2020</td> <td></td> </tr> </tbody> </table>		Original	Actual	Milling and Pavement Complete	5/1/2020	4/14/2020	ADA (Curb/Cut Ramps) Complete	7/1/2020		Traffic Striping Complete	8/1/2020		Traffic Loops Complete	10/1/2020	
	Original	Actual															
Milling and Pavement Complete	5/1/2020	4/14/2020															
ADA (Curb/Cut Ramps) Complete	7/1/2020																
Traffic Striping Complete	8/1/2020																
Traffic Loops Complete	10/1/2020																

PARTICIPATION	FUNDING	FINANCIAL SUMMARY												
<p>Consultant</p> <p>SBE N/A MBE N/A</p> <p>WBE N/A Local N/A</p> <p>Contractor</p> <p>SBE 5% MBE 0%</p> <p>WBE 0% Local 100%</p>		<table border="1"> <thead> <tr> <th>Project Budget</th> <th>Committed</th> <th>% Committed</th> <th>Paid To Date</th> </tr> <tr> <th>A</th> <th>B</th> <th>C=B/A</th> <th>D</th> </tr> </thead> <tbody> <tr> <td>\$700,000</td> <td>\$694,557</td> <td>99.22%</td> <td>\$219</td> </tr> </tbody> </table>	Project Budget	Committed	% Committed	Paid To Date	A	B	C=B/A	D	\$700,000	\$694,557	99.22%	\$219
Project Budget	Committed	% Committed	Paid To Date											
A	B	C=B/A	D											
\$700,000	\$694,557	99.22%	\$219											



Monthly Infrastructure Sales Tax Project Report

Small Cap Projects

Data Date: 04/16/2020

Report Date: 05/11/20

DESCRIPTION/TEAM	SCOPE/NOTES	SCHEDULE															
<p>Project Title: High Ridge Road from Hypoluxo Rd to Lake Osbourne D</p> <p>Project Number: 1640</p> <p>BCC District: 03</p> <p>Delivery Method: Annual Construction Contract</p> <p>Category: R04-Resurfacing</p> <p>Status: Construction</p> <p>Designer: N/A</p> <p>Contractor: Ranger</p> <p>Project Manager: Mark Kroeger</p>	<p>Scope</p> <p>Resurfacing 1.9 miles (3.8 lane miles) of High Ridge Road from Hypoluxo Road to Lake Osborne Drive.</p> <p>Notes</p> <p>Outstanding work includes updating ADA ramps, and replacing traffic loops.</p>	<table border="1"> <thead> <tr> <th></th> <th>Original</th> <th>Actual</th> </tr> </thead> <tbody> <tr> <td>Milling and Pavement Complete</td> <td>2/1/2020</td> <td>1/15/2020</td> </tr> <tr> <td>Traffic Striping Complete</td> <td>5/1/2020</td> <td>2/20/2020</td> </tr> <tr> <td>ADA (Curb/Cut Ramps) Complete</td> <td>6/1/2020</td> <td></td> </tr> <tr> <td>Traffic Loops Complete</td> <td>8/1/2020</td> <td></td> </tr> </tbody> </table>		Original	Actual	Milling and Pavement Complete	2/1/2020	1/15/2020	Traffic Striping Complete	5/1/2020	2/20/2020	ADA (Curb/Cut Ramps) Complete	6/1/2020		Traffic Loops Complete	8/1/2020	
	Original	Actual															
Milling and Pavement Complete	2/1/2020	1/15/2020															
Traffic Striping Complete	5/1/2020	2/20/2020															
ADA (Curb/Cut Ramps) Complete	6/1/2020																
Traffic Loops Complete	8/1/2020																

PARTICIPATION	FUNDING	FINANCIAL SUMMARY												
<p>Consultant</p> <p>SBE N/A MBE N/A</p> <p>WBE N/A Local N/A</p> <p>Contractor</p> <p>SBE 15% MBE TBD</p> <p>WBE TBD Local 100%</p>	<p>Fund Source (x 100K)</p>	<table border="1"> <thead> <tr> <th>Project Budget</th> <th>Committed</th> <th>% Committed</th> <th>Paid To Date</th> </tr> <tr> <th>A</th> <th>B</th> <th>C=B/A</th> <th>D</th> </tr> </thead> <tbody> <tr> <td>\$400,000</td> <td>\$384,027</td> <td>96.01%</td> <td>\$361,927</td> </tr> </tbody> </table>	Project Budget	Committed	% Committed	Paid To Date	A	B	C=B/A	D	\$400,000	\$384,027	96.01%	\$361,927
Project Budget	Committed	% Committed	Paid To Date											
A	B	C=B/A	D											
\$400,000	\$384,027	96.01%	\$361,927											

DESCRIPTION/TEAM	SCOPE/NOTES	SCHEDULE															
<p>Project Title: Central Blvd. from Indian Creek Parkway to Indiantown F</p> <p>Project Number: 1641</p> <p>BCC District: 01</p> <p>Delivery Method: Annual Construction Contract</p> <p>Category: R04-Resurfacing</p> <p>Status: Construction</p> <p>Designer: N/A</p> <p>Contractor: Ranger</p> <p>Project Manager: Mark Kroeger</p>	<p>Scope</p> <p>Resurfacing 1.8 miles (7.2 lane miles) of Central Boulevard from Indian Creek Parkway to Indiantown Road.</p> <p>Notes</p> <p>Outstanding work includes updating ADA ramps, restriping the road, and replacing traffic loops.</p>	<table border="1"> <thead> <tr> <th></th> <th>Original</th> <th>Actual</th> </tr> </thead> <tbody> <tr> <td>Milling and Pavement Complete</td> <td>3/1/2020</td> <td>2/11/2020</td> </tr> <tr> <td>Traffic Striping Complete</td> <td>6/1/2020</td> <td></td> </tr> <tr> <td>ADA (Curb/Cut Ramps) Complete</td> <td>7/1/2020</td> <td></td> </tr> <tr> <td>Traffic Loops Complete</td> <td>9/1/2020</td> <td></td> </tr> </tbody> </table>		Original	Actual	Milling and Pavement Complete	3/1/2020	2/11/2020	Traffic Striping Complete	6/1/2020		ADA (Curb/Cut Ramps) Complete	7/1/2020		Traffic Loops Complete	9/1/2020	
	Original	Actual															
Milling and Pavement Complete	3/1/2020	2/11/2020															
Traffic Striping Complete	6/1/2020																
ADA (Curb/Cut Ramps) Complete	7/1/2020																
Traffic Loops Complete	9/1/2020																

PARTICIPATION	FUNDING	FINANCIAL SUMMARY												
<p>Consultant</p> <p>SBE N/A MBE N/A</p> <p>WBE N/A Local N/A</p> <p>Contractor</p> <p>SBE 15% MBE TBD</p> <p>WBE TBD Local 100%</p>	<p>Fund Source (x 100K)</p>	<table border="1"> <thead> <tr> <th>Project Budget</th> <th>Committed</th> <th>% Committed</th> <th>Paid To Date</th> </tr> <tr> <th>A</th> <th>B</th> <th>C=B/A</th> <th>D</th> </tr> </thead> <tbody> <tr> <td>\$300,000</td> <td>\$276,622</td> <td>92.21%</td> <td>\$239,622</td> </tr> </tbody> </table>	Project Budget	Committed	% Committed	Paid To Date	A	B	C=B/A	D	\$300,000	\$276,622	92.21%	\$239,622
Project Budget	Committed	% Committed	Paid To Date											
A	B	C=B/A	D											
\$300,000	\$276,622	92.21%	\$239,622											



Monthly Infrastructure Sales Tax Project Report

Small Cap Projects

Data Date: 04/16/2020

Report Date: 05/11/20

DESCRIPTION/TEAM	SCOPE/NOTES	SCHEDULE															
<p>Project Title: Prosperity Farms Rd. from Northlake Blvd. to Alamanda</p> <p>Project Number: 1643</p> <p>BCC District: 01</p> <p>Delivery Method: Annual Construction Contract</p> <p>Category: R04-Resurfacing</p> <p>Status: Construction</p> <p>Designer: N/A</p> <p>Contractor: Ranger</p> <p>Project Manager: Mark Kroeger</p>	<p>Scope</p> <p>Resurfacing 1.5 miles (4.5 lane miles) of Prosperity Farms Road for Northlake Boulevard to Alamanda Drive.</p> <p>Notes</p> <p>Outstanding work includes milling and paving, updating ADA ramps restriping the road, and replacing traffic loops.</p>	<table border="1"> <thead> <tr> <th></th> <th style="text-align: center;">Original</th> <th style="text-align: center;">Actual</th> </tr> </thead> <tbody> <tr> <td>Milling and Pavement Complete</td> <td style="text-align: center;">6/1/2020</td> <td></td> </tr> <tr> <td>ADA (Curb/Cut Ramps) Complete</td> <td style="text-align: center;">8/1/2020</td> <td></td> </tr> <tr> <td>Traffic Striping Complete</td> <td style="text-align: center;">9/1/2020</td> <td></td> </tr> <tr> <td>Traffic Loops Complete</td> <td style="text-align: center;">11/1/2020</td> <td></td> </tr> </tbody> </table>		Original	Actual	Milling and Pavement Complete	6/1/2020		ADA (Curb/Cut Ramps) Complete	8/1/2020		Traffic Striping Complete	9/1/2020		Traffic Loops Complete	11/1/2020	
	Original	Actual															
Milling and Pavement Complete	6/1/2020																
ADA (Curb/Cut Ramps) Complete	8/1/2020																
Traffic Striping Complete	9/1/2020																
Traffic Loops Complete	11/1/2020																

PARTICIPATION	FUNDING	FINANCIAL SUMMARY												
<p>Consultant</p> <p>SBE N/A MBE N/A</p> <p>WBE N/A Local N/A</p> <p>Contractor</p> <p>SBE 5% MBE 0%</p> <p>WBE 0% Local 100%</p>		<table border="1"> <thead> <tr> <th>Project Budget</th> <th>Committed</th> <th>% Committed</th> <th>Paid To Date</th> </tr> <tr> <th style="text-align: center;">A</th> <th style="text-align: center;">B</th> <th style="text-align: center;">C=B/A</th> <th style="text-align: center;">D</th> </tr> </thead> <tbody> <tr> <td style="text-align: center;">\$200,000</td> <td style="text-align: center;">\$172,063</td> <td style="text-align: center;">86.03%</td> <td style="text-align: center;">\$63</td> </tr> </tbody> </table>	Project Budget	Committed	% Committed	Paid To Date	A	B	C=B/A	D	\$200,000	\$172,063	86.03%	\$63
Project Budget	Committed	% Committed	Paid To Date											
A	B	C=B/A	D											
\$200,000	\$172,063	86.03%	\$63											

DESCRIPTION/TEAM	SCOPE/NOTES	SCHEDULE						
<p>Project Title: Sections of Summit Blvd</p> <p>Project Number: 1653</p> <p>BCC District: 02</p> <p>Delivery Method: Annual Striping Contract</p> <p>Category: S16-Striping</p> <p>Status: Construction</p> <p>Designer: N/A</p> <p>Contractor: Southwide</p> <p>Project Manager: Larry Kelly</p>	<p>Scope</p> <p>This project consists of restriping sections of Summit Blvd.</p> <p>Notes</p> <p>The restriping construction scheduled for FY2018 has been completed. \$75,000 of the projects \$200,000 funding was advanced to FY 2018 (BT 2018 0599). The project is now funded at \$75,000 in FY 2018, \$50,000 in FY 2020, and \$75,000 in FY 2025 for a total funding of \$200,000.</p>	<table border="1"> <thead> <tr> <th></th> <th style="text-align: center;">Original</th> <th style="text-align: center;">Actual</th> </tr> </thead> <tbody> <tr> <td>Congress Ave. to Parker Ave.</td> <td style="text-align: center;">12/1/2018</td> <td style="text-align: center;">11/30/2018</td> </tr> </tbody> </table>		Original	Actual	Congress Ave. to Parker Ave.	12/1/2018	11/30/2018
	Original	Actual						
Congress Ave. to Parker Ave.	12/1/2018	11/30/2018						

PARTICIPATION	FUNDING	FINANCIAL SUMMARY												
<p>Consultant</p> <p>SBE N/A MBE NA</p> <p>WBE N/A Local N/A</p> <p>Contractor</p> <p>SBE 100% MBE 0%</p> <p>WBE 0% Local 100%</p>		<table border="1"> <thead> <tr> <th>Project Budget</th> <th>Committed</th> <th>% Committed</th> <th>Paid To Date</th> </tr> <tr> <th style="text-align: center;">A</th> <th style="text-align: center;">B</th> <th style="text-align: center;">C=B/A</th> <th style="text-align: center;">D</th> </tr> </thead> <tbody> <tr> <td style="text-align: center;">\$125,000</td> <td style="text-align: center;">\$33,085</td> <td style="text-align: center;">26.47%</td> <td style="text-align: center;">\$33,085</td> </tr> </tbody> </table>	Project Budget	Committed	% Committed	Paid To Date	A	B	C=B/A	D	\$125,000	\$33,085	26.47%	\$33,085
Project Budget	Committed	% Committed	Paid To Date											
A	B	C=B/A	D											
\$125,000	\$33,085	26.47%	\$33,085											



Monthly Infrastructure Sales Tax Project Report

Small Cap Projects

Data Date: 04/16/2020

Report Date: 05/11/20

DESCRIPTION/TEAM

SCOPE/NOTES

SCHEDULE

Project Title: Congress Avenue at Palm Beach Lakes
Project Number: 1659
BCC District: 07
Delivery Method: Design CCNA
Category: D04-Drainage Improvements
Status: Design
Designer: Arcadis
Contractor: TBD
Project Manager: David Young

Scope
 The project involves upgrading the drainage system along this intersection to alleviate flooding issues. Drainage improvements will include upsizing some existing pipes, adding a parallel trunk line system to the outfall, and adding exfiltration trench.

Notes
 The project is funded with 5-Year Road Program (RP) funding and IST funding. The project is under design (using RP funds). The const. of the project (incl. assoc. rdwy. improvements) is currently est. at \$2m. The IST partially funds the const. at \$500,000 in FY20. The project is currently scheduled to begin construction in FY21.

	Original	Actual
Design Contract Notice to Proceed	7/15/2015	7/15/2015
Design Completion	12/1/2020	
Construction Bid Date	4/12/2021	
Construction Start	8/1/2021	
Construction Complete	5/1/2022	


PARTICIPATION

FUNDING

FINANCIAL SUMMARY

Consultant
 SBE 37.6% MBE 0%
 WBE 0% Local 100%

Contractor
 SBE TBD MBE TBD
 WBE TBD Local TBD



Project Budget	Committed	% Committed	Paid To Date
A	B	C=B/A	D
\$500,000	\$0	0.00%	\$0

DESCRIPTION/TEAM

SCOPE/NOTES

SCHEDULE

Project Title: Sunset Cove Audio & Lighting System
Project Number: 17466
BCC District: 05
Delivery Method: Annual Contract
Category: P08-Public Building Repair Replacement & Expansion
Status: Design
Designer: TBD
Contractor: TBD
Project Manager: Andrew Gamble

Scope
 Existing stage lighting to be upgraded with LED lighting and stage speakers to be replaced and upgraded.
 This project is funded in:
 FY 2017 \$150,000

Notes
 No Status Change. Project is waiting to be advertised for bid.

	Original	Actual
Start Date	7/7/2017	7/7/2017
Finish Date	7/6/2018	


PARTICIPATION

FUNDING

FINANCIAL SUMMARY

Consultant
 SBE TBD MBE N/A
 WBE N/A Local TBD

Contractor
 SBE TBD MBE TBD
 WBE TBD Local TBD

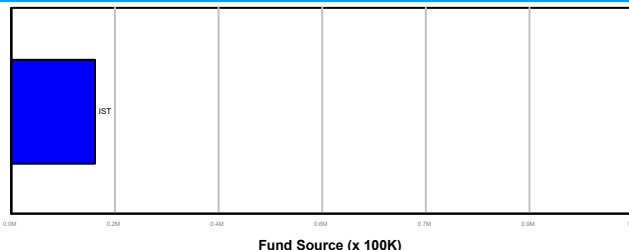

Project Budget	Committed	% Committed	Paid To Date
A	B	C=B/A	D
\$150,000	\$3,216	2.14%	\$3,216



Monthly Infrastructure Sales Tax Project Report

Small Cap Projects

Data Date: 04/16/2020

Report Date: 05/11/20

DESCRIPTION/TEAM	SCOPE/NOTES	SCHEDULE	
Project Title: Santaluces Pool Aquatic Facility Renovation Project Number: 17510 BCC District: 03 Delivery Method: CM Category: A02-Aquatic Facility Repair and Replacement Status: Construction Designer: N/A Contractor: Robling Project Manager: Tom McNamara	Scope Pool resurfacing and repairs, repainting building. - This project is funded for construction T005: \$850,000 FY 2017 Notes First phase of this project complete. Awaiting parks direction for further scope.	Original	Actual
		Start Date	11/21/2017 12/4/2017
		Finish Date	6/15/2018

PARTICIPATION	FUNDING	FINANCIAL SUMMARY			
Consultant SBE N/A MBE N/A WBE N/A Local N/A Contractor SBE 26.75% MBE N/A WBE N/A Local 100%	<p style="text-align: center;">Fund Source (x 100K)</p>	Project Budget	Committed	% Committed	Paid To Date
		A	B	C=B/A	D
		\$850,000	\$595,448	70.05%	\$595,448

DESCRIPTION/TEAM	SCOPE/NOTES	SCHEDULE	
Project Title: Delray Hlth Clinic & SC Adm Yth Svcs RR CW-ADA Project Number: 17523 BCC District: 07 Delivery Method: Annual Contract Category: G02-General Government Facilities Status: Design Designer: Colome & Associates Contractor: TBD Project Manager: David Lavinsky	Scope Renovate the existing Delray Health Clinics public first and second floor restrooms to meet ADA requirements. The scope at SC Admin Youth Services is to renovate existing staff and public restrooms to meet ADA requirements. These projects were combined into one. Notes Received 95% drawing review from ESS and FMD. Awaiting reply from Space and Interior planning department. SC Youth Services has a problem with waste piping which FMD is requesting to be included in scope. This issue is being investigated and reviewed to see if alternate methods of repair can be done so major delays will not occur.	Original	Actual
		Start Date	7/27/2017 7/27/2017
		Finish Date	12/21/2018

PARTICIPATION	FUNDING	FINANCIAL SUMMARY			
Consultant SBE 100% MBE N/A WBE N/A Local 100% Contractor SBE TBD MBE TBD WBE TBD Local TBD	<p style="text-align: center;">Fund Source (x 100K)</p>	Project Budget	Committed	% Committed	Paid To Date
		A	B	C=B/A	D
		\$250,000	\$11,774	4.71%	\$11,774



Monthly Infrastructure Sales Tax Project Report

Small Cap Projects

Data Date: 04/16/2020

Report Date: 05/11/20

DESCRIPTION/TEAM	SCOPE/NOTES	SCHEDULE	
Project Title: Lantana Health Restrooms CW-ADA Project Number: 17528 BCC District: 07 Delivery Method: TBD Category: G02-General Government Facilities Status: Design Designer: Colome & Associates Contractor: TBD Project Manager: David Lavinsky	Scope Renovate existing public restrooms on first and second floor to meet ADA requirements. Notes Project being funded with CDBG funds due to IST shortfall. Consultant funding approval BAS in signature process.	Original	Actual
		Start Date	7/7/2017
		Finish Date	4/6/2018

PARTICIPATION	FUNDING	FINANCIAL SUMMARY			
Consultant SBE 100% MBE N/A WBE N/A Local 100% Contractor SBE TBD MBE TBD WBE TBD Local TBD	<p style="text-align: center;">Fund Source (x 100K)</p>	Project Budget	Committed	% Committed	Paid To Date
		A	B	C=B/A	D
		\$0	\$0	0.00%	\$0

DESCRIPTION/TEAM	SCOPE/NOTES	SCHEDULE	
Project Title: Four Points Project Number: 17557 BCC District: 02 Delivery Method: CMR Category: G02-General Government Facilities Status: Design Designer: Colome & Associates Contractor: All Site Construction Project Manager: Rosalyn Acosta	Scope Design and Construction services for interior renovation and reconfiguration of partial 2nd floor at Four Points Facility and partial 2nd floor at Airport Center 1. Consolidate Youth Services department at Four Points Facility. Move Office of Small Business Assistance from Four Points to Airport Center Notes CSA for additional consultant services circulating for approval signatures.	Original	Actual
		Design Start	11/17/2017
		Construction Start	1/2/2019
		Completion	12/27/2019

PARTICIPATION	FUNDING	FINANCIAL SUMMARY			
Consultant SBE 100% MBE N/A WBE N/A Local 100% Contractor SBE 100% MBE 0% WBE 100% Local 100%	<p style="text-align: center;">Fund Source (x 100K)</p>	Project Budget	Committed	% Committed	Paid To Date
		A	B	C=B/A	D
		\$825,000	\$131,278	15.91%	\$90,697



Monthly Infrastructure Sales Tax Project Report

Small Cap Projects

Data Date: 04/16/2020

Report Date: 05/11/20

DESCRIPTION/TEAM				SCOPE/NOTES				SCHEDULE															
Project Title: SR-7 (Whitehorse dr. to Hypoluxo Rd.) Project Number: 1830 BCC District: BIAF Delivery Method: Design CCNA Category: S14-Street Lighting Status: Design Designer: Electrical Design Associates Contractor: Florida Power & Light Project Manager: Amy Harris				Scope The exist. SR7 high mast lighting is in need of a new LED system. The original intent was to rehab the towers (in FY21) with conversion to LED lights (in FY25). The new scope involves removing and replacing the high mast lights with new LED lighting. Project will design new LED lighting along SR7. Notes The project is under design. The IST funding of \$106,000 was advanced from FY 2025 to FY 2019 (BT 2019-0162). The project will be constructed in conjunction with the "SR7 High Mast Towers Rehab (Hypoluxo Rd. to north of Lake Worth Rd.)" street lighting project which is funded by the IST at \$500,000 in FY 2021.				<table border="1"> <thead> <tr> <th></th> <th>Original</th> <th>Actual</th> </tr> </thead> <tbody> <tr> <td>Design Contract Notice to Proceed</td> <td>5/1/2019</td> <td>4/24/2019</td> </tr> <tr> <td>Design Completion</td> <td>5/1/2020</td> <td></td> </tr> </tbody> </table>					Original	Actual	Design Contract Notice to Proceed	5/1/2019	4/24/2019	Design Completion	5/1/2020				
	Original	Actual																					
Design Contract Notice to Proceed	5/1/2019	4/24/2019																					
Design Completion	5/1/2020																						
PARTICIPATION				FUNDING				FINANCIAL SUMMARY															
Consultant SBE 100% MBE 100% WBE 100% Local 100% Contractor SBE N/A MBE N/A WBE N/A Local N/A				<p>Fund Source (x 100K)</p>				<table border="1"> <thead> <tr> <th>Project Budget</th> <th>Committed</th> <th>% Committed</th> <th>Paid To Date</th> </tr> <tr> <th>A</th> <th>B</th> <th>C=B/A</th> <th>D</th> </tr> </thead> <tbody> <tr> <td>\$106,000</td> <td>\$20,121</td> <td>18.98%</td> <td>\$904</td> </tr> </tbody> </table>				Project Budget	Committed	% Committed	Paid To Date	A	B	C=B/A	D	\$106,000	\$20,121	18.98%	\$904
Project Budget	Committed	% Committed	Paid To Date																				
A	B	C=B/A	D																				
\$106,000	\$20,121	18.98%	\$904																				

DESCRIPTION/TEAM				SCOPE/NOTES				SCHEDULE																		
Project Title: FY2019 Sports Field Lighting Replacements Project Number: T009 BCC District: Multiple Delivery Method: Sports Filed Lighting Annual Category: S12-Sports Lighting Replacement Status: Design Designer: JLRD Engineers Contractor: Musco Project Manager: Stuart Patterson				Scope Replacement of Sports Field Lighting at Carlin Park. IST FY 2019 funds: \$200,000. Notes Project will be divided into (2) packages: RFP #1, Supply Lighting Fixtures: CID currently working towards completing the RFQ package to potential suppliers. RFP #2, Installation of Lighting Fixtures: CID will develop RFQ packages for each after completion of fixtures RFQ's. Currently completing existing conditions surveys (Tierra).				<table border="1"> <thead> <tr> <th></th> <th>Original</th> <th>Actual</th> </tr> </thead> <tbody> <tr> <td>Final Completion</td> <td></td> <td></td> </tr> <tr> <td>Project Start</td> <td>6/29/2017</td> <td>6/29/2017</td> </tr> <tr> <td>Procurement (Light Fixture Vendor)</td> <td>10/16/2018</td> <td>10/16/2018</td> </tr> <tr> <td>Procurement (Installation Contractor)</td> <td>10/17/2018</td> <td></td> </tr> </tbody> </table>					Original	Actual	Final Completion			Project Start	6/29/2017	6/29/2017	Procurement (Light Fixture Vendor)	10/16/2018	10/16/2018	Procurement (Installation Contractor)	10/17/2018	
	Original	Actual																								
Final Completion																										
Project Start	6/29/2017	6/29/2017																								
Procurement (Light Fixture Vendor)	10/16/2018	10/16/2018																								
Procurement (Installation Contractor)	10/17/2018																									
PARTICIPATION				FUNDING				FINANCIAL SUMMARY																		
Consultant SBE 100% MBE N/A WBE N/A Local 100% Contractor SBE TBD MBE TBD WBE TBD Local TBD				<p>Fund Source (x 100K)</p>				<table border="1"> <thead> <tr> <th>Project Budget</th> <th>Committed</th> <th>% Committed</th> <th>Paid To Date</th> </tr> <tr> <th>A</th> <th>B</th> <th>C=B/A</th> <th>D</th> </tr> </thead> <tbody> <tr> <td>\$200,000</td> <td>\$2,883</td> <td>1.44%</td> <td>\$2,883</td> </tr> </tbody> </table>				Project Budget	Committed	% Committed	Paid To Date	A	B	C=B/A	D	\$200,000	\$2,883	1.44%	\$2,883			
Project Budget	Committed	% Committed	Paid To Date																							
A	B	C=B/A	D																							
\$200,000	\$2,883	1.44%	\$2,883																							



Monthly Infrastructure Sales Tax Project Report

Small Cap Projects

Data Date: 04/16/2020

Report Date: 05/11/20

DESCRIPTION/TEAM	SCOPE/NOTES	SCHEDULE	
<p>Project Title: FY 2017 Playground Replacements - Countywide</p> <p>Project Number: T021</p> <p>BCC District: Multiple</p> <p>Delivery Method: Annual Purchasing Contract</p> <p>Category: P06-Playground Replacement</p> <p>Status: Design</p> <p>Designer: Palm Beach County Parks</p> <p>Contractor: Multiple</p> <p>Project Manager: Rosalyn Acosta</p>	<p>Scope</p> <p>Playground Replacements at the following: Dyer Park, JPP Osborne Boundless, Juno Park, Lake Ida Park 4th Street, Paul Rardin Park, John Stretch Park, Sanders Park. IST FY 2017 funds: \$398,750; FY 2019 funds: \$156,750; Total: \$555,500</p> <p>Notes</p> <p>Parks has completed Paul Rardin and Dyer Park play grounds. Other parks forthcoming.</p>	Original	Actual
		Notice to Proceed	2/1/2019 / 2/1/2019
		Start Date	2/15/2019
		Completion Date	3/30/2019

PARTICIPATION	FUNDING	FINANCIAL SUMMARY			
<p>Consultant</p> <p>SBE N/A MBE N/A</p> <p>WBE N/A Local N/A</p> <p>Contractor</p> <p>SBE N/A MBE N/A</p> <p>WBE N/A Local N/A</p>	<p style="text-align: center;">Fund Source (x 100K)</p>	Project Budget	Committed	% Committed	Paid To Date
		A	B	C=B/A	D
		\$555,500	\$468,308	84.30%	\$233,247

DESCRIPTION/TEAM	SCOPE/NOTES	SCHEDULE	
<p>Project Title: Loxahatchee Groves Septic System Replacement</p> <p>Project Number: T032</p> <p>BCC District: 06</p> <p>Delivery Method: Annual Contract</p> <p>Category: S02-Sanitary Sewer/Septic Systems</p> <p>Status: Design</p> <p>Designer: Alan Gerwig & Assoc., Inc.</p> <p>Contractor: TBD</p> <p>Project Manager: William Munker</p>	<p>Scope</p> <p>Design work with Alan Gerwig- Remove existing septic system and connect to the County Waste Water System Force Main on Southern Boulevard . Current project budget is \$90,000. IST Funding is \$50,000 for FY17. Ad Valorum: 3602 P831-\$20,000, 3600 P834- \$20,000</p> <p>Notes</p> <p>Parks is now working with WUD to perform this work. The sewer line was installed from the center line of SR 80 to the park boundary. Awaiting WUD to finalize their revised lift station contract before finalizing the project. WUD is managing; Project expected to be completed by this fall.</p>	Original	Actual
		Project Start	9/30/2017 / 4/1/2018
		Project Completion	2/28/2019

PARTICIPATION	FUNDING	FINANCIAL SUMMARY			
<p>Consultant</p> <p>SBE 100% MBE N/A</p> <p>WBE N/A Local 100%</p> <p>Contractor</p> <p>SBE TBD MBE TBD</p> <p>WBE TBD Local TBD</p>	<p style="text-align: center;">Fund Source (x 100K)</p>	Project Budget	Committed	% Committed	Paid To Date
		A	B	C=B/A	D
		\$50,000	\$26,620	53.24%	\$26,620



Monthly Infrastructure Sales Tax Project Report

Small Cap Projects

Data Date: 04/16/2020

Report Date: 05/11/20

DESCRIPTION/TEAM	SCOPE/NOTES	SCHEDULE	
Project Title: BASCR Nature Trail Boardwalk Replacement Project Number: T039 BCC District: 05 Delivery Method: Annual Contract Category: B06-Bridge or Boardwalk Replacement Status: Construction Designer: N/A Contractor: ANZCO Project Manager: Brian McNamara	Scope Remove and replace boardwalk decking, railing, rail posts and associated hardware with new material. Notes Substantial meeting 04/29/2020. Contractor working on punch list from parks.	Original	Actual
		Project Start	7/15/2019 / 7/31/2019
		Project Completion	3/11/2020

PARTICIPATION	FUNDING	FINANCIAL SUMMARY			
Consultant SBE N/A MBE N/A WBE N/A Local N/A Contractor SBE 100% MBE 0% WBE 0% Local	<p style="text-align: center;">Fund Source (x 100K)</p>	Project Budget	Committed	% Committed	Paid To Date
		A	B	C=B/A	D
		\$417,770	\$225,000	53.86%	\$198,074

DESCRIPTION/TEAM	SCOPE/NOTES	SCHEDULE	
Project Title: Jupiter Island Pavilion Replacement Project Number: T043 BCC District: 01 Delivery Method: Annual Contract Category: G04-Group Pavilion Replacement Status: Design Designer: N/A Contractor: Andrea Construction Project Manager: William Munker	Scope Renovate existing pavilion. Renovation to include new lights, conduit, brackets, and paint. Complete replacement was not warranted. Notes Pre -Con meeting completed 4/16/20 Tentative start 5 /1/20	Original	Actual
		Project Start	6/1/2020
		Project Completion	8/10/2020

PARTICIPATION	FUNDING	FINANCIAL SUMMARY			
Consultant SBE N/A MBE N/A WBE N/A Local N/A Contractor SBE 91.87% MBE 0% WBE 0% Local 100%	<p style="text-align: center;">Fund Source (x 100K)</p>	Project Budget	Committed	% Committed	Paid To Date
		A	B	C=B/A	D
		\$150,000	\$76,995	51.33%	\$695



Monthly Infrastructure Sales Tax Project Report

Small Cap Projects

Data Date: 04/16/2020

Report Date: 05/11/20

DESCRIPTION/TEAM	SCOPE/NOTES	SCHEDULE	
Project Title: Juno Park Septic System Replacement Project Number: T056 BCC District: 01 Delivery Method: TBD Category: S02-Sanitary Sewer/Septic Systems Status: Design Designer: Civil Design Contractor: TBD Project Manager: Ben Carroll	Scope Heavily used public septic system needs replacement. Failure would result in public restroom failure. IST Funds - \$50,000 & Ad Valorem Funds - \$13,638. Notes Design in progress. Topographic survey complete. Awaiting 50% construction documents.	Original	Actual
		Project Start	1/30/2019
		Project Completion	TBD

PARTICIPATION	FUNDING	FINANCIAL SUMMARY			
Consultant SBE 100% MBE N/A WBE N/A Local 100% Contractor SBE TBD MBE TBD WBE TBD Local TBD		Project Budget	Committed	% Committed	Paid To Date
		A	B	C=B/A	D
		\$63,638	\$50,001	78.57%	\$232

DESCRIPTION/TEAM	SCOPE/NOTES	SCHEDULE	
Project Title: Beach Access Dune Crossover and Dock Repair and Rep Project Number: T071 BCC District: 01 Delivery Method: Annual Construction Contract Category: B06-Bridge or Boardwalk Replacement Status: Construction Designer: N/A Contractor: Wynn and Sons Project Manager: Ricard Gonzales	Scope This project will repair/rebuild the boardwalk #76 in Coral Cove Park. These repairs are needed to ensure safe public access to the beaches. Notes This project will remain active since it is funded over multiple years (FY19-\$25,000, FY20-\$25,000, FY21-\$25,000, FY22-\$31,226, FY23-\$35,134, FY24-\$55,000 and FY25-\$28,640). Currently, there are no active repairs at this time.	Original	Actual
		Notice to Proceed	1/2/2018
		Start Date	1/2/2018
		Completion Date	2/28/2018

PARTICIPATION	FUNDING	FINANCIAL SUMMARY			
Consultant SBE N/A MBE N/A WBE N/A Local N/A Contractor SBE 15% MBE N/A WBE N/A Local 100%		Project Budget	Committed	% Committed	Paid To Date
		A	B	C=B/A	D
		\$249,680	\$74,693	29.92%	\$74,693



Monthly Infrastructure Sales Tax Project Report

Small Cap Projects

Data Date: 04/16/2020

Report Date: 05/11/20

DESCRIPTION/TEAM	SCOPE/NOTES	SCHEDULE	
<p>Project Title: Ocean Inlet Park Street and Parking Lot Light Replacement</p> <p>Project Number: T081</p> <p>BCC District: 04</p> <p>Delivery Method: Annual Contract</p> <p>Category: P02-Parking Lot Lighting Replacement</p> <p>Status: Design</p> <p>Designer: JLRD</p> <p>Contractor: TBD</p> <p>Project Manager: Ben Carroll</p>	<p>Scope</p> <p>Replace existing parking lot lighting fixtures with LED type.</p> <p>Notes</p> <p>Boynton, Ocean Inlet, and Jupiter Farms are being bundled together. Ocean Inlet Park needs to have amber sea turtle friendly lighting with shields. Pre-bid meeting held 4/28. Bids are due 5/21</p>	Original	Actual
		Design Start	12/28/2018
		Construction Start	1/15/2020
		Project Completion	3/15/2020

PARTICIPATION	FUNDING	FINANCIAL SUMMARY			
<p>Consultant</p> <p>SBE 100% MBE N/A</p> <p>WBE N/A Local 100%</p> <p>Contractor</p> <p>SBE TBD MBE TBD</p> <p>WBE TBD Local TBD</p>	<p>Fund Source (x 100K)</p>	Project Budget	Committed	% Committed	Paid To Date
		A	B	C=B/A	D
		\$84,000	\$10,196	12.14%	\$4,334

DESCRIPTION/TEAM	SCOPE/NOTES	SCHEDULE	
<p>Project Title: Jupiter Farms Parking Lot Light Replacement</p> <p>Project Number: T083</p> <p>BCC District: 01</p> <p>Delivery Method: Annual Contract</p> <p>Category: P02-Parking Lot Lighting Replacement</p> <p>Status: Design</p> <p>Designer: JLRD</p> <p>Contractor: TBD</p> <p>Project Manager: Ben Carroll</p>	<p>Scope</p> <p>Replacement of the existing employee and visitor parking lot light fixtures with LED type.</p> <p>Notes</p> <p>Boynton, Ocean Inlet, and Jupiter Farms are being bundled together. Pre-bid meeting held 4/28. Bids are due 5/21</p>	Original	Actual
		Design Start	12/26/2018
		Construction Start	1/15/2020
		Project Completion	3/15/2020

PARTICIPATION	FUNDING	FINANCIAL SUMMARY			
<p>Consultant</p> <p>SBE 100% MBE N/A</p> <p>WBE N/A Local 100%</p> <p>Contractor</p> <p>SBE TBD MBE TBD</p> <p>WBE TBD Local TBD</p>	<p>Fund Source (x 100K)</p>	Project Budget	Committed	% Committed	Paid To Date
		A	B	C=B/A	D
		\$60,000	\$13,424	22.37%	\$5,552



Monthly Infrastructure Sales Tax Project Report

Small Cap Projects

Data Date: 04/16/2020

Report Date: 05/11/20

DESCRIPTION/TEAM	SCOPE/NOTES	SCHEDULE	
Project Title: Okeehetee North Roadway Repairs Project Number: T091 BCC District: 02 Delivery Method: Annual Construction Category: A04-Asphalt Paving & Striping Status: Construction Designer: N/A Contractor: Wynn and Sons Project Manager: Joseph Sarquis	Scope This project will repair the existing parking lot at Okeehetee Park North. Notes This project has been further delayed by the contractor. The scheduled start date is early Winter 2020.	Original	Actual
		Notice to Proceed	7/17/2019 / 7/17/2019
		Start Date	7/31/2019
		Completion Date	10/31/2019

PARTICIPATION	FUNDING	FINANCIAL SUMMARY			
Consultant SBE N/A MBE N/A WBE N/A Local N/A Contractor SBE 100% MBE 0% WBE 0% Local 100%	<p style="text-align: center;">Fund Source (x 100K)</p>	Project Budget	Committed	% Committed	Paid To Date
		A	B	C=B/A	D
		\$15,000	\$15,000	100.00%	\$39

DESCRIPTION/TEAM	SCOPE/NOTES	SCHEDULE	
Project Title: JPP Boat Ramp Replacement Project Number: T107 BCC District: BIAF Delivery Method: Annual Contract Category: F04-Fresh Water Boat Ramps Status: Design Designer: Stantec Consulting Services, Inc. Contractor: TBD Project Manager: Sunil Jagoo	Scope Replacement of the north boat ramp, removing the middle pier on the two south boat ramp and creating one single wider ramp in their place, replacement of the north and south fixed piers with floating dock piers, development of a gangway between the floating piers and the fixed fishing docks that adjust Notes Permit submitted, awaiting review. Pre-bid held 5/5/20. Bids due 5/28/20.	Original	Actual
		Schematic Design	3/31/2020
		Design Development	6/16/2020
		Permitting	7/7/2020
		Construction Documents	8/11/2020
		Construction Start	10/6/2020

PARTICIPATION	FUNDING	FINANCIAL SUMMARY			
Consultant SBE 31% MBE N/A WBE N/A Local 31% Contractor SBE TBD MBE TBD WBE TBD Local TBD	<p style="text-align: center;">Fund Source (x 100K)</p>	Project Budget	Committed	% Committed	Paid To Date
		A	B	C=B/A	D
		\$700,000	\$125	0.02%	\$125



Monthly Infrastructure Sales Tax Project Report

Small Cap Projects

Data Date: 04/16/2020

Report Date: 05/11/20

DESCRIPTION/TEAM

SCOPE/NOTES

SCHEDULE

Project Title: West Boynton Parking Lot Light Replacement
Project Number: T162
BCC District: 05
Delivery Method: TBD
Category: P02-Parking Lot Lighting Replacement
Status: Design
Designer: JLRD
Contractor: TBD
Project Manager: Ben Carroll

Scope
 Replacement of the existing parking lot light fixtures with LED type.

Notes
 Boynton, Ocean Inlet, and Jupiter Farms are being bundled together.
 Pre-bid meeting held 4/28. Bids are due 5/21


	Original	Actual
Design Start	12/26/2018	12/26/2018
Construction Start	1/15/2020	
Project Completion	3/15/2020	

PARTICIPATION

FUNDING

FINANCIAL SUMMARY

Consultant			
SBE	100%	MBE	N/A
WBE	N/A	Local	100%
Contractor			
SBE	TBD	MBE	TBD
WBE	TBD	Local	TBD

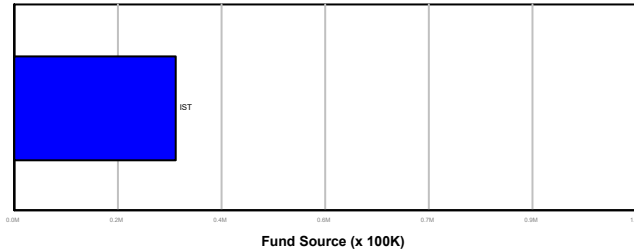

Project Budget	Committed	% Committed	Paid To Date
A	B	C=B/A	D
\$285,000	\$12,714	4.46%	\$5,646
