

# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects

Data Date: 1/21/21

Report Date: 2/5/21

### DESCRIPTION/TEAM

### SCOPE

### PHOTO

**Project Title:** Headquarters R&R

Project Number: 11206  
 BCC District: 02  
 Delivery Method: Construction Management  
 Category: S06-Sheriff - FDO  
 Status: Design  
 Designer: Leo Daly  
 Contractor: Kast Construction  
 Project Manager: Jim Daley

The project consists of the exterior hardening of the entire building consisting of new exterior walls, impact resistant doors and windows, roof replacement and structural tie-ins as well as the R&R of all major building systems and interior renovation of approx. 75% of the building. As part of the project, the Board has also approved the temp. relocation of employees occupying approx. 70% of the space to ensure continuity of operations during the construction, reduce the overall duration of the project and therefore total project cost. This project is funded in:  
 FY 2017 IST \$1,600,000  
 FY 2019 IST \$11,047,000  
 FY 2020 IST \$10,835,000  
 FY 2021 IST \$9,220,000



### SCHEDULE SUMMARY

	Original	Actual
Project Start	3/14/2016	3/14/2016
Design Start	5/9/2017	5/9/2017
Construction Start	1/31/2019	
Substantial Completion	1/31/2022	
Project Completion	2/28/2022	

### PARTICIPATION



#### Consultant

SBE 24.71%  
 Local 100%  
 WBE N/A  
 MBE N/A

#### Contractor

SBE 12.75%  
 Local 100%  
 WBE N/A  
 MBE N/A

### FUNDING

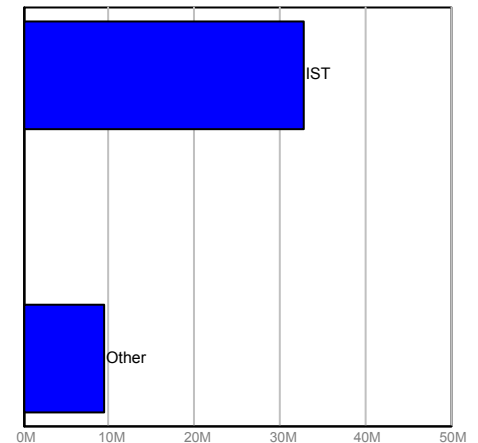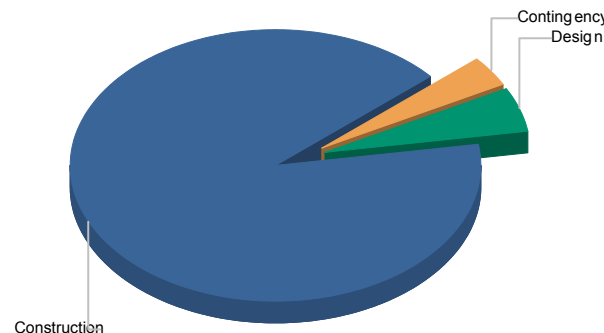

Current Budget

Fund Source

### FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$2,274,200	\$1,891,506	83.17%	\$988,488
Construction	\$38,378,000	\$1,432,043	3.73%	\$816,851
Furniture, Fixtures & Equipment	\$0	\$163,007	0.00%	\$375
Other	\$0	\$27,033	0.00%	\$27,033
Contingency	\$1,418,800	\$0	0.00%	\$0
<b>TOTAL</b>	<b>\$42,071,000</b>	<b>\$3,557,752</b>	<b>8.35%</b>	<b>\$1,832,747</b>

### NOTES


A Type 3 Transfer is scheduled for the February 18 Committee meeting to address project cost overruns. New board date for CM GMP is now 3/09/21 and expected construction start is mid March. Pre-construction inspection by Kast is ongoing. Abatement coordination is scheduled. Permit comments are being answered awaiting issuance of permit. Data and power requirements for small IT rooms is being coordinated. Oxbridge: Building has been turned over to PBSO and FMD. Trane was still having issues with one AHU. Lease has started. All pay apps from Oxbridge have been received and processed. 2300 Vista: Robling has completed all work except for add service work on the 1st floor, need to add a wall. Awaiting permit change. All the walls on the 4th floor were painted.


# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects

Data Date: 1/21/21

Report Date: 2/5/21

DESCRIPTION/TEAM	SCOPE	PHOTO
<p><b>Project Title: Ocean Inlet Park and Marina Renovation</b></p> <p>Project Number: 13367                      BCC District: 04                      Delivery Method: TBD                      Category: P08-Public Building Repair Replacement &amp; Expans                      Status: Design                      Designer: Alan Gerwig &amp; Associates, Inc.                      Contractor: TBD                      Project Manager: Rich Avery</p>	<p>The project consists of the replacement of marina components as well as new components including bulkhead wall, floating docks, floating finger docks, fixed dock, boat lifts, floating wave attenuator, landscaping, and replacement of the current Marina/Restroom and concession buildings. The project will be constructed in two phases. Phase one will consist of marina bulkhead, dock reconstruction and wave attenuator construction. The remaining scope to be completed during phase 2.</p> <p>Total available funding for this project consists of \$2,500,000 FY18 IST funds, \$2,500,000 FY20 Find Grant funds. Future funding consists of \$2,500,000 FY23 IST funds and shown as "Future Funding" within the current budget.</p>	

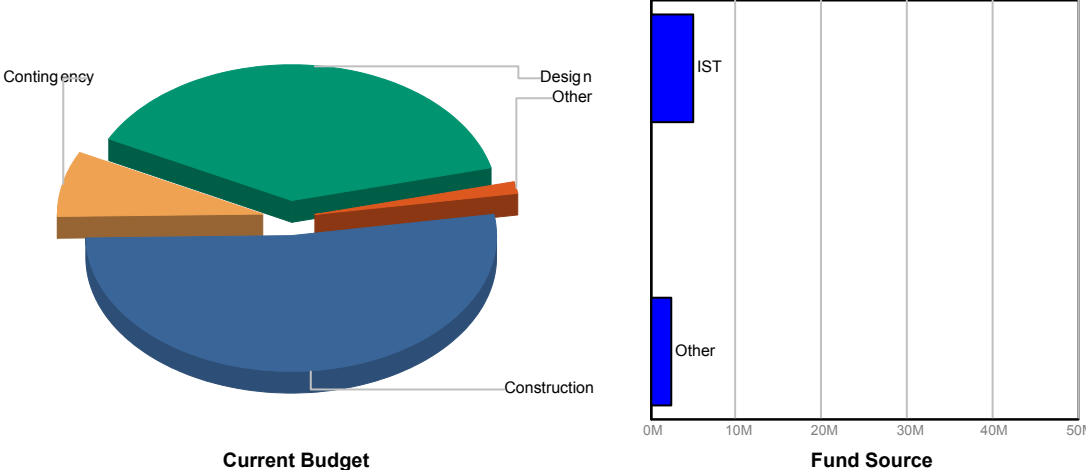SCHEDULE SUMMARY	PARTICIPATION	FUNDING															
<table border="1"> <thead> <tr> <th></th> <th>Original</th> <th>Actual</th> </tr> </thead> <tbody> <tr> <td>Phase I Start</td> <td>2/5/2018</td> <td>2/4/2018</td> </tr> <tr> <td>Design Start</td> <td>10/22/2018</td> <td>10/22/2018</td> </tr> <tr> <td>Construction Start</td> <td>12/3/2019</td> <td></td> </tr> <tr> <td>Substantial Completion</td> <td>11/3/2020</td> <td></td> </tr> </tbody> </table>		Original	Actual	Phase I Start	2/5/2018	2/4/2018	Design Start	10/22/2018	10/22/2018	Construction Start	12/3/2019		Substantial Completion	11/3/2020		<p><b>Consultant</b></p> <p>SBE 82.50%                      Local 100%                      WBE N/A                      MBE N/A</p> <p><b>Contractor</b></p> <p>SBE TBD                      Local TBD                      WBE TBD                      MBE TBD</p>	
	Original	Actual															
Phase I Start	2/5/2018	2/4/2018															
Design Start	10/22/2018	10/22/2018															
Construction Start	12/3/2019																
Substantial Completion	11/3/2020																

FINANCIAL SUMMARY				
	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$2,885,300	\$246,509	8.54%	\$246,509
Construction	\$3,906,200	\$0	0.00%	\$0
Other	\$108,500	\$82,207	75.77%	\$82,207
Contingency	\$600,000	\$0	0.00%	\$0
<b>TOTAL</b>	<b>\$7,500,000</b>	<b>\$328,716</b>	<b>4.38%</b>	<b>\$328,716</b>

**NOTES**




No status change. The project has been advertised and has been posted on VSS on 01/04/2021. Bids are due on Feb. 24, 2021.

# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects


Data Date: 1/21/21

Report Date: 2/5/21

DESCRIPTION/TEAM	SCOPE	PHOTO
<p><b>Project Title: Evidence Building</b></p> <p>Project Number: 14218                      BCC District: 02                      Delivery Method: Construction Management                      Category: S06-Sheriff - FDO                      Status: Design                      Designer: Leo Daly                      Contractor: Pirtle Construction                      Project Manager: Mike McPherson</p>	<p>The project consists of a new 2-story Evidence Storage/Crime Scene/Crime Lab Facility (Approximately 87,000 GSF) and a 12,000 GSF metal building for impound vehicle storage. The main facility will house property seized by the Sheriff's Office, Administrative Offices, Evidence Processing via the crime scene investigation unit and the crime lab. Monitored cameras, motion detectors, and restricted access with electronic logging will be provided. The facility will accommodate secure vehicle garage bays that can store large vehicles (i.e. 56' long trailers) holding evidence for investigation or transport. Site Development (16 Acres) to include user parking (public, booking officers &amp; staff), a fenced/gated impound lot (350 surface spaces) and a limited area of covered parking.</p>	 <p style="text-align: center;">  <span style="margin-left: 20px;">Palm Beach County Sheriff's Office Forensic Facility</span>  <span style="margin-left: 5px;">04-18-20</span> </p>

SCHEDULE SUMMARY		
	Original	Actual
Substantial Completion	11/5/2019	10/30/2020
Project Completion	11/26/2019	
Project Start	3/30/2016	12/21/2016
Design Start	6/28/2017	6/28/2017
Construction Start	7/5/2018	4/29/2019

PARTICIPATION	
<b>Consultant</b>	
SBE	33.21%
Local	78.96%
WBE	N/A
MBE	N/A
<b>Contractor</b>	
SBE	21.60%
Local	55%
WBE	N/A
MBE	N/A

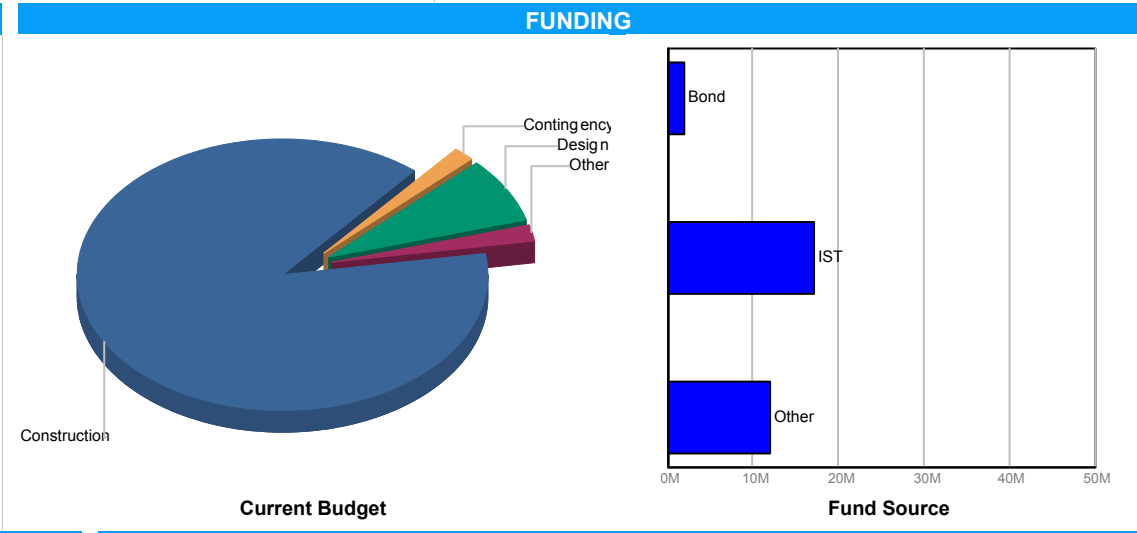

FINANCIAL SUMMARY				
	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$2,461,526	\$2,357,013	95.75%	\$1,939,523
Construction	\$27,680,589	\$27,491,339	99.32%	\$19,002,358
Furniture, Fixtures & Equipment	\$0	\$0	0.00%	\$0
Other	\$602,158	\$192,346	31.94%	\$192,346
Contingency	\$492,268	\$3,672	0.75%	\$3,672
<b>TOTAL</b>	<b>\$31,236,542</b>	<b>\$30,044,370</b>	<b>96.18%</b>	<b>\$21,137,899</b>

**NOTES**

The punch list is complete. However, the change of the roof flashing still being done. Final change orders still in progress. A positive balance is anticipated to result, and be the subject of a future transfer. The funding sources for this project are as follows: Bond \$2M, Impact Fees \$6.7M, Ad Valorem \$1.2M, and IST \$21,336,540 for a total Project Budget of \$31,236,542.

# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects

Data Date: 1/21/21

Report Date: 2/5/21

### DESCRIPTION/TEAM

### SCOPE

### PHOTO

**Project Title:** CR 880 Canal Bank Stabilization

Project Number: 1448  
 BCC District: 06  
 Delivery Method: Bid Contract Award  
 Category: C02-CR 880 Canal Bank Stabilization  
 Status: Construction  
 Designer: Wantman Group  
 Contractor: Dickerson Florida, Inc.  
 Project Manager: Holly Knight

This project will repair, restore, and stabilize the embankment along a portion of County Road 880. The South Florida Water Management District's L-13 Canal parallels and is very close to County Road 880. The embankment area for County Road 880 to the canal is minimal. The undermining of the County Road 880 embankment continues due to storm events and increased South Florida Water Management District pumping and has progressively deteriorated. Repair of the embankment is necessary to prevent the eventual collapse of County Road 880 and to ensure the integrity of County Road 880 and provide a safe roadway for the public.  
 IST Funds: FY17 \$1,000,000 FY18 \$2,000,000 FY24 \$2,000,000.



### SCHEDULE SUMMARY

	Original	Actual
Construction Notice to Proceed	6/5/2017	6/5/2017
Phase III Construction Complete	11/2/2017	10/20/2017
Phase IV-Construction Complete	12/1/2018	3/27/2019
Phase IV-Construction Notice to Proceed	6/1/2018	7/9/2018
Phase V-Construction Notice to Proceed	6/1/2019	7/1/2019
Phase V-Construction Complete	12/1/2019	11/20/2019

### PARTICIPATION

#### Consultant

SBE 15%

Local 100%

WBE 0%

MBE 0%

#### Contractor


SBE 23.4%

Local 23.4%

WBE 0%

MBE 0%

### FUNDING

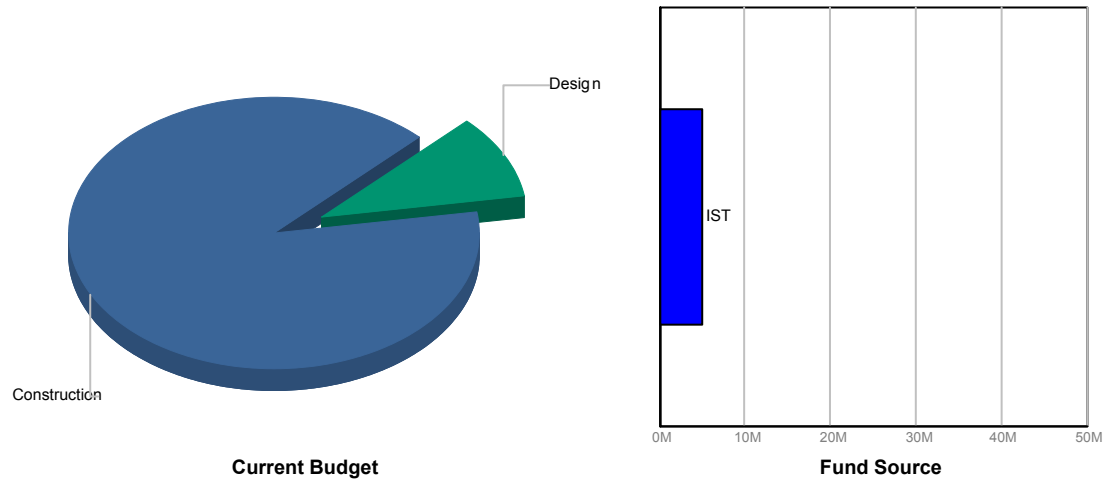

### FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$500,000	\$75,273	15.05%	\$75,273
Construction	\$4,500,000	\$2,537,336	56.39%	\$2,298,981
Contingency	\$0	\$0	0.00%	\$0
<b>TOTAL</b>	<b>\$5,000,000</b>	<b>\$2,612,609</b>	<b>52.25%</b>	<b>\$2,374,255</b>

### NOTES

Phases I and II (constructing adjacent locations) were completed in FY 2015 and FY 2016 using non-IST funding. Phase III construction is funded at \$1,000,000 in FY 2017. Construction for Phases IV & V are funded at \$2,000,000 in FY 2018. Construction is complete for Phases III, IV and V. Project will recommence upon arrival of FY 2024 funding.



# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects

Data Date: 1/21/21

Report Date: 2/5/21

### DESCRIPTION/TEAM

### SCOPE

### PHOTO

**Project Title: Main Detention Center Electronics**

Project Number: 15218  
 BCC District: 02  
 Delivery Method: Construction Management  
 Category: S06-Sheriff - FDO  
 Status: Construction  
 Designer: Leo A. Daly  
 Contractor: Hedrick Brothers Construction  
 Project Manager: Mike McPherson

Phase II - Electronics for the South, East, and West Towers at the Main Detention Center, which have continually operated since the early 1980's. These systems include door controls, intercom, nurse's call system, CCTV, upgrade of EST3 software for fire alarm and new infrastructure for the future expansion of the CCTV system.  
 Main Detention Center Electronics (B594) IST Funding  
 FY 2017 IST \$5,600,000  
 FY 2018 IST \$4,700,000  
 The total Electronics budget is \$11,235,851 of which \$1,021,161 is funded through Ad Valorem.



### SCHEDULE SUMMARY

	Original	Actual
Project Start	7/9/2015	6/9/2015
Design Start	6/21/2016	6/21/2016
Construction Start	3/19/2018	5/17/2018
Substantial Completion	3/15/2022	8/10/2020
Project Completion	6/30/2022	

### PARTICIPATION



#### Consultant

SBE 22.60%  
 Local 67%  
 WBE N/A  
 MBE N/A

#### Contractor

SBE 76.79%  
 Local 80%  
 WBE N/A  
 MBE N/A

### FUNDING

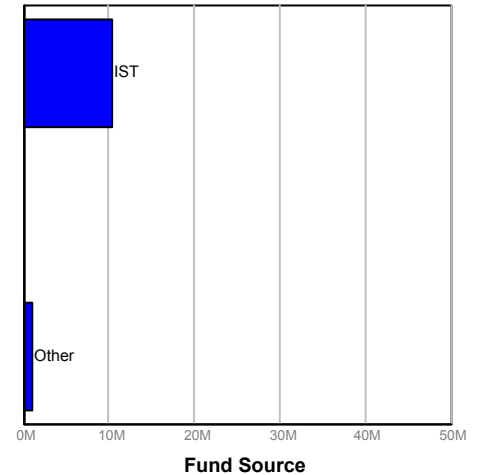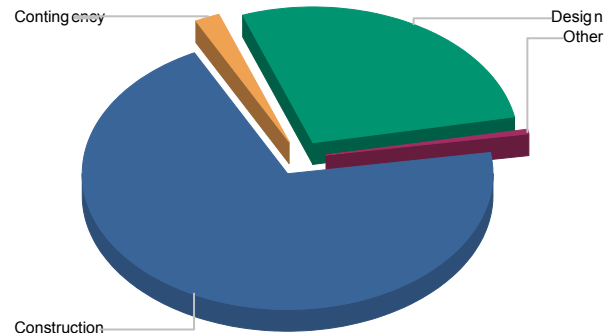

### FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$3,096,507	\$3,053,261	98.60%	\$2,060,774
Construction	\$7,868,421	\$7,141,626	90.76%	\$7,036,538
Furniture, Fixtures & Equipment	\$0	\$0	0.00%	\$0
Other	\$55,740	\$59,101	106.03%	\$59,101
Contingency	\$215,183	\$0	0.00%	\$0
<b>TOTAL</b>	<b>\$11,235,851</b>	<b>\$10,253,988</b>	<b>91.26%</b>	<b>\$9,156,413</b>

### NOTES

We are processing a change order for approval for the credit we are to receive from the construction manager. This positive balance will be the subject of a future transfer.

# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects

Data Date: 1/21/21

Report Date: 2/5/21

### DESCRIPTION/TEAM

### SCOPE

### PHOTO

**Project Title:** Palm Beach Lakes Blvd over FEC R/R

This project will rehabilitate an existing bridge that was built over 50 years ago. The project will improve traffic safety (lane widths, pedestrian barrier, railings) and may involve other improvements such as shoulders, bike lanes, and sidewalks.



Project Number: 1532  
 BCC District: 07  
 Delivery Method: Design CCNA  
 Category: B04-Bridge Modifications  
 Status: Design  
 Designer: HNTB  
 Contractor: TBD  
 Project Manager: Kathleen Farrell


### SCHEDULE SUMMARY

	Original	Actual
Project Start	9/30/2017	9/30/2017
Design Procurement Finish	9/3/2019	12/1/2019
Design Start	4/7/2020	4/7/2020
Design Finish	2/1/2024	
Permit Application	10/1/2022	
Permit Issued	10/1/2023	
Construction Start	1/1/2025	
Construction Finish	10/1/2026	
Project Completion	10/1/2026	

### PARTICIPATION

Consultant	
SBE	36.5%
Local	96%
WBE	TBD
MBE	TBD
Contractor	
SBE	TBD
Local	TBD
WBE	TBD
MBE	TBD

### FUNDING

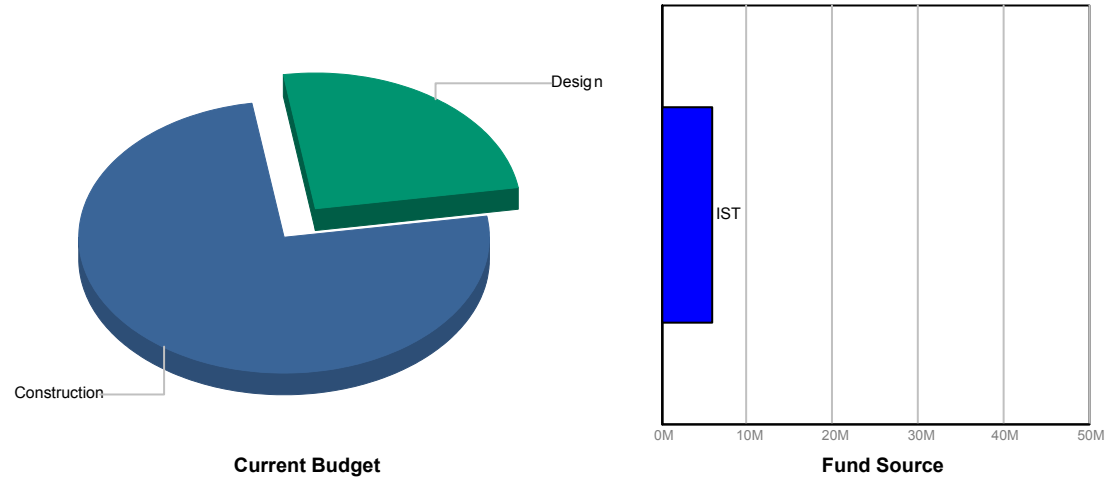

### FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$1,500,000	\$339,665	22.64%	\$136,428
Construction	\$4,500,000	\$603	0.01%	\$603
Other	\$0	\$15,327	0.00%	\$15,327
Contingency	\$0	\$0	0.00%	\$0
<b>TOTAL</b>	<b>\$6,000,000</b>	<b>\$355,596</b>	<b>5.93%</b>	<b>\$152,358</b>

### NOTES


The project is in the coordination stage with stakeholders including the City of West Palm Beach and the Community Redevelopment Agency to determine scope and design parameters for the rehabilitation of the bridge superstructure. This project is funded for design in FY 2017. Construction is currently included in the plan for FY 2021. The first phase of design (Study & Stakeholder Coordination) started on 4/7/2020.



# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects

Data Date: 1/21/21

Report Date: 2/5/21

DESCRIPTION/TEAM	SCOPE	PHOTO
<p><b>Project Title:</b> Sections of Jog Road</p> <p>Project Number: 1537</p> <p>BCC District: Multiple</p> <p>Delivery Method: Annual Striping Contract</p> <p>Category: S16-Striping</p> <p>Status: Construction</p> <p>Designer: N/A</p> <p>Contractor: Oglesby</p> <p>Project Manager: Larry Kelly</p>	<p>This project consists of restriping sections of Jog Road.</p> <p>FY 2017 \$350,000</p> <p>FY 2021 \$150,000</p> <p>FY 2022 \$100,000</p> <p>FY 2023 \$100,000</p> <p>FY 2024 \$200,000</p> <p>FY 2026 \$200,000</p>	

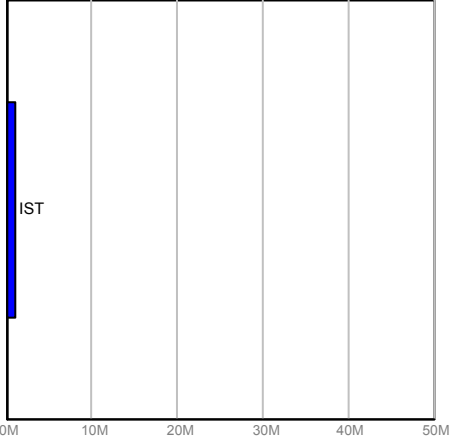SCHEDULE SUMMARY	PARTICIPATION	FUNDING																								
<table border="1"> <thead> <tr> <th></th> <th>Original</th> <th>Actual</th> </tr> </thead> <tbody> <tr> <td>10th Avenue N. to Summit Complete</td> <td>1/22/2018</td> <td>1/22/2018</td> </tr> <tr> <td>Summit to Gun Club Complete</td> <td>9/20/2017</td> <td>9/20/2017</td> </tr> <tr> <td>PGA to Hood Complete</td> <td>10/31/2017</td> <td>10/31/2017</td> </tr> <tr> <td>Wallis to Roebuck Complete</td> <td>3/7/2018</td> <td>3/7/2018</td> </tr> <tr> <td>Glades to NW 55th St.</td> <td>3/19/2019</td> <td>3/19/2019</td> </tr> <tr> <td>Gateway to S. of Hypoluxo Complete</td> <td>12/17/2018</td> <td>10/18/2018</td> </tr> <tr> <td>Hood to Donald Ross</td> <td>12/2/2020</td> <td>12/12/2020</td> </tr> </tbody> </table>		Original	Actual	10th Avenue N. to Summit Complete	1/22/2018	1/22/2018	Summit to Gun Club Complete	9/20/2017	9/20/2017	PGA to Hood Complete	10/31/2017	10/31/2017	Wallis to Roebuck Complete	3/7/2018	3/7/2018	Glades to NW 55th St.	3/19/2019	3/19/2019	Gateway to S. of Hypoluxo Complete	12/17/2018	10/18/2018	Hood to Donald Ross	12/2/2020	12/12/2020	<p><b>Consultant</b></p> <p>SBE N/A</p> <p>Local N/A</p> <p>WBE N/A</p> <p>MBE N/A</p> <p><b>Contractor</b></p> <p>SBE 61%</p> <p>Local 61%</p> <p>WBE 0%</p> <p>MBE 0%</p>	<div style="text-align: center;">  <p>Construction</p> <p><b>Current Budget</b></p> </div> <div style="text-align: center;">  <p><b>Fund Source</b></p> </div>
	Original	Actual																								
10th Avenue N. to Summit Complete	1/22/2018	1/22/2018																								
Summit to Gun Club Complete	9/20/2017	9/20/2017																								
PGA to Hood Complete	10/31/2017	10/31/2017																								
Wallis to Roebuck Complete	3/7/2018	3/7/2018																								
Glades to NW 55th St.	3/19/2019	3/19/2019																								
Gateway to S. of Hypoluxo Complete	12/17/2018	10/18/2018																								
Hood to Donald Ross	12/2/2020	12/12/2020																								

FINANCIAL SUMMARY				
	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$0	\$0	0.00%	\$0
Construction	\$1,100,000	\$363,590	33.05%	\$360,725
Contingency	\$0	\$0	0.00%	\$0
<b>TOTAL</b>	<b>\$1,100,000</b>	<b>\$363,590</b>	<b>33.05%</b>	<b>\$360,725</b>

**NOTES**

Jog Road is a North-South major County thoroughfare. This project consists of re-striping sections of Jog Road. The restriping scheduled for FY2017 has been completed.

# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects

Data Date: 1/21/21

Report Date: 2/5/21

### DESCRIPTION/TEAM

### SCOPE

### PHOTO

**Project Title:** CR 880

Resurfacing approximately 2 miles (4 lane miles) of a portion of County Road 880 from Main Street to S.R. 80 each year.



Project Number: 1539  
 BCC District: 06  
 Delivery Method: Annual Construction Contract  
 Category: R04-Resurfacing  
 Status: Construction  
 Designer: N/A  
 Contractor: Community  
 Project Manager: Mark Kroeger

### SCHEDULE SUMMARY

	Original	Actual
FY 2017 Construction Complete	12/22/2017	12/22/2017
FY 2018 Construction Complete	12/7/2018	11/30/2018
FY 2019 Construction Complete	12/31/2019	11/1/2019
FY 2020 Construction Complete	12/18/2020	12/3/2020
FY2021 Construction Complete	12/17/2021	

### PARTICIPATION


#### Consultant

SBE N/A  
 Local N/A  
 WBE N/A  
 MBE N/A

#### Contractor

SBE 8.7%  
 Local 95.8%  
 WBE 0%  
 MBE 0%

### FUNDING

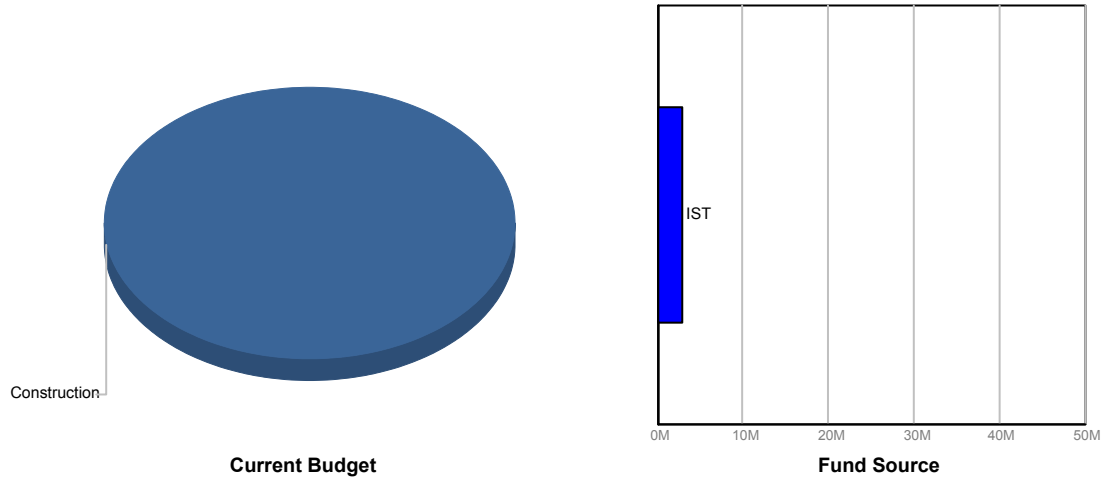

### FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$0	\$2,169	0.00%	\$2,169
Construction	\$3,000,000	\$1,008,474	33.62%	\$1,008,474
Contingency	\$0	\$0	0.00%	\$0
<b>TOTAL</b>	<b>\$3,000,000</b>	<b>\$1,073,975</b>	<b>33.69%</b>	<b>\$1,010,643</b>

### NOTES

County Road 880 is approximately 19 miles in length. This project entails resurfacing a portion (\$300,000) of County Road 880 each year. Construction complete for FY2017 thru 2020.

# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects

Data Date: 1/21/21

Report Date: 2/5/21

### DESCRIPTION/TEAM

### SCOPE

### PHOTO

**Project Title:** Brown's Farms Road

Resurfacing approximately 2 miles (4 lane miles) of a portion of Brown's Farm Road from CR 880 to South Terminus each year.

Project Number: 1540  
 BCC District: 06  
 Delivery Method: Annual Construction Contract  
 Category: R04-Resurfacing  
 Status: Construction  
 Designer: N/A  
 Contractor: Community  
 Project Manager: Mark Kroeger



### SCHEDULE SUMMARY

### PARTICIPATION

### FUNDING


	Original	Actual
FY2021 Construction Complete	12/17/2021	
FY 2020 Construction Complete	12/18/2020	12/2/2020
FY 2019 Construction Complete	12/31/2019	11/1/2019
FY 2017 Construction Complete	12/22/2017	12/22/2017
FY 2018 Construction Complete	12/1/2018	11/30/2018

#### Consultant


SBE N/A  
 Local N/A  
 WBE N/A  
 MBE N/A

#### Contractor

SBE 7.4%  
 Local 94.4%  
 WBE 0%  
 MBE 0%

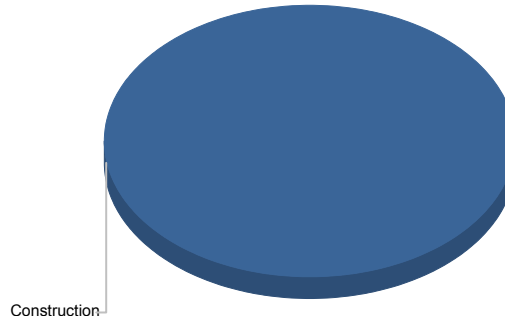

Current Budget

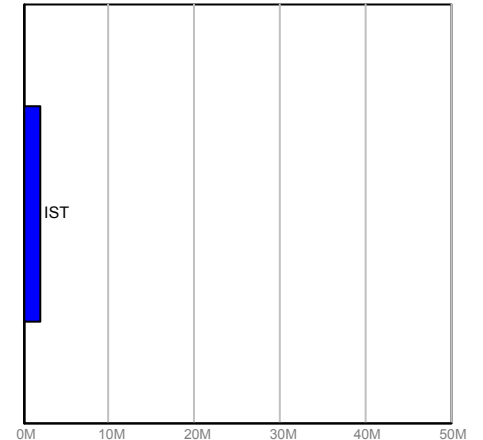

Fund Source

### FINANCIAL SUMMARY

### NOTES

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$0	\$1,515	0.00%	\$1,515
Construction	\$2,000,000	\$810,301	40.52%	\$810,301
Contingency	\$0	\$0	0.00%	\$0
<b>TOTAL</b>	<b>\$2,000,000</b>	<b>\$820,401</b>	<b>40.59%</b>	<b>\$811,816</b>

Brown's Farm Road is approximately 14 miles in length. This project entails resurfacing a portion (\$200,000) of Brown's Farm Road each year. Construction complete for FY2017 thru 2020.



# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects

Data Date: 1/21/21

Report Date: 2/5/21

### DESCRIPTION/TEAM

### SCOPE

### PHOTO

**Project Title:** Prosperity Farms Rd. over SFWMD C-17 Canal (934116)  
**Project Number:** 1555  
**BCC District:** 01  
**Delivery Method:** Design CCNA  
**Category:** B08-Bridge Replacements  
**Status:** Design  
**Designer:** Scalar  
**Contractor:** TBD - (bid)  
**Project Manager:** David Young

This project will replace an existing bridge that was built over 60 years ago. The new bridge will improve traffic safety (lane widths, bike lanes, parapets), improve roadway drainage, and enhance pedestrian sidewalk safety. Note the current bridge is weight restricted.



### SCHEDULE SUMMARY

	Original	Actual
Design Contract Notice to Proceed	11/19/2019	11/19/2019
Design Completion	2/1/2022	
Construction Bid Date	6/1/2022	
Construction Start	10/1/2022	
Construction Complete	10/1/2024	

### PARTICIPATION



#### Consultant

SBE 98%  
 Local 100%  
 WBE 0%  
 MBE 0%

#### Contractor

SBE TBD  
 Local TBD  
 WBE TBD  
 MBE TBD

### FUNDING

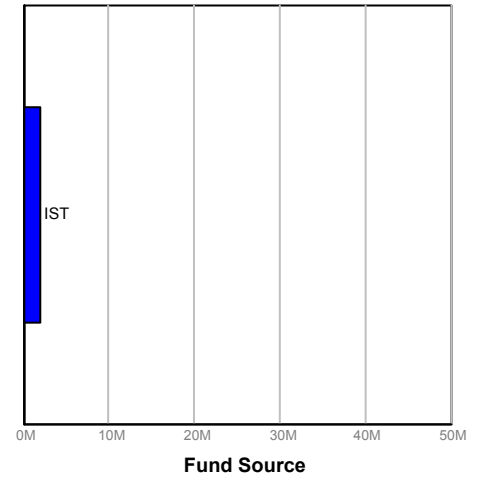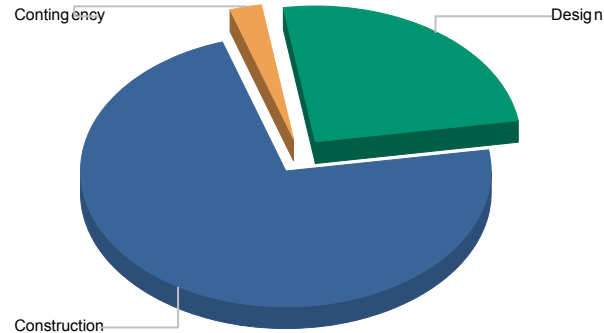

### FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$500,000	\$480,922	96.18%	\$172,149
Construction	\$1,450,000	\$5,003	0.35%	\$5,003
Contingency	\$50,000	\$8,365	16.73%	\$8,205
<b>TOTAL</b>	<b>\$2,000,000</b>	<b>\$494,290</b>	<b>24.71%</b>	<b>\$185,356</b>

### NOTES

This project is under design. Construction is funded in the plan for FY 2021.

# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects

Data Date: 1/21/21

Report Date: 2/5/21

### DESCRIPTION/TEAM

### SCOPE

### PHOTO

**Project Title:** Belvedere Rd over E-3 canal (934205 & 934206)  
**Project Number:** 1556  
**BCC District:** 02  
**Delivery Method:** Design CCNA  
**Category:** B08-Bridge Replacements  
**Status:** Design  
**Designer:** Stantec  
**Contractor:** TBD (bid)  
**Project Manager:** Kathleen Farrell

This project will replace the existing bridges that were built over 40 years ago. The new bridge(s) will improve traffic safety (lane widths, bike lanes, parapets), update the guardrail system, improve roadway drainage, restore the slope protection, and enhance pedestrian sidewalk safety.



### SCHEDULE SUMMARY

	Original	Actual
Design Contract Notice to Proceed	10/22/2019	10/22/2019
Design Completion	12/1/2021	
Construction Bid Date	3/1/2022	
Construction Start	8/1/2022	
Construction Complete	3/1/2024	

### PARTICIPATION


#### Consultant

SBE 30%  
 Local 100%  
 WBE 0%  
 MBE 0%


#### Contractor

SBE TBD  
 Local TBD  
 WBE TBD  
 MBE TBD

### FUNDING

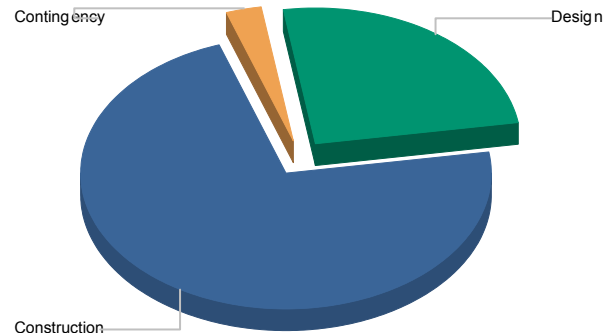

Current Budget

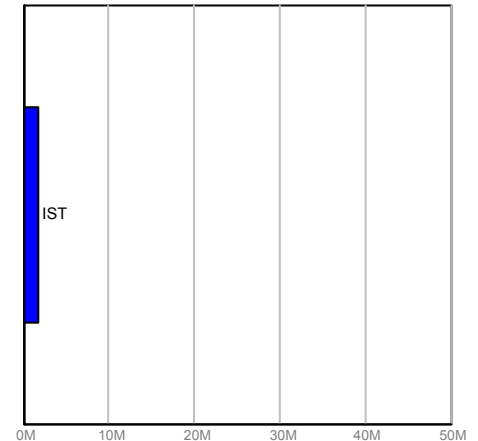

Fund Source

### FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$450,000	\$359,786	79.95%	\$52,085
Construction	\$1,300,000	\$3,226	0.25%	\$3,226
Contingency	\$50,000	\$0	0.00%	\$0
<b>TOTAL</b>	<b>\$1,800,000</b>	<b>\$363,012</b>	<b>20.17%</b>	<b>\$55,311</b>

### NOTES

This project is under design. Construction is funded in the plan for FY 2021.

# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects

Data Date: 1/21/21

Report Date: 2/5/21

### DESCRIPTION/TEAM

### SCOPE

### PHOTO

**Project Title:** Various other locations Countywide

Project Number: 1558  
 BCC District: Multiple  
 Delivery Method: Annual Construction Contract  
 Category: D02-Drainage (Pipe Replacements)  
 Status: Construction  
 Designer: N/A  
 Contractor: Hinterland  
 Project Manager: Mark Kroeger

This project will repair and/or replace existing pipe culverts and drainage structures along various roads and canals Countywide. These repairs are needed in order to properly drain and maintain the various roads and canals in a safe operating condition.



### SCHEDULE SUMMARY

### PARTICIPATION

### FUNDING


	Original	Actual
Jupiter Farms (133rd Rd. & 156th St.)	8/1/2018	3/12/2018
1069 Edgehill Road	8/15/2018	6/12/2018
Limestone Creek & Palm Garden St.	8/1/2018	7/17/2018
3261 Atlantic Road	8/15/2018	7/1/2018
Van Buren Road @ E-3 Canal	8/1/2018	6/15/2018
Jupiter Farms (4 locates)	10/15/2018	8/21/2018
6361 Wood Lake Rd./19650 Red Maple F	10/1/2018	10/1/2018
19598 Trails End Terrace	9/15/2018	8/20/2018
19582 Trails End Terrace	9/1/2018	9/1/2018
6558 Wood Lake Road	9/15/2018	9/14/2018
6126 Wood Lake Road	10/15/2018	12/12/2018
6528 Wood Lake Road	11/1/2018	12/12/2018
6464 Wood Lake Road	11/15/2018	12/18/2018

#### Consultant


SBE N/A  
 Local N/A  
 WBE N/A  
 MBE N/A

#### Contractor

SBE 100%  
 Local 100%  
 WBE 0%  
 MBE 0%



Current Budget

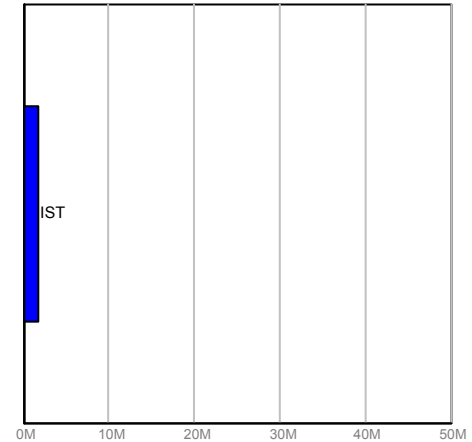

Fund Source

### FINANCIAL SUMMARY

### NOTES

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Construction	\$1,700,000	\$622,701	36.63%	\$444,628
Contingency	\$0	\$0	0.00%	\$0
<b>TOTAL</b>	<b>\$1,700,000</b>	<b>\$622,701</b>	<b>36.63%</b>	<b>\$444,628</b>

This project is funded in:  
 FY 2018 \$500,000, FY 2021 \$500,000, FY 2022 \$200,000  
 FY 2023 \$200,000, FY 2024 \$200,000, FY 2025 \$100,000

The total project is estimated at \$1,700,000.

# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects

Data Date: 1/21/21

Report Date: 2/5/21

### DESCRIPTION/TEAM

### SCOPE

### PHOTO

**Project Title:** Video Detection (80 +/- intersection)

This project will replace the traffic detection at numerous signalized intersections from the existing inductive loop system to video detection. The video detection system is more reliable and easier to maintain.



Project Number: 1580  
 BCC District: Multiple  
 Delivery Method: Annual Traffic Signals Contract  
 Category: S08-Signals and Signal Systems  
 Status: Construction  
 Designer: N/A  
 Contractor: Gerelco  
 Project Manager: Fattoush Jafar

### SCHEDULE SUMMARY

### PARTICIPATION

### FUNDING


	Original	Actual
Woolbright & Hagen Ranch	11/1/2018	4/4/2019
Belvedere & Country Club Road	12/1/2018	4/4/2019
Palm Beach Lakes & Wellesley	1/1/2019	4/4/2019
Military Tr. & Garden Lake	8/1/2018	11/21/2018
Gateway & Renaissance Commons	9/1/2018	4/3/2019
Australian & Turnage	10/1/2018	1/7/2019

#### Consultant


SBE N/A  
 Local N/A  
 WBE N/A  
 MBE N/A

#### Contractor

SBE 0%  
 Local 23%  
 WBE 0%  
 MBE 0%

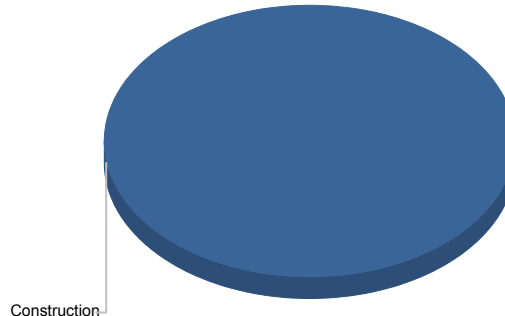

Current Budget

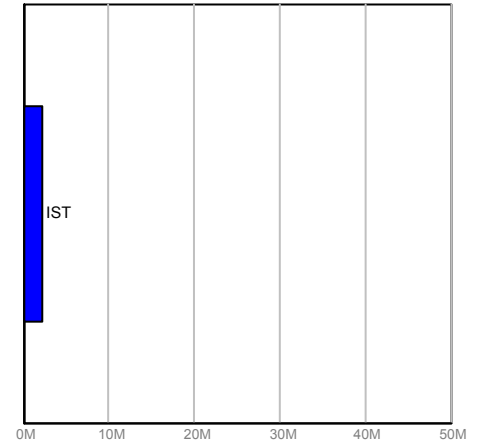

Fund Source

### FINANCIAL SUMMARY

### NOTES

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Construction	\$2,200,000	\$199,000	9.05%	\$199,000
Contingency	\$0	\$0	0.00%	\$0
<b>TOTAL</b>	<b>\$2,200,000</b>	<b>\$199,000</b>	<b>9.05%</b>	<b>\$199,000</b>

Work has been completed at six intersections. This project is funded in:  
 FY 2018 \$200,000  
 FY 2023 \$300,000  
 FY 2024 \$800,000  
 FY 2026 \$900,000  
 The total project is estimated at \$2,200,000.

# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects

Data Date: 1/21/21

Report Date: 2/5/21

### DESCRIPTION/TEAM

### SCOPE

### PHOTO

**Project Title:** FY 2018 Street Lighting LED Replacements - Countywide  
**Project Number:** 1581  
**BCC District:** CW  
**Delivery Method:** Florida Power and Light  
**Category:** S14-Street Lighting  
**Status:** Construction  
**Designer:** Florida Power and Light  
**Contractor:** Florida Power and Light  
**Project Manager:** May Cheng

These projects will replace the high pressure sodium street lights with LED lights. Many of the street lights along County roads are owned and maintained by Florida Power and Light (FPL) with the County paying all the operation and maintenance costs (including power). FPL will be responsible for the final design and installation to convert the street lighting to the newer LED technology, and the County will reimburse FPL all applicable conversion costs. The result will provide a cost savings, better quality illumination, and a more desirable environmental light source.



### SCHEDULE SUMMARY

### PARTICIPATION

### FUNDING


	Original	Actual
Gun Club Road/Bosque to Congress	8/16/2019	8/16/2019
Congress/Okeechobee to Belvedere	8/16/2019	8/16/2019
10th Avenue North/Haverhill to Kirk	12/11/2019	12/11/2019
Community/Haverhill to Military	8/16/2019	8/16/2019
Haverhill Road/WPB City to Haverhill City		
Glades Road/State Road 7 to Boca Rio		
Boynton Beach Boulevard/Turnpike to Kn		
Jog Road/Belvedere to State Road 80		
Forest Hill/Turnpike to Pinehurst & Jog to		
Haverhill/State Road 80 to Lake Worth		
Congress/Lantana to Hypoluxo & Gun Cl		
Gateway/Military to Windward		
Belvedere Road/RPB City to Haverhill Cit		

#### Consultant


SBE N/A  
 Local N/A  
 WBE N/A  
 MBE N/A

#### Contractor

SBE N/A  
 Local N/A  
 WBE N/A  
 MBE N/A

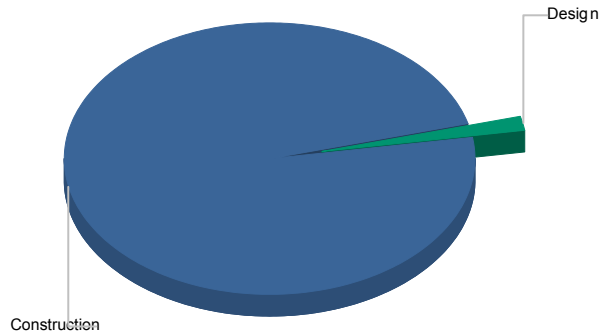

Current Budget

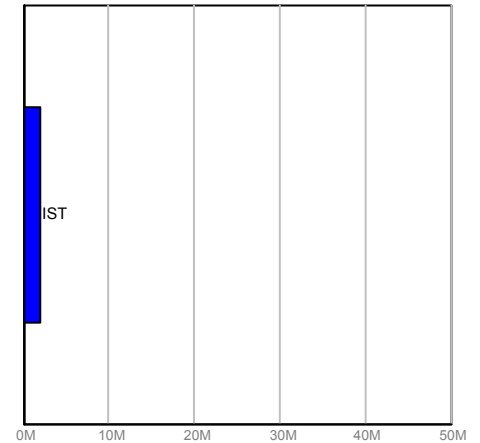

Fund Source

### FINANCIAL SUMMARY

### NOTES

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$30,000	\$18,946	63.15%	\$18,946
Construction	\$1,920,000	\$595,706	31.03%	\$441,997
Contingency	\$0	\$0	0.00%	\$0
<b>TOTAL</b>	<b>\$1,950,000</b>	<b>\$614,652</b>	<b>31.52%</b>	<b>\$460,943</b>

There are 16 street lighting projects (road segments) funded (\$1,950,000) for conversion in FY 2018. All 16 projects have been forwarded to FPL requesting final design and installation. As of 12/1/20, five projects have been completed, and the street lighting along a portion of the Hypoluxo Road project has also been converted.



# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects

Data Date: 1/21/21

Report Date: 2/5/21


### DESCRIPTION/TEAM

### SCOPE

### PHOTO

**Project Title:** CR 880 (Old SR 80) Over C-51 Canal (930940)  
**Project Number:** 1612  
**BCC District:** 06  
**Delivery Method:** Design CCNA  
**Category:** B08-Bridge Replacements  
**Status:** Design  
**Designer:** Alan Gerwig & Assoc.  
**Contractor:** TBD (Bid)  
**Project Manager:** Kathleen Farrell

This project will replace an existing bridge that was built over 80 years ago. The new bridge will improve traffic safety (lane widths and vehicle barrier walls). The current bridge is weight restricted.

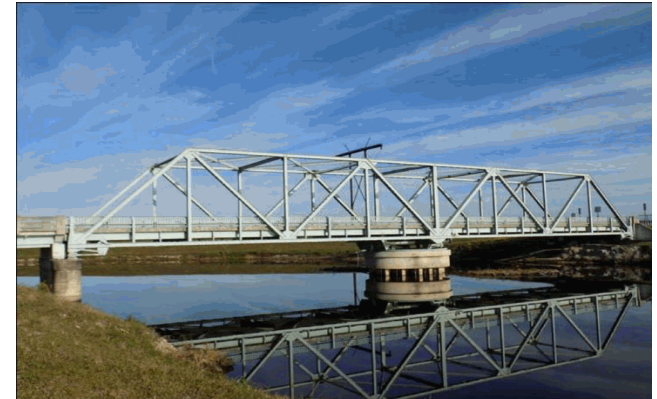

### SCHEDULE SUMMARY

	Original	Actual
Design Contract Notice to Proceed	11/9/2018	11/9/2018
Design Completion	10/28/2021	
Construction Bid Date	2/1/2022	
Construction Start	7/1/2022	
Construction Complete	12/1/2023	

### PARTICIPATION


#### Consultant

SBE 94.3%  
 Local 100%  
 WBE 0%  
 MBE 0%

#### Contractor

SBE TBD  
 Local TBD  
 WBE TBD  
 MBE TBD

### FUNDING

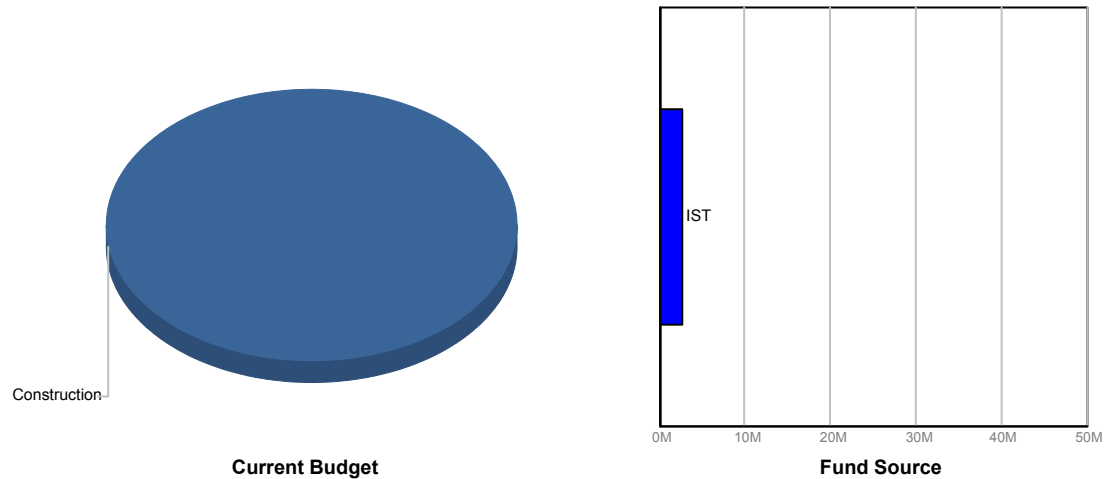

### FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Construction	\$2,700,000	\$0	0.00%	\$0
<b>TOTAL</b>	<b>\$2,700,000</b>	<b>\$0</b>	<b>0.00%</b>	<b>\$0</b>

### NOTES

This project is funded with 5-Year Road Program (RP) funding and IST funding. The project is under design (using 5-Year RP funds). The construction of the project is currently estimated at \$3.5m. The IST partially funds the construction of the project at \$2.7 m in FY 2019. The project is currently scheduled to begin construction in FY22.

# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects

Data Date: 1/21/21

Report Date: 2/5/21

### DESCRIPTION/TEAM

### SCOPE

### PHOTO

**Project Title:** Courthouse Electronics System R&R/Command Center  
**Project Number:** 16208  
**BCC District:** 07  
**Delivery Method:** Construction Management  
**Category:** J02-Judicial  
**Status:** Construction  
**Designer:** TLC Engineering  
**Contractor:** Hedrick Brothers Construction Co., Inc.  
**Project Manager:** Rich Avery

Security Systems replacement at the Main County Courthouse including the Security Management System, Access Control System, CCTV system, Duress System, Intercom, Elevator Override, and Fire Alarm. The Project will also include addressing the emergency egress procedures for the facility, as well as build-out for the expansion of the 4th floor Command Center.

Total IST, and Ad Valorem funding for this project is \$16,449,545; Total IST funds are \$12,999,700, which are comprised of FY17 IST funds of \$1,300,000 and FY18 IST funds of \$8,699,700 and FY 19 IST funds of \$3,000,000. Ad Valorem funds are \$3,449,845



### SCHEDULE SUMMARY

	Original	Actual
Project Start	2/19/2016	2/19/2016
Design Start	2/15/2017	2/15/2017
Construction - Start	11/26/2018	1/7/2019
Substantial Completion	2/1/2021	
Project Completion	4/1/2021	

### PARTICIPATION


#### Consultant

SBE 13.4%  
 Local 100%  
 WBE N/A  
 MBE N/A


#### Contractor

SBE 25%  
 Local 100%  
 WBE N/A  
 MBE N/A

### FUNDING

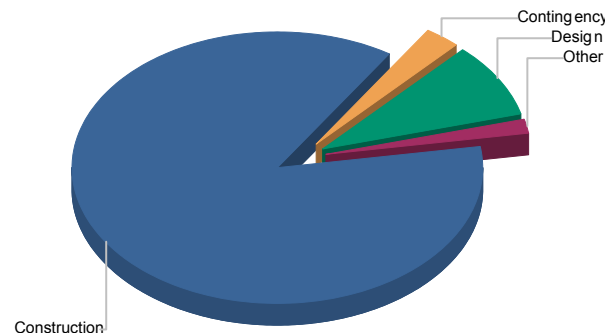

Current Budget

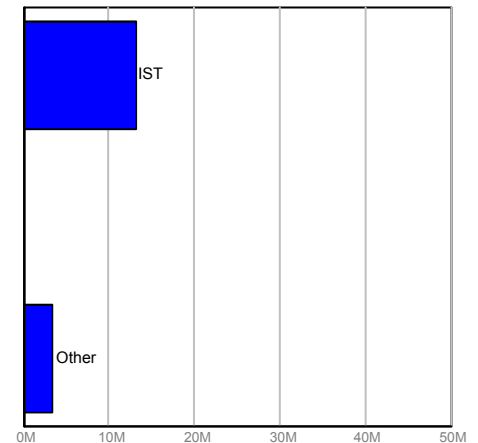

Fund Source

### FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$1,456,336	\$1,346,943	92.49%	\$365,434
Construction	\$14,303,154	\$14,237,577	99.54%	\$12,495,501
Furniture, Fixtures & Equipment	\$0	\$0	0.00%	\$0
Other	\$285,137	\$116,320	40.79%	\$116,320
Contingency	\$469,846	(\$4,546)	-0.97%	\$0
<b>TOTAL</b>	<b>\$16,514,473</b>	<b>\$15,696,295</b>	<b>95.05%</b>	<b>\$12,977,256</b>

### NOTES

Punchlist work continues for the Electronics R&R portion of the project. Work continues on the ISS closet HVAC upgrade, and other approved change orders. Current project completion is anticipated by 4/9/2021.

# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects

Data Date: 1/21/21

Report Date: 2/5/21

### DESCRIPTION/TEAM

### SCOPE

### PHOTO

**Project Title:** 6th Ave. So. over Lake Osborne (LWDD E-4 Canal)(S Br/ East bound) (934307)  
**Project Number:** 1634  
**BCC District:** 03  
**Delivery Method:** Design CCNA  
**Category:** B08-Bridge Replacements  
**Status:** Design  
**Designer:** Stantec  
**Contractor:** TBD (Bid)  
**Project Manager:** David Young

This project will replace an existing bridge that was built over 50 years ago. The new bridge will improve traffic safety (lane widths, bike lanes and barrier walls), improve roadway drainage, and enhance pedestrian sidewalk safety. The new bridge will also provide greater vertical clearance.



### SCHEDULE SUMMARY

	Original	Actual
Design Contract Notice to Proceed	7/17/2018	7/17/2018
Design Completion	12/1/2020	
Construction Bid Date	3/1/2021	
Construction Start	7/1/2021	
Construction Complete	12/1/2022	

### PARTICIPATION


#### Consultant

SBE 25%  
 Local 100%  
 WBE 0%  
 MBE 0%


#### Contractor

SBE TBD  
 Local TBD  
 WBE 0%  
 MBE 0%

### FUNDING

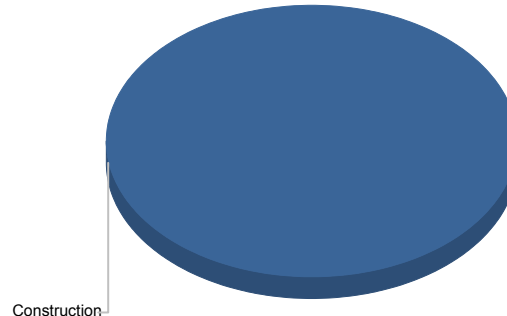

Current Budget

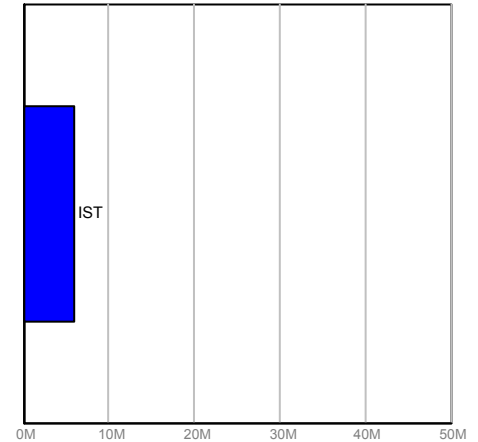

Fund Source

### FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Construction	\$6,000,000	\$0	0.00%	\$0
<b>TOTAL</b>	<b>\$6,000,000</b>	<b>\$0</b>	<b>0.00%</b>	<b>\$0</b>

### NOTES


This project is funded with 5-Year Road Program (RP) funding and IST funding. The project is under design (using 5-Year RP funds). The construction of the project is currently estimated at \$8.5m. The IST partially funds the construction of the project at \$6 m in FY 2020. The project is currently scheduled to begin construction in FY21.

# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects


Data Date: 1/21/21

Report Date: 2/5/21

DESCRIPTION/TEAM	SCOPE	PHOTO
<p><b>Project Title:</b> Hypoluxo Rd. from Military Trail to U.S. 1</p> <p>Project Number: 1663                      BCC District: Multiple                      Delivery Method: Annual Construction Contract                      Category: R04-Resurfacing                      Status: Construction                      Designer: N/A                      Contractor: Ranger                      Project Manager: Thomas Coppini</p>	<p>Resurfacing 3.7 miles (21.2 lane miles) of Hypoluxo Road from Military Trail to US 1.</p> <p>FY 2021 IST \$1,400,000</p>	

SCHEDULE SUMMARY		
	Original	Actual
Milling and Pavement Complete	2/1/2021	
ADA (Curb/Cut Ramps) Complete	4/1/2021	
Traffic Striping Complete	5/1/2021	
Traffic Loops Complete	7/1/2021	

PARTICIPATION	
<b>Consultant</b>	
SBE	N/A
Local	N/A
WBE	N/A
MBE	N/A
<b>Contractor</b>	
SBE	5%
Local	100%
WBE	0%
MBE	0%

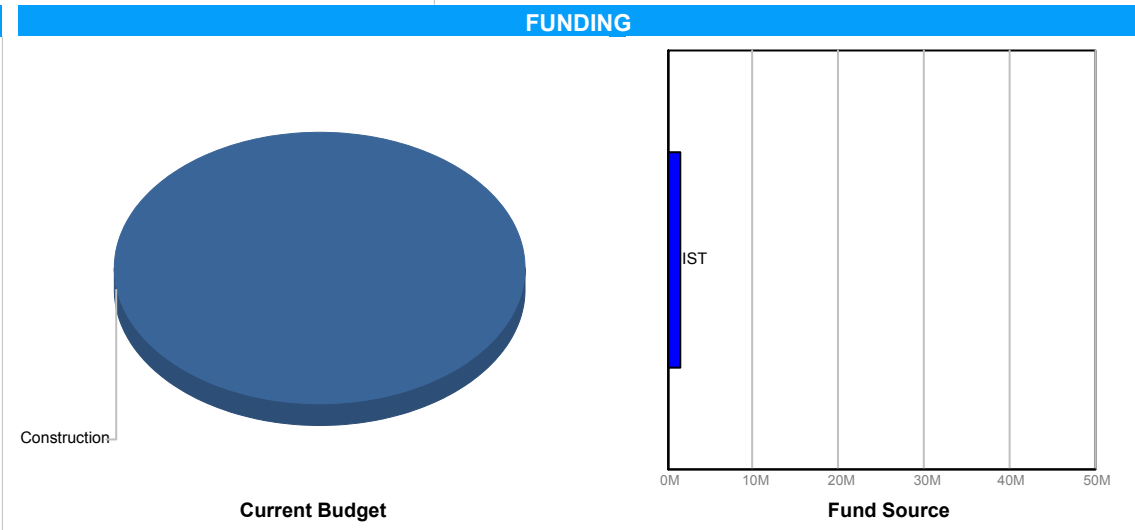

FINANCIAL SUMMARY				
	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Construction	\$1,400,000	\$1,398,500	99.89%	\$0
<b>TOTAL</b>	<b>\$1,400,000</b>	<b>\$1,398,500</b>	<b>99.89%</b>	<b>\$0</b>

**NOTES**


Outstanding work includes milling and paving, updating ADA ramps, restriping the road, and replacing traffic loops.


# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects

Data Date: 1/21/21

Report Date: 2/5/21

DESCRIPTION/TEAM	SCOPE	PHOTO
<p><b>Project Title:</b> Lake Lytal Aquatic Center Replace Public Aquatic Facility</p> <p>Project Number: 17218</p> <p>BCC District: 02</p> <p>Delivery Method: Construction Management at Risk</p> <p>Category: A02-Aquatic Facility Repair and Replacement</p> <p>Status: Design</p> <p>Designer: Harvard Jolly, Inc.</p> <p>Contractor: TBD</p> <p>Project Manager: Rosalyn Acosta</p>	<p>The project entails constructing a new multi-phase Aquatic Complex mainly on undeveloped land along Kirk Rd. within Lake Lytal Park. The existing Pool Facility is to be demolished once the new aquatic center is opened to the public. The major components of the new Aquatic Complex will be a 70 Meter competition pool with dive well, a family water play area, 6-lane warm-up pool, flow riders, slides and building amenities such as restrooms, lockers, concession stand.</p> <p>FY 2017 IST - \$4,000,000 FY 2018 IST - \$2,000,000</p>	 <p style="text-align: center; font-weight: bold; font-size: 1.2em;">LAKE LYTAL FAMILY AQUATIC CENTER</p>

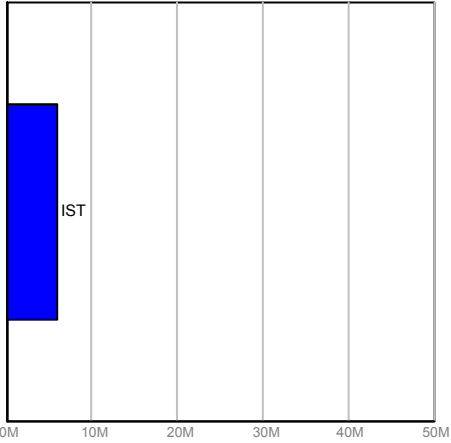SCHEDULE SUMMARY	PARTICIPATION	FUNDING																					
<table border="1"> <thead> <tr> <th></th> <th style="text-align: center;">Original</th> <th style="text-align: center;">Actual</th> </tr> </thead> <tbody> <tr> <td>Project Start</td> <td style="text-align: center;">4/19/2018</td> <td style="text-align: center;">4/19/2018</td> </tr> <tr> <td>Design Start (Master Plan)</td> <td style="text-align: center;">7/10/2018</td> <td style="text-align: center;">7/10/2018</td> </tr> <tr> <td>Design Start (Aquatic Center)</td> <td style="text-align: center;">11/20/2018</td> <td></td> </tr> <tr> <td>Construction Start</td> <td style="text-align: center;">7/1/2019</td> <td></td> </tr> <tr> <td>Substantial Completion</td> <td style="text-align: center;">7/1/2020</td> <td></td> </tr> <tr> <td>Project Completion</td> <td style="text-align: center;">9/1/2020</td> <td></td> </tr> </tbody> </table>		Original	Actual	Project Start	4/19/2018	4/19/2018	Design Start (Master Plan)	7/10/2018	7/10/2018	Design Start (Aquatic Center)	11/20/2018		Construction Start	7/1/2019		Substantial Completion	7/1/2020		Project Completion	9/1/2020		<p><b>Consultant</b></p> <p>SBE 30%</p> <p>Local 100%</p> <p>WBE N/A</p> <p>MBE N/A</p> <p><b>Contractor</b></p> <p>SBE TBD</p> <p>Local TBD</p> <p>WBE TBD</p> <p>MBE TBD</p>	<p style="text-align: center;">Current Budget</p>  <p style="text-align: center;">Fund Source</p>
	Original	Actual																					
Project Start	4/19/2018	4/19/2018																					
Design Start (Master Plan)	7/10/2018	7/10/2018																					
Design Start (Aquatic Center)	11/20/2018																						
Construction Start	7/1/2019																						
Substantial Completion	7/1/2020																						
Project Completion	9/1/2020																						

FINANCIAL SUMMARY				
	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$100,000	\$53,801	53.80%	\$53,801
Construction	\$5,900,000	\$400	0.01%	\$400
Furniture, Fixtures & Equipment	\$0	\$0	0.00%	\$0
Other	\$0	\$37,316	0.00%	\$37,316
Contingency	\$0	\$0	0.00%	\$0
<b>TOTAL</b>	<b>\$6,000,000</b>	<b>\$91,517</b>	<b>1.53%</b>	<b>\$91,517</b>

NOTES

Lease agreement approved by BCC on 1/12/21. Re-group meeting with Parks, CID, the Y, consultants (HJ) and contractor (KL) was held on 2/4/21. CID will work on authorizations for KL and HJ; bi-weekly design development meetings are slated to commence late March 2021 after authorizations are approved.



# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects

Data Date: 1/21/21

Report Date: 2/5/21

### DESCRIPTION/TEAM

### SCOPE

### PHOTO

**Project Title:** Community Park - Paulette Burdick Park  
**Project Number:** 18230  
**BCC District:** CW  
**Delivery Method:** TBD  
**Category:** N02-New Park Development  
**Status:** Design  
**Designer:** Urban Design Kilday Studio  
**Contractor:** TBD  
**Project Manager:** Rosalyn Acosta

Construction of a neighborhood park that will service Cam Estates neighborhood, Meadowbrook and Plantation CCRT areas. The Park will mainly feature a walking pathway, children's playground and basketball courts.

IST Funding included in Current FY Budget: \$1,000,000  
 IST Funding included in FY2023 Budget: \$4,900,000



### SCHEDULE SUMMARY

	Original	Actual
Pre-Scope meeting with User	8/7/2018	8/7/2018
Final Concept Drawings (Parks)	8/15/2018	8/15/2018
Pre-Scope with Consultant	8/29/2018	8/29/2018
Project Start (Due Diligence)	11/1/2018	11/28/2018
Design Start	1/7/2019	12/8/2020
Construction Start	4/1/2019	
Substantial Completion	9/1/2019	
Project Completion	10/1/2019	

### PARTICIPATION

#### Consultant

SBE 100%

Local 100%

WBE N/A

MBE N/A

#### Contractor


SBE TBD

Local TBD

WBE TBD

MBE TBD

### FUNDING

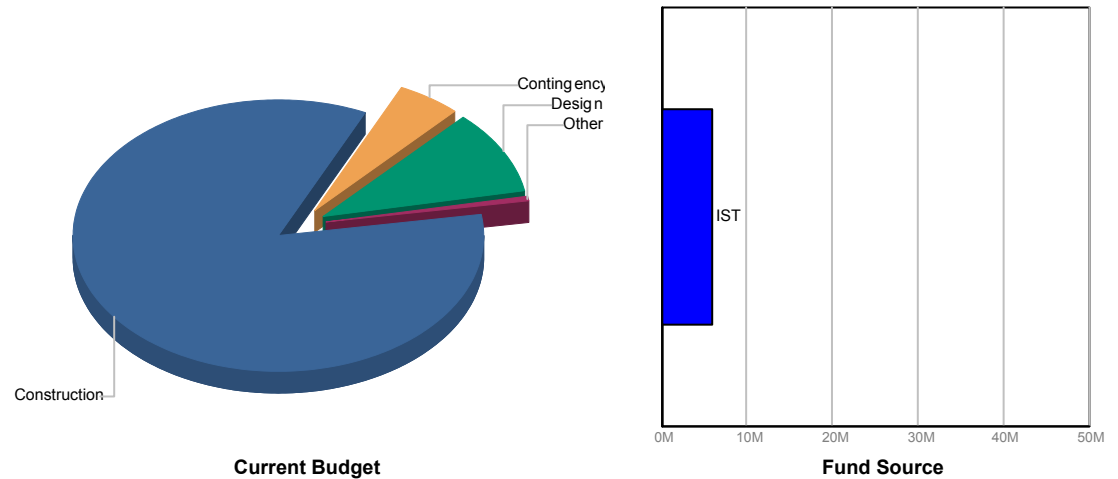

### FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$590,000	\$67,583	11.45%	\$66,942
Construction	\$5,015,000	\$71,236	1.42%	\$71,235
Furniture, Fixtures & Equipment	\$0	\$0	0.00%	\$0
Other	\$32,965	\$33,190	100.68%	\$225
Contingency	\$295,000	\$0	0.00%	\$0
<b>TOTAL</b>	<b>\$5,932,965</b>	<b>\$172,008</b>	<b>2.90%</b>	<b>\$138,402</b>

### NOTES


Design Services proposal from UDS was received and is currently under review. Parks advised CID to put a hold on project after conversations with the adjacent homeowner. Adjacent property has several encroachments to be resolved and will be up for sale in the next few months.


# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects

Data Date: 1/21/21

Report Date: 2/5/21

DESCRIPTION/TEAM	SCOPE	PHOTO
<p><b>Project Title:</b> Lake Worth West Substation</p> <p>Project Number: B607                      BCC District: Multiple                      Delivery Method: Construction Manager at Risk                      Category: S06-Sheriff - FDO                      Status: Design                      Designer: Ohlson Lavoie Collaborative                      Contractor: D Stephenson                      Project Manager: Sunil Jagoo</p>	<p>Provide dedicated office(s) within the HRC2 building (project-19220) for PBSO field personnel's use. Additional interior improvements include a multipurpose room for PBSO training purposes and HRC/community programming, as well as restrooms, circulation area, and other incidental improvements.</p> <p>FY 2019 IST \$1,213,460</p>	

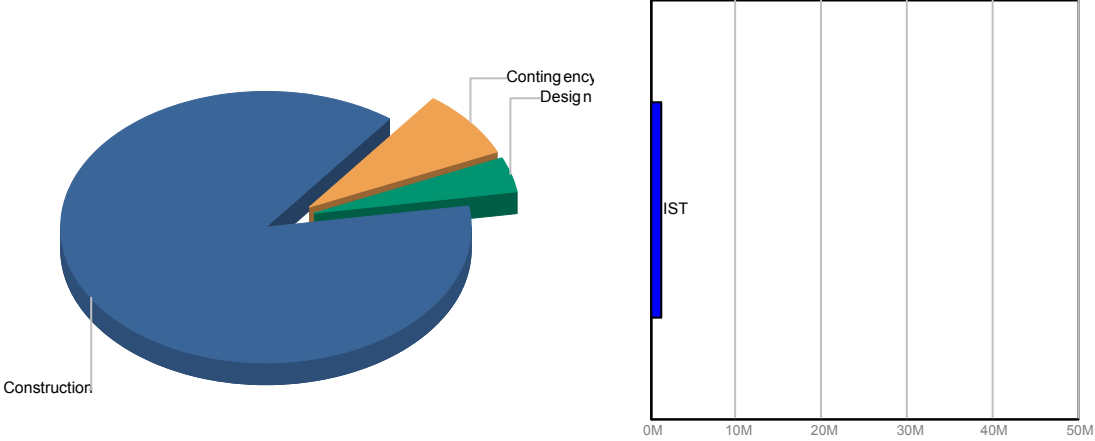SCHEDULE SUMMARY	PARTICIPATION	FUNDING				
<table border="1"> <thead> <tr> <th>Original</th> <th>Actual</th> </tr> </thead> <tbody> <tr> <td colspan="2">Please Refer to Central County Resource</td> </tr> </tbody> </table>	Original	Actual	Please Refer to Central County Resource		<p><b>Consultant</b></p> <p>SBE TBD                      Local TBD                      WBE TBD                      MBE TBD</p> <p><b>Contractor</b></p> <p>SBE TBD                      Local TBD                      WBE TBD                      MBE TBD</p>	 <p style="text-align: center;"><b>Current Budget</b></p> <p style="text-align: center;"><b>Fund Source</b></p>
Original	Actual					
Please Refer to Central County Resource						

FINANCIAL SUMMARY				
	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$50,000	\$2,227	4.45%	\$2,227
Construction	\$1,063,460	\$4,868	0.46%	\$4,868
Contingency	\$100,000	\$0	0.00%	\$0
<b>TOTAL</b>	<b>\$1,213,460</b>	<b>\$7,095</b>	<b>0.58%</b>	<b>\$7,095</b>

**NOTES**

Please refer to the Central County Resource Center report for current status and material project updates.

# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects

Data Date: 1/21/21

Report Date: 2/5/21

### DESCRIPTION/TEAM

### SCOPE

### PHOTO

**Project Title:** Housing Units for Homeless, Extremely Low Income, & Low Income  
**Project Number:** Q001  
**BCC District:** CW  
**Delivery Method:** TBD  
**Category:** H02-Housing  
**Status:** Design  
**Designer:** TBD  
**Contractor:** TBD  
**Project Manager:** Eric McClellan

This project involves the acquisition and renovation of older, possibly run down motel properties into efficiency units for use as temporary or longer term affordable housing for homeless and special populations.

This Project is funded in:  
 FY 2017 - FY 2026 for \$2,550,000 each year for a total project estimate at \$25,500,000.



### SCHEDULE SUMMARY

	Original	Actual
Project Start	9/1/2017	9/1/2017
Construction Start		
Substantial Completion		
Project Completion		
Design Start		
RFP Development Start	12/1/2017	12/1/2017
RFP Release	11/26/2018	12/19/2019
RFP Award	1/12/2021	1/12/2021

### PARTICIPATION


#### Consultant

SBE TBD  
 Local TBD  
 WBE N/A  
 MBE N/A

#### Contractor

SBE TBD  
 Local TBD  
 WBE TBD  
 MBE TBD

### FUNDING

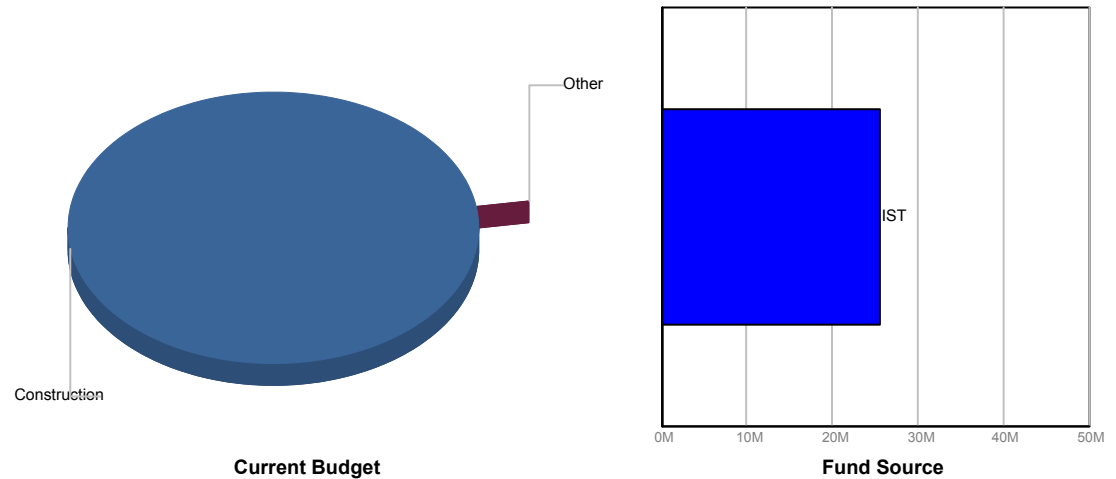

### FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$0	\$6,081	0.00%	\$6,081
Construction	\$25,470,000	\$1,010,805	3.97%	\$269,184
Furniture, Fixtures & Equipment	\$0	\$0	0.00%	\$0
Other	\$30,000	\$42,406	141.35%	\$42,406
Contingency	\$0	\$0	0.00%	\$0
<b>TOTAL</b>	<b>\$25,500,000</b>	<b>\$1,059,292</b>	<b>4.15%</b>	<b>\$317,672</b>

### NOTES


This Project will fund multiple projects over the 10 year period. Direction from the BCC was given on 9/26/2017 to proceed with an affordable housing pilot project. Staff of FD&O, DHES, Community Services, and Administration presented a proposed Project Plan for the remainder of the funding at a BCC Workshop on February 26, 2019 and received direction. The RFP for the Cottage Homes pilot project was awarded by the BCC to the WPB Housing Authority on January 12, 2021. A&E contracting by the WPBHA is now in progress. An allocation of \$1M toward renovation of a non-congregate shelter in Pahokee was approved by the BCC on Sept. 15, 2020.

# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects


Data Date: 1/21/21

Report Date: 2/5/21

DESCRIPTION/TEAM	SCOPE	PHOTO
<p><b>Project Title:</b> Vehicle Replacement</p> <p>Project Number: Q007                      BCC District: Multiple                      Delivery Method: Direct Purchase                      Category: S04-Sheriff                      Status: Construction                      Designer: N/A                      Contractor: N/A                      Project Manager: Isami Ayala-Collazo</p>	<p>This project funds the replacement of PBSO public safety vehicles and related equipment (other than radios), tools and/or services.</p> <p>FY 18 Funds: \$3,650,513                      FY 19 Funds: \$3,650,513                      FY 20 Funds: \$3,650,514                      FY 24 Funds: \$1,669,963</p>	

SCHEDULE SUMMARY		
	Original	Actual
1 Project Start	10/1/2018	5/1/2018
2 Project Completion	9/30/2024	

PARTICIPATION	
<b>Consultant</b>	
SBE	N/A
Local	N/A
WBE	N/A
MBE	N/A
<b>Contractor</b>	
SBE	N/A
Local	N/A
WBE	N/A
MBE	N/A

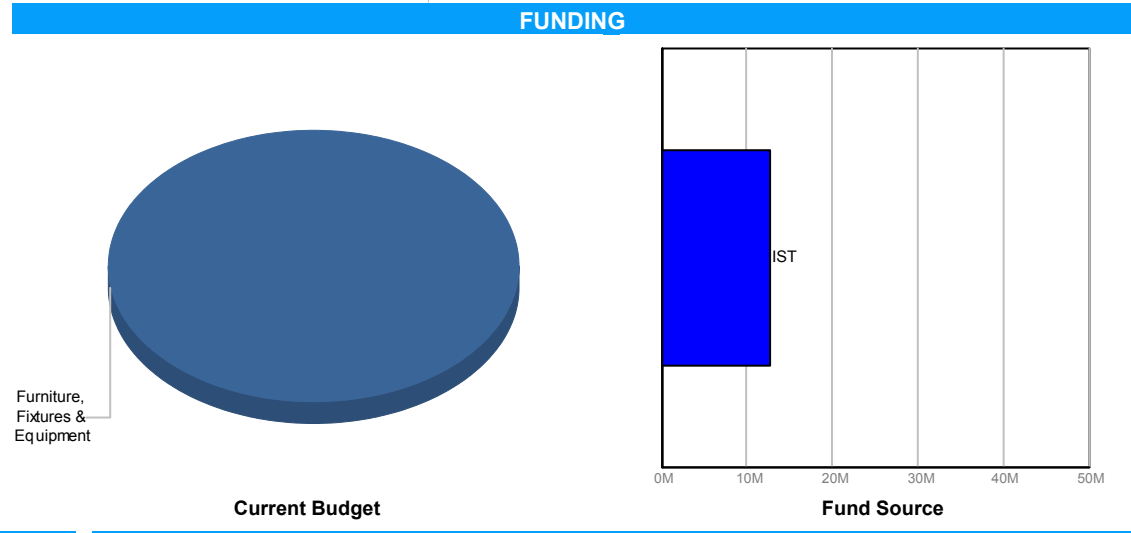

FINANCIAL SUMMARY				
	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Furniture, Fixtures & Equipment	\$12,621,503	\$7,871,863	62.37%	\$7,871,863
Other	\$0	\$0	0.00%	\$0
<b>TOTAL</b>	<b>\$12,621,503</b>	<b>\$7,871,863</b>	<b>62.37%</b>	<b>\$7,871,863</b>

**NOTES**

Prioritization, identification and cost of specific assets are determined by the Sheriff's Office with administration support being performed by FD&O through a Project Funding Agreement with the County.

# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects

Data Date: 1/21/21

Report Date: 2/5/21

### DESCRIPTION/TEAM

### SCOPE

### PHOTO

**Project Title:** Animal Care & Control

Project Number: Q008  
 BCC District: CW  
 Delivery Method: Construction Manager at Risk  
 Category: G02-General Government Facilities  
 Status: Design  
 Designer: PGAL  
 Contractor: Wharton-Smith  
 Project Manager: Rich Avery

The Animal Care & Control Renovation & Expansion project for the Belvedere Rd. campus includes: renovations to existing buildings for improved functionality; possible replacement of non-air conditioned kennel buildings with air-conditioned kennel buildings pending evaluation, pricing and approval; and the creation of new spaces necessary to facilitate current and future projected operational needs. The cost of the project includes cost-estimating services necessary in order to validate the project scope, which was derived jointly by FDO & the ACC Division via a needs assessment and programming document, as well as interim arrangements to sustain continuous operations during construction.



### SCHEDULE SUMMARY

	Original	Actual
Commence Design Comparative Study	7/24/2019	7/24/2019
PROGRAMMING	10/1/2018	10/1/2018
Design Start	2/3/2020	12/2/2020
Construction Start	12/1/2020	
Substantial Completion	7/3/2023	

### PARTICIPATION


#### Consultant

SBE 20%  
 Local 100%  
 WBE N/A  
 MBE N/A


#### Contractor

SBE 13.04%  
 Local 13.04%  
 WBE 13.04%  
 MBE 13.04%

### FUNDING

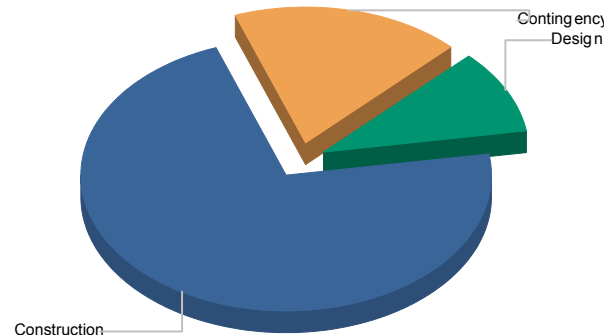

Current Budget

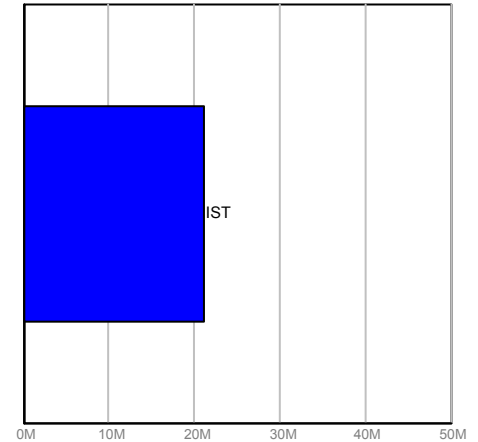

Fund Source

### FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$2,100,000	\$868,205	41.34%	\$213,948
Construction	\$15,120,000	\$213,791	1.41%	\$175,709
Contingency	\$3,780,000	\$0	0.00%	\$0
<b>TOTAL</b>	<b>\$21,000,000</b>	<b>\$1,081,996</b>	<b>5.15%</b>	<b>\$389,657</b>

### NOTES

The consultant continues with their due diligence and design efforts. The next design meeting will take place on 2/10/2021.



# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects

Data Date: 1/21/21

Report Date: 2/5/21

### DESCRIPTION/TEAM

### SCOPE

### PHOTO

**Project Title:** Central County Housing Resource Center  
**Project Number:** Q009  
**BCC District:** CW  
**Delivery Method:** Construction Manager at Risk  
**Category:** H02-Housing  
**Status:** Design  
**Designer:** Ohlson Lavoie Collaborative  
**Contractor:** D Stephenson  
**Project Manager:** Sunil Jagoo

The Homeless Resource Center 2 (HRC 2) is to provide an effective Crisis Response System that provides immediate and easy access to safe and decent temporary shelter to County residents that need it and aims to re-house people as quickly as possible while receiving wrap-around social services. The facility will compliment the County's existing Senator Philip D. Lewis Center in West Palm Beach and will consist of approximately 19,000 square feet to support 74 client beds, dining and service delivery/office areas, restrooms, laundry facilities, an intake lobby, and other incidental interior and exterior improvements. Co-located within the facility will be the improvements identified in the IST Project Plan titled PBSO Lake Worth West Substation.



### SCHEDULE SUMMARY

	Original	Actual
Program Development	11/1/2017	11/1/2017
Public Outreach	2/1/2019	2/1/2019
Design Team Solicitation	5/1/2019	9/30/2020
CM Solicitation	9/1/2019	11/26/2019
Schematic Design	11/11/2019	1/31/2020
Design Development	5/1/2020	9/28/2020
Construction Documents	10/1/2020	
Permitting	1/1/2021	
Construction	6/1/2021	
CO/Substantial Completion	9/1/2022	
Occupancy	10/3/2022	

### PARTICIPATION


**Consultant**

- SBE 0%
- Local 25%
- WBE 0%
- MBE 0%

**Contractor**

- SBE TBD
- Local TBD
- WBE TBD
- MBE TBD

### FUNDING

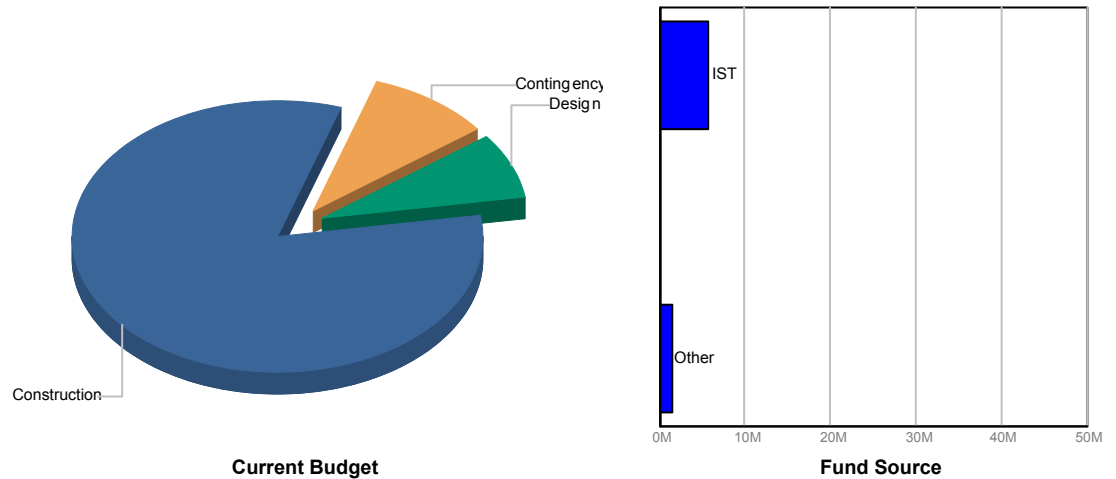

### FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$550,000	\$7,945	1.44%	\$7,795
Construction	\$5,874,843	\$29,605	0.50%	\$29,605
Contingency	\$700,000	\$0	0.00%	\$0
<b>TOTAL</b>	<b>\$7,124,843</b>	<b>\$37,550</b>	<b>0.53%</b>	<b>\$37,400</b>

### NOTES

Construction cost estimate is over budget so a revised construction cost estimate was requested with some modification to the drawings to save costs. Awaiting the revised cost estimate. Preparation of Construction Documents is in progress. Funding includes \$5.7 M from IST in FY19 and CDBG funds in the total amount of \$1,424,843

# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects

Data Date: 1/21/21

Report Date: 2/5/21

### DESCRIPTION/TEAM

### SCOPE

### PHOTO

**Project Title:** South County Administrative Complex

Project Number: Q010  
 BCC District: 07  
 Delivery Method: Varies  
 Category: G02-General Government Facilities  
 Status: Design  
 Designer: Varies  
 Contractor: Varies  
 Project Manager: Eric McClellan

This project funds essential Renewal and Replacement (R&R) needs to sustain the continuous operation of this 40+ year old complex prior to its future redevelopment. As such there is no defined scope of work. Any funds remaining at such time that redevelopment is funded would be utilized toward professional design services for the redevelopment. Funding includes \$3M each in FY 2020 and FY 2021, for a total of \$6M.



### SCHEDULE SUMMARY

### PARTICIPATION

### FUNDING

Original	Actual
N/A. See notes for current activity.	


#### Consultant

SBE 100%  
 Local 100%  
 WBE 78.6%  
 MBE 0%


#### Contractor

SBE TBD  
 Local TBD  
 WBE TBD  
 MBE TBD

Construction



Current Budget

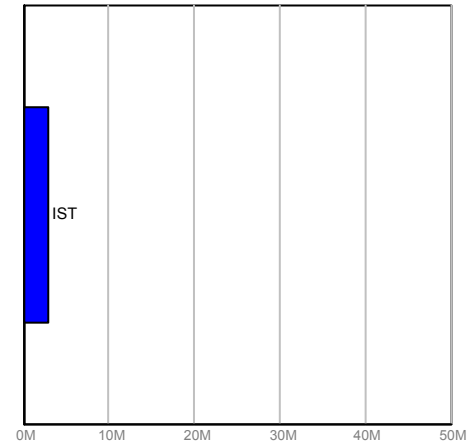

Fund Source

### FINANCIAL SUMMARY

### NOTES

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Construction	\$3,000,000	\$69,471	2.32%	\$4,854
Other	\$0	\$0	0.00%	\$0
<b>TOTAL</b>	<b>\$3,000,000</b>	<b>\$69,471</b>	<b>2.32%</b>	<b>\$4,854</b>

Paved vehicular surfaces throughout the complex are in need of R&R. Reconfiguration of a driveway for improved circulation, consistency with a future master plan and cross access with an adjacent property will be implemented same time to preclude future duplication of work and lost investment. Planning and design services to permit this scope of work are currently being procured.

A scope of work for other R&R needs is currently under development.

# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects

Data Date: 1/21/21

Report Date: 2/5/21

### DESCRIPTION/TEAM

### SCOPE

### PHOTO

**Project Title:** Detention Center Facilities R/R (Phases 3-5)  
**Project Number:** Q019  
**BCC District:** Multiple  
**Delivery Method:** Construction Management  
**Category:** S06-Sheriff - FDO  
**Status:** Construction  
**Designer:** Leo A. Daly  
**Contractor:** Hedrick Brothers Construction  
**Project Manager:** Mike McPherson

Phases 3-5 consist of the East Tower and West Tower which are located at the Main Detention Center. The West Detention Center is located in Belle Glade. The design for both towers and the West Detention Center will require repairing and replacing MEP, Fire Sprinkler System, Low Voltage Systems and interior finishes.  
 Detention Center Facilities R/R (Phases 3-5)  
 FY 2018 IST \$8,500,000  
 FY 2019 IST \$14,700,000  
 FY 2020 IST \$9,800,000



### SCHEDULE SUMMARY

	Original	Actual
East Tower Design Start	11/12/2018	7/11/2019
East Tower Construction Start	10/14/2019	
East Tower Substantial Completion	11/10/2020	

### PARTICIPATION


#### Consultant

SBE 19.88%  
 Local 67%  
 WBE N/A  
 MBE N/A


#### Contractor

SBE 63%  
 Local 84%  
 WBE N/A  
 MBE N/A

### FUNDING

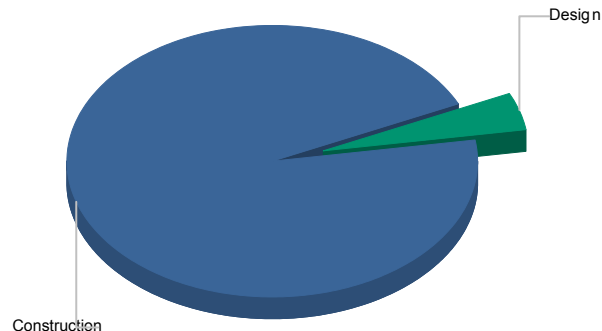

Current Budget

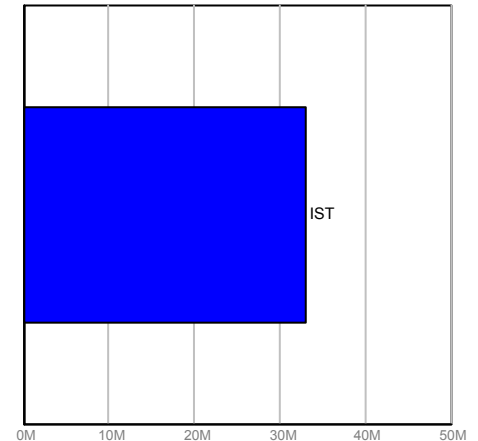

Fund Source

### FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$1,500,000	\$1,949,106	129.94%	\$384,113
Construction	\$31,595,881	\$20,211,765	63.97%	\$7,161,974
Other	\$0	\$1,293,581	0.00%	\$813,240
Contingency	\$0	\$0	0.00%	\$0
<b>TOTAL</b>	<b>\$33,095,881</b>	<b>\$23,454,452</b>	<b>70.87%</b>	<b>\$8,359,327</b>

### NOTES


Main Detention Center East Tower: Construction is on going which includes submittals and RFI's being issued. In addition, electrical, plumbing, and HVAC are ongoing.  
 Main Detention Center West Tower: We are scheduled to receive the design development drawings on Feb. 16.  
 West Detention Center: No status change. The DOP change order is now being processed. The credit from the CM will follow.



# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects

Data Date: 1/21/21

Report Date: 2/5/21

DESCRIPTION/TEAM	SCOPE	PHOTO
<p><b>Project Title:</b> West Boynton Park Athletic Field Renovations Sports Turf</p> <p>Project Number: T002</p> <p>BCC District: 03</p> <p>Delivery Method: TBD</p> <p>Category: A06-Athletic Field Renovations</p> <p>Status: Design</p> <p>Designer: Florida Transportation Engineering</p> <p>Contractor: TBD</p> <p>Project Manager: Stuart Patterson</p>	<p>Replacement of existing grass field turf with synthetic turf on multi-purpose field 1 &amp; 2.</p> <p>Funded:</p> <p>FY 2020 \$1,000,000</p> <p>FY 2023 \$1,000,000</p>	

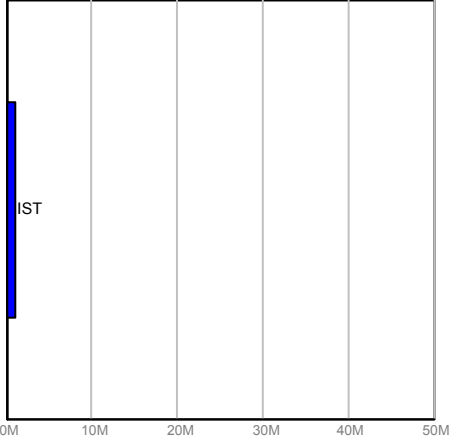SCHEDULE SUMMARY	PARTICIPATION	FUNDING																											
<table border="1"> <thead> <tr> <th></th> <th>Original</th> <th>Actual</th> </tr> </thead> <tbody> <tr> <td>Begin Existing Site Surveys</td> <td>1/29/2020</td> <td>1/29/2020</td> </tr> <tr> <td>Complete Existing Site Surveys</td> <td>6/30/2020</td> <td>5/18/2020</td> </tr> <tr> <td>Design RFP Final Selection</td> <td>10/29/2020</td> <td>10/29/2020</td> </tr> <tr> <td>Finalization of Existing Site Surveys</td> <td>8/30/2020</td> <td>9/18/2020</td> </tr> <tr> <td>Design RFP Proposals Due</td> <td>9/4/2020</td> <td>9/10/2020</td> </tr> <tr> <td>Consultant Contract Issuance</td> <td>12/14/2020</td> <td></td> </tr> <tr> <td>Design Completion</td> <td>7/2/2021</td> <td></td> </tr> <tr> <td>Turf Supplier RFP Proposal Due</td> <td>4/30/2021</td> <td></td> </tr> </tbody> </table>		Original	Actual	Begin Existing Site Surveys	1/29/2020	1/29/2020	Complete Existing Site Surveys	6/30/2020	5/18/2020	Design RFP Final Selection	10/29/2020	10/29/2020	Finalization of Existing Site Surveys	8/30/2020	9/18/2020	Design RFP Proposals Due	9/4/2020	9/10/2020	Consultant Contract Issuance	12/14/2020		Design Completion	7/2/2021		Turf Supplier RFP Proposal Due	4/30/2021		<p><b>Consultant</b></p> <p>SBE TBD</p> <p>Local TBD</p> <p>WBE TBD</p> <p>MBE TBD</p> <p><b>Contractor</b></p> <p>SBE TBD</p> <p>Local TBD</p> <p>WBE TBD</p> <p>MBE TBD</p>	 <p>Current Budget</p>  <p>Fund Source</p>
	Original	Actual																											
Begin Existing Site Surveys	1/29/2020	1/29/2020																											
Complete Existing Site Surveys	6/30/2020	5/18/2020																											
Design RFP Final Selection	10/29/2020	10/29/2020																											
Finalization of Existing Site Surveys	8/30/2020	9/18/2020																											
Design RFP Proposals Due	9/4/2020	9/10/2020																											
Consultant Contract Issuance	12/14/2020																												
Design Completion	7/2/2021																												
Turf Supplier RFP Proposal Due	4/30/2021																												

FINANCIAL SUMMARY				
	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$0	\$7,921	0.00%	\$7,921
Construction	\$1,000,000	\$15,650	1.57%	\$15,650
Furniture, Fixtures & Equipment	\$0	\$0	0.00%	\$0
Other	\$0	\$76	0.00%	\$76
Contingency	\$0	\$0	0.00%	\$0
<b>TOTAL</b>	<b>\$1,000,000</b>	<b>\$23,647</b>	<b>2.36%</b>	<b>\$23,647</b>

**NOTES**

Florida Transportation Engineering selected for engineering services . Contract in process; Due to \$ amount of design fees and complexity of negotiations, Team has decided to revise its schedule & submit for April, 2021 BCC meeting. Turf Supplier RFP to be completed at 50% design. Construction RFP will be developed for each package upon completion of supplier RFP. Anticipated that project will consist of (6) separate bid packages.

# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects


Data Date: 1/21/21

Report Date: 2/5/21

DESCRIPTION/TEAM	SCOPE	PHOTO
<p><b>Project Title:</b> FY2017 Sports Field Lighting Replacement</p> <p>Project Number: T006</p> <p>BCC District: Multiple</p> <p>Delivery Method: Sports Field Lighting Annual</p> <p>Category: S12-Sports Lighting Replacement</p> <p>Status: Design</p> <p>Designer: JLRD Engineers</p> <p>Contractor: Musco</p> <p>Project Manager: Stuart Patterson</p>	<p>Replacement of Sports Field Lighting at Bert Winters Park, Caloosa Park, Glades Pioneer Park, Juno South Park, Jupiter Farms Park, Okeeheelee Park, Pinewoods Park, (Burt Aaronson) South County Regional Park and Westgate Park.</p> <p>IST FY 2017 funds: \$4,100,000.</p>	

SCHEDULE SUMMARY		
	Original	Actual
Project Start	6/29/2017	6/29/2017
Procurement (Light Fixture Vendor)	10/16/2018	10/16/2018
Procurement (Installation Contractor)	10/17/2018	5/9/2019
Final Completion	10/2/2020	
Bidding Package 1	11/6/2019	11/6/2019
Construction Phase 1	2/3/2020	2/3/2020
Construction Completion Phase 1	7/2/2020	8/24/2020
Bidding Package 2	2/13/2020	2/13/2020
Construction Start Phase 2	5/11/2020	
Construction Completion Phase 2	7/17/2020	
Bidding Package 3	3/26/2020	3/26/2020
Construction Start Phase 3	6/15/2020	
Construction Completion Phase 3	8/28/2020	

PARTICIPATION	
<b>Consultant</b>	
SBE	100%
Local	100%
WBE	N/A
MBE	N/A
<b>Contractor</b>	
SBE	0%
Local	75%
WBE	0%
MBE	0%

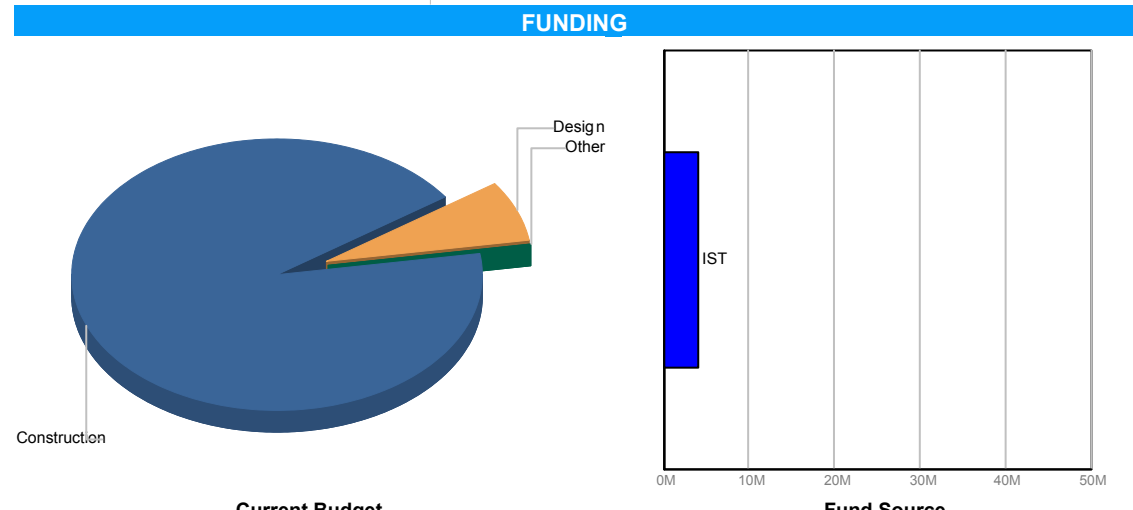

FINANCIAL SUMMARY				
	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$299,161	\$18,683	6.25%	\$18,683
Construction	\$3,800,000	\$3,640,584	95.80%	\$3,062,592
Other	\$839	\$2,952	351.65%	\$2,952
<b>TOTAL</b>	<b>\$4,100,000</b>	<b>\$3,662,218</b>	<b>89.32%</b>	<b>\$3,084,227</b>

**NOTES**

Okeeheelee Park Tennis Courts (Package 1), Jupiter Farms Park (Package 1), Caloosa Park (Package 1), Juno Park (Package 2), & Westgate Park (Package 2): Completed

Bert Winters Park (Package 2): NTP 4/2/2020. SC 1/14/21. Constr. start 12/21/20. In close-out

Glades Pioneer Park (Package 2): All base work complete. Additional SOW executed. Anticipated completion by end of Feb.

S County Regional Park (Package 3): NTP 6/3/2020 SC expected 3/1/21. Currently in Construction Additional SOW executed. Anticipated completion by end of Feb.

Okeeheelee Park Remainder (Package 3) - Project Awarded; NTP Issued 9/9/20; Currently in Construction.

Pinewoods Park (Package 3): NTP 6/1/2020. SC 12/18/20. Currently in Close-out.



# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects

Data Date: 1/21/21

Report Date: 2/5/21

### DESCRIPTION/TEAM

### SCOPE

### PHOTO

**Project Title:** FY2018 Sports Field Lighting Replacement

Project Number: T007  
 BCC District: Multiple  
 Delivery Method: Sports Field Lighting Annual  
 Category: S12-Sports Lighting Replacement  
 Status: Design  
 Designer: JLRD Engineers  
 Contractor: Musco  
 Project Manager: Stuart Patterson

Replacement of Sports Field Lighting at Dyer Park, Lake Charleston Park and (Burt Aaronson) South County Regional Park.  
 IST FY 2018 funds: \$1,200,000.



### SCHEDULE SUMMARY

	Original	Actual
Bidding Package 1	11/6/2019	11/6/2019
Construction Start Phase 1	2/3/2020	2/3/2020
Construction Completion Phase 1	7/2/2020	8/24/2020
Bidding Package 2	2/13/2020	2/13/2020
Construction Start Phase 2	5/11/2020	
Construction Completion Phase 2	7/17/2020	
Bidding Package 3	3/26/2020	3/26/2020
Construction Start Phase 3	6/15/2020	
Construction Completion Phase 3		
Project Start	6/29/2017	6/29/2017
Procurement (Light Fixture Vendor)	10/16/2018	10/16/2018
Procurement (Installation Contractor)	10/17/2018	5/9/2019
Final Completion	10/2/2020	

### PARTICIPATION


#### Consultant

SBE 100%  
 Local 100%  
 WBE N/A  
 MBE N/A

#### Contractor

SBE 0%  
 Local 75%  
 WBE 0%  
 MBE 0%

### FUNDING

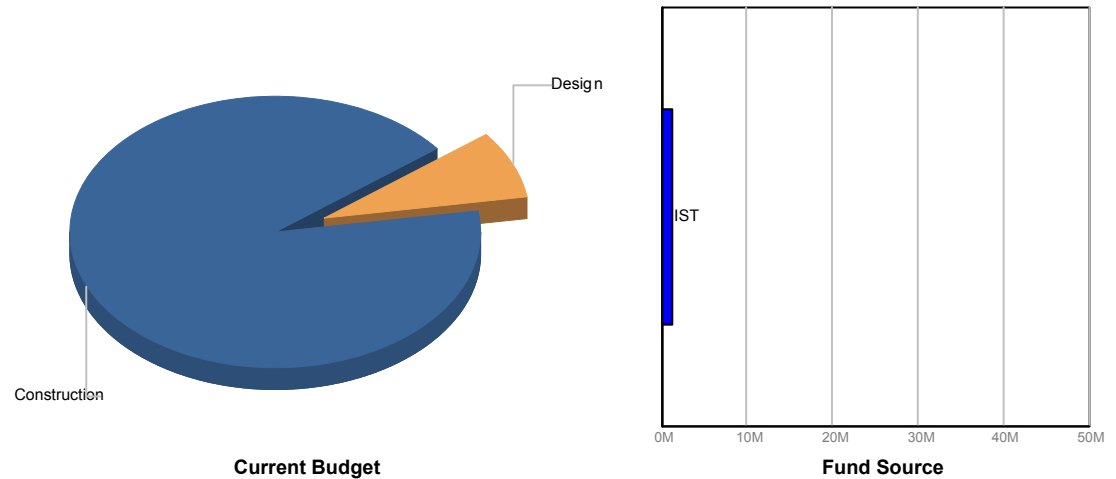

### FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$96,000	\$25,711	26.78%	\$25,711
Construction	\$1,104,000	\$189,668	17.18%	\$91,869
<b>TOTAL</b>	<b>\$1,200,000</b>	<b>\$215,379</b>	<b>17.95%</b>	<b>\$117,579</b>

### NOTES

Lake Charleston Park (Package 1): Completed

S County Regional Park (Package 3): NTP 6/3/2020 SC expected 3/1/21. Currently in Construction Additional SOW executed. Anticipated completion by end of Feb..


Dyer Park (Package 3): No status change. NTP 6/1/2020. Substantial completion dependent on permit issuance. Elec engineering dwgs in progress. Permit submittal TBD



# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects

Data Date: 1/21/21

Report Date: 2/5/21

DESCRIPTION/TEAM	SCOPE	PHOTO
<p><b>Project Title:</b> FY2020 Sports Field Lighting Replacement</p> <p>Project Number: T010</p> <p>BCC District: Multiple</p> <p>Delivery Method: Sports Field Lighting Annual</p> <p>Category: S12-Sports Lighting Replacement</p> <p>Status: Design</p> <p>Designer: JLRD Engineers</p> <p>Contractor: Musco</p> <p>Project Manager: Stuart Patterson</p>	<p>Lake Lytal Athletic Courts, Haverhill Tennis &amp; Racquetball Courts, BASCR Basketball Courts, Duncan Padgett Park Raquetball Courts</p> <p>IST Funds = \$1,300,000.</p>	

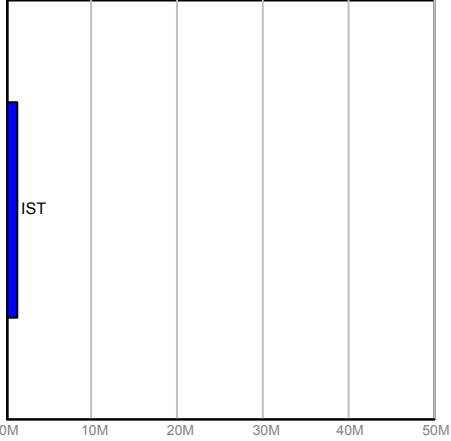SCHEDULE SUMMARY	PARTICIPATION	FUNDING												
<table border="1"> <thead> <tr> <th></th> <th>Original</th> <th>Actual</th> </tr> </thead> <tbody> <tr> <td>Project Start</td> <td>6/29/2017</td> <td>6/29/2017</td> </tr> <tr> <td>Procurement (Light Fixture Vendor)</td> <td>10/16/2018</td> <td>10/16/2018</td> </tr> <tr> <td>Procurement (Installation Contractor)</td> <td>10/17/2018</td> <td></td> </tr> </tbody> </table>		Original	Actual	Project Start	6/29/2017	6/29/2017	Procurement (Light Fixture Vendor)	10/16/2018	10/16/2018	Procurement (Installation Contractor)	10/17/2018		<p><b>Consultant</b></p> <p>SBE 100%</p> <p>Local 100%</p> <p>WBE N/A</p> <p>MBE N/A</p> <p><b>Contractor</b></p> <p>SBE TBD</p> <p>Local TBD</p> <p>WBE TBD</p> <p>MBE TBD</p>	 <p style="text-align: center;"><b>Current Budget</b></p>  <p style="text-align: center;"><b>Fund Source</b></p>
	Original	Actual												
Project Start	6/29/2017	6/29/2017												
Procurement (Light Fixture Vendor)	10/16/2018	10/16/2018												
Procurement (Installation Contractor)	10/17/2018													

FINANCIAL SUMMARY				
	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$130,000	\$70,434	54.18%	\$70,434
Construction	\$1,170,000	\$0	0.00%	\$0
<b>TOTAL</b>	<b>\$1,300,000</b>	<b>\$70,434</b>	<b>5.42%</b>	<b>\$70,434</b>

**NOTES**

Project will be divided into (2) packages: RFP #1, Supply Lighting Fixtures: Musco Lighting selected. Scheduled for BCC approval 1/12/2021 RFP #2, Installation of Lighting Fixtures: CID will develop RFQ packages for each after completion of fixtures RFQ's.



# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects

Data Date: 1/21/21

Report Date: 2/5/21

### DESCRIPTION/TEAM

### SCOPE

### PHOTO

**Project Title: Bert Winters Park Redevelopment**

Project Number: T041  
 BCC District: 01  
 Delivery Method: Annual Contract  
 Category: E02-Existing Park Redevelopment or Expansion  
 Status: Design  
 Designer: Architecture Green  
 Contractor: TBD  
 Project Manager: Sunil Jagoo

Demolish former PBMI building, tennis courts, and playground. Remove lights and poles servicing Field 2. Renovate Baseball Field 1. Construct new regulation 220' x 360' multipurpose field. Construct new 30' x 60' rental pavilion. Construct new playground area. Renovate existing day use dock for public use. Construct new paved parking, curbing, landscaping, sidewalks and picnic areas. Install new underground infrastructure and site lighting.



The project is funded in:  
 FY 2019 IST \$200,000  
 FY 2021 IST \$1,500,000  
 FY 2021 FIND Grant TBD

### SCHEDULE SUMMARY

	Original	Actual
Project Start	8/22/2019	8/22/2019
Asbestos Report Initiated	8/23/2019	8/23/2019
Asbestos Report Completion	10/1/2019	10/1/2019
Demolition Start	11/12/2019	4/16/2020
Demolition Completion	12/5/2019	8/17/2020
Design Completion	TBD	

### PARTICIPATION


#### Consultant

SBE TBD  
 Local TBD  
 WBE N/A  
 MBE N/A


#### Contractor

SBE TBD  
 Local TBD  
 WBE TBD  
 MBE TBD

### FUNDING



Current Budget

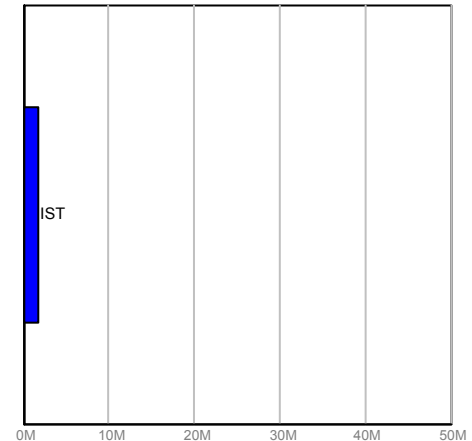

Fund Source

### FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Construction	\$1,700,000	\$103,947	6.11%	\$77,477
Other	\$0	\$1,965	0.00%	\$1,965
Contingency	\$0	\$270	0.00%	\$270
<b>TOTAL</b>	<b>\$1,700,000</b>	<b>\$106,182</b>	<b>6.25%</b>	<b>\$79,712</b>

### NOTES

CSA issued to Consultant, Kick-off meeting held 1/2/2021

# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects

Data Date: 1/21/21

Report Date: 2/5/21

### DESCRIPTION/TEAM

### SCOPE

### PHOTO

**Project Title:** Aqua Crest Pool Facility Replacement

Project Number: T077  
 BCC District: 07  
 Delivery Method: CMR  
 Category: A02-Aquatic Facility Repair and Replacement  
 Status: Design  
 Designer: Ohlson Lavoie Collaborative  
 Contractor: TBD  
 Project Manager: Rosalyn Acosta

The work consist of the design and renovation of the existing Aqua Crest pool facility. The scope includes but is not limited to: pool improvements such as leak detection, re-surface, lane marker replacement, filtration system replacement; pool deck renovations; demolition of wadding pool; new splash pad; relocation of ticketing booth, admin offices, guards room and weight's room; bathroom renovations; new shade structures and Marquee sign.



### SCHEDULE SUMMARY

	Original	Actual
Pre-Scope meeting	2/20/2019	2/20/2019
Design Services Advertisement	6/17/2019	8/4/2019
Consultant BCC Approval	1/14/2020	
Design Start	1/21/2020	
Construction Start	3/9/2021	
Substantial Completion	3/8/2022	
Project Close-out	5/3/2022	

### PARTICIPATION


#### Consultant

SBE TBD  
 Local TBD  
 WBE N/A  
 MBE N/A


#### Contractor

SBE TBD  
 Local TBD  
 WBE TBD  
 MBE TBD

### FUNDING

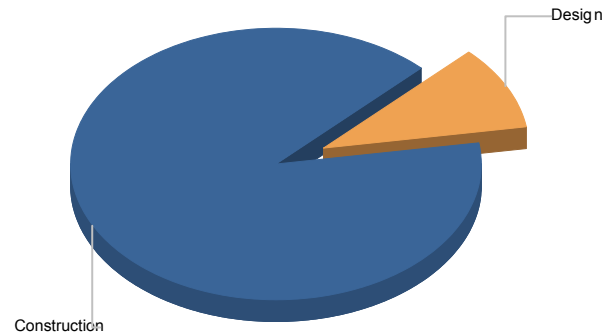

Current Budget

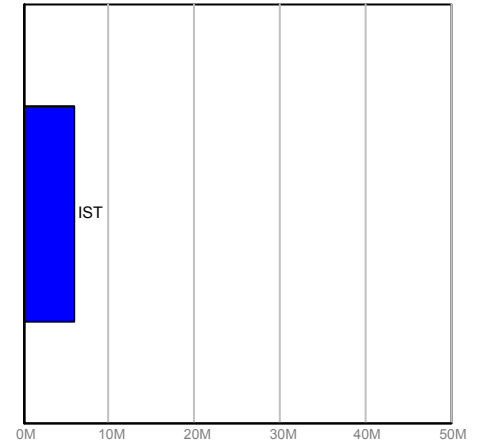

Fund Source

### FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$600,000	\$123,025	20.50%	\$76,065
Construction	\$5,400,000	\$14,058	0.26%	\$14,058
<b>TOTAL</b>	<b>\$6,000,000</b>	<b>\$137,084</b>	<b>2.28%</b>	<b>\$90,123</b>

### NOTES

CID was notified by Parks that feedback on additional funding is expected after BCC meeting in March, until then the project continues on hold.

# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects

Data Date: 1/21/21

Report Date: 2/5/21

### DESCRIPTION/TEAM

### SCOPE

### PHOTO

**Project Title:** Dyer Park Athletic Field Renovation

Replacement of existing grass field turf with synthetic turf on multi-purpose field 3, 4, & 5 as well as additional damaged area.  
Funded: FY 2020 \$6,000,000



Project Number: T099  
BCC District: 07  
Delivery Method: TBD  
Category: A06-Athletic Field Renovations  
Status: Design  
Designer: Florida Transportation Engineering  
Contractor: TBD  
Project Manager: Stuart Patterson

### SCHEDULE SUMMARY

	Original	Actual
Begin Existing Site Surveys	1/29/2020	1/29/2020
Complete Existing Site Surveys	6/30/2020	5/18/2020
Design RFP Final Selection	10/29/2020	10/29/2020
Consultant Contract Issuance	12/14/2020	
Design Completion	7/2/2021	
Turf Supplier RFP Proposal Due	4/30/2021	
Finalization of Existing Site Surveys	8/30/2020	9/18/2020
Design RFP Proposals Due	9/4/2020	9/10/2020

### PARTICIPATION

#### Consultant

SBE TBD

Local TBD

WBE TBD

MBE TBD

#### Contractor


SBE TBD

Local TBD

WBE TBD

MBE TBD

### FUNDING

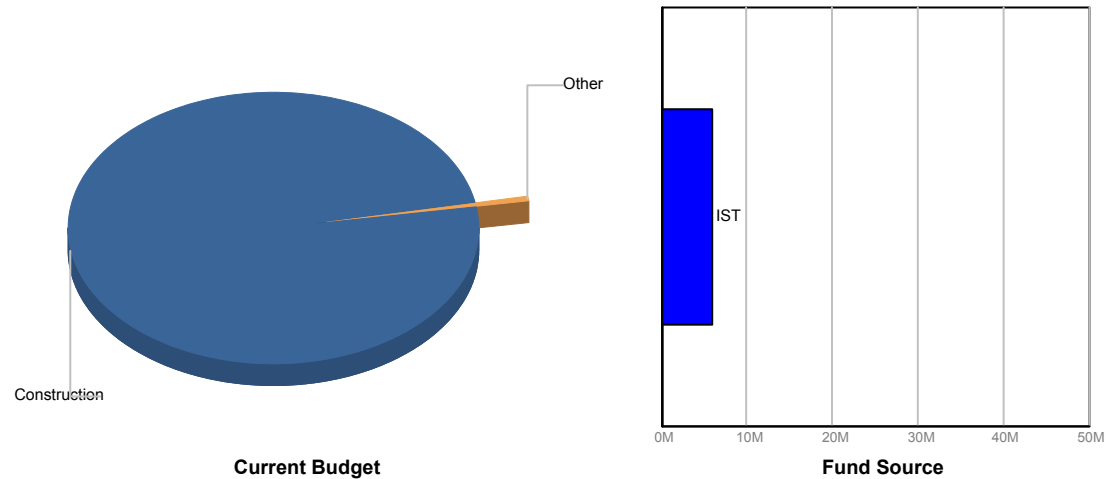

### FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Construction	\$5,970,000	\$17,250	0.29%	\$17,250
Other	\$30,000	\$17,781	59.27%	\$17,781
<b>TOTAL</b>	<b>\$6,000,000</b>	<b>\$35,031</b>	<b>0.58%</b>	<b>\$35,031</b>

### NOTES

Florida Transportation Engineering selected for engineering services . Contract in process; Due to \$ amount of design fees and complexity of negotiations, Team has decided to revise its schedule & submit for April, 2021 BCC meeting. Turf Supplier RFP to be completed at 50% design. Construction RFP will be developed for each package upon completion of supplier RFP. Anticipated that project will consist of (6) separate bid packages.

# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects

Data Date: 1/21/21

Report Date: 2/5/21

### DESCRIPTION/TEAM

### SCOPE

### PHOTO

**Project Title:** Caloosa Park Athletic Field Renovation

Replacement of existing grass field turf with synthetic turf on multi-purpose field 1 & 3 as well as softball field 4.  
Funded: FY 2020 \$4,000,000



Project Number: T100  
BCC District: 04  
Delivery Method: TBD  
Category: A06-Athletic Field Renovations  
Status: Design  
Designer: Florida Transportation Engineering  
Contractor: TBD  
Project Manager: Stuart Patterson

### SCHEDULE SUMMARY

	Original	Actual
Begin Existing Site Surveys	1/29/2020	1/29/2020
Complete Existing Site Surveys	6/30/2020	5/18/2020
Consultant Contract Issuance	12/14/2020	
Design Completion	7/2/2021	
Turf Supplier RFP Proposal Due	4/30/2021	
Finalization of Existing Site Surveys	8/30/2020	9/18/2020
Design RFP Proposals Due	9/4/2020	9/10/2020
Design RFP Final Selection	10/29/2020	10/29/2020

### PARTICIPATION

#### Consultant

SBE TBD

Local TBD

WBE TBD

MBE TBD

#### Contractor


SBE TBD

Local TBD

WBE TBD

MBE TBD

### FUNDING

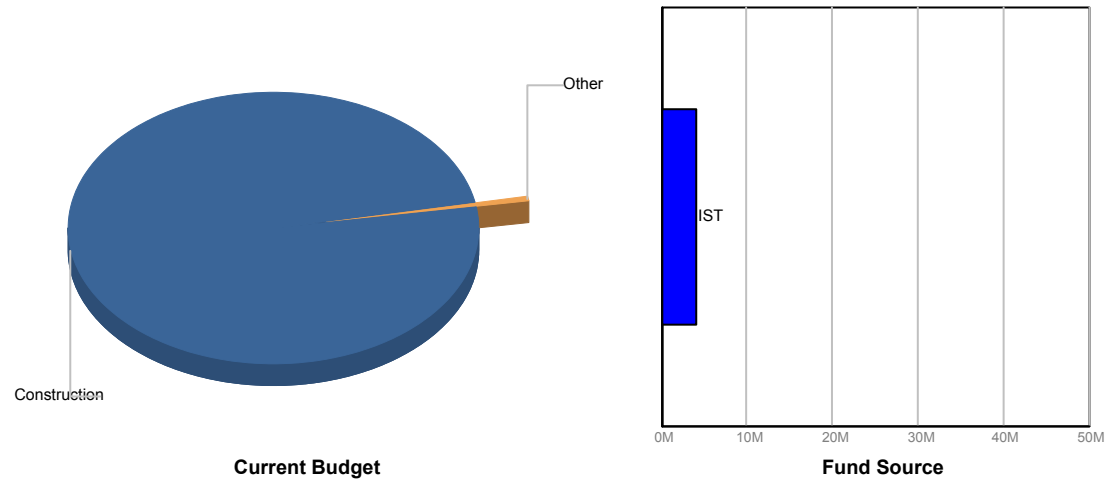

### FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Construction	\$3,980,000	\$22,215	0.56%	\$22,215
Other	\$20,000	\$10,434	52.17%	\$10,434
<b>TOTAL</b>	<b>\$4,000,000</b>	<b>\$32,649</b>	<b>0.82%</b>	<b>\$32,649</b>

### NOTES

Florida Transportation Engineering selected for engineering services . Contract in process; Due to \$ amount of design fees and complexity of negotiations, Team has decided to revise its schedule & submit for April, 2021 BCC meeting. Turf Supplier RFP to be completed at 50% design. Construction RFP will be developed for each package upon completion of supplier RFP. Anticipated that project will consist of (6) separate bid packages.

# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects

Data Date: 1/21/21

Report Date: 2/5/21

### DESCRIPTION/TEAM

### SCOPE

### PHOTO

**Project Title:** JPP Athletic Field Renovation

Replacement of existing grass field turf with synthetic turf on the Miracle League Field as well as softball fields 2 & 3.  
Funded: FY 2020 \$3,222,000



Project Number: T101  
BCC District: 03  
Delivery Method: TBD  
Category: A06-Athletic Field Renovations  
Status: Design  
Designer: Florida Transportation Engineering  
Contractor: TBD  
Project Manager: Stuart Patterson

### SCHEDULE SUMMARY

	Original	Actual
Design RFP Final Selection	10/29/2020	10/29/2020
Finalization of Existing Site Surveys	8/30/2020	9/18/2020
Design RFP Proposals Due	9/4/2020	9/10/2020
Consultant Contract Issuance	12/14/2020	
Design Completion	7/2/2021	
Turf Supplier RFP Proposal Due	4/30/2021	
Begin Existing Site Surveys	1/29/2020	1/29/2020
Complete Existing Site Surveys	6/30/2020	5/18/2020

### PARTICIPATION

#### Consultant

SBE TBD

Local TBD

WBE TBD

MBE TBD

#### Contractor


SBE TBD

Local TBD

WBE TBD

MBE TBD

### FUNDING

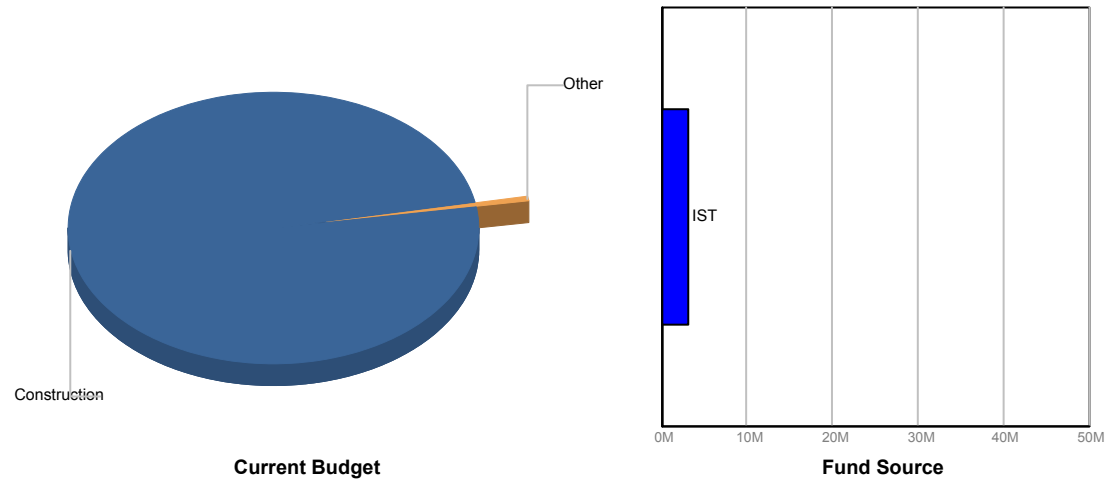

### FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Construction	\$3,204,000	\$16,860	0.53%	\$16,860
Other	\$16,000	\$8,536	53.35%	\$8,536
<b>TOTAL</b>	<b>\$3,220,000</b>	<b>\$25,396</b>	<b>0.79%</b>	<b>\$25,396</b>

### NOTES

Florida Transportation Engineering selected for engineering services . Contract in process; Due to \$ amount of design fees and complexity of negotiations, Team has decided to revise its schedule & submit for April, 2021 BCC meeting. Turf Supplier RFP to be completed at 50% design. Construction RFP will be developed for each package upon completion of supplier RFP. Anticipated that project will consist of (6) separate bid packages.



# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects

Data Date: 1/21/21

Report Date: 2/5/21

### DESCRIPTION/TEAM

### SCOPE

### PHOTO

**Project Title:** Loggers Run Park Athletic Field Renovation  
**Project Number:** T102  
**BCC District:** 05  
**Delivery Method:** TBD  
**Category:** A06-Athletic Field Renovations  
**Status:** Design  
**Designer:** TBD  
**Contractor:** TBD  
**Project Manager:** Stuart Patterson

Replacement of existing grass field turf with synthetic turf on multi-purpose field 1 & 2.  
 Funded: FY 2020 \$3,200,000



### SCHEDULE SUMMARY

	Original	Actual
Consultant Contract Issuance	12/14/2020	
Design Completion	7/2/2021	
Turf Supplier RFP Proposal Due	4/30/2021	
Finalization of Existing Site Surveys	8/30/2020	9/18/2020
Design RFP Proposals Due	9/4/2020	9/10/2020
Design RFP Final Selection	10/29/2020	10/29/2020
Begin Existing Site Surveys	1/29/2020	1/29/2020
Complete Existing Site Surveys	6/30/2020	5/18/2020

### PARTICIPATION


#### Consultant

SBE TBD  
 Local TBD  
 WBE TBD  
 MBE TBD

#### Contractor

SBE TBD  
 Local TBD  
 WBE TBD  
 MBE TBD

### FUNDING

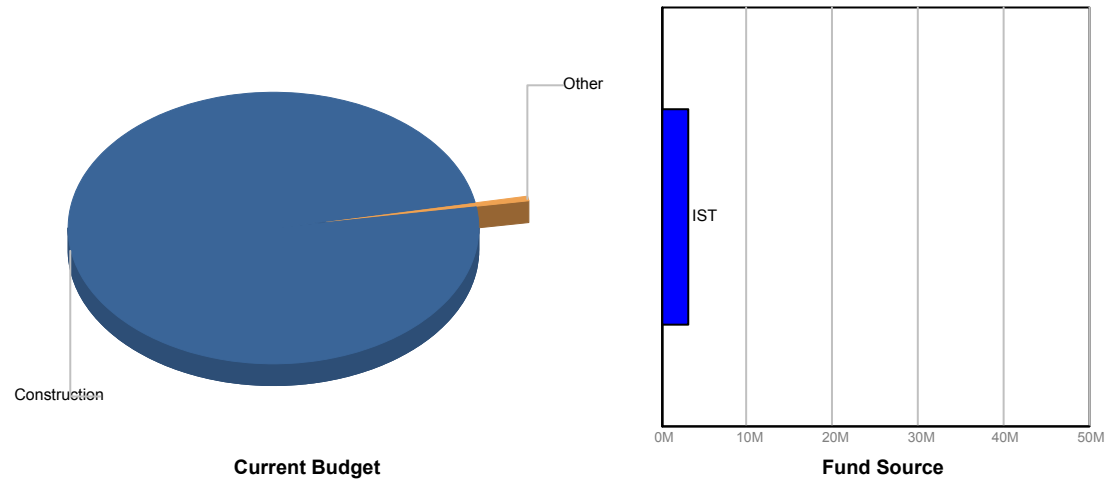

### FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Construction	\$3,184,000	\$13,750	0.43%	\$13,750
Other	\$16,000	\$12,400	77.50%	\$12,400
<b>TOTAL</b>	<b>\$3,200,000</b>	<b>\$26,150</b>	<b>0.82%</b>	<b>\$26,150</b>

### NOTES


Florida Transportation Engineering selected for engineering services . Contract in process; Due to \$ amount of design fees and complexity of negotiations, Team has decided to revise its schedule & submit for April, 2021 BCC meeting. Turf Supplier RFP to be completed at 50% design. Construction RFP will be developed for each package upon completion of supplier RFP. Anticipated that project will consist of (6) separate bid packages.

# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects


Data Date: 1/21/21

Report Date: 2/5/21

DESCRIPTION/TEAM	SCOPE	PHOTO
<p><b>Project Title:</b> Samuel Friedland District Park Expansion</p> <p>Project Number: T103</p> <p>BCC District: 06</p> <p>Delivery Method: TBD</p> <p>Category: A06-Athletic Field Renovations</p> <p>Status: Design</p> <p>Designer: Florida Transportation Engineering</p> <p>Contractor: TBD</p> <p>Project Manager: Stuart Patterson</p>	<p>Replacement of existing grass field turf with synthetic turf on multi-purpose field 9 &amp; 10 as well as the open play field.</p> <p>Funded: FY 2020 \$3,000,000</p>	

SCHEDULE SUMMARY		
	Original	Actual
Begin Existing Site Surveys	1/20/2020	1/29/2020
Complete Existing Site Surveys	6/30/2020	5/18/2020
Design RFP Final Selection	10/29/2020	10/29/2020
Finalization of Existing Site Surveys	8/30/2020	9/18/2020
Design RFP Proposals Due	9/4/2020	9/10/2020
Consultant Contract Issuance	12/14/2020	
Design Completion	7/2/2021	
Turf Supplier RFP Proposal Due	4/30/2021	

PARTICIPATION	
<b>Consultant</b>	
SBE	TBD
Local	TBD
WBE	TBD
MBE	TBD
<b>Contractor</b>	
SBE	TBD
Local	TBD
WBE	TBD
MBE	TBD

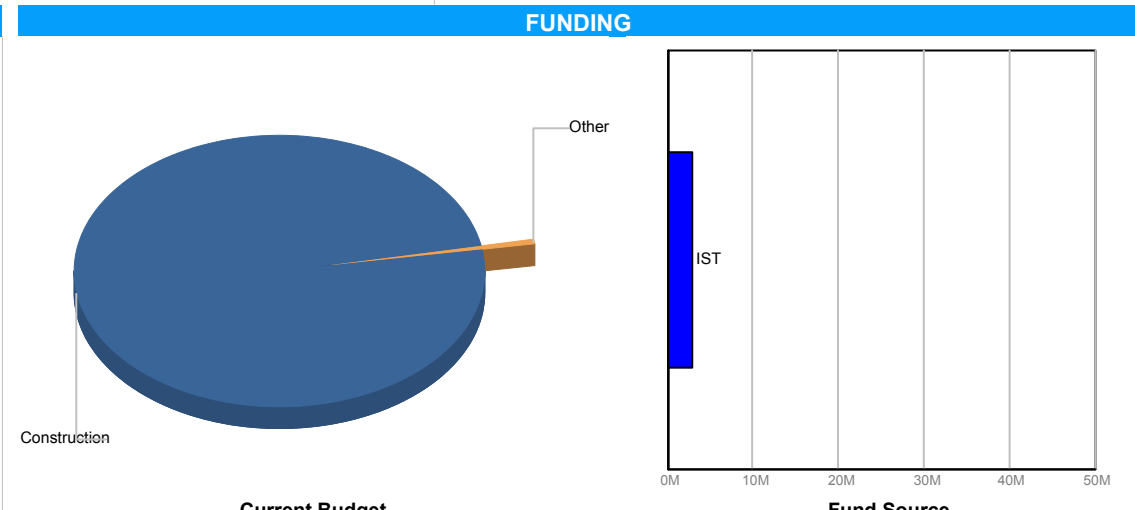

FINANCIAL SUMMARY				
	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Construction	\$2,985,000	\$12,967	0.43%	\$12,967
Other	\$15,000	\$7,197	47.98%	\$7,197
<b>TOTAL</b>	<b>\$3,000,000</b>	<b>\$20,164</b>	<b>0.67%</b>	<b>\$20,164</b>

**NOTES**

Florida Transportation Engineering selected for engineering services . Contract in process; Due to \$ amount of design fees and complexity of negotiations, Team has decided to revise its schedule & submit for April, 2021 BCC meeting. Turf Supplier RFP to be completed at 50% design. Construction RFP will be developed for each package upon completion of supplier RFP. Anticipated that project will consist of (6) separate bid packages.



# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects

Data Date: 1/21/21

Report Date: 2/5/21

### DESCRIPTION/TEAM

### SCOPE

### PHOTO

**Project Title:** Canyon's District Park New Park Development  
**Project Number:** T122  
**BCC District:** 05  
**Delivery Method:** Construction Manager at Risk  
**Category:** N02-New Park Development  
**Status:** Design  
**Designer:** Architecture Green  
**Contractor:** Kaufman Lynn  
**Project Manager:** Rosalyn Acosta

The project consists of the construction of a 52 acre Park south of Boynton Beach Blvd, along the west side of Acme Dairy Rd. with the Canyon Lakes Communities bordering the south and west limits of the site. The park will be constructed in two phases. Phase I will need to be completed in order to transfer the multi-purpose activities that currently take place on two existing soccer fields located to the west of the park. Once transferred the old soccer fields site will become the site of the new Canyon District Library.  
  
 FT2021 IST \$12,000,000



### SCHEDULE SUMMARY

	Original	Actual
GMP Approval	1/14/2021	
Construction Start	1/27/2021	
Construction Completion	1/27/2022	
Project Completion	3/27/2022	

### PARTICIPATION


**Consultant**

- SBE 75.93%
- Local 100%
- WBE 21.41%
- MBE 0%

**Contractor**

- SBE 22.32%
- Local 100%
- WBE 22.32%
- MBE 22.32%

### FUNDING

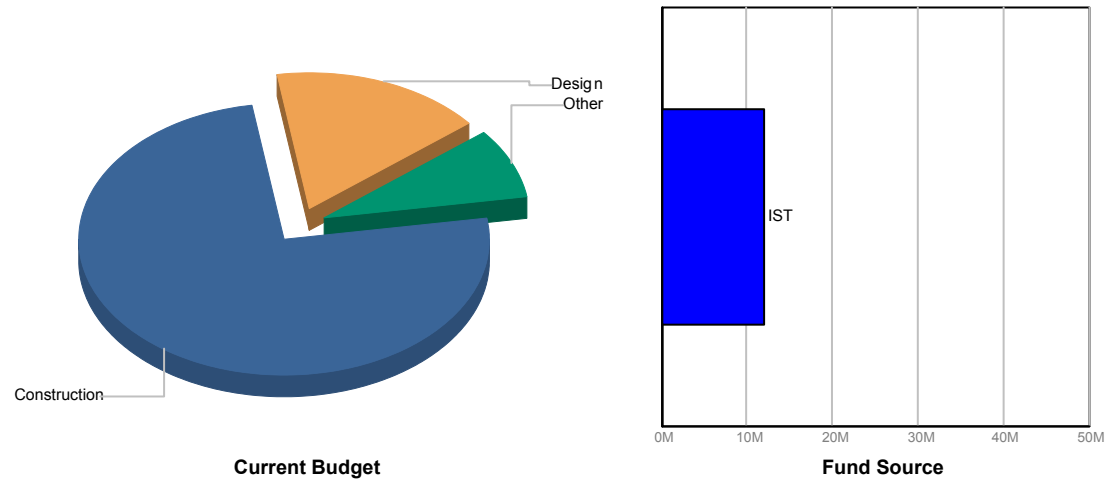

### FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$0	\$0	0.00%	\$0
Construction	\$11,000,000	\$10,793,121	98.12%	\$0
Other	\$1,000,000	\$0	0.00%	\$0
<b>TOTAL</b>	<b>\$12,000,000</b>	<b>\$10,793,121</b>	<b>89.94%</b>	<b>\$0</b>

### NOTES

CM mobilization started mid January, Silt fence and project sign have been erected; clearing and grubbing has commenced. CIP received notification from Parks that the contractor had mistakenly removed understory canopy and vegetation along the westside buffer that is owned by Canyon Lakes HOA. A meeting with KL, Parks, CID and CL HOA will be held on site on 2/8/21.
