



Monthly Infrastructure Sales Tax Project Report

Small Cap Projects

Data Date: 2/19/2026

Report Date: 2/28/2026

DESCRIPTION/TEAM

SCOPE/NOTES

SCHEDULE

Project Title: Florida Mango Rd. over LWDD Lat. 9 Canal (PB934337)
Project Number: 1491
BCC District: 03
Delivery Method: Design CCNA
Category: B08-Bridge Replacements
Status: Construction
Designer: Stanley Consultants
Contractor: TBD (bid)
Project Manager: Maroun Azzi

Scope
 This project will replace an existing bridge that was built over 50 years ago. The new bridge will improve traffic safety (lane widths, bike lanes, parapets), update the guardrail system, improve roadway drainage, improve the slope protection, and enhance pedestrian sidewalk safety.

Notes
 The project is funded with 5-Yr Rd Program funding and IST funding. Design is complete. The const. of the project (including rdwy improvements) is currently est. at \$3.3m. The IST partially funds the bridge const. at \$700k. The project is delayed and scheduled to begin construction in FY26 (after utility relocations).


	Original	Actual
Design Contract Notice to Proceed	9/20/2016	9/20/2016
Design Completion	1/11/2023	1/11/2023
Construction Bid Date	5/1/2026	
Construction Start	10/15/2026	
Construction Complete	12/25/2027	

PARTICIPATION

FUNDING

FINANCIAL SUMMARY

Consultant
 SBE 18%
 Local 100%
Contractor
 SBE TBD
 Local TBD



Project Budget	Committed	% Committed	Paid To Date
A	B	C=B/A	D
\$1,050,000	\$4,606	0.44%	\$4,606

DESCRIPTION/TEAM

SCOPE/NOTES

SCHEDULE

Project Title: Smith Sundry Rd. over LWDD Lat. 33 Canal
Project Number: 1521
BCC District: 05
Delivery Method: Design CCNA
Category: B04-Bridge Modifications
Status: Design
Designer: WGI, Inc.
Contractor: TBD (bid)
Project Manager: Kristine Frazell-Smith

Scope
 This project will replace an existing bridge that was built over 50 years ago. The new bridge will improve traffic safety (lane widths, bike lanes, parapets), update the guardrail system, improve roadway drainage, restore the slope protection, and enhance pedestrian sidewalk safety.

Notes
 Design is ongoing (65% complete). The scheduled dates have been revised to reflect design and permitting delays and to address stakeholder concerns.


	Original	Actual
Design Contract Notice to Proceed	3/13/2018	3/21/2018
Design Completion	4/1/2026	
Construction Bid Date	7/1/2026	
Construction Start	11/1/2026	
Construction Complete	4/1/2028	

PARTICIPATION

FUNDING

FINANCIAL SUMMARY

Consultant
 SBE 62.5%
 Local 100%
Contractor
 SBE TBD
 Local TBD



Project Budget	Committed	% Committed	Paid To Date
A	B	C=B/A	D
\$1,750,000	\$469,544	26.83%	\$397,094



Monthly Infrastructure Sales Tax Project Report

Small Cap Projects

Data Date: 2/19/2026

Report Date: 2/28/2026

DESCRIPTION/TEAM		SCOPE/NOTES	SCHEDULE																																											
Project Title: Sections of Military Trail Project Number: 1541 BCC District: CW Delivery Method: Annual Striping Contract Category: S16-Striping Status: Construction Designer: N/A Contractor: Oglesby Const., Inc./Southwide Industries Inc. Project Manager: Larry Kelly		Scope This project consists of restriping sections of Military Trail. Notes Restriping along Military Trail is done on an as needed basis as funding allows. The project is funded at \$200,000 in FY 2017 and FY 2021 and \$100,000 in FY 2022 thru FY 2026 for a total funding of \$900,000.	<table border="1"> <thead> <tr> <th></th> <th>Original</th> <th>Actual</th> </tr> </thead> <tbody> <tr> <td>Palmetto Park to Clint Moore Complete</td> <td>11/20/2017</td> <td>11/20/2017</td> </tr> <tr> <td>18th Street to Palmetto Park Complete</td> <td>12/18/2017</td> <td>12/18/2017</td> </tr> <tr> <td>Clint Moore to Live Oak Blvd.</td> <td>12/4/2023</td> <td>12/4/2023</td> </tr> <tr> <td>Live Oak Blvd. to Lake Blvd.</td> <td>1/10/2024</td> <td>1/10/2024</td> </tr> <tr> <td>Lake Blvd. to Lake Ida Rd.</td> <td>1/19/2024</td> <td>1/19/2024</td> </tr> <tr> <td>Lake Ida to Pipers Glen</td> <td>2/16/2024</td> <td>2/16/2024</td> </tr> <tr> <td>Pipers Glen to Cedar Point</td> <td>3/27/2024</td> <td>3/27/2024</td> </tr> <tr> <td>Cedar Point to Gateway</td> <td>11/12/2024</td> <td>11/12/2024</td> </tr> </tbody> </table>		Original	Actual	Palmetto Park to Clint Moore Complete	11/20/2017	11/20/2017	18th Street to Palmetto Park Complete	12/18/2017	12/18/2017	Clint Moore to Live Oak Blvd.	12/4/2023	12/4/2023	Live Oak Blvd. to Lake Blvd.	1/10/2024	1/10/2024	Lake Blvd. to Lake Ida Rd.	1/19/2024	1/19/2024	Lake Ida to Pipers Glen	2/16/2024	2/16/2024	Pipers Glen to Cedar Point	3/27/2024	3/27/2024	Cedar Point to Gateway	11/12/2024	11/12/2024	<table border="1"> <thead> <tr> <th>Project Budget</th> <th>Committed</th> <th>% Committed</th> <th>Paid To Date</th> </tr> <tr> <th>A</th> <th>B</th> <th>C=B/A</th> <th>D</th> </tr> </thead> <tbody> <tr> <td>\$900,000</td> <td>\$682,607</td> <td>75.85%</td> <td>\$639,419</td> </tr> </tbody> </table>				Project Budget	Committed	% Committed	Paid To Date	A	B	C=B/A	D	\$900,000	\$682,607	75.85%	\$639,419
	Original	Actual																																												
Palmetto Park to Clint Moore Complete	11/20/2017	11/20/2017																																												
18th Street to Palmetto Park Complete	12/18/2017	12/18/2017																																												
Clint Moore to Live Oak Blvd.	12/4/2023	12/4/2023																																												
Live Oak Blvd. to Lake Blvd.	1/10/2024	1/10/2024																																												
Lake Blvd. to Lake Ida Rd.	1/19/2024	1/19/2024																																												
Lake Ida to Pipers Glen	2/16/2024	2/16/2024																																												
Pipers Glen to Cedar Point	3/27/2024	3/27/2024																																												
Cedar Point to Gateway	11/12/2024	11/12/2024																																												
Project Budget	Committed	% Committed	Paid To Date																																											
A	B	C=B/A	D																																											
\$900,000	\$682,607	75.85%	\$639,419																																											
PARTICIPATION		FUNDING	FINANCIAL SUMMARY																																											
Consultant SBE N/A Local N/A Contractor SBE 92% Local 92%																																														

DESCRIPTION/TEAM		SCOPE/NOTES	SCHEDULE																																								
Project Title: Lake Osborne Dr. over Lake Bass Canal (PB934354) Project Number: 1542 BCC District: 02 Delivery Method: Design CCNA Category: B04-Bridge Modifications Status: Design Designer: Stantec Contractor: TBD (bid) Project Manager: Kristine Frazell-Smith		Scope This project will replace an existing bridge that was built over 60 years ago. The project will improve traffic safety (lane widths, bike lanes, parapets), update the guardrail system, improve roadway drainage, restore the slope protection, and enhance pedestrian sidewalk safety. Notes Design is ongoing (70% complete). Project is delayed to address stakeholder concerns.	<table border="1"> <thead> <tr> <th></th> <th>Original</th> <th>Actual</th> </tr> </thead> <tbody> <tr> <td>Design Contract NTP</td> <td>8/2/2017</td> <td>8/2/2017</td> </tr> <tr> <td>Study Start</td> <td>8/2/2017</td> <td>8/2/2017</td> </tr> <tr> <td>Study Complete</td> <td>5/1/2018</td> <td>5/1/2018</td> </tr> <tr> <td>Design Completion</td> <td>12/1/2026</td> <td></td> </tr> <tr> <td>Construction Bid Date</td> <td>3/1/2027</td> <td></td> </tr> <tr> <td>Construction Start</td> <td>7/1/2027</td> <td></td> </tr> <tr> <td>Construction Complete</td> <td>7/1/2028</td> <td></td> </tr> </tbody> </table>		Original	Actual	Design Contract NTP	8/2/2017	8/2/2017	Study Start	8/2/2017	8/2/2017	Study Complete	5/1/2018	5/1/2018	Design Completion	12/1/2026		Construction Bid Date	3/1/2027		Construction Start	7/1/2027		Construction Complete	7/1/2028		<table border="1"> <thead> <tr> <th>Project Budget</th> <th>Committed</th> <th>% Committed</th> <th>Paid To Date</th> </tr> <tr> <th>A</th> <th>B</th> <th>C=B/A</th> <th>D</th> </tr> </thead> <tbody> <tr> <td>\$1,500,000</td> <td>\$401,428</td> <td>26.76%</td> <td>\$307,707</td> </tr> </tbody> </table>				Project Budget	Committed	% Committed	Paid To Date	A	B	C=B/A	D	\$1,500,000	\$401,428	26.76%	\$307,707
	Original	Actual																																									
Design Contract NTP	8/2/2017	8/2/2017																																									
Study Start	8/2/2017	8/2/2017																																									
Study Complete	5/1/2018	5/1/2018																																									
Design Completion	12/1/2026																																										
Construction Bid Date	3/1/2027																																										
Construction Start	7/1/2027																																										
Construction Complete	7/1/2028																																										
Project Budget	Committed	% Committed	Paid To Date																																								
A	B	C=B/A	D																																								
\$1,500,000	\$401,428	26.76%	\$307,707																																								
PARTICIPATION		FUNDING	FINANCIAL SUMMARY																																								
Consultant SBE 28.9% Local 95% Contractor SBE TBD Local TBD																																											



Monthly Infrastructure Sales Tax Project Report

Small Cap Projects

Data Date: 2/19/2026

Report Date: 2/28/2026

DESCRIPTION/TEAM	SCOPE/NOTES	SCHEDULE																											
<p>Project Title: Sections of Congress Avenue</p> <p>Project Number: 1543</p> <p>BCC District: Multiple</p> <p>Delivery Method: Annual Striping Contract</p> <p>Category: S16-Striping</p> <p>Status: Construction</p> <p>Designer: N/A</p> <p>Contractor: Oglesby/Southwide</p> <p>Project Manager: Larry Kelly</p>	<p>Scope</p> <p>This project consists of restriping sections of Congress Avenue.</p> <p>Notes</p> <p>Restriping along Congress Avenue is done on an as needed basis as funding allows. The project is funded at \$100,000 in FY 2017 and FY 2021 thru FY 2025 and \$200,000 in FY 2026 for a total funding of \$800,000.</p>	<table border="1"> <thead> <tr> <th></th> <th style="text-align: center;">Original</th> <th style="text-align: center;">Actual</th> </tr> </thead> <tbody> <tr> <td>Palm Beach Lakes to 45th Street Comple</td> <td style="text-align: center;">10/6/2017</td> <td style="text-align: center;">10/6/2017</td> </tr> <tr> <td>Okeechobee to Palm Beach Lakes Comp</td> <td style="text-align: center;">2/6/2018</td> <td style="text-align: center;">2/6/2018</td> </tr> <tr> <td>Silver Beach to Water Tower</td> <td style="text-align: center;">3/18/2019</td> <td style="text-align: center;">3/18/2019</td> </tr> <tr> <td>Southwest 30th Ave. to Golf Rd.</td> <td style="text-align: center;">2/11/2021</td> <td style="text-align: center;">2/11/2021</td> </tr> <tr> <td>Linton to Lake Ida</td> <td style="text-align: center;">12/1/2021</td> <td style="text-align: center;">1/11/2022</td> </tr> <tr> <td>Yamato to Clint Moore</td> <td style="text-align: center;">3/1/2022</td> <td style="text-align: center;">2/15/2022</td> </tr> <tr> <td>West Park Ave. to Nothlake</td> <td style="text-align: center;">4/1/2022</td> <td style="text-align: center;">3/25/2022</td> </tr> <tr> <td>MLK to Blue Heron</td> <td style="text-align: center;">4/1/2022</td> <td style="text-align: center;">3/25/2022</td> </tr> </tbody> </table>		Original	Actual	Palm Beach Lakes to 45th Street Comple	10/6/2017	10/6/2017	Okeechobee to Palm Beach Lakes Comp	2/6/2018	2/6/2018	Silver Beach to Water Tower	3/18/2019	3/18/2019	Southwest 30th Ave. to Golf Rd.	2/11/2021	2/11/2021	Linton to Lake Ida	12/1/2021	1/11/2022	Yamato to Clint Moore	3/1/2022	2/15/2022	West Park Ave. to Nothlake	4/1/2022	3/25/2022	MLK to Blue Heron	4/1/2022	3/25/2022
	Original	Actual																											
Palm Beach Lakes to 45th Street Comple	10/6/2017	10/6/2017																											
Okeechobee to Palm Beach Lakes Comp	2/6/2018	2/6/2018																											
Silver Beach to Water Tower	3/18/2019	3/18/2019																											
Southwest 30th Ave. to Golf Rd.	2/11/2021	2/11/2021																											
Linton to Lake Ida	12/1/2021	1/11/2022																											
Yamato to Clint Moore	3/1/2022	2/15/2022																											
West Park Ave. to Nothlake	4/1/2022	3/25/2022																											
MLK to Blue Heron	4/1/2022	3/25/2022																											

PARTICIPATION	FUNDING	FINANCIAL SUMMARY												
<p>Consultant</p> <p>SBE N/A</p> <p>Local N/A</p> <p>Contractor</p> <p>SBE 68%</p> <p>Local 68%</p>		<table border="1"> <thead> <tr> <th style="text-align: center;">Project Budget</th> <th style="text-align: center;">Committed</th> <th style="text-align: center;">% Committed</th> <th style="text-align: center;">Paid To Date</th> </tr> <tr> <th style="text-align: center;">A</th> <th style="text-align: center;">B</th> <th style="text-align: center;">C=B/A</th> <th style="text-align: center;">D</th> </tr> </thead> <tbody> <tr> <td style="text-align: center;">\$800,000</td> <td style="text-align: center;">\$331,657</td> <td style="text-align: center;">41.46%</td> <td style="text-align: center;">\$242,334</td> </tr> </tbody> </table>	Project Budget	Committed	% Committed	Paid To Date	A	B	C=B/A	D	\$800,000	\$331,657	41.46%	\$242,334
Project Budget	Committed	% Committed	Paid To Date											
A	B	C=B/A	D											
\$800,000	\$331,657	41.46%	\$242,334											

DESCRIPTION/TEAM	SCOPE/NOTES	SCHEDULE									
<p>Project Title: Sections of Gateway Blvd.</p> <p>Project Number: 1544</p> <p>BCC District: 02</p> <p>Delivery Method: Annual Striping Contract</p> <p>Category: S16-Striping</p> <p>Status: Construction</p> <p>Designer: N/A</p> <p>Contractor: Southwide</p> <p>Project Manager: Larry Kelly</p>	<p>Scope</p> <p>This project consists of restriping sections of Gateway Boulevard.</p> <p>Notes</p> <p>Restriping along Gateway Blvd. is done on an as needed basis as funding allows. The project is funded at \$100,000 in FY 2017 and FY 2025 for a total funding of \$200,000.</p>	<table border="1"> <thead> <tr> <th></th> <th style="text-align: center;">Original</th> <th style="text-align: center;">Actual</th> </tr> </thead> <tbody> <tr> <td>Hagen Ranch Road to Jog Road Comple</td> <td style="text-align: center;">8/24/2017</td> <td style="text-align: center;">8/24/2017</td> </tr> <tr> <td>Military to Congress Complete</td> <td style="text-align: center;">1/22/2018</td> <td style="text-align: center;">1/22/2018</td> </tr> </tbody> </table>		Original	Actual	Hagen Ranch Road to Jog Road Comple	8/24/2017	8/24/2017	Military to Congress Complete	1/22/2018	1/22/2018
	Original	Actual									
Hagen Ranch Road to Jog Road Comple	8/24/2017	8/24/2017									
Military to Congress Complete	1/22/2018	1/22/2018									

PARTICIPATION	FUNDING	FINANCIAL SUMMARY												
<p>Consultant</p> <p>SBE N/A</p> <p>Local N/A</p> <p>Contractor</p> <p>SBE 100%</p> <p>Local 100%</p>		<table border="1"> <thead> <tr> <th style="text-align: center;">Project Budget</th> <th style="text-align: center;">Committed</th> <th style="text-align: center;">% Committed</th> <th style="text-align: center;">Paid To Date</th> </tr> <tr> <th style="text-align: center;">A</th> <th style="text-align: center;">B</th> <th style="text-align: center;">C=B/A</th> <th style="text-align: center;">D</th> </tr> </thead> <tbody> <tr> <td style="text-align: center;">\$200,000</td> <td style="text-align: center;">\$77,327</td> <td style="text-align: center;">38.66%</td> <td style="text-align: center;">\$77,327</td> </tr> </tbody> </table>	Project Budget	Committed	% Committed	Paid To Date	A	B	C=B/A	D	\$200,000	\$77,327	38.66%	\$77,327
Project Budget	Committed	% Committed	Paid To Date											
A	B	C=B/A	D											
\$200,000	\$77,327	38.66%	\$77,327											



Monthly Infrastructure Sales Tax Project Report

Small Cap Projects

Data Date: 2/19/2026

Report Date: 2/28/2026

DESCRIPTION/TEAM	SCOPE/NOTES	SCHEDULE						
<p>Project Title: Sections of Seacrest Blvd.</p> <p>Project Number: 1545</p> <p>BCC District: 07</p> <p>Delivery Method: Annual Striping Contract</p> <p>Category: S16-Striping</p> <p>Status: Construction</p> <p>Designer: N/A</p> <p>Contractor: Southwide</p> <p>Project Manager: Larry Kelly</p>	<p>Scope</p> <p>This project consists of restriping sections of Seacrest Boulevard.</p> <p>Notes</p> <p>Restriping along Seacrest Blvd. is done on an as needed basis as funding allows. The project is funded at \$50,000 in FY 2017, FY 2020, FY 2023 and FY 2025 for a total funding of \$200,000.</p>	<table border="1"> <thead> <tr> <th></th> <th style="text-align: center;">Original</th> <th style="text-align: center;">Actual</th> </tr> </thead> <tbody> <tr> <td>SW 26th to Boynton Beach Blvd. Comple</td> <td style="text-align: center;">9/6/2017</td> <td style="text-align: center;">9/6/2017</td> </tr> </tbody> </table>		Original	Actual	SW 26th to Boynton Beach Blvd. Comple	9/6/2017	9/6/2017
	Original	Actual						
SW 26th to Boynton Beach Blvd. Comple	9/6/2017	9/6/2017						

PARTICIPATION	FUNDING	FINANCIAL SUMMARY												
<p>Consultant</p> <p>SBE N/A</p> <p>Local N/A</p> <p>Contractor</p> <p>SBE 100%</p> <p>Local 100%</p>		<table border="1"> <thead> <tr> <th style="text-align: center;">Project Budget</th> <th style="text-align: center;">Committed</th> <th style="text-align: center;">% Committed</th> <th style="text-align: center;">Paid To Date</th> </tr> <tr> <th style="text-align: center;">A</th> <th style="text-align: center;">B</th> <th style="text-align: center;">C=B/A</th> <th style="text-align: center;">D</th> </tr> </thead> <tbody> <tr> <td style="text-align: center;">\$200,000</td> <td style="text-align: center;">\$31,991</td> <td style="text-align: center;">16.00%</td> <td style="text-align: center;">\$31,991</td> </tr> </tbody> </table>	Project Budget	Committed	% Committed	Paid To Date	A	B	C=B/A	D	\$200,000	\$31,991	16.00%	\$31,991
Project Budget	Committed	% Committed	Paid To Date											
A	B	C=B/A	D											
\$200,000	\$31,991	16.00%	\$31,991											

DESCRIPTION/TEAM	SCOPE/NOTES	SCHEDULE												
<p>Project Title: Sections of Old Dixie Hwy.</p> <p>Project Number: 1546</p> <p>BCC District: 07</p> <p>Delivery Method: Annual Striping Contract</p> <p>Category: S16-Striping</p> <p>Status: Construction</p> <p>Designer: N/A</p> <p>Contractor: Southwide</p> <p>Project Manager: Larry Kelly</p>	<p>Scope</p> <p>This project consists of restriping sections of Old Dixie Highway.</p> <p>Notes</p> <p>Restriping along Old Dixie Hwy. is done on an as needed basis as funding allows. The project is funded at \$50,000 in FY 2017, and \$100,000 in FY 2021 and FY 2023, and \$125,000 in FY 2026 for a total funding of \$375,000.</p>	<table border="1"> <thead> <tr> <th></th> <th style="text-align: center;">Original</th> <th style="text-align: center;">Actual</th> </tr> </thead> <tbody> <tr> <td>Boca Raton city limits to Lindell Road Cor</td> <td style="text-align: center;">11/20/2017</td> <td style="text-align: center;">11/20/2017</td> </tr> <tr> <td>NE 2nd Street to Glades Road Complete</td> <td style="text-align: center;">11/20/2017</td> <td style="text-align: center;">11/20/2017</td> </tr> <tr> <td>Alt. A-1-A to County Line Rd.</td> <td style="text-align: center;">7/1/2021</td> <td style="text-align: center;">6/25/2021</td> </tr> </tbody> </table>		Original	Actual	Boca Raton city limits to Lindell Road Cor	11/20/2017	11/20/2017	NE 2nd Street to Glades Road Complete	11/20/2017	11/20/2017	Alt. A-1-A to County Line Rd.	7/1/2021	6/25/2021
	Original	Actual												
Boca Raton city limits to Lindell Road Cor	11/20/2017	11/20/2017												
NE 2nd Street to Glades Road Complete	11/20/2017	11/20/2017												
Alt. A-1-A to County Line Rd.	7/1/2021	6/25/2021												

PARTICIPATION	FUNDING	FINANCIAL SUMMARY												
<p>Consultant</p> <p>SBE N/A</p> <p>Local N/A</p> <p>Contractor</p> <p>SBE 100%</p> <p>Local 100%</p>		<table border="1"> <thead> <tr> <th style="text-align: center;">Project Budget</th> <th style="text-align: center;">Committed</th> <th style="text-align: center;">% Committed</th> <th style="text-align: center;">Paid To Date</th> </tr> <tr> <th style="text-align: center;">A</th> <th style="text-align: center;">B</th> <th style="text-align: center;">C=B/A</th> <th style="text-align: center;">D</th> </tr> </thead> <tbody> <tr> <td style="text-align: center;">\$375,000</td> <td style="text-align: center;">\$28,739</td> <td style="text-align: center;">7.66%</td> <td style="text-align: center;">\$28,739</td> </tr> </tbody> </table>	Project Budget	Committed	% Committed	Paid To Date	A	B	C=B/A	D	\$375,000	\$28,739	7.66%	\$28,739
Project Budget	Committed	% Committed	Paid To Date											
A	B	C=B/A	D											
\$375,000	\$28,739	7.66%	\$28,739											



Monthly Infrastructure Sales Tax Project Report

Small Cap Projects

Data Date: 2/19/2026

Report Date: 2/28/2026

DESCRIPTION/TEAM	SCOPE/NOTES	SCHEDULE									
<p>Project Title: Sections of Clint Moore Road</p> <p>Project Number: 1547</p> <p>BCC District: Multiple</p> <p>Delivery Method: Annual Striping Contract</p> <p>Category: S16-Striping</p> <p>Status: Construction</p> <p>Designer: N/A</p> <p>Contractor: Southwide</p> <p>Project Manager: Larry Kelly</p>	<p>Scope</p> <p>This project consists of restriping sections of Clint Moore Road.</p> <p>Notes</p> <p>Restriping along Clint Moore Road is done on an as needed basis as funding allows. The project is funded at \$50,000 in FY 2017 and FY 2022, and \$100,000 in FY 2026 for a total funding of \$200,000.</p>	<table border="1"> <thead> <tr> <th></th> <th>Original</th> <th>Actual</th> </tr> </thead> <tbody> <tr> <td>Military to Congress Complete</td> <td>9/6/2017</td> <td>9/6/2017</td> </tr> <tr> <td>Turnpike Overpass to Jog</td> <td>12/29/2020</td> <td>12/29/2020</td> </tr> </tbody> </table>		Original	Actual	Military to Congress Complete	9/6/2017	9/6/2017	Turnpike Overpass to Jog	12/29/2020	12/29/2020
	Original	Actual									
Military to Congress Complete	9/6/2017	9/6/2017									
Turnpike Overpass to Jog	12/29/2020	12/29/2020									

PARTICIPATION	FUNDING	FINANCIAL SUMMARY												
<p>Consultant</p> <p>SBE N/A</p> <p>Local N/A</p> <p>Contractor</p> <p>SBE 100%</p> <p>Local 100%</p>		<table border="1"> <thead> <tr> <th>Project Budget</th> <th>Committed</th> <th>% Committed</th> <th>Paid To Date</th> </tr> <tr> <th>A</th> <th>B</th> <th>C=B/A</th> <th>D</th> </tr> </thead> <tbody> <tr> <td>\$200,000</td> <td>\$47,104</td> <td>23.55%</td> <td>\$47,104</td> </tr> </tbody> </table>	Project Budget	Committed	% Committed	Paid To Date	A	B	C=B/A	D	\$200,000	\$47,104	23.55%	\$47,104
Project Budget	Committed	% Committed	Paid To Date											
A	B	C=B/A	D											
\$200,000	\$47,104	23.55%	\$47,104											

DESCRIPTION/TEAM	SCOPE/NOTES	SCHEDULE									
<p>Project Title: Sections of Hagen Ranch Road</p> <p>Project Number: 1548</p> <p>BCC District: Multiple</p> <p>Delivery Method: Annual Striping Contract</p> <p>Category: S16-Striping</p> <p>Status: Construction</p> <p>Designer: N/A</p> <p>Contractor: Southwide</p> <p>Project Manager: Larry Kelly</p>	<p>Scope</p> <p>This project consists of restriping sections of Hagen Ranch Road.</p> <p>Notes</p> <p>Restriping along Hagen Ranch Road is done on an as needed basis as funding allows. The project is funded at \$50,000 in FY 2017 and FY 2021, and \$100,000 in FY 2024, and \$75,000 in FY 2026 for a total funding of \$275,000.</p>	<table border="1"> <thead> <tr> <th></th> <th>Original</th> <th>Actual</th> </tr> </thead> <tbody> <tr> <td>Atlantic to Flavor Pict Complete</td> <td>7/31/2017</td> <td>7/11/2017</td> </tr> <tr> <td>Gateway to Flavor Pict</td> <td>11/3/2023</td> <td>11/3/2023</td> </tr> </tbody> </table>		Original	Actual	Atlantic to Flavor Pict Complete	7/31/2017	7/11/2017	Gateway to Flavor Pict	11/3/2023	11/3/2023
	Original	Actual									
Atlantic to Flavor Pict Complete	7/31/2017	7/11/2017									
Gateway to Flavor Pict	11/3/2023	11/3/2023									

PARTICIPATION	FUNDING	FINANCIAL SUMMARY												
<p>Consultant</p> <p>SBE N/A</p> <p>Local N/A</p> <p>Contractor</p> <p>SBE 100%</p> <p>Local 100%</p>		<table border="1"> <thead> <tr> <th>Project Budget</th> <th>Committed</th> <th>% Committed</th> <th>Paid To Date</th> </tr> <tr> <th>A</th> <th>B</th> <th>C=B/A</th> <th>D</th> </tr> </thead> <tbody> <tr> <td>\$275,000</td> <td>\$59,090</td> <td>21.49%</td> <td>\$59,090</td> </tr> </tbody> </table>	Project Budget	Committed	% Committed	Paid To Date	A	B	C=B/A	D	\$275,000	\$59,090	21.49%	\$59,090
Project Budget	Committed	% Committed	Paid To Date											
A	B	C=B/A	D											
\$275,000	\$59,090	21.49%	\$59,090											



Monthly Infrastructure Sales Tax Project Report

Small Cap Projects

Data Date: 2/19/2026

Report Date: 2/28/2026

DESCRIPTION/TEAM

SCOPE/NOTES

SCHEDULE

Project Title: Sections of Randolph Siding Rd.
Project Number: 1559
BCC District: 01
Delivery Method: Annual Construction Contract
Category: D02-Drainage (Pipe Replacements)
Status: Close Out
Designer: N/A
Contractor: Wynn & Sons and Johnson & Davis
Project Manager: Mark Kroeger

Scope
 This project will repair and/or replace existing pipe culverts and drainage structures along Randolph Siding Road. These repairs are needed in order to properly drain and maintain Randolph Siding Road in a safe operating condition.

Notes
 This project is funded at \$300k in FY 2018 and FY 2021 for a total funding of \$600,000. Work is complete. A Type 1 transfer to sweep the remaining balance of the project to reserves is forthcoming.

	Original	Actual
110th to Jupiter Farms Road Complete	6/1/2018	5/10/2018
@Alexander Run	5/1/2019	6/7/2019
Sites 1, 2, & 4	11/13/2025	11/13/2025
Sites 5, 6 & 8	11/13/2025	11/13/2025

PARTICIPATION

FUNDING

FINANCIAL SUMMARY

Consultant


SBE N/A

Local N/A

Contractor

SBE 34.5%

Local 100%



Project Budget	Committed	% Committed	Paid To Date
A	B	C=B/A	D
\$600,000	\$238,661	39.78%	\$238,661

DESCRIPTION/TEAM

SCOPE/NOTES

SCHEDULE

Project Title: Boynton Beach Blvd. & Seacrest Blvd.
Project Number: 1578
BCC District: 07
Delivery Method: Design CCNA
Category: S08-Signals and Signal Systems
Status: Design
Designer: Wantman Group
Contractor: TBD
Project Manager: May Cheng

Scope
 This project will replace the existing span-wire signal system with a mast arm signal system.
 FY 2018 IST \$400,000
 FY 2022 IST \$250,000

Notes
 Design of the project is ON HOLD. Utility and right-of-way (ROW) issues still unresolved. The County has requested that the FDOT replace this signal as part of an upcoming State project. Project is on hold.

	Original	Actual
Construction Start - TBD		
Construction Complete - TBD		
Design NTP Issued	4/19/2019	4/7/2019
Design Complete	6/1/2023	

PARTICIPATION

FUNDING

FINANCIAL SUMMARY

Consultant


SBE 0%

Local 100%

Contractor

SBE TBD

Local TBD

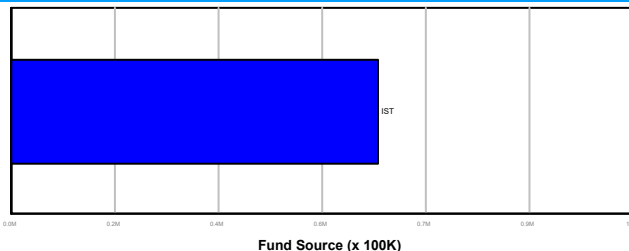

Project Budget	Committed	% Committed	Paid To Date
A	B	C=B/A	D
\$650,000	\$72,176	11.10%	\$14,925



Monthly Infrastructure Sales Tax Project Report

Small Cap Projects

Data Date: 2/19/2026

Report Date: 2/28/2026

DESCRIPTION/TEAM	SCOPE/NOTES	SCHEDULE																					
<p>Project Title: Sections of Lyons Road</p> <p>Project Number: 1597</p> <p>BCC District: Multiple</p> <p>Delivery Method: Annual Striping Contract</p> <p>Category: S16-Striping</p> <p>Status: Construction</p> <p>Designer: N/A</p> <p>Contractor: Oglesby/Southwide</p> <p>Project Manager: Larry Kelly</p>	<p>Scope</p> <p>This project consists of restriping sections of Lyons Road.</p> <p>Notes</p> <p>Restriping along Lyons Road is done on an as needed basis as funding allows. The project is funded at \$200,000 in FY 2018, FY 2022, and FY 2025 for a total funding of \$600,000.</p>	<table border="1"> <thead> <tr> <th></th> <th>Original</th> <th>Actual</th> </tr> </thead> <tbody> <tr> <td>Connector Road to Lantana Road</td> <td>5/14/2018</td> <td>5/7/2018</td> </tr> <tr> <td>Wendy Ln to Palm Beach Plantation Blvd</td> <td>3/20/2019</td> <td>3/20/2019</td> </tr> <tr> <td>Glades to Yamato</td> <td>8/1/2021</td> <td>3/24/2022</td> </tr> <tr> <td>Yamato to Clint Moore</td> <td>8/1/2022</td> <td>8/1/2022</td> </tr> <tr> <td>Happy Hollow to L-30</td> <td>1/5/2023</td> <td>1/5/2023</td> </tr> <tr> <td>Stribling to Forest Hill</td> <td>9/1/2023</td> <td>9/1/2023</td> </tr> </tbody> </table>		Original	Actual	Connector Road to Lantana Road	5/14/2018	5/7/2018	Wendy Ln to Palm Beach Plantation Blvd	3/20/2019	3/20/2019	Glades to Yamato	8/1/2021	3/24/2022	Yamato to Clint Moore	8/1/2022	8/1/2022	Happy Hollow to L-30	1/5/2023	1/5/2023	Stribling to Forest Hill	9/1/2023	9/1/2023
	Original	Actual																					
Connector Road to Lantana Road	5/14/2018	5/7/2018																					
Wendy Ln to Palm Beach Plantation Blvd	3/20/2019	3/20/2019																					
Glades to Yamato	8/1/2021	3/24/2022																					
Yamato to Clint Moore	8/1/2022	8/1/2022																					
Happy Hollow to L-30	1/5/2023	1/5/2023																					
Stribling to Forest Hill	9/1/2023	9/1/2023																					

PARTICIPATION	FUNDING	FINANCIAL SUMMARY												
<p>Consultant</p> <p>SBE N/A</p> <p>Local N/A</p> <p>Contractor</p> <p>SBE 40%</p> <p>Local 40%</p>		<table border="1"> <thead> <tr> <th>Project Budget</th> <th>Committed</th> <th>% Committed</th> <th>Paid To Date</th> </tr> <tr> <th>A</th> <th>B</th> <th>C=B/A</th> <th>D</th> </tr> </thead> <tbody> <tr> <td>\$600,000</td> <td>\$244,183</td> <td>40.70%</td> <td>\$244,183</td> </tr> </tbody> </table>	Project Budget	Committed	% Committed	Paid To Date	A	B	C=B/A	D	\$600,000	\$244,183	40.70%	\$244,183
Project Budget	Committed	% Committed	Paid To Date											
A	B	C=B/A	D											
\$600,000	\$244,183	40.70%	\$244,183											

DESCRIPTION/TEAM	SCOPE/NOTES	SCHEDULE																					
<p>Project Title: Sections of Haverhill Road</p> <p>Project Number: 1598</p> <p>BCC District: Multiple</p> <p>Delivery Method: Annual Striping Contract</p> <p>Category: S16-Striping</p> <p>Status: Construction</p> <p>Designer: N/A</p> <p>Contractor: Oglesby/Southwide</p> <p>Project Manager: Larry Kelly</p>	<p>Scope</p> <p>This project consists of restriping sections of Haverhill Road.</p> <p>Notes</p> <p>Restriping along Haverhill Road is done on an as needed basis as funding allows. Project is funded at \$100,000 in FY 2018, FY 2021, FY 2023, and FY 2026 for a total funding of \$400,000.</p>	<table border="1"> <thead> <tr> <th></th> <th>Original</th> <th>Actual</th> </tr> </thead> <tbody> <tr> <td>Lantana Road to Hypoluxo Road</td> <td>5/14/2018</td> <td>5/2/2018</td> </tr> <tr> <td>10th Ave. N to Purdy Lane</td> <td>9/1/2019</td> <td>9/1/2019</td> </tr> <tr> <td>Caribbean to Beeline</td> <td>6/1/2020</td> <td>6/10/2020</td> </tr> <tr> <td>Forest Hill to Summit</td> <td>9/22/2023</td> <td>9/22/2023</td> </tr> <tr> <td>Belvedere to Elmhurst</td> <td>9/26/2023</td> <td>9/26/2023</td> </tr> <tr> <td>Purdy to Forest Hill</td> <td>9/19/2024</td> <td>9/19/2024</td> </tr> </tbody> </table>		Original	Actual	Lantana Road to Hypoluxo Road	5/14/2018	5/2/2018	10th Ave. N to Purdy Lane	9/1/2019	9/1/2019	Caribbean to Beeline	6/1/2020	6/10/2020	Forest Hill to Summit	9/22/2023	9/22/2023	Belvedere to Elmhurst	9/26/2023	9/26/2023	Purdy to Forest Hill	9/19/2024	9/19/2024
	Original	Actual																					
Lantana Road to Hypoluxo Road	5/14/2018	5/2/2018																					
10th Ave. N to Purdy Lane	9/1/2019	9/1/2019																					
Caribbean to Beeline	6/1/2020	6/10/2020																					
Forest Hill to Summit	9/22/2023	9/22/2023																					
Belvedere to Elmhurst	9/26/2023	9/26/2023																					
Purdy to Forest Hill	9/19/2024	9/19/2024																					

PARTICIPATION	FUNDING	FINANCIAL SUMMARY												
<p>Consultant</p> <p>SBE N/A</p> <p>Local N/A</p> <p>Contractor</p> <p>SBE 45%</p> <p>Local 45%</p>		<table border="1"> <thead> <tr> <th>Project Budget</th> <th>Committed</th> <th>% Committed</th> <th>Paid To Date</th> </tr> <tr> <th>A</th> <th>B</th> <th>C=B/A</th> <th>D</th> </tr> </thead> <tbody> <tr> <td>\$400,000</td> <td>\$121,646</td> <td>30.41%</td> <td>\$121,646</td> </tr> </tbody> </table>	Project Budget	Committed	% Committed	Paid To Date	A	B	C=B/A	D	\$400,000	\$121,646	30.41%	\$121,646
Project Budget	Committed	% Committed	Paid To Date											
A	B	C=B/A	D											
\$400,000	\$121,646	30.41%	\$121,646											



Monthly Infrastructure Sales Tax Project Report

Small Cap Projects

Data Date: 2/19/2026

Report Date: 2/28/2026

DESCRIPTION/TEAM	SCOPE/NOTES	SCHEDULE															
<p>Project Title: Sections of Belvedere Road</p> <p>Project Number: 1599</p> <p>BCC District: Multiple</p> <p>Delivery Method: Annual Striping Contract</p> <p>Category: S16-Striping</p> <p>Status: Construction</p> <p>Designer: N/A</p> <p>Contractor: Oglesby/Southwide</p> <p>Project Manager: Larry Kelly</p>	<p>Scope</p> <p>This project consists of restriping sections of Belvedere Road.</p> <p>Notes</p> <p>Restriping along Belvedere Road is done on an as needed basis as funding allows. The project is funded at \$100,000 in FY 2018, and \$50,000 in FY 2022 and FY 2025, and \$125,000 in FY 2024 for a total funding of \$325,000.</p>	<table border="1"> <thead> <tr> <th></th> <th>Original</th> <th>Actual</th> </tr> </thead> <tbody> <tr> <td>Haverhill Road to Drexel Road</td> <td>7/14/2018</td> <td>8/20/2018</td> </tr> <tr> <td>Benoist Farms Road to SR7</td> <td>3/1/2022</td> <td>3/3/2022</td> </tr> <tr> <td>Military Trail to 8th St.</td> <td>4/1/2022</td> <td>3/3/2022</td> </tr> <tr> <td>Haverhill to Military</td> <td>6/15/2022</td> <td>6/15/2022</td> </tr> </tbody> </table>		Original	Actual	Haverhill Road to Drexel Road	7/14/2018	8/20/2018	Benoist Farms Road to SR7	3/1/2022	3/3/2022	Military Trail to 8th St.	4/1/2022	3/3/2022	Haverhill to Military	6/15/2022	6/15/2022
	Original	Actual															
Haverhill Road to Drexel Road	7/14/2018	8/20/2018															
Benoist Farms Road to SR7	3/1/2022	3/3/2022															
Military Trail to 8th St.	4/1/2022	3/3/2022															
Haverhill to Military	6/15/2022	6/15/2022															

PARTICIPATION	FUNDING	FINANCIAL SUMMARY												
<p>Consultant</p> <p>SBE N/A</p> <p>Local N/A</p> <p>Contractor</p> <p>SBE 100%</p> <p>Local 100%</p>	<p>Fund Source (x 100K)</p>	<table border="1"> <thead> <tr> <th>Project Budget</th> <th>Committed</th> <th>% Committed</th> <th>Paid To Date</th> </tr> <tr> <th>A</th> <th>B</th> <th>C=B/A</th> <th>D</th> </tr> </thead> <tbody> <tr> <td>\$325,000</td> <td>\$111,164</td> <td>34.20%</td> <td>\$111,164</td> </tr> </tbody> </table>	Project Budget	Committed	% Committed	Paid To Date	A	B	C=B/A	D	\$325,000	\$111,164	34.20%	\$111,164
Project Budget	Committed	% Committed	Paid To Date											
A	B	C=B/A	D											
\$325,000	\$111,164	34.20%	\$111,164											

DESCRIPTION/TEAM	SCOPE/NOTES	SCHEDULE																					
<p>Project Title: Sections of Yamato Road</p> <p>Project Number: 1603</p> <p>BCC District: Multiple</p> <p>Delivery Method: Annual Striping Contract</p> <p>Category: S16-Striping</p> <p>Status: Construction</p> <p>Designer: N/A</p> <p>Contractor: Oglesby/Southwide</p> <p>Project Manager: Larry Kelly</p>	<p>Scope</p> <p>This project consists of restriping sections of Yamato Road.</p> <p>Notes</p> <p>Restriping along Yamato Road is done on an as needed basis as funding allows. The project is funded at \$75,000 in FY 2018 and \$50,000 in FY 2020 and FY 2023 for a total funding of \$175,000.</p>	<table border="1"> <thead> <tr> <th></th> <th>Original</th> <th>Actual</th> </tr> </thead> <tbody> <tr> <td>SR7 to Lyons</td> <td>8/1/2018</td> <td>11/1/2018</td> </tr> <tr> <td>Gatehouse Drive to Jog Road</td> <td>8/1/2018</td> <td>11/1/2018</td> </tr> <tr> <td>Cain to SR7</td> <td>8/19/2021</td> <td>1/31/2022</td> </tr> <tr> <td>Turnpike Overpass to Jog Road</td> <td>8/12/2022</td> <td>8/12/2022</td> </tr> <tr> <td>SR7 to Lyons</td> <td>11/19/2024</td> <td>11/19/2024</td> </tr> <tr> <td>Lyons to Boca Dr. West</td> <td>11/19/2024</td> <td>11/19/2024</td> </tr> </tbody> </table>		Original	Actual	SR7 to Lyons	8/1/2018	11/1/2018	Gatehouse Drive to Jog Road	8/1/2018	11/1/2018	Cain to SR7	8/19/2021	1/31/2022	Turnpike Overpass to Jog Road	8/12/2022	8/12/2022	SR7 to Lyons	11/19/2024	11/19/2024	Lyons to Boca Dr. West	11/19/2024	11/19/2024
	Original	Actual																					
SR7 to Lyons	8/1/2018	11/1/2018																					
Gatehouse Drive to Jog Road	8/1/2018	11/1/2018																					
Cain to SR7	8/19/2021	1/31/2022																					
Turnpike Overpass to Jog Road	8/12/2022	8/12/2022																					
SR7 to Lyons	11/19/2024	11/19/2024																					
Lyons to Boca Dr. West	11/19/2024	11/19/2024																					

PARTICIPATION	FUNDING	FINANCIAL SUMMARY												
<p>Consultant</p> <p>SBE N/A</p> <p>Local N/A</p> <p>Contractor</p> <p>SBE 100%</p> <p>Local 100%</p>	<p>Fund Source (x 100K)</p>	<table border="1"> <thead> <tr> <th>Project Budget</th> <th>Committed</th> <th>% Committed</th> <th>Paid To Date</th> </tr> <tr> <th>A</th> <th>B</th> <th>C=B/A</th> <th>D</th> </tr> </thead> <tbody> <tr> <td>\$175,000</td> <td>\$120,570</td> <td>68.90%</td> <td>\$120,570</td> </tr> </tbody> </table>	Project Budget	Committed	% Committed	Paid To Date	A	B	C=B/A	D	\$175,000	\$120,570	68.90%	\$120,570
Project Budget	Committed	% Committed	Paid To Date											
A	B	C=B/A	D											
\$175,000	\$120,570	68.90%	\$120,570											



Monthly Infrastructure Sales Tax Project Report

Small Cap Projects

Data Date: 2/19/2026

Report Date: 2/28/2026

DESCRIPTION/TEAM	SCOPE/NOTES	SCHEDULE																					
<p>Project Title: Sections of Indiantown Road Striping</p> <p>Project Number: 1604</p> <p>BCC District: 01</p> <p>Delivery Method: Annual Striping Contract</p> <p>Category: S16-Striping</p> <p>Status: Construction</p> <p>Designer: N/A</p> <p>Contractor: Oglesby/Southwide</p> <p>Project Manager: Larry Kelly</p>	<p>Scope</p> <p>This project consists of restriping sections of Indiantown Road.</p> <p>Notes</p> <p>Restriping along Indiantown Road is done on an as needed basis as funding allows. The project is funded at \$75,000 in FY 2018, and \$100,000 in FY 2021, FY 2023, and FY 2025 for a total funding of \$375,000.</p>	<table border="1"> <thead> <tr> <th></th> <th>Original</th> <th>Actual</th> </tr> </thead> <tbody> <tr> <td>Beeline Highway to east for 1/2 mile</td> <td>7/14/2018</td> <td>1/9/2019</td> </tr> <tr> <td>Cortona Blvd. to Taylor Rd.</td> <td>1/29/2022</td> <td>4/4/2022</td> </tr> <tr> <td>Brian Way to Jupiter Farms Rd.</td> <td>2/1/2022</td> <td>4/4/2022</td> </tr> <tr> <td>Pratt Whitney to Brian Way</td> <td>7/13/2023</td> <td>7/13/2023</td> </tr> <tr> <td>Beeline to Pratt Whitney</td> <td>8/28/2023</td> <td>8/28/2023</td> </tr> <tr> <td>Brian Way to Taylor Rd.</td> <td>3/19/2025</td> <td>3/19/2025</td> </tr> </tbody> </table>		Original	Actual	Beeline Highway to east for 1/2 mile	7/14/2018	1/9/2019	Cortona Blvd. to Taylor Rd.	1/29/2022	4/4/2022	Brian Way to Jupiter Farms Rd.	2/1/2022	4/4/2022	Pratt Whitney to Brian Way	7/13/2023	7/13/2023	Beeline to Pratt Whitney	8/28/2023	8/28/2023	Brian Way to Taylor Rd.	3/19/2025	3/19/2025
	Original	Actual																					
Beeline Highway to east for 1/2 mile	7/14/2018	1/9/2019																					
Cortona Blvd. to Taylor Rd.	1/29/2022	4/4/2022																					
Brian Way to Jupiter Farms Rd.	2/1/2022	4/4/2022																					
Pratt Whitney to Brian Way	7/13/2023	7/13/2023																					
Beeline to Pratt Whitney	8/28/2023	8/28/2023																					
Brian Way to Taylor Rd.	3/19/2025	3/19/2025																					

PARTICIPATION	FUNDING	FINANCIAL SUMMARY												
<p>Consultant</p> <p>SBE N/A</p> <p>Local N/A</p> <p>Contractor</p> <p>SBE 100%</p> <p>Local 100%</p>		<table border="1"> <thead> <tr> <th>Project Budget</th> <th>Committed</th> <th>% Committed</th> <th>Paid To Date</th> </tr> <tr> <th>A</th> <th>B</th> <th>C=B/A</th> <th>D</th> </tr> </thead> <tbody> <tr> <td>\$375,000</td> <td>\$206,140</td> <td>54.97%</td> <td>\$206,140</td> </tr> </tbody> </table>	Project Budget	Committed	% Committed	Paid To Date	A	B	C=B/A	D	\$375,000	\$206,140	54.97%	\$206,140
Project Budget	Committed	% Committed	Paid To Date											
A	B	C=B/A	D											
\$375,000	\$206,140	54.97%	\$206,140											

DESCRIPTION/TEAM	SCOPE/NOTES	SCHEDULE															
<p>Project Title: Sections of Hypoluxo Road</p> <p>Project Number: 1606</p> <p>BCC District: Multiple</p> <p>Delivery Method: Annual Striping Contract</p> <p>Category: S16-Striping</p> <p>Status: Construction</p> <p>Designer: N/A</p> <p>Contractor: Oglesby/Southwide</p> <p>Project Manager: Larry Kelly</p>	<p>Scope</p> <p>This project consists of restriping sections of Hypoluxo Road.</p> <p>Notes</p> <p>Restriping along Hypoluxo Road is done on an as needed basis as funding allows. The project is funded at \$75,000 in FY 2018, \$100,000 in FY 2021 and FY 2024 for a total funding of \$275,000.</p>	<table border="1"> <thead> <tr> <th></th> <th>Original</th> <th>Actual</th> </tr> </thead> <tbody> <tr> <td>Hagen Ranch Road to Jog Road</td> <td>8/1/2018</td> <td>10/19/2018</td> </tr> <tr> <td>Jog Road to Military Trail</td> <td>9/1/2018</td> <td>10/19/2018</td> </tr> <tr> <td>SR7 to Hagen Ranch Rd.</td> <td>7/1/2021</td> <td>12/8/2021</td> </tr> <tr> <td>SR7 to Lyons</td> <td>9/11/2023</td> <td>9/11/2023</td> </tr> </tbody> </table>		Original	Actual	Hagen Ranch Road to Jog Road	8/1/2018	10/19/2018	Jog Road to Military Trail	9/1/2018	10/19/2018	SR7 to Hagen Ranch Rd.	7/1/2021	12/8/2021	SR7 to Lyons	9/11/2023	9/11/2023
	Original	Actual															
Hagen Ranch Road to Jog Road	8/1/2018	10/19/2018															
Jog Road to Military Trail	9/1/2018	10/19/2018															
SR7 to Hagen Ranch Rd.	7/1/2021	12/8/2021															
SR7 to Lyons	9/11/2023	9/11/2023															

PARTICIPATION	FUNDING	FINANCIAL SUMMARY												
<p>Consultant</p> <p>SBE N/A</p> <p>Local N/A</p> <p>Contractor</p> <p>SBE 100%</p> <p>Local 100%</p>		<table border="1"> <thead> <tr> <th>Project Budget</th> <th>Committed</th> <th>% Committed</th> <th>Paid To Date</th> </tr> <tr> <th>A</th> <th>B</th> <th>C=B/A</th> <th>D</th> </tr> </thead> <tbody> <tr> <td>\$275,000</td> <td>\$102,518</td> <td>37.28%</td> <td>\$102,518</td> </tr> </tbody> </table>	Project Budget	Committed	% Committed	Paid To Date	A	B	C=B/A	D	\$275,000	\$102,518	37.28%	\$102,518
Project Budget	Committed	% Committed	Paid To Date											
A	B	C=B/A	D											
\$275,000	\$102,518	37.28%	\$102,518											



Monthly Infrastructure Sales Tax Project Report

Small Cap Projects

Data Date: 2/19/2026

Report Date: 2/28/2026

DESCRIPTION/TEAM	SCOPE/NOTES	SCHEDULE															
<p>Project Title: Sections of Australian Avenue</p> <p>Project Number: 1607</p> <p>BCC District: 07</p> <p>Delivery Method: Annual Striping Contract</p> <p>Category: S16-Striping</p> <p>Status: Construction</p> <p>Designer: N/A</p> <p>Contractor: Oglesby/Southwide</p> <p>Project Manager: Larry Kelly</p>	<p>Scope</p> <p>This project consists of restriping sections of Australian Avenue.</p> <p>Notes</p> <p>Restriping along Australian Avenue is done on an as needed basis as funding allows. The project is funded at \$75,000 in FY 2018, \$125,000 in FY 2022 and FY 2026 for a total funding of \$325,000.</p>	<table border="1"> <thead> <tr> <th></th> <th>Original</th> <th>Actual</th> </tr> </thead> <tbody> <tr> <td>Banyan Blvd. to Palm Beach Lake Blvd.</td> <td>7/1/2018</td> <td>1/29/2019</td> </tr> <tr> <td>Belvedere to Airport Hilton</td> <td>3/1/2022</td> <td>2/25/2022</td> </tr> <tr> <td>25th St. to 45th St.</td> <td>4/1/2022</td> <td>3/25/2022</td> </tr> <tr> <td>Old Okeechobee to Mercer</td> <td>4/10/2022</td> <td>4/12/2022</td> </tr> </tbody> </table>		Original	Actual	Banyan Blvd. to Palm Beach Lake Blvd.	7/1/2018	1/29/2019	Belvedere to Airport Hilton	3/1/2022	2/25/2022	25th St. to 45th St.	4/1/2022	3/25/2022	Old Okeechobee to Mercer	4/10/2022	4/12/2022
	Original	Actual															
Banyan Blvd. to Palm Beach Lake Blvd.	7/1/2018	1/29/2019															
Belvedere to Airport Hilton	3/1/2022	2/25/2022															
25th St. to 45th St.	4/1/2022	3/25/2022															
Old Okeechobee to Mercer	4/10/2022	4/12/2022															

PARTICIPATION	FUNDING	FINANCIAL SUMMARY												
<p>Consultant</p> <p>SBE N/A</p> <p>Local N/A</p> <p>Contractor</p> <p>SBE 100%</p> <p>Local 100%</p>	<p>Fund Source (x 100K)</p>	<table border="1"> <thead> <tr> <th>Project Budget</th> <th>Committed</th> <th>% Committed</th> <th>Paid To Date</th> </tr> <tr> <th>A</th> <th>B</th> <th>C=B/A</th> <th>D</th> </tr> </thead> <tbody> <tr> <td>\$325,000</td> <td>\$82,032</td> <td>25.24%</td> <td>\$82,032</td> </tr> </tbody> </table>	Project Budget	Committed	% Committed	Paid To Date	A	B	C=B/A	D	\$325,000	\$82,032	25.24%	\$82,032
Project Budget	Committed	% Committed	Paid To Date											
A	B	C=B/A	D											
\$325,000	\$82,032	25.24%	\$82,032											

DESCRIPTION/TEAM	SCOPE/NOTES	SCHEDULE															
<p>Project Title: Sections of Lantana Road</p> <p>Project Number: 1608</p> <p>BCC District: Multiple</p> <p>Delivery Method: Annual Striping Contract</p> <p>Category: S16-Striping</p> <p>Status: Construction</p> <p>Designer: N/A</p> <p>Contractor: Oglesby/Southwide</p> <p>Project Manager: Larry Kelly</p>	<p>Scope</p> <p>This project consists of restriping sections of Lantana Road.</p> <p>Notes</p> <p>The project is funded at \$75,000 in FY2018, \$100,000 FY2022, FY2024 and FY2026 for a total funding of \$375,000.</p>	<table border="1"> <thead> <tr> <th></th> <th>Original</th> <th>Actual</th> </tr> </thead> <tbody> <tr> <td>Palm Breezes Dr. to S. Congress Ave.</td> <td>7/1/2021</td> <td>7/1/2021</td> </tr> <tr> <td>Hagen Ranch Rd to Jog Rd</td> <td>3/25/2024</td> <td>3/25/2024</td> </tr> <tr> <td>Jog Rd to Haverhill Rd</td> <td>6/11/2025</td> <td>6/11/2025</td> </tr> <tr> <td>Coongress to I-95</td> <td>7/7/2025</td> <td>7/7/2025</td> </tr> </tbody> </table>		Original	Actual	Palm Breezes Dr. to S. Congress Ave.	7/1/2021	7/1/2021	Hagen Ranch Rd to Jog Rd	3/25/2024	3/25/2024	Jog Rd to Haverhill Rd	6/11/2025	6/11/2025	Coongress to I-95	7/7/2025	7/7/2025
	Original	Actual															
Palm Breezes Dr. to S. Congress Ave.	7/1/2021	7/1/2021															
Hagen Ranch Rd to Jog Rd	3/25/2024	3/25/2024															
Jog Rd to Haverhill Rd	6/11/2025	6/11/2025															
Coongress to I-95	7/7/2025	7/7/2025															

PARTICIPATION	FUNDING	FINANCIAL SUMMARY												
<p>Consultant</p> <p>SBE N/A</p> <p>Local N/A</p> <p>Contractor</p> <p>SBE 100%</p> <p>Local 100%</p>	<p>Fund Source (x 100K)</p>	<table border="1"> <thead> <tr> <th>Project Budget</th> <th>Committed</th> <th>% Committed</th> <th>Paid To Date</th> </tr> <tr> <th>A</th> <th>B</th> <th>C=B/A</th> <th>D</th> </tr> </thead> <tbody> <tr> <td>\$375,000</td> <td>\$137,139</td> <td>36.57%</td> <td>\$137,139</td> </tr> </tbody> </table>	Project Budget	Committed	% Committed	Paid To Date	A	B	C=B/A	D	\$375,000	\$137,139	36.57%	\$137,139
Project Budget	Committed	% Committed	Paid To Date											
A	B	C=B/A	D											
\$375,000	\$137,139	36.57%	\$137,139											



Monthly Infrastructure Sales Tax Project Report

Small Cap Projects

Data Date: 2/19/2026

Report Date: 2/28/2026

DESCRIPTION/TEAM	SCOPE/NOTES	SCHEDULE						
<p>Project Title: Sections of Okeechobee Blvd.</p> <p>Project Number: 1609</p> <p>BCC District: Multiple</p> <p>Delivery Method: Annual Striping Contract</p> <p>Category: S16-Striping</p> <p>Status: Construction</p> <p>Designer: N/A</p> <p>Contractor: Oglesby/Southwide</p> <p>Project Manager: Larry Kelly</p>	<p>Scope</p> <p>This project consists of restriping sections of Okeechobee Boulevard.</p> <p>Notes</p> <p>Restriping along Okeechobee Blvd. is done on an as needed basis as funding allows. The project is funded at \$50,000 in FY 2018 and FY 2023, and \$100,000 in FY 2026 for a total funding of \$200,000.</p>	<table border="1"> <thead> <tr> <th></th> <th style="text-align: center;">Original</th> <th style="text-align: center;">Actual</th> </tr> </thead> <tbody> <tr> <td>Royal Palm Beach Blvd to SR 7</td> <td style="text-align: center;">5/14/2018</td> <td style="text-align: center;">7/14/2018</td> </tr> </tbody> </table>		Original	Actual	Royal Palm Beach Blvd to SR 7	5/14/2018	7/14/2018
	Original	Actual						
Royal Palm Beach Blvd to SR 7	5/14/2018	7/14/2018						

PARTICIPATION	FUNDING	FINANCIAL SUMMARY												
<p>Consultant</p> <p>SBE N/A</p> <p>Local N/A</p> <p>Contractor</p> <p>SBE 100%</p> <p>Local 100%</p>		<table border="1"> <thead> <tr> <th style="text-align: center;">Project Budget</th> <th style="text-align: center;">Committed</th> <th style="text-align: center;">% Committed</th> <th style="text-align: center;">Paid To Date</th> </tr> <tr> <th style="text-align: center;">A</th> <th style="text-align: center;">B</th> <th style="text-align: center;">C=B/A</th> <th style="text-align: center;">D</th> </tr> </thead> <tbody> <tr> <td style="text-align: center;">\$200,000</td> <td style="text-align: center;">\$44,835</td> <td style="text-align: center;">22.42%</td> <td style="text-align: center;">\$44,835</td> </tr> </tbody> </table>	Project Budget	Committed	% Committed	Paid To Date	A	B	C=B/A	D	\$200,000	\$44,835	22.42%	\$44,835
Project Budget	Committed	% Committed	Paid To Date											
A	B	C=B/A	D											
\$200,000	\$44,835	22.42%	\$44,835											

DESCRIPTION/TEAM	SCOPE/NOTES	SCHEDULE									
<p>Project Title: Sections of 10th Avenue North</p> <p>Project Number: 1610</p> <p>BCC District: 03</p> <p>Delivery Method: Annual Striping Contract</p> <p>Category: S16-Striping</p> <p>Status: Construction</p> <p>Designer: N/A</p> <p>Contractor: Oglesby/Southwide</p> <p>Project Manager: Larry Kelly</p>	<p>Scope</p> <p>This project consists of restriping sections of 10th Avenue North.</p> <p>Notes</p> <p>Restriping along 10th Avenue North is done on an as needed basis as funding allows. The project is funded at \$50,000 in FY 2018 and FY 2023, and \$100,000 in FY 2026 for a total funding of \$200,000.</p>	<table border="1"> <thead> <tr> <th></th> <th style="text-align: center;">Original</th> <th style="text-align: center;">Actual</th> </tr> </thead> <tbody> <tr> <td>Pinehurst Dr. to Jog Rd.</td> <td style="text-align: center;">5/15/2018</td> <td style="text-align: center;">8/9/2018</td> </tr> <tr> <td>Congress to Florida Mango</td> <td style="text-align: center;">4/4/2021</td> <td style="text-align: center;">3/9/2021</td> </tr> </tbody> </table>		Original	Actual	Pinehurst Dr. to Jog Rd.	5/15/2018	8/9/2018	Congress to Florida Mango	4/4/2021	3/9/2021
	Original	Actual									
Pinehurst Dr. to Jog Rd.	5/15/2018	8/9/2018									
Congress to Florida Mango	4/4/2021	3/9/2021									

PARTICIPATION	FUNDING	FINANCIAL SUMMARY												
<p>Consultant</p> <p>SBE N/A</p> <p>Local N/A</p> <p>Contractor</p> <p>SBE 100%</p> <p>Local 100%</p>		<table border="1"> <thead> <tr> <th style="text-align: center;">Project Budget</th> <th style="text-align: center;">Committed</th> <th style="text-align: center;">% Committed</th> <th style="text-align: center;">Paid To Date</th> </tr> <tr> <th style="text-align: center;">A</th> <th style="text-align: center;">B</th> <th style="text-align: center;">C=B/A</th> <th style="text-align: center;">D</th> </tr> </thead> <tbody> <tr> <td style="text-align: center;">\$200,000</td> <td style="text-align: center;">\$22,553</td> <td style="text-align: center;">11.28%</td> <td style="text-align: center;">\$22,553</td> </tr> </tbody> </table>	Project Budget	Committed	% Committed	Paid To Date	A	B	C=B/A	D	\$200,000	\$22,553	11.28%	\$22,553
Project Budget	Committed	% Committed	Paid To Date											
A	B	C=B/A	D											
\$200,000	\$22,553	11.28%	\$22,553											



Monthly Infrastructure Sales Tax Project Report

Small Cap Projects

Data Date: 2/19/2026

Report Date: 2/28/2026

DESCRIPTION/TEAM	SCOPE/NOTES	SCHEDULE																		
<p>Project Title: Sections of 45th Street</p> <p>Project Number: 1611</p> <p>BCC District: 07</p> <p>Delivery Method: Annual Striping Contract</p> <p>Category: S16-Striping</p> <p>Status: Construction</p> <p>Designer: N/A</p> <p>Contractor: Oglesby/Southwide</p> <p>Project Manager: Larry Kelly</p>	<p>Scope</p> <p>This project consists of restriping sections of 45th Street.</p> <p>Notes</p> <p>Restriping along 45th Street is done on an as needed basis as funding allows. The project is funded at \$50,000 in FY 2018 and FY 2023, and \$75,000 in FY 2026 for a total funding of \$175,000.</p>	<table border="1"> <thead> <tr> <th></th> <th>Original</th> <th>Actual</th> </tr> </thead> <tbody> <tr> <td>Military Trail to I-95</td> <td>7/1/2018</td> <td>1/16/2019</td> </tr> <tr> <td>Greenwood Ave. to Broadway Blvd.</td> <td>3/11/2019</td> <td>3/18/2019</td> </tr> <tr> <td>Haverhill to Military</td> <td>6/25/2021</td> <td>6/25/2021</td> </tr> <tr> <td>Military to Northpoint</td> <td>12/4/2024</td> <td>12/11/2024</td> </tr> <tr> <td>Jog to Haverhill</td> <td>2/20/2025</td> <td>2/20/2025</td> </tr> </tbody> </table>		Original	Actual	Military Trail to I-95	7/1/2018	1/16/2019	Greenwood Ave. to Broadway Blvd.	3/11/2019	3/18/2019	Haverhill to Military	6/25/2021	6/25/2021	Military to Northpoint	12/4/2024	12/11/2024	Jog to Haverhill	2/20/2025	2/20/2025
	Original	Actual																		
Military Trail to I-95	7/1/2018	1/16/2019																		
Greenwood Ave. to Broadway Blvd.	3/11/2019	3/18/2019																		
Haverhill to Military	6/25/2021	6/25/2021																		
Military to Northpoint	12/4/2024	12/11/2024																		
Jog to Haverhill	2/20/2025	2/20/2025																		

PARTICIPATION	FUNDING	FINANCIAL SUMMARY												
<p>Consultant</p> <p>SBE N/A</p> <p>Local N/A</p> <p>Contractor</p> <p>SBE 100%</p> <p>Local 100%</p>		<table border="1"> <thead> <tr> <th>Project Budget</th> <th>Committed</th> <th>% Committed</th> <th>Paid To Date</th> </tr> <tr> <th>A</th> <th>B</th> <th>C=B/A</th> <th>D</th> </tr> </thead> <tbody> <tr> <td>\$175,000</td> <td>\$96,686</td> <td>55.25%</td> <td>\$96,686</td> </tr> </tbody> </table>	Project Budget	Committed	% Committed	Paid To Date	A	B	C=B/A	D	\$175,000	\$96,686	55.25%	\$96,686
Project Budget	Committed	% Committed	Paid To Date											
A	B	C=B/A	D											
\$175,000	\$96,686	55.25%	\$96,686											

DESCRIPTION/TEAM	SCOPE/NOTES	SCHEDULE																		
<p>Project Title: Congress Ave. over PBC Lat. 2 Canal (934251)</p> <p>Project Number: 1614</p> <p>BCC District: 02</p> <p>Delivery Method: Design CCNA</p> <p>Category: B08-Bridge Replacements</p> <p>Status: Construction</p> <p>Designer: Stantec</p> <p>Contractor: TBD (bid)</p> <p>Project Manager: Maroun Azzi</p>	<p>Scope</p> <p>This project will replace an existing bridge that was built over 50 years ago. The new bridge will improve traffic safety (lane widths, geometry, and parapets), improve roadway drainage, and enhance pedestrian sidewalk safety.</p> <p>Notes</p> <p>Design is complete - pending bid. FY 2019 IST \$200,000; FY 2023 IST \$1,000,000 The scheduled dates have been revised to depict design, utility and permitting delays.</p>	<table border="1"> <thead> <tr> <th></th> <th>Original</th> <th>Actual</th> </tr> </thead> <tbody> <tr> <td>Design Contract Notice to Proceed</td> <td>2/1/2020</td> <td>1/15/2020</td> </tr> <tr> <td>Design Completion</td> <td>6/1/2026</td> <td>12/1/2025</td> </tr> <tr> <td>Construction Bid Date</td> <td>10/1/2026</td> <td></td> </tr> <tr> <td>Construction Start</td> <td>1/1/2027</td> <td></td> </tr> <tr> <td>Construction Complete</td> <td>1/1/2029</td> <td></td> </tr> </tbody> </table>		Original	Actual	Design Contract Notice to Proceed	2/1/2020	1/15/2020	Design Completion	6/1/2026	12/1/2025	Construction Bid Date	10/1/2026		Construction Start	1/1/2027		Construction Complete	1/1/2029	
	Original	Actual																		
Design Contract Notice to Proceed	2/1/2020	1/15/2020																		
Design Completion	6/1/2026	12/1/2025																		
Construction Bid Date	10/1/2026																			
Construction Start	1/1/2027																			
Construction Complete	1/1/2029																			

PARTICIPATION	FUNDING	FINANCIAL SUMMARY												
<p>Consultant</p> <p>SBE 31%</p> <p>Local 100%</p> <p>Contractor</p> <p>SBE TBD</p> <p>Local TBD</p>		<table border="1"> <thead> <tr> <th>Project Budget</th> <th>Committed</th> <th>% Committed</th> <th>Paid To Date</th> </tr> <tr> <th>A</th> <th>B</th> <th>C=B/A</th> <th>D</th> </tr> </thead> <tbody> <tr> <td>\$1,200,000</td> <td>\$189,077</td> <td>15.76%</td> <td>\$133,039</td> </tr> </tbody> </table>	Project Budget	Committed	% Committed	Paid To Date	A	B	C=B/A	D	\$1,200,000	\$189,077	15.76%	\$133,039
Project Budget	Committed	% Committed	Paid To Date											
A	B	C=B/A	D											
\$1,200,000	\$189,077	15.76%	\$133,039											



Monthly Infrastructure Sales Tax Project Report

Small Cap Projects

Data Date: 2/19/2026

Report Date: 2/28/2026

DESCRIPTION/TEAM	SCOPE/NOTES	SCHEDULE																		
<p>Project Title: Sam Senter Rd. over Ocean Canal (SFWMD Lat. 13 Canal)</p> <p>Project Number: 1615</p> <p>BCC District: 06</p> <p>Delivery Method: Design CCNA</p> <p>Category: B08-Bridge Replacements</p> <p>Status: Construction</p> <p>Designer: Stanley Consultants</p> <p>Contractor: TBD (bid)</p> <p>Project Manager: Maroun Azzi</p>	<p>Scope</p> <p>This project will replace an existing bridge that was built over 50 years ago. The new bridge will improve traffic safety (lane widths, geometry, and parapets), improve roadway drainage and turning movements and enhance pedestrian sidewalk safety.</p> <p>Notes</p> <p>The project is funded with 5-Year Road Program (RP) funding and IST funding. Design is complete. Construction of project (including associated roadway improvements) is currently est. at \$16m. The IST partially funds design (\$150k) in FY19 and const. (\$450k) in FY22.</p>	<table border="1"> <thead> <tr> <th></th> <th>Original</th> <th>Actual</th> </tr> </thead> <tbody> <tr> <td>Design Contract Notice to Proceed</td> <td>12/1/2020</td> <td>6/10/2021</td> </tr> <tr> <td>Design Completion</td> <td>8/1/2025</td> <td>12/1/2025</td> </tr> <tr> <td>Construction Bid Date</td> <td>4/6/2026</td> <td></td> </tr> <tr> <td>Construction Start</td> <td>12/1/2026</td> <td></td> </tr> <tr> <td>Construction Complete</td> <td>12/1/2028</td> <td></td> </tr> </tbody> </table>		Original	Actual	Design Contract Notice to Proceed	12/1/2020	6/10/2021	Design Completion	8/1/2025	12/1/2025	Construction Bid Date	4/6/2026		Construction Start	12/1/2026		Construction Complete	12/1/2028	
	Original	Actual																		
Design Contract Notice to Proceed	12/1/2020	6/10/2021																		
Design Completion	8/1/2025	12/1/2025																		
Construction Bid Date	4/6/2026																			
Construction Start	12/1/2026																			
Construction Complete	12/1/2028																			

PARTICIPATION	FUNDING	FINANCIAL SUMMARY												
<p>Consultant</p> <p>SBE 21.2%</p> <p>Local 100%</p> <p>Contractor</p> <p>SBE TBD</p> <p>Local TBD</p>		<table border="1"> <thead> <tr> <th>Project Budget</th> <th>Committed</th> <th>% Committed</th> <th>Paid To Date</th> </tr> <tr> <th>A</th> <th>B</th> <th>C=B/A</th> <th>D</th> </tr> </thead> <tbody> <tr> <td>\$600,000</td> <td>\$90,558</td> <td>15.09%</td> <td>\$90,558</td> </tr> </tbody> </table>	Project Budget	Committed	% Committed	Paid To Date	A	B	C=B/A	D	\$600,000	\$90,558	15.09%	\$90,558
Project Budget	Committed	% Committed	Paid To Date											
A	B	C=B/A	D											
\$600,000	\$90,558	15.09%	\$90,558											

DESCRIPTION/TEAM	SCOPE/NOTES	SCHEDULE																		
<p>Project Title: A1A from US1 to Donald Ross</p> <p>Project Number: 1617</p> <p>BCC District: 01</p> <p>Delivery Method: Design CCNA</p> <p>Category: D04-Drainage Improvements</p> <p>Status: Bidding</p> <p>Designer: Baxter Woodman</p> <p>Contractor: TBD</p> <p>Project Manager: Carlos Bojorge</p>	<p>Scope</p> <p>The project involves addressing drainage issues along A 1A (US 1 to Donald Ross) to alleviate chronic or extended flooding. Drainage improvements include adding a new system and outfall, and adding exfiltration trench. The project is funded with IST funding (\$1m) and ARPA funding (\$500k).</p> <p>Notes</p> <p>Design is complete. FY 2019 IST \$100,000; FY 2021 IST \$400,000; FY 2022 IST \$500,000 The scheduled dates have been revised to depict coordination, design, utility and permitting delays.</p>	<table border="1"> <thead> <tr> <th></th> <th>Original</th> <th>Actual</th> </tr> </thead> <tbody> <tr> <td>Design Contract Notice to Proceed</td> <td>4/28/2020</td> <td>5/6/2020</td> </tr> <tr> <td>Design Completion</td> <td>6/1/2025</td> <td>12/1/2025</td> </tr> <tr> <td>Construction Bid Date</td> <td>4/1/2026</td> <td></td> </tr> <tr> <td>Construction Start</td> <td>12/1/2026</td> <td></td> </tr> <tr> <td>Construction Complete</td> <td>12/1/2027</td> <td></td> </tr> </tbody> </table>		Original	Actual	Design Contract Notice to Proceed	4/28/2020	5/6/2020	Design Completion	6/1/2025	12/1/2025	Construction Bid Date	4/1/2026		Construction Start	12/1/2026		Construction Complete	12/1/2027	
	Original	Actual																		
Design Contract Notice to Proceed	4/28/2020	5/6/2020																		
Design Completion	6/1/2025	12/1/2025																		
Construction Bid Date	4/1/2026																			
Construction Start	12/1/2026																			
Construction Complete	12/1/2027																			

PARTICIPATION	FUNDING	FINANCIAL SUMMARY												
<p>Consultant</p> <p>SBE 27.8%</p> <p>Local 100%</p> <p>Contractor</p> <p>SBE TBD</p> <p>Local TBD</p>		<table border="1"> <thead> <tr> <th>Project Budget</th> <th>Committed</th> <th>% Committed</th> <th>Paid To Date</th> </tr> <tr> <th>A</th> <th>B</th> <th>C=B/A</th> <th>D</th> </tr> </thead> <tbody> <tr> <td>\$1,000,000</td> <td>\$125,874</td> <td>12.59%</td> <td>\$120,616</td> </tr> </tbody> </table>	Project Budget	Committed	% Committed	Paid To Date	A	B	C=B/A	D	\$1,000,000	\$125,874	12.59%	\$120,616
Project Budget	Committed	% Committed	Paid To Date											
A	B	C=B/A	D											
\$1,000,000	\$125,874	12.59%	\$120,616											



Monthly Infrastructure Sales Tax Project Report

Small Cap Projects

Data Date: 2/19/2026

Report Date: 2/28/2026

DESCRIPTION/TEAM	SCOPE/NOTES	SCHEDULE															
<p>Project Title: Lantana Rd. from I-95 to US-1</p> <p>Project Number: 1620</p> <p>BCC District: 07</p> <p>Delivery Method: Annual Construction Contract</p> <p>Category: R04-Resurfacing</p> <p>Status: Construction</p> <p>Designer: N/A</p> <p>Contractor: M&M Asphalt Maintenance, Inc.</p> <p>Project Manager: Chase Miller</p>	<p>Scope</p> <p>Resurfacing 1.1 miles (5.5 lane miles) of Lantana Road from I-95 to US 1.</p> <p>FY2019 IST \$500,000</p> <p>FY2022 IST \$100,000</p> <p>Notes</p> <p>Outstanding work includes milling and paving, updating ADA ramps, restriping the road, and replacing traffic loops.</p>	<table border="1"> <thead> <tr> <th></th> <th>Original</th> <th>Actual</th> </tr> </thead> <tbody> <tr> <td>Milling and Pavement Complete</td> <td>8/1/2026</td> <td></td> </tr> <tr> <td>Traffic Striping Complete</td> <td>9/15/2026</td> <td></td> </tr> <tr> <td>ADA (Curb/Cut Ramps) Complete</td> <td>10/1/2026</td> <td></td> </tr> <tr> <td>Traffic Loops Complete</td> <td>12/14/2026</td> <td></td> </tr> </tbody> </table>		Original	Actual	Milling and Pavement Complete	8/1/2026		Traffic Striping Complete	9/15/2026		ADA (Curb/Cut Ramps) Complete	10/1/2026		Traffic Loops Complete	12/14/2026	
	Original	Actual															
Milling and Pavement Complete	8/1/2026																
Traffic Striping Complete	9/15/2026																
ADA (Curb/Cut Ramps) Complete	10/1/2026																
Traffic Loops Complete	12/14/2026																

PARTICIPATION	FUNDING	FINANCIAL SUMMARY												
<p>Consultant</p> <p>SBE N/A</p> <p>Local N/A</p> <p>Contractor</p> <p>SBE 15%</p> <p>Local 100%</p>		<table border="1"> <thead> <tr> <th>Project Budget</th> <th>Committed</th> <th>% Committed</th> <th>Paid To Date</th> </tr> <tr> <th>A</th> <th>B</th> <th>C=B/A</th> <th>D</th> </tr> </thead> <tbody> <tr> <td>\$600,000</td> <td>\$575,984</td> <td>96.00%</td> <td>\$125,984</td> </tr> </tbody> </table>	Project Budget	Committed	% Committed	Paid To Date	A	B	C=B/A	D	\$600,000	\$575,984	96.00%	\$125,984
Project Budget	Committed	% Committed	Paid To Date											
A	B	C=B/A	D											
\$600,000	\$575,984	96.00%	\$125,984											

DESCRIPTION/TEAM	SCOPE/NOTES	SCHEDULE															
<p>Project Title: Congress Ave. north of Linton Blvd.</p> <p>Project Number: 1636</p> <p>BCC District: 07</p> <p>Delivery Method: Design CCNA</p> <p>Category: D04-Drainage Improvements</p> <p>Status: Design</p> <p>Designer: CDI</p> <p>Contractor: TBD</p> <p>Project Manager: Will Carey</p>	<p>Scope</p> <p>The project involves addressing drainage issues along Congress Ave . (north of Linton) to alleviate chronic or extended flooding. Drainage improvements include adding exfiltration trench. The project is funded with IST funding (\$500k) and ARPA funding (\$500k).</p> <p>Notes</p> <p>Study completed. Design is ongoing (45% complete).</p>	<table border="1"> <thead> <tr> <th></th> <th>Original</th> <th>Actual</th> </tr> </thead> <tbody> <tr> <td>Design Contract Notice to Proceed</td> <td>4/29/2020</td> <td>4/29/2020</td> </tr> <tr> <td>Design Completion</td> <td>9/1/2026</td> <td></td> </tr> <tr> <td>Construction Start</td> <td>12/1/2026</td> <td></td> </tr> <tr> <td>Construction Complete</td> <td>12/1/2027</td> <td></td> </tr> </tbody> </table>		Original	Actual	Design Contract Notice to Proceed	4/29/2020	4/29/2020	Design Completion	9/1/2026		Construction Start	12/1/2026		Construction Complete	12/1/2027	
	Original	Actual															
Design Contract Notice to Proceed	4/29/2020	4/29/2020															
Design Completion	9/1/2026																
Construction Start	12/1/2026																
Construction Complete	12/1/2027																

PARTICIPATION	FUNDING	FINANCIAL SUMMARY												
<p>Consultant</p> <p>SBE 100%</p> <p>Local 100%</p> <p>Contractor</p> <p>SBE TBD</p> <p>Local TBD</p>		<table border="1"> <thead> <tr> <th>Project Budget</th> <th>Committed</th> <th>% Committed</th> <th>Paid To Date</th> </tr> <tr> <th>A</th> <th>B</th> <th>C=B/A</th> <th>D</th> </tr> </thead> <tbody> <tr> <td>\$500,000</td> <td>\$80,516</td> <td>16.10%</td> <td>\$80,516</td> </tr> </tbody> </table>	Project Budget	Committed	% Committed	Paid To Date	A	B	C=B/A	D	\$500,000	\$80,516	16.10%	\$80,516
Project Budget	Committed	% Committed	Paid To Date											
A	B	C=B/A	D											
\$500,000	\$80,516	16.10%	\$80,516											



Monthly Infrastructure Sales Tax Project Report

Small Cap Projects

Data Date: 2/19/2026

Report Date: 2/28/2026

DESCRIPTION/TEAM	SCOPE/NOTES	SCHEDULE									
<p>Project Title: Countywide Street Lighting FY20 (frmly Boca Chase Driv</p> <p>Project Number: 1648</p> <p>BCC District: CW</p> <p>Delivery Method: Florida Power and Light</p> <p>Category: S14-Street Lighting</p> <p>Status: Construction</p> <p>Designer: Florida Power & Light</p> <p>Contractor: Florida Power & Light</p> <p>Project Manager: May Cheng</p>	<p>Scope</p> <p>These projects replace the high pressure sodium lights with LED lights. Many of the street lights along Conty roads are owned and maintained by FPL with the County paying all the operation and maintenance costs. FPL will be responsible for final design and installation and the County will reimburse FPL.</p> <p>Notes</p> <p>There are two street lighting projects (road segments) funded (\$12,000) for conversion in FY 2020. All projects have been forwarded to FPL for design and installation. The result will provide a cost savings, better quality illumination and a more desirable environmental light source.</p>	<table border="1"> <thead> <tr> <th></th> <th style="text-align: center;">Original</th> <th style="text-align: center;">Actual</th> </tr> </thead> <tbody> <tr> <td>Boca Chase/Cain to 102 Way S.</td> <td></td> <td></td> </tr> <tr> <td>Lake Worth Rd @Pinehurst</td> <td></td> <td></td> </tr> </tbody> </table>		Original	Actual	Boca Chase/Cain to 102 Way S.			Lake Worth Rd @Pinehurst		
	Original	Actual									
Boca Chase/Cain to 102 Way S.											
Lake Worth Rd @Pinehurst											

PARTICIPATION	FUNDING	FINANCIAL SUMMARY												
<p>Consultant</p> <p>SBE N/A</p> <p>Local N/A</p> <p>Contractor</p> <p>SBE N/A</p> <p>Local N/A</p>	<p style="text-align: center;">Fund Source (x 100K)</p>	<table border="1"> <thead> <tr> <th>Project Budget</th> <th>Committed</th> <th>% Committed</th> <th>Paid To Date</th> </tr> <tr> <th style="text-align: center;">A</th> <th style="text-align: center;">B</th> <th style="text-align: center;">C=B/A</th> <th style="text-align: center;">D</th> </tr> </thead> <tbody> <tr> <td style="text-align: right;">\$12,000</td> <td style="text-align: right;">\$494</td> <td style="text-align: right;">4.12%</td> <td style="text-align: right;">\$494</td> </tr> </tbody> </table>	Project Budget	Committed	% Committed	Paid To Date	A	B	C=B/A	D	\$12,000	\$494	4.12%	\$494
Project Budget	Committed	% Committed	Paid To Date											
A	B	C=B/A	D											
\$12,000	\$494	4.12%	\$494											

DESCRIPTION/TEAM	SCOPE/NOTES	SCHEDULE						
<p>Project Title: Sections of Lawrence Road</p> <p>Project Number: 1648</p> <p>BCC District: Multiple</p> <p>Delivery Method: Annual Striping Contract</p> <p>Category: S16-Striping</p> <p>Status: Construction</p> <p>Designer: N/A</p> <p>Contractor: Southwide</p> <p>Project Manager: Larry Kelly</p>	<p>Scope</p> <p>This project consists of restriping sections of Lawrence Road.</p> <p>Notes</p> <p>Restriping along Lawrence Road is done on an as needed basis as funding allows. The project is funded at \$50,000 in FY 2020 and FY 2023, and \$100,000 in FY 2025, for a total funding of \$200,000.</p>	<table border="1"> <thead> <tr> <th></th> <th style="text-align: center;">Original</th> <th style="text-align: center;">Actual</th> </tr> </thead> <tbody> <tr> <td>Kewanee Rd. to Lantana</td> <td style="text-align: center;">3/1/2021</td> <td style="text-align: center;">3/22/2021</td> </tr> </tbody> </table>		Original	Actual	Kewanee Rd. to Lantana	3/1/2021	3/22/2021
	Original	Actual						
Kewanee Rd. to Lantana	3/1/2021	3/22/2021						

PARTICIPATION	FUNDING	FINANCIAL SUMMARY												
<p>Consultant</p> <p>SBE N/A</p> <p>Local 100%</p> <p>Contractor</p> <p>SBE 100%</p> <p>Local 100%</p>	<p style="text-align: center;">Fund Source (x 100K)</p>	<table border="1"> <thead> <tr> <th>Project Budget</th> <th>Committed</th> <th>% Committed</th> <th>Paid To Date</th> </tr> <tr> <th style="text-align: center;">A</th> <th style="text-align: center;">B</th> <th style="text-align: center;">C=B/A</th> <th style="text-align: center;">D</th> </tr> </thead> <tbody> <tr> <td style="text-align: right;">\$200,000</td> <td style="text-align: right;">\$10,852</td> <td style="text-align: right;">5.43%</td> <td style="text-align: right;">\$10,852</td> </tr> </tbody> </table>	Project Budget	Committed	% Committed	Paid To Date	A	B	C=B/A	D	\$200,000	\$10,852	5.43%	\$10,852
Project Budget	Committed	% Committed	Paid To Date											
A	B	C=B/A	D											
\$200,000	\$10,852	5.43%	\$10,852											



Monthly Infrastructure Sales Tax Project Report

Small Cap Projects

Data Date: 2/19/2026

Report Date: 2/28/2026

DESCRIPTION/TEAM	SCOPE/NOTES	SCHEDULE															
<p>Project Title: Sections of Donald Ross Road</p> <p>Project Number: 1649</p> <p>BCC District: 01</p> <p>Delivery Method: Annual Striping Contract</p> <p>Category: S16-Striping</p> <p>Status: Construction</p> <p>Designer: N/A</p> <p>Contractor: Southwide</p> <p>Project Manager: Larry Kelly</p>	<p>Scope</p> <p>This project consists of restriping sections of Donald Ross Road.</p> <p>Notes</p> <p>Restriping along Donald Ross Road is done on an as needed basis as funding allows. The project is funded at \$50,000 in FY 2020, \$125,000 in FY 2024, and \$25,000 in FY 2026 for a total funding of \$200,000.</p>	<table border="1"> <thead> <tr> <th></th> <th>Original</th> <th>Actual</th> </tr> </thead> <tbody> <tr> <td>64th Dr. to Jog Road</td> <td>4/2/2021</td> <td>3/6/2021</td> </tr> <tr> <td>Prosperity Farms Road to US 1</td> <td>4/21/2022</td> <td>4/19/2022</td> </tr> <tr> <td>Alt. A-1-A to Prosperity Farms Road</td> <td>8/10/2023</td> <td>8/10/2023</td> </tr> <tr> <td>US 1 to A-1-A</td> <td>8/24/2023</td> <td>8/24/2023</td> </tr> </tbody> </table>		Original	Actual	64th Dr. to Jog Road	4/2/2021	3/6/2021	Prosperity Farms Road to US 1	4/21/2022	4/19/2022	Alt. A-1-A to Prosperity Farms Road	8/10/2023	8/10/2023	US 1 to A-1-A	8/24/2023	8/24/2023
	Original	Actual															
64th Dr. to Jog Road	4/2/2021	3/6/2021															
Prosperity Farms Road to US 1	4/21/2022	4/19/2022															
Alt. A-1-A to Prosperity Farms Road	8/10/2023	8/10/2023															
US 1 to A-1-A	8/24/2023	8/24/2023															

PARTICIPATION	FUNDING	FINANCIAL SUMMARY												
<p>Consultant</p> <p>SBE N/A</p> <p>Local N/A</p> <p>Contractor</p> <p>SBE 100%</p> <p>Local 100%</p>		<table border="1"> <thead> <tr> <th>Project Budget</th> <th>Committed</th> <th>% Committed</th> <th>Paid To Date</th> </tr> <tr> <th>A</th> <th>B</th> <th>C=B/A</th> <th>D</th> </tr> </thead> <tbody> <tr> <td>\$200,000</td> <td>\$49,346</td> <td>24.67%</td> <td>\$49,346</td> </tr> </tbody> </table>	Project Budget	Committed	% Committed	Paid To Date	A	B	C=B/A	D	\$200,000	\$49,346	24.67%	\$49,346
Project Budget	Committed	% Committed	Paid To Date											
A	B	C=B/A	D											
\$200,000	\$49,346	24.67%	\$49,346											

DESCRIPTION/TEAM	SCOPE/NOTES	SCHEDULE						
<p>Project Title: Sections of Summit Blvd</p> <p>Project Number: 1653</p> <p>BCC District: 03</p> <p>Delivery Method: Annual Striping Contract</p> <p>Category: S16-Striping</p> <p>Status: Construction</p> <p>Designer: N/A</p> <p>Contractor: Southwide</p> <p>Project Manager: Larry Kelly</p>	<p>Scope</p> <p>This project consists of restriping sections of Summit Blvd.</p> <p>Notes</p> <p>Restriping along Summit Blvd. is done on an as needed basis as funding allows. \$75,000 of the projects \$200,000 funding was advanced to FY 2018 (BT 2018 0599). The project is now funded at \$75,000 in FY 2018, \$50,000 in FY 2020, and \$75,000 in FY 2025 for a total funding of \$200,000.</p>	<table border="1"> <thead> <tr> <th></th> <th>Original</th> <th>Actual</th> </tr> </thead> <tbody> <tr> <td>Congress Ave. to Parker Ave.</td> <td>12/1/2018</td> <td>11/30/2018</td> </tr> </tbody> </table>		Original	Actual	Congress Ave. to Parker Ave.	12/1/2018	11/30/2018
	Original	Actual						
Congress Ave. to Parker Ave.	12/1/2018	11/30/2018						

PARTICIPATION	FUNDING	FINANCIAL SUMMARY												
<p>Consultant</p> <p>SBE N/A</p> <p>Local N/A</p> <p>Contractor</p> <p>SBE 100%</p> <p>Local 100%</p>		<table border="1"> <thead> <tr> <th>Project Budget</th> <th>Committed</th> <th>% Committed</th> <th>Paid To Date</th> </tr> <tr> <th>A</th> <th>B</th> <th>C=B/A</th> <th>D</th> </tr> </thead> <tbody> <tr> <td>\$200,000</td> <td>\$33,462</td> <td>16.73%</td> <td>\$33,462</td> </tr> </tbody> </table>	Project Budget	Committed	% Committed	Paid To Date	A	B	C=B/A	D	\$200,000	\$33,462	16.73%	\$33,462
Project Budget	Committed	% Committed	Paid To Date											
A	B	C=B/A	D											
\$200,000	\$33,462	16.73%	\$33,462											



Monthly Infrastructure Sales Tax Project Report

Small Cap Projects

Data Date: 2/19/2026

Report Date: 2/28/2026

DESCRIPTION/TEAM

SCOPE/NOTES

SCHEDULE

Project Title: Congress Avenue at Palm Beach Lakes
Project Number: 1659
BCC District: 07
Delivery Method: Design CCNA
Category: D04-Drainage Improvements
Status: Design
Designer: Arcadis
Contractor: TBD
Project Manager: Maroun Azzi

Scope
 The project involves upgrading the drainage system along this intersection to alleviate flooding issues. Drainage improvements will include upsizing some existing pipes, adding a parallel trunk line system to the outfall, and adding exfiltration trench.

Notes
 The project is funded with 5-Year Road Program (RP) funding and IST funding. Const. of the project (incl. assoc. rdwy. improvements) is currently est. at \$2.5m. The IST partially funds the const. at \$500,000 in FY20. The project is currently delayed and scheduled to begin const. in FY26 due to utility relocation delays.

	Original	Actual
Design Contract Notice to Proceed	7/15/2015	7/15/2015
Design Completion	8/1/2022	12/1/2022
Construction Bid Date	4/1/2026	
Construction Start	10/1/2026	
Construction Complete	4/1/2028	


PARTICIPATION

FUNDING

FINANCIAL SUMMARY

Consultant
 SBE 37.6%
 Local 100%

Contractor
 SBE TBD
 Local TBD



Project Budget	Committed	% Committed	Paid To Date
A	B	C=B/A	D
\$500,000	\$0	0.00%	\$0

DESCRIPTION/TEAM

SCOPE/NOTES

SCHEDULE

Project Title: Haverhill Rd from Lake Worth Road to 10th Ave.
Project Number: 1660
BCC District: 03
Delivery Method: Design CCNA
Category: D04-Drainage Improvements
Status: Design
Designer: Mock Roos
Contractor: TBD
Project Manager: Carlos Bojorge

Scope
 The project involves addressing drainage issues along Haverhill Rd. (Lake Worth to 10th) to alleviate chronic or extended flooding.

Notes
 Design is pending. The project is funded for design (\$100k) in FY21 and for construction (\$400k) in FY23.

	Original	Actual
Study Start	11/1/2022	10/4/2022
Study Complete	12/1/2024	12/1/2024
Design Start	8/1/2026	
Design Complete	12/1/2027	
Construction Start	6/1/2028	
Construction Complete	9/1/2029	


PARTICIPATION

FUNDING

FINANCIAL SUMMARY

Consultant
 SBE 41%
 Local 100%

Contractor
 SBE TBD
 Local TBD

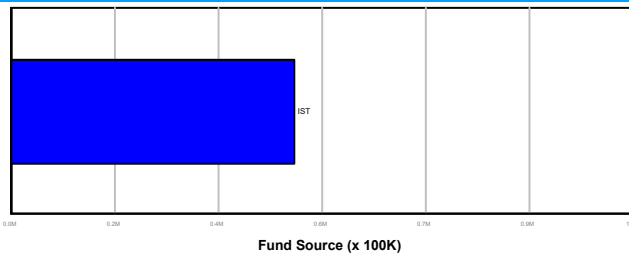

Project Budget	Committed	% Committed	Paid To Date
A	B	C=B/A	D
\$500,000	\$121,463	24.29%	\$116,755



Monthly Infrastructure Sales Tax Project Report

Small Cap Projects

Data Date: 2/19/2026

Report Date: 2/28/2026

DESCRIPTION/TEAM	SCOPE/NOTES	SCHEDULE															
Project Title: Le Chalet Blvd. & Military Trail Project Number: 1675 BCC District: 02 Delivery Method: Design CCNA Category: S08-Signals and Signal Systems Status: Design Designer: Propel Engineering, Inc. Contractor: TBD Project Manager: May Cheng	Scope This project will replace the existing span-wire signal system with a mast arm signal system. FY 2021 IST \$400,000 FY 2022 IST \$150,000 Notes Design of the original signal replacement project has ended as this signal will now be replaced as part of an intersection improvement (adding a 2nd WB left turn lane). As such, the schedule for the project has been revised to a much later date.	<table border="1"> <thead> <tr> <th></th> <th>Original</th> <th>Actual</th> </tr> </thead> <tbody> <tr> <td>Design NTP Issued</td> <td>5/14/2021</td> <td>4/7/2021</td> </tr> <tr> <td>Design Complete</td> <td>1/1/2027</td> <td></td> </tr> <tr> <td>Construction Start</td> <td>5/1/2027</td> <td></td> </tr> <tr> <td>Construction Complete</td> <td>8/1/2028</td> <td></td> </tr> </tbody> </table>		Original	Actual	Design NTP Issued	5/14/2021	4/7/2021	Design Complete	1/1/2027		Construction Start	5/1/2027		Construction Complete	8/1/2028	
	Original	Actual															
Design NTP Issued	5/14/2021	4/7/2021															
Design Complete	1/1/2027																
Construction Start	5/1/2027																
Construction Complete	8/1/2028																

PARTICIPATION	FUNDING	FINANCIAL SUMMARY												
Consultant SBE 92% Local 100% Contractor SBE TBD Local TBD	<p>Fund Source (x 100K)</p>	<table border="1"> <thead> <tr> <th>Project Budget</th> <th>Committed</th> <th>% Committed</th> <th>Paid To Date</th> </tr> <tr> <th>A</th> <th>B</th> <th>C=B/A</th> <th>D</th> </tr> </thead> <tbody> <tr> <td>\$550,000</td> <td>\$111,772</td> <td>20.32%</td> <td>\$91,859</td> </tr> </tbody> </table>	Project Budget	Committed	% Committed	Paid To Date	A	B	C=B/A	D	\$550,000	\$111,772	20.32%	\$91,859
Project Budget	Committed	% Committed	Paid To Date											
A	B	C=B/A	D											
\$550,000	\$111,772	20.32%	\$91,859											

DESCRIPTION/TEAM	SCOPE/NOTES	SCHEDULE									
Project Title: SR-7 High Mast Towers Rehab(Hypoluxo to N. of Lake W Project Number: 1681 BCC District: Multiple Delivery Method: Reimbursement Category: S14-Street Lighting Status: Permitting Designer: Florida Power & Light Contractor: Florida Power & Light Project Manager: May Cheng	Scope The existing SR7 high mast lighting is in need of a new LED system. The original intent was to rehab the towers (in FY21) with conversion to LED lights (in FY25). The new scope involves removing and replacing the high mast lights with new LED lighting. Notes The project is funded at \$500k (FY21). Design is complete - pending permit from FDOT. PBC will reimburse Florida Power & Light after they install the lighting.	<table border="1"> <thead> <tr> <th></th> <th>Original</th> <th>Actual</th> </tr> </thead> <tbody> <tr> <td>Construction Start</td> <td>12/1/2025</td> <td></td> </tr> <tr> <td>Construction Complete</td> <td>9/1/2026</td> <td></td> </tr> </tbody> </table>		Original	Actual	Construction Start	12/1/2025		Construction Complete	9/1/2026	
	Original	Actual									
Construction Start	12/1/2025										
Construction Complete	9/1/2026										

PARTICIPATION	FUNDING	FINANCIAL SUMMARY												
Consultant SBE N/A Local N/A Contractor SBE N/A Local N/A	<p>Fund Source (x 100K)</p>	<table border="1"> <thead> <tr> <th>Project Budget</th> <th>Committed</th> <th>% Committed</th> <th>Paid To Date</th> </tr> <tr> <th>A</th> <th>B</th> <th>C=B/A</th> <th>D</th> </tr> </thead> <tbody> <tr> <td>\$500,000</td> <td>\$837</td> <td>0.17%</td> <td>\$837</td> </tr> </tbody> </table>	Project Budget	Committed	% Committed	Paid To Date	A	B	C=B/A	D	\$500,000	\$837	0.17%	\$837
Project Budget	Committed	% Committed	Paid To Date											
A	B	C=B/A	D											
\$500,000	\$837	0.17%	\$837											



Monthly Infrastructure Sales Tax Project Report

Small Cap Projects

Data Date: 2/19/2026

Report Date: 2/28/2026

DESCRIPTION/TEAM	SCOPE/NOTES	SCHEDULE	
Project Title: Summit Blvd. & Haverhill Road Project Number: 1713 BCC District: 03 Delivery Method: Design CCNA Category: S08-Signals and Signal Systems Status: Construction Designer: Simmons & White, Inc. Contractor: Gerelco Traffic Controls, Inc. Project Manager: May Cheng	Scope This project will replace the existing span-wire signal system with a mast arm signal system. FY 2022 IST \$100,000 FY 2023 IST \$450,000 FY 2024 IST \$150,000 Notes Construction is ongoing (25% complete). A Budget Transfer (BT 24-0635) was approved on 6/4/24 that increased the funding by \$150,000.	Original	Actual
		Design NTP Issued	2/24/2022
		Design Complete	2/3/2025
		Construction Start	4/22/2025
		Construction Complete	9/1/2026

PARTICIPATION	FUNDING	FINANCIAL SUMMARY			
Consultant SBE 80% Local 100% Contractor SBE 0% Local 100%	<p style="text-align: center;">Fund Source (x 100K)</p>	Project Budget	Committed	% Committed	Paid To Date
		A	B	C=B/A	D
		\$700,000	\$614,607	87.80%	\$238,426

DESCRIPTION/TEAM	SCOPE/NOTES	SCHEDULE	
Project Title: Countywide Street Lighting FY22 (frmly Okeechobee Blv Project Number: 1718 BCC District: CW Delivery Method: Florida Power and Light Category: S14-Street Lighting Status: Design Designer: Florida Power & Light Contractor: Florida Power & Light Project Manager: May Cheng	Scope These projects replace the high pressure sodium lights with LED lights. Many of the street lights along County roads are owned and maintained by FPL with the County paying all the operation and maintenance costs. FPL will be responsible for final design and installation and the County will reimburse FPL. Notes There are 8 street lighting projects (road segments) funded (\$840,000) for conversion in FY 2022. As of 12/1/2025, four projects have been completed. The result will provide a cost savings, better quality illumination and a more desirable environmental light source.	Original	Actual
		Yamato/SR 7 to Boca City Limits	
		West Atlantic/Turnpike to Military	
		Okeechobee/Turpike to WPB City Limits	
		Summit/Jog to C-51 Canal	
		Seacrest/Hypoluxo to Mentone Rd	6/1/2022
		Boynton Beach/SR 7 to Turnpike	7/2/2025
		Northlake/Kelso Dr to Military	12/1/2025
		Donald Ross/Jog to 64th Dr. N.	12/1/2025

PARTICIPATION	FUNDING	FINANCIAL SUMMARY			
Consultant SBE N/A Local N/A Contractor SBE N/A Local N/A	<p style="text-align: center;">Fund Source (x 100K)</p>	Project Budget	Committed	% Committed	Paid To Date
		A	B	C=B/A	D
		\$840,000	\$96,284	11.46%	\$94,585



Monthly Infrastructure Sales Tax Project Report

Small Cap Projects

Data Date: 2/19/2026

Report Date: 2/28/2026

DESCRIPTION/TEAM	SCOPE/NOTES	SCHEDULE									
<p>Project Title: Sections of Linton Blvd.</p> <p>Project Number: 1726</p> <p>BCC District: Multiple</p> <p>Delivery Method: Annual Striping Contract</p> <p>Category: S16-Striping</p> <p>Status: Construction</p> <p>Designer: N/A</p> <p>Contractor: Southwide</p> <p>Project Manager: Erika Leighton</p>	<p>Scope</p> <p>This project consists of restriping sections of Linton Blvd.</p> <p>Notes</p> <p>Restriping along Linton Blvd. is done on an as needed basis as funding allows. The project is funded at \$75,000 in FY2022, and \$50,000 in FY2024 and FY2026 for a total funding of \$175,000.</p>	<table border="1"> <thead> <tr> <th></th> <th>Original</th> <th>Actual</th> </tr> </thead> <tbody> <tr> <td>Congress to US 1</td> <td>10/6/2025</td> <td>10/6/2025</td> </tr> <tr> <td>Military to Congress</td> <td>10/6/2025</td> <td>10/6/2025</td> </tr> </tbody> </table>		Original	Actual	Congress to US 1	10/6/2025	10/6/2025	Military to Congress	10/6/2025	10/6/2025
	Original	Actual									
Congress to US 1	10/6/2025	10/6/2025									
Military to Congress	10/6/2025	10/6/2025									

PARTICIPATION	FUNDING	FINANCIAL SUMMARY												
<p>Consultant</p> <p>SBE N/A</p> <p>Local N/A</p> <p>Contractor</p> <p>SBE 100%</p> <p>Local 100%</p>	<p>Fund Source (x 100K)</p>	<table border="1"> <thead> <tr> <th>Project Budget</th> <th>Committed</th> <th>% Committed</th> <th>Paid To Date</th> </tr> <tr> <th>A</th> <th>B</th> <th>C=B/A</th> <th>D</th> </tr> </thead> <tbody> <tr> <td>\$175,000</td> <td>\$123,765</td> <td>70.72%</td> <td>\$123,765</td> </tr> </tbody> </table>	Project Budget	Committed	% Committed	Paid To Date	A	B	C=B/A	D	\$175,000	\$123,765	70.72%	\$123,765
Project Budget	Committed	% Committed	Paid To Date											
A	B	C=B/A	D											
\$175,000	\$123,765	70.72%	\$123,765											

DESCRIPTION/TEAM	SCOPE/NOTES	SCHEDULE						
<p>Project Title: Sections of Woolbright Road</p> <p>Project Number: 1727</p> <p>BCC District: Multiple</p> <p>Delivery Method: Annual Striping Contract</p> <p>Category: S16-Striping</p> <p>Status: Construction</p> <p>Designer: N/A</p> <p>Contractor: Southwide</p> <p>Project Manager: Larry Kelly</p>	<p>Scope</p> <p>This project consists of restriping sections of Woolbright Road.</p> <p>Notes</p> <p>Restriping along Woolbright Road is done on an as needed basis as funding allows. The project is funded at \$50,000 in FY2022 and \$150,000 in FY2026 for a total funding of \$200,000.</p>	<table border="1"> <thead> <tr> <th></th> <th>Original</th> <th>Actual</th> </tr> </thead> <tbody> <tr> <td>Federal to Ocean</td> <td>9/22/2023</td> <td>9/22/2023</td> </tr> </tbody> </table>		Original	Actual	Federal to Ocean	9/22/2023	9/22/2023
	Original	Actual						
Federal to Ocean	9/22/2023	9/22/2023						

PARTICIPATION	FUNDING	FINANCIAL SUMMARY												
<p>Consultant</p> <p>SBE N/A</p> <p>Local N/A</p> <p>Contractor</p> <p>SBE 100%</p> <p>Local 100%</p>	<p>Fund Source (x 100K)</p>	<table border="1"> <thead> <tr> <th>Project Budget</th> <th>Committed</th> <th>% Committed</th> <th>Paid To Date</th> </tr> <tr> <th>A</th> <th>B</th> <th>C=B/A</th> <th>D</th> </tr> </thead> <tbody> <tr> <td>\$200,000</td> <td>\$5,912</td> <td>2.96%</td> <td>\$5,912</td> </tr> </tbody> </table>	Project Budget	Committed	% Committed	Paid To Date	A	B	C=B/A	D	\$200,000	\$5,912	2.96%	\$5,912
Project Budget	Committed	% Committed	Paid To Date											
A	B	C=B/A	D											
\$200,000	\$5,912	2.96%	\$5,912											



Monthly Infrastructure Sales Tax Project Report

Small Cap Projects

Data Date: 2/19/2026

Report Date: 2/28/2026

DESCRIPTION/TEAM	SCOPE/NOTES	SCHEDULE															
<p>Project Title: Old Dixie Hwy. from Alt A-1-A to County Line Rd.</p> <p>Project Number: 1742</p> <p>BCC District: 01</p> <p>Delivery Method: Annual Striping Contract</p> <p>Category: R04-Resurfacing</p> <p>Status: Construction</p> <p>Designer: N/A</p> <p>Contractor: Ranger</p> <p>Project Manager: Trace Doyle</p>	<p>Scope</p> <p>Resurfacing 1.4 miles (5.2 lane miles) of Old Dixie Highway from Alternate A-1-A to County Line Road.</p> <p>Notes</p> <p>Outstanding work includes milling and paving, updating ADA ramps, restriping the road, and replacing traffic loops.</p>	<table border="1"> <thead> <tr> <th></th> <th>Original</th> <th>Actual</th> </tr> </thead> <tbody> <tr> <td>ADA (Curb/Cut Ramps) Complete</td> <td>4/1/2026</td> <td></td> </tr> <tr> <td>Milling and Pavement Complete</td> <td>8/1/2026</td> <td></td> </tr> <tr> <td>Traffic Striping Complete</td> <td>10/1/2026</td> <td></td> </tr> <tr> <td>Traffic Loops Complete</td> <td>12/1/2026</td> <td></td> </tr> </tbody> </table>		Original	Actual	ADA (Curb/Cut Ramps) Complete	4/1/2026		Milling and Pavement Complete	8/1/2026		Traffic Striping Complete	10/1/2026		Traffic Loops Complete	12/1/2026	
	Original	Actual															
ADA (Curb/Cut Ramps) Complete	4/1/2026																
Milling and Pavement Complete	8/1/2026																
Traffic Striping Complete	10/1/2026																
Traffic Loops Complete	12/1/2026																

PARTICIPATION	FUNDING	FINANCIAL SUMMARY												
<p>Consultant</p> <p>SBE N/A</p> <p>Local N/A</p> <p>Contractor</p> <p>SBE 15%</p> <p>Local 100%</p>	<p>Fund Source (x 100K)</p>	<table border="1"> <thead> <tr> <th>Project Budget</th> <th>Committed</th> <th>% Committed</th> <th>Paid To Date</th> </tr> <tr> <th>A</th> <th>B</th> <th>C=B/A</th> <th>D</th> </tr> </thead> <tbody> <tr> <td>\$500,000</td> <td>\$70,942</td> <td>14.19%</td> <td>\$1,136</td> </tr> </tbody> </table>	Project Budget	Committed	% Committed	Paid To Date	A	B	C=B/A	D	\$500,000	\$70,942	14.19%	\$1,136
Project Budget	Committed	% Committed	Paid To Date											
A	B	C=B/A	D											
\$500,000	\$70,942	14.19%	\$1,136											

DESCRIPTION/TEAM	SCOPE/NOTES	SCHEDULE															
<p>Project Title: 15th Street & Tamarind Avenue</p> <p>Project Number: 1757</p> <p>BCC District: 07</p> <p>Delivery Method: Design CCNA</p> <p>Category: S08-Signals and Signal Systems</p> <p>Status: Construction</p> <p>Designer: Simmons & White, Inc.</p> <p>Contractor: Gerelco Traffic Controls, Inc.</p> <p>Project Manager: May Cheng</p>	<p>Scope</p> <p>This project will replace the existing span-wire signal system with a mast arm signal system.</p> <p>FY 2023 IST \$500,000</p> <p>Notes</p> <p>Construction is pending.</p>	<table border="1"> <thead> <tr> <th></th> <th>Original</th> <th>Actual</th> </tr> </thead> <tbody> <tr> <td>Design NTP Issued</td> <td>9/13/2023</td> <td>10/4/2023</td> </tr> <tr> <td>Design Completion</td> <td>8/1/2025</td> <td>2/4/2025</td> </tr> <tr> <td>Construction Start</td> <td>11/1/2025</td> <td></td> </tr> <tr> <td>Construction Completion</td> <td>12/1/2026</td> <td></td> </tr> </tbody> </table>		Original	Actual	Design NTP Issued	9/13/2023	10/4/2023	Design Completion	8/1/2025	2/4/2025	Construction Start	11/1/2025		Construction Completion	12/1/2026	
	Original	Actual															
Design NTP Issued	9/13/2023	10/4/2023															
Design Completion	8/1/2025	2/4/2025															
Construction Start	11/1/2025																
Construction Completion	12/1/2026																

PARTICIPATION	FUNDING	FINANCIAL SUMMARY												
<p>Consultant</p> <p>SBE 28%</p> <p>Local 100%</p> <p>Contractor</p> <p>SBE 0%</p> <p>Local 100%</p>	<p>Fund Source (x 100K)</p>	<table border="1"> <thead> <tr> <th>Project Budget</th> <th>Committed</th> <th>% Committed</th> <th>Paid To Date</th> </tr> <tr> <th>A</th> <th>B</th> <th>C=B/A</th> <th>D</th> </tr> </thead> <tbody> <tr> <td>\$500,000</td> <td>\$69,870</td> <td>13.97%</td> <td>\$27,483</td> </tr> </tbody> </table>	Project Budget	Committed	% Committed	Paid To Date	A	B	C=B/A	D	\$500,000	\$69,870	13.97%	\$27,483
Project Budget	Committed	% Committed	Paid To Date											
A	B	C=B/A	D											
\$500,000	\$69,870	13.97%	\$27,483											



Monthly Infrastructure Sales Tax Project Report

Small Cap Projects

Data Date: 2/19/2026

Report Date: 2/28/2026

DESCRIPTION/TEAM	SCOPE/NOTES	SCHEDULE															
<p>Project Title: Cascades Isle Blvd. & Jog Road</p> <p>Project Number: 1758</p> <p>BCC District: 03</p> <p>Delivery Method: Design CCNA</p> <p>Category: S08-Signals and Signal Systems</p> <p>Status: Design</p> <p>Designer: Simmons & White, Inc.</p> <p>Contractor: TBD</p> <p>Project Manager: May Cheng</p>	<p>Scope</p> <p>This project will replace the existing span-wire signal system with a mast arm signal system.</p> <p>FY 2023 IST \$450,000</p> <p>Notes</p> <p>Design is ongoing (95% complete).</p>	<table border="1"> <thead> <tr> <th></th> <th>Original</th> <th>Actual</th> </tr> </thead> <tbody> <tr> <td>Design NTP Issued</td> <td>4/1/2023</td> <td>4/1/2023</td> </tr> <tr> <td>Design Complete</td> <td>10/1/2026</td> <td></td> </tr> <tr> <td>Construction Start</td> <td>1/1/2027</td> <td></td> </tr> <tr> <td>Construction Complete</td> <td>2/1/2028</td> <td></td> </tr> </tbody> </table>		Original	Actual	Design NTP Issued	4/1/2023	4/1/2023	Design Complete	10/1/2026		Construction Start	1/1/2027		Construction Complete	2/1/2028	
	Original	Actual															
Design NTP Issued	4/1/2023	4/1/2023															
Design Complete	10/1/2026																
Construction Start	1/1/2027																
Construction Complete	2/1/2028																

PARTICIPATION	FUNDING	FINANCIAL SUMMARY												
<p>Consultant</p> <p>SBE 13%</p> <p>Local 100%</p> <p>Contractor</p> <p>SBE 0%</p> <p>Local 100%</p>		<table border="1"> <thead> <tr> <th>Project Budget</th> <th>Committed</th> <th>% Committed</th> <th>Paid To Date</th> </tr> <tr> <th>A</th> <th>B</th> <th>C=B/A</th> <th>D</th> </tr> </thead> <tbody> <tr> <td>\$450,000</td> <td>\$173,286</td> <td>38.51%</td> <td>\$97,895</td> </tr> </tbody> </table>	Project Budget	Committed	% Committed	Paid To Date	A	B	C=B/A	D	\$450,000	\$173,286	38.51%	\$97,895
Project Budget	Committed	% Committed	Paid To Date											
A	B	C=B/A	D											
\$450,000	\$173,286	38.51%	\$97,895											

DESCRIPTION/TEAM	SCOPE/NOTES	SCHEDULE															
<p>Project Title: Donald Ross Road & Military Trail</p> <p>Project Number: 1759</p> <p>BCC District: 01</p> <p>Delivery Method: Design CCNA</p> <p>Category: S08-Signals and Signal Systems</p> <p>Status: Design</p> <p>Designer: Propel Engineering</p> <p>Contractor: TBD</p> <p>Project Manager: May Cheng</p>	<p>Scope</p> <p>This project will replace the existing span-wire signal system with a mast arm signal system.</p> <p>FY 2023 IST \$150,000</p> <p>FY 2024 IST \$500,000</p> <p>Notes</p> <p>Design of the project is in progress. The signal replacement work is included in a 5-Year Road Program improvement project. The roadway improvement includes converting existing northbound dual left turn lanes into northbound triple left turn lanes.</p>	<table border="1"> <thead> <tr> <th></th> <th>Original</th> <th>Actual</th> </tr> </thead> <tbody> <tr> <td>Design NTP Issued</td> <td>6/27/2022</td> <td>6/27/2022</td> </tr> <tr> <td>Design Complete</td> <td>11/1/2025</td> <td></td> </tr> <tr> <td>Construction Start</td> <td>6/1/2026</td> <td></td> </tr> <tr> <td>Construction Complete</td> <td>7/1/2027</td> <td></td> </tr> </tbody> </table>		Original	Actual	Design NTP Issued	6/27/2022	6/27/2022	Design Complete	11/1/2025		Construction Start	6/1/2026		Construction Complete	7/1/2027	
	Original	Actual															
Design NTP Issued	6/27/2022	6/27/2022															
Design Complete	11/1/2025																
Construction Start	6/1/2026																
Construction Complete	7/1/2027																

PARTICIPATION	FUNDING	FINANCIAL SUMMARY												
<p>Consultant</p> <p>SBE 94%</p> <p>Local 100%</p> <p>Contractor</p> <p>SBE TBD</p> <p>Local TBD</p>		<table border="1"> <thead> <tr> <th>Project Budget</th> <th>Committed</th> <th>% Committed</th> <th>Paid To Date</th> </tr> <tr> <th>A</th> <th>B</th> <th>C=B/A</th> <th>D</th> </tr> </thead> <tbody> <tr> <td>\$650,000</td> <td>\$0</td> <td>0.00%</td> <td>\$0</td> </tr> </tbody> </table>	Project Budget	Committed	% Committed	Paid To Date	A	B	C=B/A	D	\$650,000	\$0	0.00%	\$0
Project Budget	Committed	% Committed	Paid To Date											
A	B	C=B/A	D											
\$650,000	\$0	0.00%	\$0											



Monthly Infrastructure Sales Tax Project Report

Small Cap Projects

Data Date: 2/19/2026

Report Date: 2/28/2026

DESCRIPTION/TEAM

SCOPE/NOTES

SCHEDULE

Project Title: CR-700 over SFWMD L-13 Canal (930085)
Project Number: 1776
BCC District: 06
Delivery Method: Design CCNA
Category: B04-Bridge Modifications
Status: Design
Designer: RJ Behar
Contractor: TBD
Project Manager: Will Carey

Scope
 The original scope was to modify or rehab the bridge. Subsequently a more detailed consultant study (4/27/20) concluded that bridge "could be left as is for 10 years" with a pile jacket repair.

Notes
 The repair cost for the pile jacket repair is estimated at \$100k-\$150k. Design of the pile jacket repair is ongoing (96% complete). Project is delayed due to ongoing coordination with the CR 880 over C-51 canal bridge replacement project (bid together).

	Original	Actual
Design Contract Notice to Proceed	2/4/2021	2/4/2021
Design Completion	12/1/2025	
Construction Bid Date	4/1/2026	
Construction Start	9/1/2026	
Construction Complete	9/1/2027	


PARTICIPATION

FUNDING

FINANCIAL SUMMARY

Consultant
 SBE 84.6%
 Local 100%

Contractor
 SBE TBD
 Local TBD



Project Budget	Committed	% Committed	Paid To Date
A	B	C=B/A	D
\$150,000	\$59,931	39.95%	\$36,213

DESCRIPTION/TEAM

SCOPE/NOTES

SCHEDULE

Project Title: CR-880 over SFWMD L-14 Canal @ 6 Mile Bend (930038)
Project Number: 1777
BCC District: 06
Delivery Method: Design CCNA
Category: B04-Bridge Modifications
Status: Design
Designer: RJ Behar
Contractor: TBD
Project Manager: Maroun Azzi

Scope
 This project will address the two safety deficiencies in the bridge-barrier wall height and bridge (slope) drainage.

Notes
 Study complete. Design pending. The scheduled dates have been revised to reflect operational and design delays.

	Original	Actual
Study Start	1/1/2023	1/31/2023
Study Completion	1/1/2024	1/1/2024
Design Start	12/1/2025	
Design Complete	12/1/2026	
Construction Bid Date	6/1/2027	
Construction Start	12/1/2027	
Construction Complete	6/1/2028	


PARTICIPATION

FUNDING

FINANCIAL SUMMARY

Consultant
 SBE 15%
 Local 100%

Contractor
 SBE TBD
 Local TBD

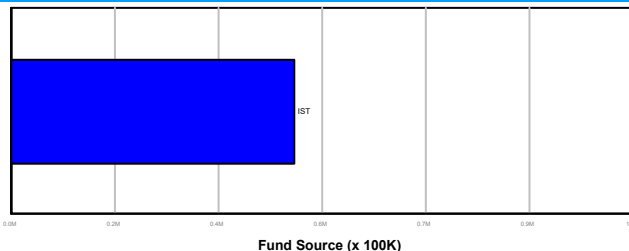

Project Budget	Committed	% Committed	Paid To Date
A	B	C=B/A	D
\$500,000	\$30,728	6.15%	\$20,913



Monthly Infrastructure Sales Tax Project Report

Small Cap Projects

Data Date: 2/19/2026

Report Date: 2/28/2026

DESCRIPTION/TEAM	SCOPE/NOTES	SCHEDULE												
<p>Project Title: Seminole Manor (residential roads)</p> <p>Project Number: 1783</p> <p>BCC District: 02</p> <p>Delivery Method: Annual Construction Contract</p> <p>Category: R04-Resurfacing</p> <p>Status: Construction</p> <p>Designer: N/A</p> <p>Contractor: Ranger</p> <p>Project Manager: Chase Miller</p>	<p>Scope</p> <p>Resurfacing 5 miles (10 lane miles) of the residential streets within the Seminole Manor Subdivision.</p> <p>Notes</p> <p>Outstanding work includes milling and paving, updating ADA ramps, and restriping the road. Project is delayed due to pending drainage repairs.</p>	<table border="1"> <thead> <tr> <th></th> <th>Original</th> <th>Actual</th> </tr> </thead> <tbody> <tr> <td>Milling and Pavement Complete</td> <td>12/1/2026</td> <td></td> </tr> <tr> <td>ADA (Curb/Cut Ramps) Complete</td> <td>2/1/2027</td> <td></td> </tr> <tr> <td>Traffic Striping Complete</td> <td>2/1/2027</td> <td></td> </tr> </tbody> </table>		Original	Actual	Milling and Pavement Complete	12/1/2026		ADA (Curb/Cut Ramps) Complete	2/1/2027		Traffic Striping Complete	2/1/2027	
	Original	Actual												
Milling and Pavement Complete	12/1/2026													
ADA (Curb/Cut Ramps) Complete	2/1/2027													
Traffic Striping Complete	2/1/2027													

PARTICIPATION	FUNDING	FINANCIAL SUMMARY												
<p>Consultant</p> <p>SBE N/A</p> <p>Local N/A</p> <p>Contractor</p> <p>SBE 15%</p> <p>Local 100%</p>	IST	<table border="1"> <thead> <tr> <th>Project Budget</th> <th>Committed</th> <th>% Committed</th> <th>Paid To Date</th> </tr> <tr> <th>A</th> <th>B</th> <th>C=B/A</th> <th>D</th> </tr> </thead> <tbody> <tr> <td style="text-align: right;">\$700,000</td> <td style="text-align: right;">\$2,376</td> <td style="text-align: right;">0.34%</td> <td style="text-align: right;">\$2,376</td> </tr> </tbody> </table>	Project Budget	Committed	% Committed	Paid To Date	A	B	C=B/A	D	\$700,000	\$2,376	0.34%	\$2,376
Project Budget	Committed	% Committed	Paid To Date											
A	B	C=B/A	D											
\$700,000	\$2,376	0.34%	\$2,376											

DESCRIPTION/TEAM	SCOPE/NOTES	SCHEDULE									
<p>Project Title: Cam Estates (residential roads)</p> <p>Project Number: 1784</p> <p>BCC District: 02</p> <p>Delivery Method: Annual Construction Contract</p> <p>Category: R04-Resurfacing</p> <p>Status: Construction</p> <p>Designer: N/A</p> <p>Contractor: Ranger</p> <p>Project Manager: Chase Miller</p>	<p>Scope</p> <p>Resurfacing 4.3 miles (8.6 lane miles) of the residential Streets within the Cam Estates Subdivision.</p> <p>Notes</p> <p>Outstanding work includes milling and paving, and restriping the road.</p>	<table border="1"> <thead> <tr> <th></th> <th>Original</th> <th>Actual</th> </tr> </thead> <tbody> <tr> <td>Milling and Pavement Complete</td> <td>12/1/2026</td> <td></td> </tr> <tr> <td>Traffic Striping Complete</td> <td>3/1/2027</td> <td></td> </tr> </tbody> </table>		Original	Actual	Milling and Pavement Complete	12/1/2026		Traffic Striping Complete	3/1/2027	
	Original	Actual									
Milling and Pavement Complete	12/1/2026										
Traffic Striping Complete	3/1/2027										

PARTICIPATION	FUNDING	FINANCIAL SUMMARY												
<p>Consultant</p> <p>SBE N/A</p> <p>Local N/A</p> <p>Contractor</p> <p>SBE 15%</p> <p>Local 100%</p>	<p style="text-align: center;">Fund Source (x 100K)</p>	<table border="1"> <thead> <tr> <th>Project Budget</th> <th>Committed</th> <th>% Committed</th> <th>Paid To Date</th> </tr> <tr> <th>A</th> <th>B</th> <th>C=B/A</th> <th>D</th> </tr> </thead> <tbody> <tr> <td style="text-align: right;">\$650,000</td> <td style="text-align: right;">\$647,206</td> <td style="text-align: right;">99.57%</td> <td style="text-align: right;">\$2,206</td> </tr> </tbody> </table>	Project Budget	Committed	% Committed	Paid To Date	A	B	C=B/A	D	\$650,000	\$647,206	99.57%	\$2,206
Project Budget	Committed	% Committed	Paid To Date											
A	B	C=B/A	D											
\$650,000	\$647,206	99.57%	\$2,206											



Monthly Infrastructure Sales Tax Project Report

Small Cap Projects

Data Date: 2/19/2026

Report Date: 2/28/2026

DESCRIPTION/TEAM	SCOPE/NOTES	SCHEDULE																								
<p>Project Title: Countywide Street Lighting FY24 (fmrly Woolbright Roa</p> <p>Project Number: 1804</p> <p>BCC District: CW</p> <p>Delivery Method: Florida Power and Light</p> <p>Category: S14-Street Lighting</p> <p>Status: Design</p> <p>Designer: Florida Power & Light</p> <p>Contractor: Florida Power & Light</p> <p>Project Manager: May Cheng</p>	<p>Scope</p> <p>These projects replace the high pressure sodium lights with LED lights. Many of the street lights along County roads are owned and maintained by FPL with the County paying all the operation and maintenance costs. FPL will be responsible for final design and installation and the County will reimburse FPL.</p> <p>Notes</p> <p>There are 7 street lighting projects (road segments) funded (\$815,000) for conversion in FY 2024. As of 12/1/25, three projects have been completed. The result will provide a cost savings, better quality illumination and a more desirable environmental light source.</p>	<table border="1"> <thead> <tr> <th></th> <th>Original</th> <th>Actual</th> </tr> </thead> <tbody> <tr> <td>SW 18th (E.&W. of Powerline)</td> <td></td> <td></td> </tr> <tr> <td>Westgate/Military to Congress</td> <td></td> <td></td> </tr> <tr> <td>Powerline/Glades to Broward County Line</td> <td></td> <td></td> </tr> <tr> <td>Woolbright/Hagen Ranch to Knuth</td> <td></td> <td></td> </tr> <tr> <td>Seminole Pratt Whitney/Sycamore to Whi</td> <td>6/3/2025</td> <td>6/3/2025</td> </tr> <tr> <td>Seminole Pratt Whitney/Whitton Dr. to SF</td> <td>6/3/2025</td> <td>6/3/2025</td> </tr> <tr> <td>Northlake/Coconut to Ibis</td> <td>12/1/2025</td> <td>12/1/2025</td> </tr> </tbody> </table>		Original	Actual	SW 18th (E.&W. of Powerline)			Westgate/Military to Congress			Powerline/Glades to Broward County Line			Woolbright/Hagen Ranch to Knuth			Seminole Pratt Whitney/Sycamore to Whi	6/3/2025	6/3/2025	Seminole Pratt Whitney/Whitton Dr. to SF	6/3/2025	6/3/2025	Northlake/Coconut to Ibis	12/1/2025	12/1/2025
	Original	Actual																								
SW 18th (E.&W. of Powerline)																										
Westgate/Military to Congress																										
Powerline/Glades to Broward County Line																										
Woolbright/Hagen Ranch to Knuth																										
Seminole Pratt Whitney/Sycamore to Whi	6/3/2025	6/3/2025																								
Seminole Pratt Whitney/Whitton Dr. to SF	6/3/2025	6/3/2025																								
Northlake/Coconut to Ibis	12/1/2025	12/1/2025																								

PARTICIPATION	FUNDING	FINANCIAL SUMMARY												
<p>Consultant</p> <p>SBE N/A</p> <p>Local N/A</p> <p>Contractor</p> <p>SBE N/A</p> <p>Local N/A</p>	<p>Fund Source (x 100K)</p>	<table border="1"> <thead> <tr> <th>Project Budget</th> <th>Committed</th> <th>% Committed</th> <th>Paid To Date</th> </tr> <tr> <th>A</th> <th>B</th> <th>C=B/A</th> <th>D</th> </tr> </thead> <tbody> <tr> <td>\$815,000</td> <td>\$22,102</td> <td>2.71%</td> <td>\$22,102</td> </tr> </tbody> </table>	Project Budget	Committed	% Committed	Paid To Date	A	B	C=B/A	D	\$815,000	\$22,102	2.71%	\$22,102
Project Budget	Committed	% Committed	Paid To Date											
A	B	C=B/A	D											
\$815,000	\$22,102	2.71%	\$22,102											

DESCRIPTION/TEAM	SCOPE/NOTES	SCHEDULE															
<p>Project Title: Belvedere Rd. from Australian Ave. to U.S. 1</p> <p>Project Number: 1818</p> <p>BCC District: 02</p> <p>Delivery Method: Annual Construction Contract</p> <p>Category: R04-Resurfacing</p> <p>Status: Construction</p> <p>Designer: N/A</p> <p>Contractor: M&M Asphalt Maintenance</p> <p>Project Manager: Chase Miller</p>	<p>Scope</p> <p>Resurfacing 1.3 miles (6.0 lane miles) of Belvedere Road from Australian Avenue to US 1.</p> <p>Notes</p> <p>Outstanding work includes milling and paving, updating ADA ramps, restriping the road, and replacing traffic loops.</p>	<table border="1"> <thead> <tr> <th></th> <th>Original</th> <th>Actual</th> </tr> </thead> <tbody> <tr> <td>ADA (Curb/Cut Ramps) Complete</td> <td>8/11/2026</td> <td></td> </tr> <tr> <td>Milling and Pavement Complete</td> <td>10/11/2026</td> <td></td> </tr> <tr> <td>Traffic Striping Complete</td> <td>11/11/2026</td> <td></td> </tr> <tr> <td>Traffic Loops Complete</td> <td>1/1/2027</td> <td></td> </tr> </tbody> </table>		Original	Actual	ADA (Curb/Cut Ramps) Complete	8/11/2026		Milling and Pavement Complete	10/11/2026		Traffic Striping Complete	11/11/2026		Traffic Loops Complete	1/1/2027	
	Original	Actual															
ADA (Curb/Cut Ramps) Complete	8/11/2026																
Milling and Pavement Complete	10/11/2026																
Traffic Striping Complete	11/11/2026																
Traffic Loops Complete	1/1/2027																

PARTICIPATION	FUNDING	FINANCIAL SUMMARY												
<p>Consultant</p> <p>SBE N/A</p> <p>Local N/A</p> <p>Contractor</p> <p>SBE 10%</p> <p>Local 100%</p>	<p>Fund Source (x 100K)</p>	<table border="1"> <thead> <tr> <th>Project Budget</th> <th>Committed</th> <th>% Committed</th> <th>Paid To Date</th> </tr> <tr> <th>A</th> <th>B</th> <th>C=B/A</th> <th>D</th> </tr> </thead> <tbody> <tr> <td>\$900,000</td> <td>\$80,679</td> <td>8.96%</td> <td>\$80,679</td> </tr> </tbody> </table>	Project Budget	Committed	% Committed	Paid To Date	A	B	C=B/A	D	\$900,000	\$80,679	8.96%	\$80,679
Project Budget	Committed	% Committed	Paid To Date											
A	B	C=B/A	D											
\$900,000	\$80,679	8.96%	\$80,679											



Monthly Infrastructure Sales Tax Project Report

Small Cap Projects

Data Date: 2/19/2026

Report Date: 2/28/2026

DESCRIPTION/TEAM	SCOPE/NOTES	SCHEDULE															
<p>Project Title: Ponderosa Dr. from Judge Winnikoff Rd. to Glades Rd.</p> <p>Project Number: 1823</p> <p>BCC District: 05</p> <p>Delivery Method: Annual Construction Contract</p> <p>Category: R04-Resurfacing</p> <p>Status: Construction</p> <p>Designer: N/A</p> <p>Contractor: M&M Asphalt Maintenance</p> <p>Project Manager: Chase Miller</p>	<p>Scope</p> <p>Resurfacing 1.9 miles (3.8 lane miles) of Ponderosa Drive from Judge Winnikoff Road to Glades Road.</p> <p>Notes</p> <p>Outstanding work includes milling and paving, updating ADA ramps, restriping the road, and replacing traffic loops.</p>	<table border="1"> <thead> <tr> <th></th> <th>Original</th> <th>Actual</th> </tr> </thead> <tbody> <tr> <td>Milling and Pavement Complete</td> <td>10/1/2026</td> <td></td> </tr> <tr> <td>Traffic Striping Complete</td> <td>12/1/2026</td> <td></td> </tr> <tr> <td>ADA (Curb/Cut Ramps) Complete</td> <td>1/1/2027</td> <td></td> </tr> <tr> <td>Traffic Loops Complete</td> <td>3/1/2027</td> <td></td> </tr> </tbody> </table>		Original	Actual	Milling and Pavement Complete	10/1/2026		Traffic Striping Complete	12/1/2026		ADA (Curb/Cut Ramps) Complete	1/1/2027		Traffic Loops Complete	3/1/2027	
	Original	Actual															
Milling and Pavement Complete	10/1/2026																
Traffic Striping Complete	12/1/2026																
ADA (Curb/Cut Ramps) Complete	1/1/2027																
Traffic Loops Complete	3/1/2027																

PARTICIPATION	FUNDING	FINANCIAL SUMMARY												
<p>Consultant</p> <p>SBE N/A</p> <p>Local N/A</p> <p>Contractor</p> <p>SBE 10%</p> <p>Local 100%</p>	<p>Fund Source (x 100K)</p>	<table border="1"> <thead> <tr> <th>Project Budget</th> <th>Committed</th> <th>% Committed</th> <th>Paid To Date</th> </tr> <tr> <th>A</th> <th>B</th> <th>C=B/A</th> <th>D</th> </tr> </thead> <tbody> <tr> <td>\$490,000</td> <td>\$49,882</td> <td>10.18%</td> <td>\$49,882</td> </tr> </tbody> </table>	Project Budget	Committed	% Committed	Paid To Date	A	B	C=B/A	D	\$490,000	\$49,882	10.18%	\$49,882
Project Budget	Committed	% Committed	Paid To Date											
A	B	C=B/A	D											
\$490,000	\$49,882	10.18%	\$49,882											

DESCRIPTION/TEAM	SCOPE/NOTES	SCHEDULE															
<p>Project Title: Lakeside Green/Willow Pond Rd. (residential roads)</p> <p>Project Number: 1824</p> <p>BCC District: 02</p> <p>Delivery Method: Annual Construction Contract</p> <p>Category: R04-Resurfacing</p> <p>Status: Construction</p> <p>Designer: N/A</p> <p>Contractor: M&M Asphalt Maintenance</p> <p>Project Manager: Chase Miller</p>	<p>Scope</p> <p>Resurfacing 4.1 miles (8.2 lane miles) of the residential streets within the Lakeside Green Subdivision (including Willow Pond Road).</p> <p>Notes</p> <p>Outstanding work includes milling and paving, updating ADA ramps, restriping the road and replacing traffic loops.</p>	<table border="1"> <thead> <tr> <th></th> <th>Original</th> <th>Actual</th> </tr> </thead> <tbody> <tr> <td>Milling and Pavement Complete</td> <td>11/28/2026</td> <td></td> </tr> <tr> <td>Traffic Striping Complete</td> <td>1/1/2027</td> <td></td> </tr> <tr> <td>ADA (Curb/Cut Ramps) Complete</td> <td>1/15/2027</td> <td></td> </tr> <tr> <td>Traffic Loops Complete</td> <td>3/1/2027</td> <td></td> </tr> </tbody> </table>		Original	Actual	Milling and Pavement Complete	11/28/2026		Traffic Striping Complete	1/1/2027		ADA (Curb/Cut Ramps) Complete	1/15/2027		Traffic Loops Complete	3/1/2027	
	Original	Actual															
Milling and Pavement Complete	11/28/2026																
Traffic Striping Complete	1/1/2027																
ADA (Curb/Cut Ramps) Complete	1/15/2027																
Traffic Loops Complete	3/1/2027																

PARTICIPATION	FUNDING	FINANCIAL SUMMARY												
<p>Consultant</p> <p>SBE N/A</p> <p>Local N/A</p> <p>Contractor</p> <p>SBE 10%</p> <p>Local 100%</p>	<p>Fund Source (x 100K)</p>	<table border="1"> <thead> <tr> <th>Project Budget</th> <th>Committed</th> <th>% Committed</th> <th>Paid To Date</th> </tr> <tr> <th>A</th> <th>B</th> <th>C=B/A</th> <th>D</th> </tr> </thead> <tbody> <tr> <td>\$720,000</td> <td>\$10,835</td> <td>1.50%</td> <td>\$10,835</td> </tr> </tbody> </table>	Project Budget	Committed	% Committed	Paid To Date	A	B	C=B/A	D	\$720,000	\$10,835	1.50%	\$10,835
Project Budget	Committed	% Committed	Paid To Date											
A	B	C=B/A	D											
\$720,000	\$10,835	1.50%	\$10,835											



Monthly Infrastructure Sales Tax Project Report

Small Cap Projects

Data Date: 2/19/2026

Report Date: 2/28/2026

DESCRIPTION/TEAM	SCOPE/NOTES	SCHEDULE																											
<p>Project Title: Street Lighting LED Replacements Countywide FY25</p> <p>Project Number: 1828</p> <p>BCC District: CW</p> <p>Delivery Method: Florida Power and Light</p> <p>Category: S14-Street Lighting</p> <p>Status: Design</p> <p>Designer: Florida Power and Light</p> <p>Contractor: Florida Power and Light</p> <p>Project Manager: May Cheng</p>	<p>Scope</p> <p>These projects replace high pressure sodium street lights with LED lights. Many of the lights along County roads are owned and maintained by FPL with the County paying the operation and maintenance costs. FPL will be responsible for final design and installation and the County will reimburse FPL.</p> <p>Notes</p> <p>There are 9 street lighting projects funded (\$916,000) for conversion in FY 2025. As of 12/1/2025, 0 projects have been completed. The result will provide a cost savings, better quality illumination, and a more desirable environmental light source.</p>	<table border="1"> <thead> <tr> <th></th> <th style="text-align: center;">Original</th> <th style="text-align: center;">Actual</th> </tr> </thead> <tbody> <tr> <td colspan="3">Discretionary Projects (438 lights)</td> </tr> <tr> <td>SR7 (north of Clint Moore to north of Glac</td> <td></td> <td></td> </tr> <tr> <td>Australian Ave. and Congress @ SR80 fl</td> <td></td> <td></td> </tr> <tr> <td>Jog Rd. (Joe DeLong to Gateway)</td> <td></td> <td></td> </tr> <tr> <td>Beeline Hwy @Pratt Whitney</td> <td></td> <td></td> </tr> <tr> <td>SR7 @Boynton Beach Blvd</td> <td></td> <td></td> </tr> <tr> <td>SR7 @Atlantic Ave</td> <td></td> <td></td> </tr> <tr> <td>Lake Ida and Via Flora Roundabout</td> <td></td> <td></td> </tr> </tbody> </table>		Original	Actual	Discretionary Projects (438 lights)			SR7 (north of Clint Moore to north of Glac			Australian Ave. and Congress @ SR80 fl			Jog Rd. (Joe DeLong to Gateway)			Beeline Hwy @Pratt Whitney			SR7 @Boynton Beach Blvd			SR7 @Atlantic Ave			Lake Ida and Via Flora Roundabout		
	Original	Actual																											
Discretionary Projects (438 lights)																													
SR7 (north of Clint Moore to north of Glac																													
Australian Ave. and Congress @ SR80 fl																													
Jog Rd. (Joe DeLong to Gateway)																													
Beeline Hwy @Pratt Whitney																													
SR7 @Boynton Beach Blvd																													
SR7 @Atlantic Ave																													
Lake Ida and Via Flora Roundabout																													

PARTICIPATION	FUNDING	FINANCIAL SUMMARY												
<p>Consultant</p> <p>SBE N/A</p> <p>Local N/A</p> <p>Contractor</p> <p>SBE N/A</p> <p>Local N/A</p>	<p>Fund Source (x 100K)</p>	<table border="1"> <thead> <tr> <th>Project Budget</th> <th>Committed</th> <th>% Committed</th> <th>Paid To Date</th> </tr> <tr> <th>A</th> <th>B</th> <th>C=B/A</th> <th>D</th> </tr> </thead> <tbody> <tr> <td style="text-align: right;">\$916,000</td> <td style="text-align: right;">\$42,058</td> <td style="text-align: right;">4.59%</td> <td style="text-align: right;">\$35,414</td> </tr> </tbody> </table>	Project Budget	Committed	% Committed	Paid To Date	A	B	C=B/A	D	\$916,000	\$42,058	4.59%	\$35,414
Project Budget	Committed	% Committed	Paid To Date											
A	B	C=B/A	D											
\$916,000	\$42,058	4.59%	\$35,414											

DESCRIPTION/TEAM	SCOPE/NOTES	SCHEDULE									
<p>Project Title: SR-7 (Whitehorse Dr. to Hypoluxo Rd.)</p> <p>Project Number: 1830</p> <p>BCC District: BIAF</p> <p>Delivery Method: Design CCNA</p> <p>Category: S14-Street Lighting</p> <p>Status: Design</p> <p>Designer: Electrical Design Associates</p> <p>Contractor: Florida Power & Light</p> <p>Project Manager: May Cheng</p>	<p>Scope</p> <p>The exist. SR7 high mast lighting is in need of a new LED system. The original intent was to rehab the towers (in FY21) with conversion to LED lights (in FY25). The new scope involves removing and replacing the high mast lights with new LED lighting. Project will design new LED lighting along SR7.</p> <p>Notes</p> <p>Design is complete. The IST funding of \$106k was advanced from FY25 to FY19 (BT 2019-0162). The project will be built with the "SR7 High Mast Towers Rehab (Hypoluxo to Lake Worth)" street lighting project which is funded by the IST at \$500k in FY21. The design contract will remain open for any post design services.</p>	<table border="1"> <thead> <tr> <th></th> <th style="text-align: center;">Original</th> <th style="text-align: center;">Actual</th> </tr> </thead> <tbody> <tr> <td>Design Contract Notice to Proceed</td> <td style="text-align: center;">5/1/2019</td> <td style="text-align: center;">4/24/2019</td> </tr> <tr> <td>Design Completion</td> <td style="text-align: center;">5/1/2020</td> <td style="text-align: center;">11/1/2020</td> </tr> </tbody> </table>		Original	Actual	Design Contract Notice to Proceed	5/1/2019	4/24/2019	Design Completion	5/1/2020	11/1/2020
	Original	Actual									
Design Contract Notice to Proceed	5/1/2019	4/24/2019									
Design Completion	5/1/2020	11/1/2020									

PARTICIPATION	FUNDING	FINANCIAL SUMMARY												
<p>Consultant</p> <p>SBE 100%</p> <p>Local 100%</p> <p>Contractor</p> <p>SBE N/A</p> <p>Local N/A</p>	<p>Fund Source (x 100K)</p>	<table border="1"> <thead> <tr> <th>Project Budget</th> <th>Committed</th> <th>% Committed</th> <th>Paid To Date</th> </tr> <tr> <th>A</th> <th>B</th> <th>C=B/A</th> <th>D</th> </tr> </thead> <tbody> <tr> <td style="text-align: right;">\$106,000</td> <td style="text-align: right;">\$27,584</td> <td style="text-align: right;">26.02%</td> <td style="text-align: right;">\$26,034</td> </tr> </tbody> </table>	Project Budget	Committed	% Committed	Paid To Date	A	B	C=B/A	D	\$106,000	\$27,584	26.02%	\$26,034
Project Budget	Committed	% Committed	Paid To Date											
A	B	C=B/A	D											
\$106,000	\$27,584	26.02%	\$26,034											



Monthly Infrastructure Sales Tax Project Report

Small Cap Projects

Data Date: 2/19/2026

Report Date: 2/28/2026

DESCRIPTION/TEAM	SCOPE/NOTES	SCHEDULE	
Project Title: FY 2019 Playground Replacements-Countywide Project Number: T028 BCC District: Multiple Delivery Method: Minor Construction Annual Contract Category: P06-Playground Replacement Status: Design Designer: Varies Contractor: TBD Project Manager: Javier Torres	Scope Per Transfer #18-01 Includes JPP Campground, JPP Mound Circle, Lake Belvedere Estates, South Bay RV, Coral Cove Park, Lake Charleston Park, and BASCR Playgrounds. Notes Phase II: JPP Campsites, Lake Charleston, and Lake Belvedere Estates: The 95% CD package was delivered on 1/23/26, received and accepted. Parks is reviewing the DD for all five playgrounds to incorporate the new canopy structures. Phase III: JPP Mound Circle, South Bay RV, Coral Cove, and BASCR: No activity.	Original	Actual
		Project Start	10/28/2022 10/28/2022
		Phase I Substantial Completion	12/19/2022 11/10/2023
		Phase II Construction Start	6/12/2023
		Phase III Start	3/8/2024

PARTICIPATION	FUNDING	FINANCIAL SUMMARY			
Consultant		Project Budget	Committed	% Committed	Paid To Date
SBE Varies		A	B	C=B/A	D
Local Varies		\$820,750	\$33,324	4.06%	\$33,324
Contractor					
SBE TBD					
Local TBD					

DESCRIPTION/TEAM	SCOPE/NOTES	SCHEDULE	
Project Title: Haverhill Park Racquetball Court Replacement Project Number: T037 BCC District: 02 Delivery Method: Annual Contract Category: S10-Sport Court Replacement/ Resurfacing Status: Design Designer: Song & Associates Contractor: TBD Project Manager: David Polson	Scope FY18 \$270,000 IST FY19(\$268,749) IST FY22 \$268,749 IST FY24 \$32,940 IST Notes CID Project Manager again requested a proposal for expanded services from Song and Associates on 1/12/2026 and is awaiting a response.	Original	Actual
		Project Start	1/10/2022 3/1/2023

PARTICIPATION	FUNDING	FINANCIAL SUMMARY			
Consultant		Project Budget	Committed	% Committed	Paid To Date
SBE TBD		A	B	C=B/A	D
Local TBD		\$802,940	\$43,133	5.37%	\$33,579
Contractor					
SBE TBD					
Local TBD					



Monthly Infrastructure Sales Tax Project Report

Small Cap Projects

Data Date: 2/19/2026

Report Date: 2/28/2026

DESCRIPTION/TEAM	SCOPE/NOTES	SCHEDULE	
Project Title: Juno Park Septic System Replacement Project Number: T056 BCC District: 01 Delivery Method: Annual Contract Category: S02-Sanitary Sewer/Septic Systems Status: Construction Designer: Civil Design Contractor: Ralph-Della Pietra, Inc Project Manager: Benjamin Carroll	Scope Heavily used public septic system needs replacement. Failure would result in public restroom failure. IST Funds - \$929,016 & Ad Valorem Funds - \$13,638. Notes Contractor is replacing the Schedule 40 couplings that are breaking and causing the pressure tests to fail. Schedule 80 couplings will be installed to determine whether the system holds pressure.	Original	Actual
		Project Start	1/30/2019
		Project Completion	12/31/2020

PARTICIPATION	FUNDING	FINANCIAL SUMMARY			
Consultant SBE 100% Local 100% Contractor SBE 30.58 Local 100%		Project Budget	Committed	% Committed	Paid To Date
		A	B	C=B/A	D
		\$1,008,147	\$850,469	84.36%	\$659,622

DESCRIPTION/TEAM	SCOPE/NOTES	SCHEDULE	
Project Title: Beach Access Dune Crossover and Dock Repair and Rej Project Number: T071 BCC District: 01 Delivery Method: Annual Construction Contract Category: B06-Bridge or Boardwalk Replacement Status: Construction Designer: N/A Contractor: Wynn and Sons Project Manager: Brian Mcnamara	Scope Countywide repair of various beach access infrastructure, dune crossovers and docks to address physical conditions that pose potential hazards. A total of \$250,000 is budgeted through appropriations scheduled to continue thru FY2025. Notes Boardwalk #76 in Coral Cove Park is complete. Awaiting identification of next project by Parks.	Original	Actual
		Notice to Proceed-"boardwalk #76/CCP"	1/2/2018
		Start Date-"boardwalk #76/CCP"	1/2/2018
		Completion Date-"boardwalk #76/CCP"	2/28/2018
			10/17/2023

PARTICIPATION	FUNDING	FINANCIAL SUMMARY			
Consultant SBE N/A Local N/A Contractor SBE 15% Local 100%		Project Budget	Committed	% Committed	Paid To Date
		A	B	C=B/A	D
		\$250,000	\$145,967	58.39%	\$145,967



Monthly Infrastructure Sales Tax Project Report

Small Cap Projects

Data Date: 2/19/2026

Report Date: 2/28/2026

DESCRIPTION/TEAM	SCOPE/NOTES	SCHEDULE		
<p>Project Title: Ocean Inlet Park Street and Parking Lot Light Replacement</p> <p>Project Number: T081</p> <p>BCC District: 04</p> <p>Delivery Method: Annual Contract</p> <p>Category: P02-Parking Lot Lighting Replacement</p> <p>Status: Design</p> <p>Designer: JLRD</p> <p>Contractor: TBD</p> <p>Project Manager: Ben Carroll</p>	<p>Scope</p> <p>Replace existing parking lot lighting fixtures with LED type.</p> <p>Notes</p> <p>The project is on hold by Parks until ERM completes their bulkhead improvements at Boynton Inlet before moving forward with the project again.</p>	Original	Actual	
		Design Start	12/28/2018	12/28/2018
		Construction Start	1/15/2020	
		Project Completion	3/15/2020	

PARTICIPATION	FUNDING	FINANCIAL SUMMARY			
<p>Consultant</p> <p>SBE 100%</p> <p>Local 100%</p> <p>Contractor</p> <p>SBE TBD</p> <p>Local TBD</p>		Project Budget	Committed	% Committed	Paid To Date
		A	B	C=B/A	D
		\$84,000	\$10,870	12.94%	\$9,698

DESCRIPTION/TEAM	SCOPE/NOTES	SCHEDULE		
<p>Project Title: JPP Triplex Building Replacement</p> <p>Project Number: T105</p> <p>BCC District: 03</p> <p>Delivery Method: Annual Contract</p> <p>Category: P08-Public Building Repair Replacement & Expansion</p> <p>Status: Design</p> <p>Designer: Colome' and Associates</p> <p>Contractor: TBD</p> <p>Project Manager: David Polson</p>	<p>Scope</p> <p>Replacement of the John Prince Park Triplex Building which includes a restroom and concession stand.</p> <p>FY2020 \$780,000 IST</p> <p>FY2024 \$95,160 IST</p> <p>Notes</p> <p>Asbestos survey is in process of being completed. Colomé has submitted a proposal for design services, and Supplement #4 to CSA #7 is in progress.</p>	Original	Actual	
		Design Start	11/30/2020	11/30/2020
		Design Completion	5/3/2021	2/26/2024
		Bidding Procurement	7/5/2021	
		Construction Start	11/1/2021	
		Project Completion	2/7/2022	

PARTICIPATION	FUNDING	FINANCIAL SUMMARY			
<p>Consultant</p> <p>SBE 55.8%</p> <p>Local 100%</p> <p>Contractor</p> <p>SBE TBD</p> <p>Local TBD</p>		Project Budget	Committed	% Committed	Paid To Date
		A	B	C=B/A	D
		\$875,160	\$137,900	15.76%	\$110,588



Monthly Infrastructure Sales Tax Project Report

Small Cap Projects

Data Date: 2/19/2026

Report Date: 2/28/2026

DESCRIPTION/TEAM	SCOPE/NOTES	SCHEDULE	
Project Title: Caloosa Park Racquetball Court Replacement Project Number: T106 BCC District: 04 Delivery Method: Annual Contract Category: S10-Sport Court Replacement/ Resurfacing Status: Close Out Designer: Song & Associates Contractor: Ralph-Della Pietra, Inc Project Manager: Washington Molina	Scope Remove and replace 16 existing Racquetball Courts with new Racquetball Courts. This includes design, permitting, demolition of existing and installations of new Courts. Notes Processing contractor's final pay application. Type 1 Transfer may be forthcoming.	Original	Actual
		Design Start	4/15/2022 / 4/15/2022
		Permitting	3/20/2023 / 9/4/2024
		NTP	7/22/2024 / 7/22/2024
		Construction Start	9/16/2024 / 9/16/2024
		Substantial Completion	2/8/2025 / 10/3/2025
		Punch List Verified	3/12/2025 / 3/12/2025

PARTICIPATION	FUNDING	FINANCIAL SUMMARY			
Consultant SBE 21.15% Local 100% Contractor SBE 26.92% Local 100%	<p style="text-align: center;">Fund Source (x 100K)</p>	Project Budget	Committed	% Committed	Paid To Date
		A	B	C=B/A	D
		\$877,568	\$736,019	83.87%	\$717,031

DESCRIPTION/TEAM	SCOPE/NOTES	SCHEDULE	
Project Title: JPP Boat Ramp Replacement Project Number: T107 BCC District: 03 Delivery Method: Annual Contract Category: F04-Fresh Water Boat Ramps Status: Close Out Designer: Stantec Consulting Services, Inc. Contractor: All-Site Project Manager: Sunil Jagoo	Scope Replacement of the north boat ramp, removing the middle pier on the two south boat ramp and creating one single wider ramp in their place, replacement of the north and south fixed piers with floating dock piers, development of a gangway between the floating piers and the fixed fishing docks that adjust Notes CID is awaiting the revised as-builts from the contractor to close out the project.	Original	Actual
		Schematic Design	3/31/2020 / 5/31/2019
		Design Development	6/16/2020 / 10/29/2019
		Permitting	7/7/2020 / 4/22/2020
		Construction Documents	8/11/2020 / 11/5/2020
		Construction Start	10/6/2020 / 2/1/2021
		Construction Completion	11/5/2021 / 1/7/2022
		Project Completion	12/31/2021

PARTICIPATION	FUNDING	FINANCIAL SUMMARY			
Consultant SBE 31% Local 31% Contractor SBE 100% Local 100%	<p style="text-align: center;">Fund Source (x 100K)</p>	Project Budget	Committed	% Committed	Paid To Date
		A	B	C=B/A	D
		\$448,800	\$390,148	86.93%	\$390,148



Monthly Infrastructure Sales Tax Project Report

Small Cap Projects

Data Date: 2/19/2026

Report Date: 2/28/2026

DESCRIPTION/TEAM	SCOPE/NOTES	SCHEDULE	
Project Title: Gulfstream Park Septic System Replacement Project Number: T114 BCC District: 04 Delivery Method: Annual Contract Category: S02-Sanitary Sewer/Septic Systems Status: Construction Designer: Chen Moore Contractor: Amici Engineering Contractors Project Manager: Bob Hamilton	Scope Conversion of the existing septic system servicing the park, Ocean Rescue office and caretakers residence to a sewer system . FY20: \$100,000 Notes Project is on hold until lift station is installed. Long lead time for the lift station.	Original	Actual
		Start Date	10/19/2021 12/24/2024
		Completion Date	4/29/2025

PARTICIPATION	FUNDING	FINANCIAL SUMMARY			
Consultant SBE 100% Local 100% Contractor SBE 20.45% Local 100%	<p style="text-align: center;">Fund Source (x 100K)</p>	Project Budget	Committed	% Committed	Paid To Date
		A	B	C=B/A	D
		\$100,000	\$65,444	65.44%	\$56,154

DESCRIPTION/TEAM	SCOPE/NOTES	SCHEDULE	
Project Title: Countywide Fencing Replacement Project Number: T117 BCC District: Multiple Delivery Method: Annual Purchasing Category: F02-Fencing Replacement Status: Close Out Designer: N/A Contractor: Tropic Fence Inc Project Manager: Diego Torres-Malaga	Scope This project will replace the chain-link fences at various parks countywide. This project is funded in: FY20 \$70,000, FY21 \$58,479, FY22 \$81,521, FY23 \$80,001, FY24 \$138,000, and FY25 \$71,999 Notes The current residual balance will be fully expended on an upcoming fencing project, which will replace chain link fences at various parks countywide.	Original	Actual
		Notice to Proceed	6/25/2020 6/25/2020
		Start Date	7/20/2020 8/17/2020
		Completion Date	8/20/2020

PARTICIPATION	FUNDING	FINANCIAL SUMMARY			
Consultant SBE N/A Local N/A Contractor SBE 0% Local 50%	<p style="text-align: center;">Fund Source (x 100K)</p>	Project Budget	Committed	% Committed	Paid To Date
		A	B	C=B/A	D
		\$500,000	\$500,000	100.00%	\$328,708



Monthly Infrastructure Sales Tax Project Report

Small Cap Projects

Data Date: 2/19/2026

Report Date: 2/28/2026

DESCRIPTION/TEAM	SCOPE/NOTES	SCHEDULE	
<p>Project Title: Duncan Padgett Maintenance Office Septic System Repl;</p> <p>Project Number: T119</p> <p>BCC District: 06</p> <p>Delivery Method: Annual Contract</p> <p>Category: S02-Sanitary Sewer/Septic Systems</p> <p>Status: Design</p> <p>Designer: Chen Moore</p> <p>Contractor: TBD</p> <p>Project Manager: Bob Hamilton</p>	<p>Scope</p> <p>Duncan Park & Glades District Field</p> <p>- The location of the existing system, cannot be the same location for the new system. This is due to lack of available area (light poles, etc.) because of the height of the new system. The new system will be an estimated 4' tall.</p> <p>Notes</p> <p>Design has commenced to connect the restroom within the Maintenance Office to a sewer system. The design consultant is Chen Moore which was procured through a WUD annual design contract. Design and Construction will be funded through allocated ARPA funds. Awaiting first set of design drawings.</p>	Original	Actual
		Project Start	5/28/2020 5/28/2020
		Project Completion	1/28/2021

PARTICIPATION	FUNDING	FINANCIAL SUMMARY			
<p>Consultant</p> <p>SBE 48.3%</p> <p>Local 100%</p> <p>Contractor</p> <p>SBE TBD</p> <p>Local TBD</p>	<p style="text-align: center;">Fund Source (x 100K)</p>	Project Budget	Committed	% Committed	Paid To Date
		A	B	C=B/A	D
		\$5,747	\$5,747	100.01%	\$5,747

DESCRIPTION/TEAM	SCOPE/NOTES	SCHEDULE	
<p>Project Title: Lake Lytal Softball Complex Building Replacement</p> <p>Project Number: T128</p> <p>BCC District: 02</p> <p>Delivery Method: Annual Contract</p> <p>Category: P08-Public Building Repair Replacement & Expansion</p> <p>Status: Design</p> <p>Designer: TBD</p> <p>Contractor: TBD</p> <p>Project Manager: Bob Hamilton</p>	<p>Scope</p> <p>IST FY21 \$780,000, FY22 \$73,400, and FY24 \$104,115</p> <p>Notes</p> <p>Demolition work of the former concession building is completed. An RFP has yet to be issued for the construction of the new building. Project will be managed by CID.</p>	Original	Actual
		Asbestos Removal	5/1/2024 5/1/2024
		Demolition	1/6/2025 1/6/2025

PARTICIPATION	FUNDING	FINANCIAL SUMMARY			
<p>Consultant</p> <p>SBE TBD</p> <p>Local TBD</p> <p>Contractor</p> <p>SBE TBD</p> <p>Local TBD</p>	<p style="text-align: center;">Fund Source (x 100K)</p>	Project Budget	Committed	% Committed	Paid To Date
		A	B	C=B/A	D
		\$957,515	\$14,527	1.52%	\$14,527



Monthly Infrastructure Sales Tax Project Report

Small Cap Projects

Data Date: 2/19/2026

Report Date: 2/28/2026

DESCRIPTION/TEAM	SCOPE/NOTES	SCHEDULE	
Project Title: Triangle Park Restroom Replacement Project Number: T138 BCC District: 06 Delivery Method: Annual Contract Category: R02-Restroom Replacement Status: Design Designer: Song & Associates Contractor: TBD Project Manager: Javier Torres	Scope Remove and replaced restroom building. IST Funded: FY21 \$271,000, FY22 \$18,100, and FY24 \$35,148 Notes The consultant is updating the proposal.	Original	Actual
		9/30/2025	

PARTICIPATION	FUNDING	FINANCIAL SUMMARY			
Consultant SBE TBD Local TBD Contractor SBE TBD Local TBD		Project Budget	Committed	% Committed	Paid To Date
		A	B	C=B/A	D
		\$323,248	\$7,562	2.34%	\$7,562

DESCRIPTION/TEAM	SCOPE/NOTES	SCHEDULE	
Project Title: Lake Lytal Park Racquetball Court Replacement Project Number: T139 BCC District: 02 Delivery Method: Annual Contract Category: S10-Sport Court Replacement/ Resurfacing Status: Design Designer: Song & Associates Contractor: TBD Project Manager: David Polson	Scope Demolish and replace the racquetball court at Lake Lytal . Work should consist of furnishings all materials, permits and equipment. IST Funded: FY21 \$271,000, FY22 \$18,100,FY24 \$35,148, and FY25 \$300,000 Notes CID Project Manager again requested a proposal for expanded services from Song and Associates on 1/12/2026 and is awaiting a response.	Original	Actual
		3/31/2022	3/31/2022

PARTICIPATION	FUNDING	FINANCIAL SUMMARY			
Consultant SBE TBD Local TBD Contractor SBE TBD Local TBD		Project Budget	Committed	% Committed	Paid To Date
		A	B	C=B/A	D
		\$623,248	\$40,041	6.42%	\$33,216



Monthly Infrastructure Sales Tax Project Report

Small Cap Projects

Data Date: 2/19/2026

Report Date: 2/28/2026

DESCRIPTION/TEAM	SCOPE/NOTES	SCHEDULE	
Project Title: BASCR Boat Ramp Replacement Project Number: T140 BCC District: 05 Delivery Method: Annual Contract Category: F04-Fresh Water Boat Ramps Status: Permitting Designer: WGI Contractor: TBD Project Manager: Washington Molina	Scope Replace existing boat ramps, providing materials, labor, and equipment. Includes design, permitting, demolition, and installation of new concrete ramps and piers. Parks request they match the ramps being replaced at John Prince Park. IST Funded: FY21 \$250K, FY22 \$17.5K, FY24 \$32,635 and FY26 Notes Parks confirmed available funds for the project, and CID is proceeding with the permitting process.	Original	Actual
		Design Start	1/5/2023 / 3/5/2024
		Design Complete	10/10/2025 / 10/10/2025
		Permitting	2/6/2026

PARTICIPATION	FUNDING	FINANCIAL SUMMARY			
Consultant SBE 62.4 Local 100% Contractor SBE TBD Local TBD	<p style="text-align: center;">Fund Source (x 100K)</p>	Project Budget	Committed	% Committed	Paid To Date
		A	B	C=B/A	D
		\$593,135	\$33,659	5.67%	\$24,497

DESCRIPTION/TEAM	SCOPE/NOTES	SCHEDULE	
Project Title: Jupiter Beach Park Parking Lot Light Replacement Project Number: T141 BCC District: 01 Delivery Method: Annual Contract Category: P02-Parking Lot Lighting Replacement Status: Design Designer: TBD Contractor: TBD Project Manager: Nick Chimienti	Scope Replacement of the existing parking lot light fixtures with LED type. IST Funded: FY21 \$250,000, FY22 \$17,500, FY24 \$32,635 and FY26 \$151,000 Notes CID is awaiting on the new MEP design contract.	Original	Actual
		Design Proposal	10/31/2024 / 10/31/2025

PARTICIPATION	FUNDING	FINANCIAL SUMMARY			
Consultant SBE TBD Local TBD Contractor SBE TBD Local TBD	<p style="text-align: center;">Fund Source (x 100K)</p>	Project Budget	Committed	% Committed	Paid To Date
		A	B	C=B/A	D
		\$451,135	\$451	0.10%	\$451



Monthly Infrastructure Sales Tax Project Report

Small Cap Projects

Data Date: 2/19/2026

Report Date: 2/28/2026

DESCRIPTION/TEAM	SCOPE/NOTES	SCHEDULE															
<p>Project Title: Ocean Reef Park Parking Lot Light Replacement</p> <p>Project Number: T142</p> <p>BCC District: 01</p> <p>Delivery Method: Annual Contract</p> <p>Category: P02-Parking Lot Lighting Replacement</p> <p>Status: Close Out</p> <p>Designer: JLRD</p> <p>Contractor: Grid-One Electrical Construction, Inc.</p> <p>Project Manager: Ben Carroll</p>	<p>Scope</p> <p>Replacement of the existing parking lot light fixtures with LED type.</p> <p>FY 2021 \$250,000</p> <p>FY 2022 \$17,500</p> <p>Notes</p> <p>Project close out is pending the final pay application from JLRD.</p>	<table border="1"> <thead> <tr> <th></th> <th>Original</th> <th>Actual</th> </tr> </thead> <tbody> <tr> <td>Project Start</td> <td>4/25/2021</td> <td>4/25/2021</td> </tr> <tr> <td>Project Completion</td> <td>11/1/2021</td> <td></td> </tr> <tr> <td>Substantial Completion</td> <td>12/18/2024</td> <td>12/18/2024</td> </tr> <tr> <td>Construction Complete</td> <td>12/18/2024</td> <td>12/18/2024</td> </tr> </tbody> </table>		Original	Actual	Project Start	4/25/2021	4/25/2021	Project Completion	11/1/2021		Substantial Completion	12/18/2024	12/18/2024	Construction Complete	12/18/2024	12/18/2024
	Original	Actual															
Project Start	4/25/2021	4/25/2021															
Project Completion	11/1/2021																
Substantial Completion	12/18/2024	12/18/2024															
Construction Complete	12/18/2024	12/18/2024															

PARTICIPATION	FUNDING	FINANCIAL SUMMARY												
<p>Consultant</p> <p>SBE 98%</p> <p>Local 100%</p> <p>Contractor</p> <p>SBE 100%</p> <p>Local 98%</p>		<table border="1"> <thead> <tr> <th>Project Budget</th> <th>Committed</th> <th>% Committed</th> <th>Paid To Date</th> </tr> <tr> <th>A</th> <th>B</th> <th>C=B/A</th> <th>D</th> </tr> </thead> <tbody> <tr> <td>\$267,500</td> <td>\$267,500</td> <td>100.00%</td> <td>\$267,105</td> </tr> </tbody> </table>	Project Budget	Committed	% Committed	Paid To Date	A	B	C=B/A	D	\$267,500	\$267,500	100.00%	\$267,105
Project Budget	Committed	% Committed	Paid To Date											
A	B	C=B/A	D											
\$267,500	\$267,500	100.00%	\$267,105											

DESCRIPTION/TEAM	SCOPE/NOTES	SCHEDULE															
<p>Project Title: Caloosa Park Light Replacement</p> <p>Project Number: T144</p> <p>BCC District: 04</p> <p>Delivery Method: Annual Contract</p> <p>Category: P02-Parking Lot Lighting Replacement</p> <p>Status: Permitting</p> <p>Designer: JLRD</p> <p>Contractor: Pyke Electric Inc.</p> <p>Project Manager: Ben Carroll</p>	<p>Scope</p> <p>Replacement of the existing parking lot light fixtures with LED type.</p> <p>FY 2021 \$200,000</p> <p>FY 2022 \$16,000</p> <p>FY 2024 \$38,880</p> <p>Notes</p> <p>Project is currently on hold due to permitting requirements. The City of Boynton Beach has requested additional lighting, which is requires a design change.</p>	<table border="1"> <thead> <tr> <th></th> <th>Original</th> <th>Actual</th> </tr> </thead> <tbody> <tr> <td>Project Start</td> <td>4/25/2021</td> <td>4/25/2021</td> </tr> <tr> <td>Project Completion</td> <td>11/1/2021</td> <td></td> </tr> <tr> <td>Bidding in Advertising</td> <td>4/9/2025</td> <td>4/9/2025</td> </tr> <tr> <td>Notice to Proceed to contractor</td> <td>8/28/2025</td> <td>8/28/2025</td> </tr> </tbody> </table>		Original	Actual	Project Start	4/25/2021	4/25/2021	Project Completion	11/1/2021		Bidding in Advertising	4/9/2025	4/9/2025	Notice to Proceed to contractor	8/28/2025	8/28/2025
	Original	Actual															
Project Start	4/25/2021	4/25/2021															
Project Completion	11/1/2021																
Bidding in Advertising	4/9/2025	4/9/2025															
Notice to Proceed to contractor	8/28/2025	8/28/2025															

PARTICIPATION	FUNDING	FINANCIAL SUMMARY												
<p>Consultant</p> <p>SBE 100%</p> <p>Local 100%</p> <p>Contractor</p> <p>SBE 100%</p> <p>Local 100%</p>		<table border="1"> <thead> <tr> <th>Project Budget</th> <th>Committed</th> <th>% Committed</th> <th>Paid To Date</th> </tr> <tr> <th>A</th> <th>B</th> <th>C=B/A</th> <th>D</th> </tr> </thead> <tbody> <tr> <td>\$331,880</td> <td>\$254,880</td> <td>76.80%</td> <td>\$25,135</td> </tr> </tbody> </table>	Project Budget	Committed	% Committed	Paid To Date	A	B	C=B/A	D	\$331,880	\$254,880	76.80%	\$25,135
Project Budget	Committed	% Committed	Paid To Date											
A	B	C=B/A	D											
\$331,880	\$254,880	76.80%	\$25,135											



Monthly Infrastructure Sales Tax Project Report

Small Cap Projects

Data Date: 2/19/2026

Report Date: 2/28/2026

DESCRIPTION/TEAM	SCOPE/NOTES	SCHEDULE	
Project Title: Carlin Park Parking Lot Light Replacement Project Number: T145 BCC District: 01 Delivery Method: Annual Contract Category: P02-Parking Lot Lighting Replacement Status: Construction Designer: JLRD Contractor: Grid One Electrical Construction, Inc. Project Manager: Ben Carroll	Scope Replace existing parking lot lighting fixtures with LED type. FY 2021 \$200,000 FY 2022 \$16,000 FY 2024 \$26,352 Notes FSPM reached out to the contractor, and they can begin work in approximately two weeks, regardless of whether the change order for monitoring the excavation is approved. Work is expected to start on 3/23/26."	Original	Actual
		Project Start	11/13/2020 11/27/2024
		Project Completion	12/2/2022
		Notice to Proceed to contractor	11/27/2024 11/27/2024
		Substantial Completion	11/27/2025

PARTICIPATION	FUNDING	FINANCIAL SUMMARY			
Consultant SBE 100% Local 100% Contractor SBE 31% Local 100%	<p style="text-align: center;">Fund Source (x 100K)</p>	Project Budget	Committed	% Committed	Paid To Date
		A	B	C=B/A	D
		\$242,352	\$242,352	100.00%	\$19,461

DESCRIPTION/TEAM	SCOPE/NOTES	SCHEDULE	
Project Title: Sunset Cove Pavilion Replacement Project Number: T146 BCC District: 05 Delivery Method: Annual Contract Category: G04-Group Pavilion Replacement Status: Close Out Designer: Alan Gerwig & Associates Contractor: Republic Construction Project Manager: Ben Carroll	Scope Renovate/Replace Existing Pavilion FY 2021 IST \$150,000 FY 2022 IST \$9,500 FY 2024 IST \$19,459 Notes CID is awaiting the correct OSBD forms from Republic Construction in order to process the change order and final payment.	Original	Actual
		Project Start	9/30/2021 9/30/2021
		Design Completion	4/29/2022 1/20/2023
		Project Completion	2/24/2023

PARTICIPATION	FUNDING	FINANCIAL SUMMARY			
Consultant SBE 100% Local 100% Contractor SBE 100% Local 100%	<p style="text-align: center;">Fund Source (x 100K)</p>	Project Budget	Committed	% Committed	Paid To Date
		A	B	C=B/A	D
		\$178,959	\$70,295	39.28%	\$70,295



Monthly Infrastructure Sales Tax Project Report

Small Cap Projects

Data Date: 2/19/2026

Report Date: 2/28/2026

DESCRIPTION/TEAM	SCOPE/NOTES	SCHEDULE	
Project Title: JPP Center Drive Pavilion Replacement Project Number: T148 BCC District: 03 Delivery Method: Annual Contract Category: G04-Group Pavilion Replacement Status: Design Designer: GM2 Engineering Associates, Inc. Contractor: TBD Project Manager: Ben Carroll	Scope Renovate/Replace Existing Pavilion FY 2021 IST \$150,000 FY 2022 IST \$9,500 FY 2024 IST \$19,459 Notes FSPM met with the electrical engineer last week to finalize the MEP plan. The last remaining item is to finalize the drawings.	Original	Actual
		Project Start	9/30/2021 / 9/30/2021
		Design Completion	4/29/2022
		Project Completion	2/24/2023
		CSA Executed	1/6/2025 / 1/6/2025

PARTICIPATION	FUNDING	FINANCIAL SUMMARY			
Consultant SBE 68% Local 100% Contractor SBE TBD Local TBD		Project Budget	Committed	% Committed	Paid To Date
		A	B	C=B/A	D
		\$350,959	\$38,500	10.97%	\$5,082

DESCRIPTION/TEAM	SCOPE/NOTES	SCHEDULE	
Project Title: Morikami Park Septic System Replacement Project Number: T149 BCC District: 05 Delivery Method: Annual Contract Category: S02-Sanitary Sewer/Septic Systems Status: Construction Designer: CDI Contractor: Amici General Contractors LLC. Project Manager: WUD	Scope Remove septic system and connect to nearest sewer line. Notes BCC approved the construction contract with Amici General Contractors LLC. on 9/17/24. Total project cost is \$463,735. ARPA funds will cover the remaining balance. Project is currently under construction.	Original	Actual
		Design Start	7/6/2021 / 7/6/2021
		Construction	4/15/2024 / 9/17/2024

PARTICIPATION	FUNDING	FINANCIAL SUMMARY			
Consultant SBE 100% Local 100% Contractor SBE 20.45% Local 100%		Project Budget	Committed	% Committed	Paid To Date
		A	B	C=B/A	D
		\$159,500	\$45,169	28.32%	\$30,169



Monthly Infrastructure Sales Tax Project Report

Small Cap Projects

Data Date: 2/19/2026

Report Date: 2/28/2026

DESCRIPTION/TEAM	SCOPE/NOTES	SCHEDULE	
<p>Project Title: Lake Lytal Park Septic System Replacement</p> <p>Project Number: T154</p> <p>BCC District: 03</p> <p>Delivery Method: Annual Contract</p> <p>Category: S02-Sanitary Sewer/Septic Systems</p> <p>Status: Design</p> <p>Designer: Chen Moore</p> <p>Contractor: TBD</p> <p>Project Manager: Bob Hamilton</p>	<p>Scope</p> <p>Remove existing septic system and connect to the County Waste Water System Force Main</p> <p>FY 2021 IST \$50,000, FY 2022 IST \$4,000, and FY 2024 IST (\$53,910).</p> <p>Notes</p> <p>Project is currently under design. Chen Moore is the design consultant and was procured using WUD's annual design contract. WUD is the Project Manager. Awaiting first set of design drawings. ARPA funds will cover the remaining balance.</p>	Original	Actual
		Project Start	4/26/2021
		Project Completion	12/20/2021

PARTICIPATION	FUNDING	FINANCIAL SUMMARY			
<p>Consultant</p> <p>SBE 35.27%</p> <p>Local 100%</p> <p>Contractor</p> <p>SBE TBD</p> <p>Local TBD</p>		Project Budget	Committed	% Committed	Paid To Date
		A	B	C=B/A	D
		\$90	\$90	100.17%	\$90

DESCRIPTION/TEAM	SCOPE/NOTES	SCHEDULE	
<p>Project Title: Okeehetee Park Ski Lake Boat Ramp Replacement</p> <p>Project Number: T160</p> <p>BCC District: 02</p> <p>Delivery Method: Annual Contract</p> <p>Category: F04-Fresh Water Boat Ramps</p> <p>Status: Design</p> <p>Designer: R.J. Behar & Company</p> <p>Contractor: TBD</p> <p>Project Manager: Washington Molina</p>	<p>Scope</p> <p>Install a new boat ramp and relocate the west floating dock as necessary to accommodate the new work. The existing boat ramp is to remain in use, and then removed, upon completion of the new ramp. IST Funded: FY22 \$474K and FY24 \$57,828</p> <p>Notes</p> <p>Received 90% submittal plans from the consultant.</p>	Original	Actual
		Project Start	11/17/2024
		Design Start	8/8/2025
		Design 60% Submittal Plans	8/22/2025
		Design 95% Submittal Plans	11/3/2025

PARTICIPATION	FUNDING	FINANCIAL SUMMARY			
<p>Consultant</p> <p>SBE 22.54%</p> <p>Local 100%</p> <p>Contractor</p> <p>SBE TBD</p> <p>Local TBD</p>		Project Budget	Committed	% Committed	Paid To Date
		A	B	C=B/A	D
		\$901,828	\$59,937	6.65%	\$45,998



Monthly Infrastructure Sales Tax Project Report

Small Cap Projects

Data Date: 2/19/2026


Report Date: 2/28/2026

DESCRIPTION/TEAM	SCOPE/NOTES	SCHEDULE	
<p>Project Title: Okeeheelee Park Street and Parking Lot Light Replacement</p> <p>Project Number: T161</p> <p>BCC District: 02</p> <p>Delivery Method: Annual Contract</p> <p>Category: P02-Parking Lot Lighting Replacement</p> <p>Status: Permitting</p> <p>Designer: JLRD</p> <p>Contractor: Grid One Electrical Construction, Inc.</p> <p>Project Manager: Benjamin Carroll</p>	<p>Scope</p> <p>Okeeheelee Park Site Lighting Replacement is located @ 7715 Forest Hill Blvd, West Palm Beach. Professional services shall include electrical engineering design services for the replacement of 56 new pole-mounted LED fixtures and 67 new LED fixtures.</p> <p>Notes</p> <p>Submittals have been received and sent to the engineer for approval.</p>	Original	Actual
		Construction Start TBD	
		Design Start	7/22/2022
		Design Complete	9/15/2023

PARTICIPATION	FUNDING	FINANCIAL SUMMARY			
Consultant		Project Budget	Committed	% Committed	Paid To Date
SBE 0%		A	B	C=B/A	D
Local 100%	IST	\$801,312	\$655,313	81.78%	\$37,746
Contractor					
SBE 29%					
Local 100%					

DESCRIPTION/TEAM	SCOPE/NOTES	SCHEDULE	
<p>Project Title: West Boynton Parking Lot Light Replacement</p> <p>Project Number: T162</p> <p>BCC District: 02</p> <p>Delivery Method: TBD</p> <p>Category: P02-Parking Lot Lighting Replacement</p> <p>Status: Permitting</p> <p>Designer: JLRD</p> <p>Contractor: South Atlantic Electric, Inc.</p> <p>Project Manager: Ben Carroll</p>	<p>Scope</p> <p>Replacement of the existing parking lot light fixtures with LED type.</p> <p>FY 2019 IST \$285,000</p> <p>FY 2022 IST \$42,100</p> <p>FY 2024 IST \$39,906</p> <p>Notes</p> <p>This project involves fixture replacement only. The fixtures have been ordered, with delivery expected on 4/26.</p>	Original	Actual
		Design Start	12/26/2018
		Construction Start	1/15/2020
		Project Completion	3/15/2020
		NTP Issued	8/28/2025
		Permit	11/7/2025

PARTICIPATION	FUNDING	FINANCIAL SUMMARY			
Consultant		Project Budget	Committed	% Committed	Paid To Date
SBE 100%		A	B	C=B/A	D
Local 100%	IST	\$522,006	\$220,058	42.16%	\$19,330
Contractor					
SBE 100%					
Local 100%					

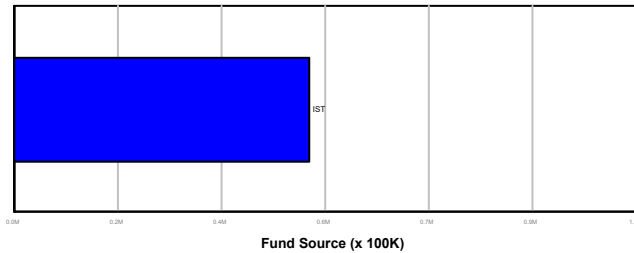



Monthly Infrastructure Sales Tax Project Report

Small Cap Projects

Data Date: 2/19/2026

Report Date: 2/28/2026

DESCRIPTION/TEAM	SCOPE/NOTES	SCHEDULE	
<p>Project Title: Morikami Park Light Replacement</p> <p>Project Number: T164</p> <p>BCC District: 05</p> <p>Delivery Method: Annual Contract</p> <p>Category: P02-Parking Lot Lighting Replacement</p> <p>Status: Construction</p> <p>Designer: JLRD</p> <p>Contractor: Grid One Electrical Construction, Inc.</p> <p>Project Manager: Benjamin Carroll</p>	<p>Scope</p> <p>The project includes replacing light fixtures at the museum parking lot, loading zone, and walkway. Convert current lights.</p> <p>IST Funded: FY22 \$167,640 ,FY24 \$20,452 and FY26 \$641,000.</p> <p>Notes</p> <p>Poles are onsite and awaiting fixtures from Cree, with delivery expected in May 2026. Pay App #3 has been received.</p>	Original	Actual
		Design Start	7/22/2022 / 7/22/2022
		Design Complete	9/15/2023 / 9/15/2023
		Grid-One Awarded	3/6/2025 / 6/13/2025

PARTICIPATION	FUNDING	FINANCIAL SUMMARY			
<p>Consultant</p> <p>SBE 0%</p> <p>Local 100%</p> <p>Contractor</p> <p>SBE 29%</p> <p>Local 100%</p>	<p style="text-align: center;">Fund Source (x 100K)</p>	Project Budget	Committed	% Committed	Paid To Date
		A	B	C=B/A	D
		\$829,092	\$188,092	22.69%	\$22,730

DESCRIPTION/TEAM	SCOPE/NOTES	SCHEDULE	
<p>Project Title: Caloosa Park Roadway Repairs</p> <p>Project Number: T170</p> <p>BCC District: 04</p> <p>Delivery Method: Annual Contract</p> <p>Category: A04-Asphalt Paving & Striping</p> <p>Status: Close Out</p> <p>Designer: N/A</p> <p>Contractor: Wynn and Sons</p> <p>Project Manager: Garry Monnett</p>	<p>Scope</p> <p>Repairs to internal roadways within Caloosa Park.</p> <p>Notes</p> <p>Project was completed on 2/19/26, CRC approved payment to the vendor on 3/04/26, invoice was sent to Payables on 03/04/26. Account should be at \$0.00 balance when paid by Payables.</p>	Original	Actual
		Scoping	1/3/2023 / 1/3/2023
		Quote	3/1/2023 / 4/4/2023
		Work Commencement	4/3/2023
		Completion	8/31/2023

PARTICIPATION	FUNDING	FINANCIAL SUMMARY			
<p>Consultant</p> <p>SBE N/A</p> <p>Local N/A</p> <p>Contractor</p> <p>SBE 20%</p> <p>Local 100%</p>	<p style="text-align: center;">Fund Source (x 100K)</p>	Project Budget	Committed	% Committed	Paid To Date
		A	B	C=B/A	D
		\$26,200	\$48	0.19%	\$48



Monthly Infrastructure Sales Tax Project Report

Small Cap Projects

Data Date: 2/19/2026


Report Date: 2/28/2026

DESCRIPTION/TEAM	SCOPE/NOTES	SCHEDULE	
Project Title: BASCR Street and Parking Lot Light Replacement Project Number: T179 BCC District: 05 Delivery Method: Annual Contract Category: P02-Parking Lot Lighting Replacement Status: Design Designer: FICE Contractor: TBD Project Manager: Eric Chimienti	Scope Replacement of existing light fixtures with LED lights at street and parking lots. New LED fixtures will improve lighting for safety as well as energy efficiency. IST Funded: FY23 \$638,600, FY24 \$77,909 and FY26 \$285,000. Notes The MEP contract expired on 11/16/2025, and CID was unable to finalize the CSA before it lapsed. CID will need to wait for a new FICE contract to obtain a new proposal and proceed with the work. CID is awaiting on the new MEP design contract.	Original	Actual
		Project Start	12/5/2024 9/15/2025

PARTICIPATION	FUNDING	FINANCIAL SUMMARY			
Consultant		Project Budget	Committed	% Committed	Paid To Date
SBE	TBD	A	B	C=B/A	D
Local	TBD	\$1,001,509	\$1,450	0.14%	\$1,450
Contractor					
SBE	TBD				
Local	TBD				

DESCRIPTION/TEAM	SCOPE/NOTES	SCHEDULE	
Project Title: Canal Point Community Center Building Replacement Project Number: T180 BCC District: 06 Delivery Method: Annual Contract Category: P08-Public Building Repair Replacement & Expansion Status: Design Designer: TBD Contractor: TBD Project Manager: Javier Torres	Scope Replacement of the Canal Point Community Center (more than 30 years old). Heavily used community center in Glades. IST Funded: FY23 \$595,000 and FY24 \$72,590. Notes The design services proposal was updated and resubmitted. Currently under review by the CID team.	Original	Actual
		Pre-Design	8/11/2025 8/11/2025

PARTICIPATION	FUNDING	FINANCIAL SUMMARY			
Consultant		Project Budget	Committed	% Committed	Paid To Date
SBE	TBD	A	B	C=B/A	D
Local	TBD	\$667,590	\$5,233	0.78%	\$5,233
Contractor					
SBE	TBD				
Local	TBD				

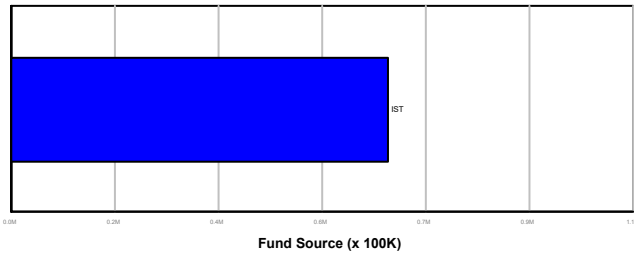



Monthly Infrastructure Sales Tax Project Report

Small Cap Projects

Data Date: 2/19/2026

Report Date: 2/28/2026

DESCRIPTION/TEAM	SCOPE/NOTES	SCHEDULE	
Project Title: JPP Street and Parking Lot Light Replacement Project Number: T184 BCC District: 03 Delivery Method: Annual Contract Category: P02-Parking Lot Lighting Replacement Status: Design Designer: FICE Contractor: TBD Project Manager: Eric Chimienti	Scope Replacement of existing light fixtures with LED lights at street and parking lots. New LED fixtures will improve lighting for safety as well as energy efficiency. IST Funded: FY23 \$352,000 and FY24 \$42,944. Notes The MEP contract expired on 11/16/2025, and CID was unable to finalize the CSA before it lapsed. CID will need to wait for a new contract to obtain a new proposal and proceed with the work. CID is awaiting on the new MEP design contract.	Original	Actual
		3/10/2025	3/10/2025

PARTICIPATION	FUNDING	FINANCIAL SUMMARY			
Consultant SBE TBD Local TBD Contractor SBE TBD Local TBD	<p style="text-align: center;">Fund Source (x 100K)</p>	Project Budget	Committed	% Committed	Paid To Date
		A	B	C=B/A	D
		\$500,944	\$799	0.16%	\$799

DESCRIPTION/TEAM	SCOPE/NOTES	SCHEDULE	
Project Title: JPP Daycamp Restroom Replacement Project Number: T186 BCC District: 03 Delivery Method: Annual Contract Category: R02-Restroom Replacement Status: Design Designer: TBD Contractor: TBD Project Manager: David Polson	Scope Old public restroom approaching the end of its expected useful life (in daycamp area of John Prince Park) is in need of replacement (more than 25 years old). IST Funded: FY23 \$319,300 and FY24 \$38,955. Notes CID Project Manager again requested a proposal for expanded services from Song and Associates on 1/12/2026 and is awaiting a response. Asbestos Survey report received on 3/3/26 with negative results.	Original	Actual
		11/18/2025	
		11/19/2025	

PARTICIPATION	FUNDING	FINANCIAL SUMMARY			
Consultant SBE TBD Local TBD Contractor SBE TBD Local TBD	<p style="text-align: center;">Fund Source (x 100K)</p>	Project Budget	Committed	% Committed	Paid To Date
		A	B	C=B/A	D
		\$358,255	\$725	0.20%	\$725



Monthly Infrastructure Sales Tax Project Report

Small Cap Projects

Data Date: 2/19/2026

Report Date: 2/28/2026

DESCRIPTION/TEAM	SCOPE/NOTES	SCHEDULE	
<p>Project Title: Dyer Park Street and Parking Lot Light Replacement</p> <p>Project Number: T190</p> <p>BCC District: 07</p> <p>Delivery Method: Annual Contract</p> <p>Category: P02-Parking Lot Lighting Replacement</p> <p>Status: Close Out</p> <p>Designer: N/A</p> <p>Contractor: Protect Video Inc</p> <p>Project Manager: Charlene LaMattina</p>	<p>Scope</p> <p>Replacement of existing light fixtures with LED lights at street and parking lots. New LED fixtures will provide energy saving and improve lighting for safety.</p> <p>IST Funded: FY23 \$229,280 and FY24 \$27,972.</p> <p>Notes</p> <p>Supplement 1 has been executed and sent to the contractor. Warranty information has been received, and the Final Pay Application is forthcoming. The Type 1 Transfer may also be forthcoming.</p>	Original	Actual
		Project Start	10/21/2023 / 2/11/2025
		Notice to Proceed to contractor	1/14/2025 / 4/14/2025
		Final Pay Application	7/31/2025

PARTICIPATION	FUNDING	FINANCIAL SUMMARY			
<p>Consultant</p> <p>SBE N/A</p> <p>Local N/A</p> <p>Contractor</p> <p>SBE 100%</p> <p>Local 100%</p>		Project Budget	Committed	% Committed	Paid To Date
		A	B	C=B/A	D
		\$259,890	\$113,090	43.51%	\$113,090

DESCRIPTION/TEAM	SCOPE/NOTES	SCHEDULE	
<p>Project Title: Duncan Padgett Park Picnic Area Improvements</p> <p>Project Number: T200</p> <p>BCC District: 06</p> <p>Delivery Method: Annual Contract</p> <p>Category: G04-Group Pavilion Replacement</p> <p>Status: Design</p> <p>Designer: Song & Associates</p> <p>Contractor: TBD</p> <p>Project Manager: Javier Torres</p>	<p>Scope</p> <p>Improving the area around the Duncan Padgett Park Picnic tables.</p> <p>IST Funded: FY21 \$235,000 ,FY24 \$28,670 and FY25 \$200,000.</p> <p>Notes</p> <p>Completed the 95% CDs with the updated pavilion foundation design, incorporated the title update into the survey, and revised the final CDs per Parks & Recreation request to remove items overlapping with the playground replacement project.</p>	Original	Actual
		Design Completion	4/1/2022
		Bidding	5/1/2022
		Construction Start	8/1/2022
		Project Completion	12/1/2022

PARTICIPATION	FUNDING	FINANCIAL SUMMARY			
<p>Consultant</p> <p>SBE 20%</p> <p>Local 100%</p> <p>Contractor</p> <p>SBE TBD</p> <p>Local TBD</p>		Project Budget	Committed	% Committed	Paid To Date
		A	B	C=B/A	D
		\$463,670	\$121,421	26.19%	\$103,336
