

# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects

Data Date: 7/15/2021

Report Date: 8/12/2021

### DESCRIPTION/TEAM

### SCOPE

### PHOTO

**Project Title:** Headquarters R&R

Project Number: 11206  
 BCC District: 02  
 Delivery Method: Construction Management  
 Category: S06-Sheriff - FDO  
 Status: Design  
 Designer: Leo Daly  
 Contractor: Kast Construction  
 Project Manager: Jim Daley

The project consists of the exterior hardening of the entire building consisting of new exterior walls, impact resistant doors and windows, roof replacement and structural tie-ins as well as the R&R of all major building systems and interior renovation of approx. 75% of the building. As part of the project, the Board has also approved the temp. relocation of employees occupying approx. 70% of the space to ensure continuity of operations during the construction, reduce the overall duration of the project and therefore total project cost. This project is funded in:

FY 2017 IST \$1,600,000  
 FY 2019 IST \$11,047,000  
 FY 2020 IST \$10,835,000  
 FY 2021 IST \$17,620,000



### SCHEDULE SUMMARY

	Original	Actual
Project Start	3/14/2016	3/14/2016
Design Start	5/9/2017	5/9/2017
Construction Start	1/31/2019	3/22/2021
Substantial Completion	1/31/2022	
Project Completion	2/28/2022	

### PARTICIPATION


#### Consultant

SBE 24.71%  
 Local 100%  
 WBE N/A  
 MBE N/A


#### Contractor

SBE 12.75%  
 Local 100%  
 WBE N/A  
 MBE N/A

### FUNDING

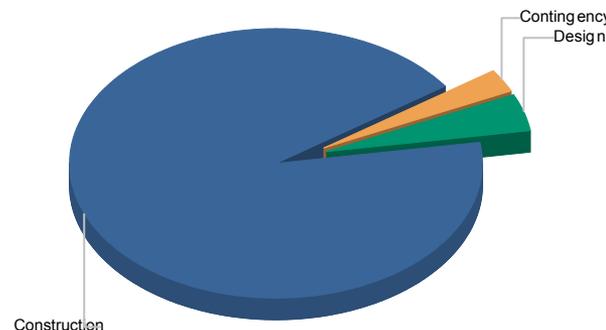

Current Budget

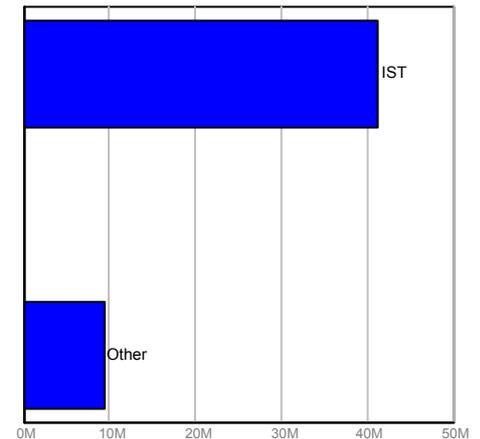

Fund Source

### FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$2,274,200	\$2,666,679	117.26%	\$2,013,368
Construction	\$46,915,796	\$35,314,514	75.27%	\$1,001,629
Furniture, Fixtures & Equipment	\$0	\$163,007	0.00%	\$162,841
Other	\$0	\$27,033	0.00%	\$27,033
Contingency	\$1,418,800	\$0	0.00%	\$0
<b>TOTAL</b>	<b>\$50,608,796</b>	<b>\$38,171,232</b>	<b>75.42%</b>	<b>\$3,204,870</b>

### NOTES

Most of Phase 1 demolition on 1st and 2nd floor has been completed. No work on 3rd floor yet. The concrete block wall has started on the W side & wrapped around to the N side, about half way up. Windows are being removed as they go. Roofing has started as well. Abatement plan for Phase 2 is pending. Interior framing has started for the walls. Cameras & DVR stack are being removed by ESS. CID has just received the first set of change orders to be processed.

# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects


Data Date: 7/15/2021

Report Date: 8/12/2021

DESCRIPTION/TEAM	SCOPE	PHOTO
<p><b>Project Title: Ocean Inlet Park and Marina Renovation</b></p> <p>Project Number: 13367                      BCC District: 04                      Delivery Method: TBD                      Category: P08-Public Building Repair Replacement &amp; Expans                      Status: Design                      Designer: Alan Gerwig &amp; Associates, Inc.                      Contractor: TBD                      Project Manager: Rich Avery</p>	<p>The project consists of the replacement of marina components as well as new components including bulkhead wall, floating docks, floating finger docks, fixed dock, boat lifts, floating wave attenuator, landscaping, and replacement of the current Marina/Restroom and concession buildings. The project will be constructed in two phases. Phase one will consist of marina bulkhead, dock reconstruction and wave attenuator construction. The remaining scope to be completed during phase 2.</p> <p>Total available funding for this project consists of \$2,500,000 FY18 IST funds, \$2,500,000 FY20 Find Grant funds. Future funding consists of \$2,500,000 FY23 IST funds and shown as "Future Funding" within the current budget.</p>	

SCHEDULE SUMMARY		
	Original	Actual
Phase I Start	2/5/2018	2/4/2018
Design Start	10/22/2018	10/22/2018
Construction Start	12/3/2019	
Substantial Completion	11/3/2020	

PARTICIPATION	
<b>Consultant</b>	
SBE	82.50%
Local	100%
WBE	N/A
MBE	N/A
<b>Contractor</b>	
SBE	TBD
Local	TBD
WBE	TBD
MBE	TBD

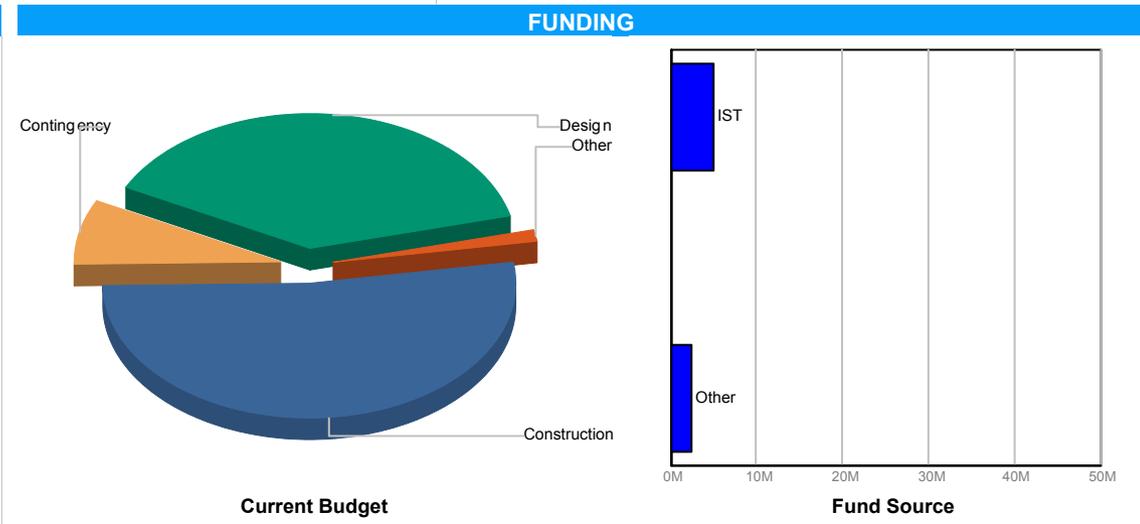

FINANCIAL SUMMARY				
	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$2,885,300	\$248,298	8.61%	\$248,298
Construction	\$3,906,200	\$0	0.00%	\$0
Other	\$108,500	\$82,207	75.77%	\$82,207
Contingency	\$600,000	\$0	0.00%	\$0
<b>TOTAL</b>	<b>\$7,500,000</b>	<b>\$330,505</b>	<b>4.41%</b>	<b>\$330,505</b>

**NOTES**

Bids were received and a responsive bidder selected. The notice of intent to award has been issue to Poseidon Dredge & Marine, Inc. Contract documentation is being assembled and processed. It is anticipated that the project will go to the BCC for final approval on Oct. 19th

# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects

Data Date: 7/15/2021

Report Date: 8/12/2021

### DESCRIPTION/TEAM

### SCOPE

### PHOTO

**Project Title: Evidence Building**

Project Number: 14218  
 BCC District: 02  
 Delivery Method: Construction Management  
 Category: S06-Sheriff - FDO  
 Status: Design  
 Designer: Leo Daly  
 Contractor: Pirtle Construction  
 Project Manager: Jeffrey Halverson

The project consists of a new 2-story Evidence Storage/Crime Scene/Crime Lab Facility (Approximately 87,000 GSF) and a 12,000 GSF metal building for impound vehicle storage. The main facility will house property seized by the Sheriff's Office, Administrative Offices, Evidence Processing via the crime scene investigation unit and the crime lab. Monitored cameras, motion detectors, and restricted access with electronic logging will be provided. The facility will accommodate secure vehicle garage bays that can store large vehicles (i.e. 56' long trailers) holding evidence for investigation or transport. Site Development (16 Acres) to include user parking (public, booking officers & staff), a fenced/gated impound lot (350 surface spaces) and a limited area of covered parking.



Palm Beach County Sheriff's Office Forensic Facility



### SCHEDULE SUMMARY

	Original	Actual
Substantial Completion	11/5/2019	10/30/2020
Project Completion	11/26/2019	
Project Start	3/30/2016	12/21/2016
Design Start	6/28/2017	6/28/2017
Construction Start	7/5/2018	4/29/2019

### PARTICIPATION


#### Consultant

SBE 33.21%  
 Local 78.96%  
 WBE N/A  
 MBE N/A

#### Contractor

SBE 21.60%  
 Local 55%  
 WBE N/A  
 MBE N/A

### FUNDING

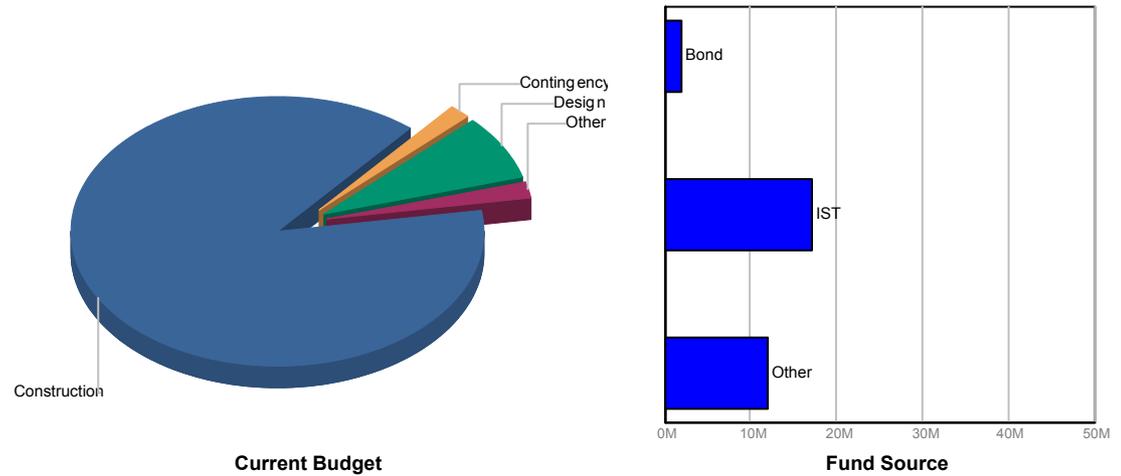

### FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$2,461,526	\$2,343,527	95.21%	\$1,960,419
Construction	\$27,680,589	\$28,130,164	101.62%	\$19,220,970
Furniture, Fixtures & Equipment	\$0	\$0	0.00%	\$0
Other	\$602,158	\$192,346	31.94%	\$192,346
Contingency	\$492,268	\$3,672	0.75%	\$3,672
<b>TOTAL</b>	<b>\$31,236,542</b>	<b>\$30,669,709</b>	<b>98.19%</b>	<b>\$21,377,407</b>

### NOTES

Processing of final change orders to closeout the project is still in progress. Final punchlist items include oily drips from the ceiling and surface cracks in the topper slab in the main evidence vault as well as the generator exhaust reroute. Deviation for visible equipment is proceeding to the 8/26/2021 BCC Zoning meeting. The funding sources for this project are as follows: Bond \$2M, Impact Fees \$6.7M, Ad Valorem \$1.2M, and IST \$21,336,540 for a total Project Budget of \$31,236,542.

# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects

Data Date: 7/15/2021

Report Date: 8/12/2021

### DESCRIPTION/TEAM

### SCOPE

### PHOTO

**Project Title:** CR 880 Canal Bank Stabilization

Project Number: 1448  
 BCC District: 06  
 Delivery Method: Bid Contract Award  
 Category: C02-CR 880 Canal Bank Stabilization  
 Status: Construction  
 Designer: Wantman Group  
 Contractor: Dickerson Florida, Inc.  
 Project Manager: Holly Knight

This project will repair, restore, and stabilize the embankment along a portion of County Road 880. The South Florida Water Management District's L-13 Canal parallels and is very close to County Road 880. The embankment area for County Road 880 to the canal is minimal. The undermining of the County Road 880 embankment continues due to storm events and increased South Florida Water Management District pumping and has progressively deteriorated. Repair of the embankment is necessary to prevent the eventual collapse of County Road 880 and to ensure the integrity of County Road 880 and provide a safe roadway for the public.  
 IST Funds: FY17 \$1,000,000 FY18 \$2,000,000 FY24 \$2,000,000.



### SCHEDULE SUMMARY

	Original	Actual
Construction Notice to Proceed	6/5/2017	6/5/2017
Phase III Construction Complete	11/2/2017	10/20/2017
Phase IV-Construction Complete	12/1/2018	3/27/2019
Phase IV-Construction Notice to Proceed	6/1/2018	7/9/2018
Phase V-Construction Notice to Proceed	6/1/2019	7/1/2019
Phase V-Construction Complete	12/1/2019	11/20/2019

### PARTICIPATION


#### Consultant

SBE 15%  
 Local 100%  
 WBE 0%  
 MBE 0%

#### Contractor

SBE 23.4%  
 Local 23.4%  
 WBE 0%  
 MBE 0%

### FUNDING

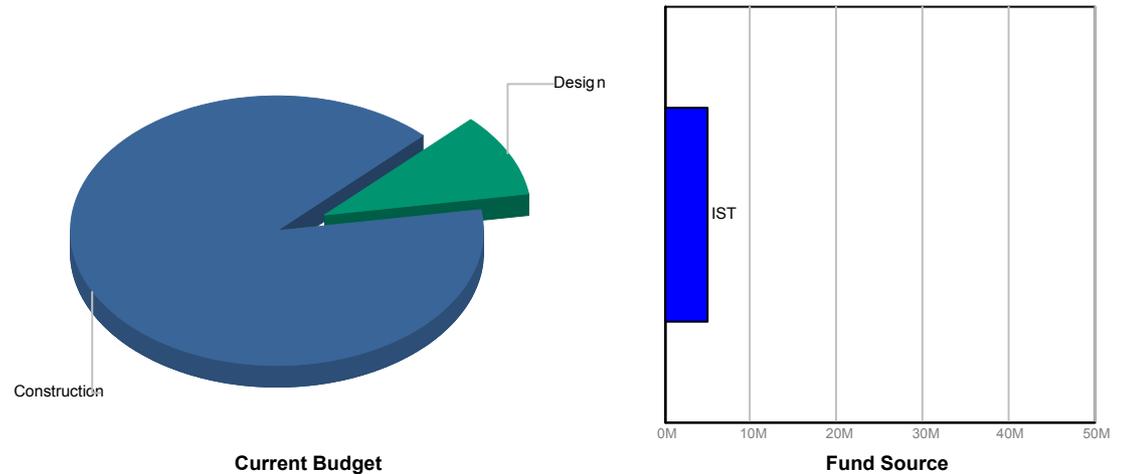

### FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$500,000	\$75,698	15.14%	\$75,698
Construction	\$4,500,000	\$2,537,336	56.39%	\$2,311,606
Contingency	\$0	\$0	0.00%	\$0
<b>TOTAL</b>	<b>\$5,000,000</b>	<b>\$2,613,034</b>	<b>52.26%</b>	<b>\$2,387,304</b>

### NOTES

Phases I and II (constructing adjacent locations) were completed in FY 2015 and FY 2016 using non-IST funding. Phase III construction is funded at \$1,000,000 in FY 2017. Construction for Phases IV & V are funded at \$2,000,000 in FY 2018. Construction is complete for Phases III, IV and V. Project will recommence upon arrival of FY 2024 funding.



# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects

Data Date: 7/15/2021

Report Date: 8/12/2021

DESCRIPTION/TEAM	SCOPE	PHOTO
<p><b>Project Title: Main Detention Center Electronics</b></p> <p>Project Number: 15218                      BCC District: 02                      Delivery Method: Construction Management                      Category: S06-Sheriff - FDO                      Status: Construction                      Designer: Leo A. Daly                      Contractor: Hedrick Brothers Construction                      Project Manager: Jeffrey Halverson</p>	<p>Phase II - Electronics for the South, East, and West Towers at the Main Detention Center, which have continually operated since the early 1980's. These systems include door controls, intercom, nurse's call system, CCTV, upgrade of EST3 software for fire alarm and new infrastructure for the future expansion of the CCTV system.</p> <p>Main Detention Center Electronics (B594) IST Funding                      FY 2017 IST \$5,600,000                      FY 2018 IST \$4,700,000                      The total Electronics budget is \$11,235,851 of which \$1,021,161 is funded through Ad Valorem.</p>	

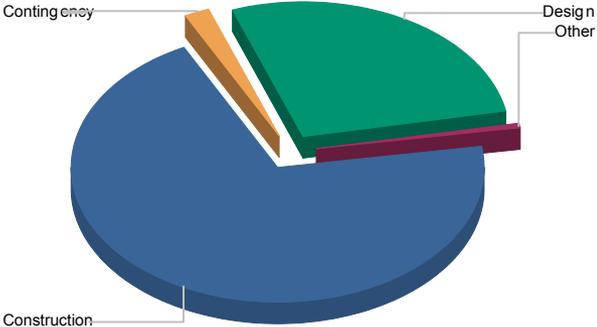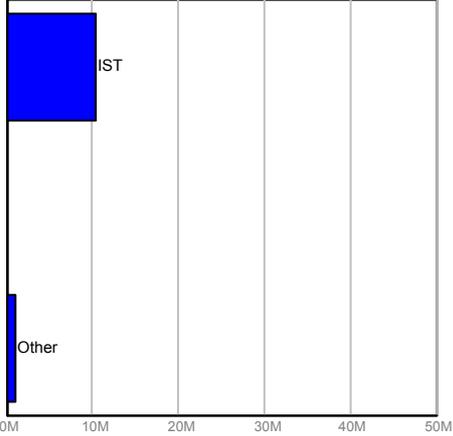SCHEDULE SUMMARY	PARTICIPATION	FUNDING																		
<table border="1"> <thead> <tr> <th></th> <th>Original</th> <th>Actual</th> </tr> </thead> <tbody> <tr> <td>Project Start</td> <td>7/9/2015</td> <td>6/9/2015</td> </tr> <tr> <td>Design Start</td> <td>6/21/2016</td> <td>6/21/2016</td> </tr> <tr> <td>Construction Start</td> <td>3/19/2018</td> <td>5/17/2018</td> </tr> <tr> <td>Substantial Completion</td> <td>3/15/2022</td> <td>8/10/2020</td> </tr> <tr> <td>Project Completion</td> <td>6/30/2022</td> <td></td> </tr> </tbody> </table>		Original	Actual	Project Start	7/9/2015	6/9/2015	Design Start	6/21/2016	6/21/2016	Construction Start	3/19/2018	5/17/2018	Substantial Completion	3/15/2022	8/10/2020	Project Completion	6/30/2022		<p><b>Consultant</b></p> <p>SBE 22.60%                      Local 67%                      WBE N/A                      MBE N/A</p> <p><b>Contractor</b></p> <p>SBE 76.79%                      Local 80%                      WBE N/A                      MBE N/A</p>	 <p style="text-align: center;"><b>Current Budget</b></p>  <p style="text-align: center;"><b>Fund Source</b></p>
	Original	Actual																		
Project Start	7/9/2015	6/9/2015																		
Design Start	6/21/2016	6/21/2016																		
Construction Start	3/19/2018	5/17/2018																		
Substantial Completion	3/15/2022	8/10/2020																		
Project Completion	6/30/2022																			

FINANCIAL SUMMARY				
	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$3,096,507	\$3,053,730	98.62%	\$2,855,440
Construction	\$7,868,421	\$7,157,168	90.96%	\$7,046,538
Furniture, Fixtures & Equipment	\$0	\$0	0.00%	\$0
Other	\$55,740	\$59,101	106.03%	\$59,101
Contingency	\$215,183	\$0	0.00%	\$0
<b>TOTAL</b>	<b>\$11,235,851</b>	<b>\$10,269,999</b>	<b>91.40%</b>	<b>\$9,961,079</b>

**NOTES**

No status change. We are processing a change order for approval for the credit we are to receive from the construction manager. This positive balance will be the subject of a future transfer.

# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects

Data Date: 7/15/2021

Report Date: 8/12/2021

### DESCRIPTION/TEAM

### SCOPE

### PHOTO

**Project Title:** Palm Beach Lakes Blvd over FEC R/R

This project will rehabilitate an existing bridge that was built over 50 years ago. The project will improve traffic safety (lane widths, pedestrian barrier, railings) and may involve other improvements such as shoulders, bike lanes, and sidewalks.



Project Number: 1532  
 BCC District: 07  
 Delivery Method: Design CCNA  
 Category: B04-Bridge Modifications  
 Status: Design  
 Designer: HNTB  
 Contractor: TBD  
 Project Manager: Kathleen Farrell


### SCHEDULE SUMMARY

	Original	Actual
Project Start	9/30/2017	9/30/2017
Consultant Procurement Finish	9/3/2019	12/1/2019
Study Start	4/7/2020	4/7/2020
Design Complete	6/1/2024	
Permit Application	2/1/2023	
Permit Issued	1/1/2024	
Construction Start	4/1/2025	
Construction Complete	4/1/2027	
Study Complete	11/11/2021	
Design Start	2/1/2022	

### PARTICIPATION

Consultant	
SBE	36.5%
Local	96%
WBE	TBD
MBE	TBD
Contractor	
SBE	TBD
Local	TBD
WBE	TBD
MBE	TBD

### FUNDING

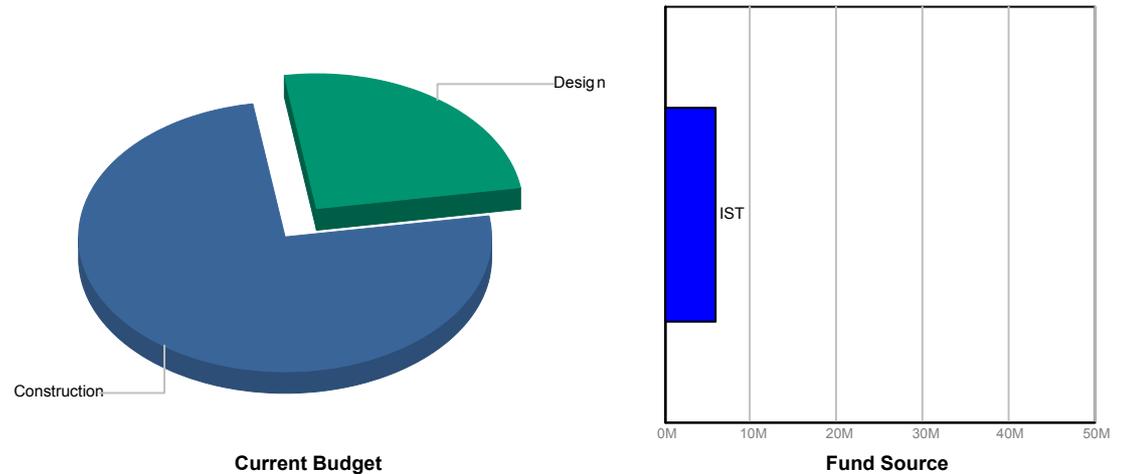

### FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$1,500,000	\$351,302	23.42%	\$270,513
Construction	\$4,500,000	\$603	0.01%	\$603
Other	\$0	\$15,327	0.00%	\$15,327
Contingency	\$0	\$0	0.00%	\$0
<b>TOTAL</b>	<b>\$6,000,000</b>	<b>\$367,232</b>	<b>6.12%</b>	<b>\$286,444</b>

### NOTES

The project is in the coordination stage with stakeholders including the City of West Palm Beach and the Community Redevelopment Agency to determine scope and design parameters for the rehabilitation of the bridge superstructure. This project is funded for design in FY 2017. Construction is currently included in the plan for FY 2021. The first phase of design (Study & Stakeholder Coordination) started on 4/7/2020.



# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects

Data Date: 7/15/2021

Report Date: 8/12/2021

DESCRIPTION/TEAM	SCOPE	PHOTO
<p><b>Project Title:</b> Sections of Jog Road</p> <p>Project Number: 1537</p> <p>BCC District: Multiple</p> <p>Delivery Method: Annual Striping Contract</p> <p>Category: S16-Striping</p> <p>Status: Construction</p> <p>Designer: N/A</p> <p>Contractor: Oglesby</p> <p>Project Manager: Larry Kelly</p>	<p>This project consists of restriping sections of Jog Road.</p> <p>FY 2017 \$350,000</p> <p>FY 2021 \$150,000</p> <p>FY 2022 \$100,000</p> <p>FY 2023 \$100,000</p> <p>FY 2024 \$200,000</p> <p>FY 2026 \$200,000</p>	

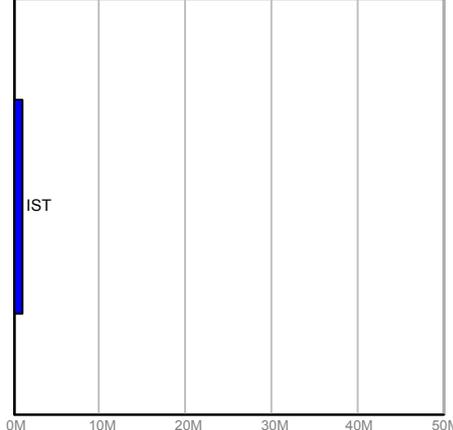SCHEDULE SUMMARY	PARTICIPATION	FUNDING																											
<table border="1"> <thead> <tr> <th></th> <th>Original</th> <th>Actual</th> </tr> </thead> <tbody> <tr> <td>10th Avenue N. to Summit Complete</td> <td>1/22/2018</td> <td>1/22/2018</td> </tr> <tr> <td>Summit to Gun Club Complete</td> <td>9/20/2017</td> <td>9/20/2017</td> </tr> <tr> <td>PGA to Hood Complete</td> <td>10/31/2017</td> <td>10/31/2017</td> </tr> <tr> <td>Wallis to Roebuck Complete</td> <td>3/7/2018</td> <td>3/7/2018</td> </tr> <tr> <td>Glades to NW 55th St.</td> <td>3/19/2019</td> <td>3/19/2019</td> </tr> <tr> <td>Gateway to S. of Hypoluxo Complete</td> <td>12/17/2018</td> <td>10/18/2018</td> </tr> <tr> <td>Hood to Donald Ross</td> <td>12/2/2020</td> <td>12/12/2020</td> </tr> <tr> <td>N. Oriole to Lake Ida</td> <td>4/3/2021</td> <td>3/9/2021</td> </tr> </tbody> </table>		Original	Actual	10th Avenue N. to Summit Complete	1/22/2018	1/22/2018	Summit to Gun Club Complete	9/20/2017	9/20/2017	PGA to Hood Complete	10/31/2017	10/31/2017	Wallis to Roebuck Complete	3/7/2018	3/7/2018	Glades to NW 55th St.	3/19/2019	3/19/2019	Gateway to S. of Hypoluxo Complete	12/17/2018	10/18/2018	Hood to Donald Ross	12/2/2020	12/12/2020	N. Oriole to Lake Ida	4/3/2021	3/9/2021	<p><b>Consultant</b></p> <p>SBE N/A</p> <p>Local N/A</p> <p>WBE N/A</p> <p>MBE N/A</p> <p><b>Contractor</b></p> <p>SBE 61%</p> <p>Local 61%</p> <p>WBE 0%</p> <p>MBE 0%</p>	<div style="text-align: center;">  <p>Construction</p> <p><b>Current Budget</b></p> </div> <div style="text-align: center;">  <p>IST</p> <p><b>Fund Source</b></p> </div>
	Original	Actual																											
10th Avenue N. to Summit Complete	1/22/2018	1/22/2018																											
Summit to Gun Club Complete	9/20/2017	9/20/2017																											
PGA to Hood Complete	10/31/2017	10/31/2017																											
Wallis to Roebuck Complete	3/7/2018	3/7/2018																											
Glades to NW 55th St.	3/19/2019	3/19/2019																											
Gateway to S. of Hypoluxo Complete	12/17/2018	10/18/2018																											
Hood to Donald Ross	12/2/2020	12/12/2020																											
N. Oriole to Lake Ida	4/3/2021	3/9/2021																											

FINANCIAL SUMMARY				
	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$0	\$0	0.00%	\$0
Construction	\$1,100,000	\$367,455	33.40%	\$367,455
Contingency	\$0	\$0	0.00%	\$0
<b>TOTAL</b>	<b>\$1,100,000</b>	<b>\$367,455</b>	<b>33.40%</b>	<b>\$367,455</b>

**NOTES**

Jog Road is a North-South major County thoroughfare. This project consists of re-striping sections of Jog Road. Restriping continues on an as needed basis.

# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects

Data Date: 7/15/2021

Report Date: 8/12/2021

### DESCRIPTION/TEAM

### SCOPE

### PHOTO

**Project Title: CR 880**

Project Number: 1539  
 BCC District: 06  
 Delivery Method: Annual Construction Contract  
 Category: R04-Resurfacing  
 Status: Construction  
 Designer: N/A  
 Contractor: Community  
 Project Manager: Mark Kroeger

Resurfacing approximately 2 miles (4 lane miles) of a portion of County Road 880 from Main Street to S.R. 80 each year.



### SCHEDULE SUMMARY

	Original	Actual
FY 2017 Construction Complete	12/22/2017	12/22/2017
FY 2018 Construction Complete	12/7/2018	11/30/2018
FY 2019 Construction Complete	12/31/2019	11/1/2019
FY 2020 Construction Complete	12/18/2020	12/3/2020
FY2021 Construction Complete	12/17/2021	

### PARTICIPATION


#### Consultant

SBE N/A  
 Local N/A  
 WBE N/A  
 MBE N/A

#### Contractor

SBE 8.7%  
 Local 95.8%  
 WBE 0%  
 MBE 0%

### FUNDING

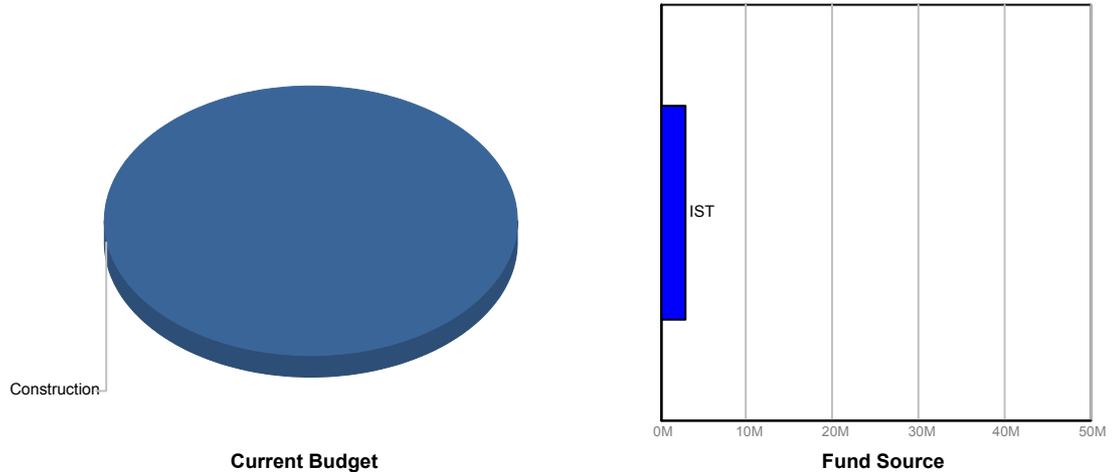

### FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$0	\$2,169	0.00%	\$2,169
Construction	\$3,000,000	\$1,179,094	39.30%	\$1,008,689
Contingency	\$0	\$0	0.00%	\$0
<b>TOTAL</b>	<b>\$3,000,000</b>	<b>\$1,181,263</b>	<b>39.38%</b>	<b>\$1,010,857</b>

### NOTES

County Road 880 is approximately 19 miles in length. This project entails resurfacing a portion (\$300,000) of County Road 880 each year. Construction complete for FY2017 thru 2020.

# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects

Data Date: 7/15/2021

Report Date: 8/12/2021

### DESCRIPTION/TEAM

### SCOPE

### PHOTO

**Project Title:** Brown's Farms Road

Resurfacing approximately 2 miles (4 lane miles) of a portion of Brown's Farm Road from CR 880 to South Terminus each year.

Project Number: 1540  
 BCC District: 06  
 Delivery Method: Annual Construction Contract  
 Category: R04-Resurfacing  
 Status: Construction  
 Designer: N/A  
 Contractor: Community  
 Project Manager: Mark Kroeger



### SCHEDULE SUMMARY

### PARTICIPATION

### FUNDING


	Original	Actual
FY2021 Construction Complete	12/17/2021	
FY 2020 Construction Complete	12/18/2020	12/2/2020
FY 2019 Construction Complete	12/31/2019	11/1/2019
FY 2017 Construction Complete	12/22/2017	12/22/2017
FY 2018 Construction Complete	12/1/2018	11/30/2018

**Consultant**

SBE N/A  
 Local N/A  
 WBE N/A  
 MBE N/A

**Contractor**

SBE 7.4%  
 Local 94.4%  
 WBE 0%  
 MBE 0%

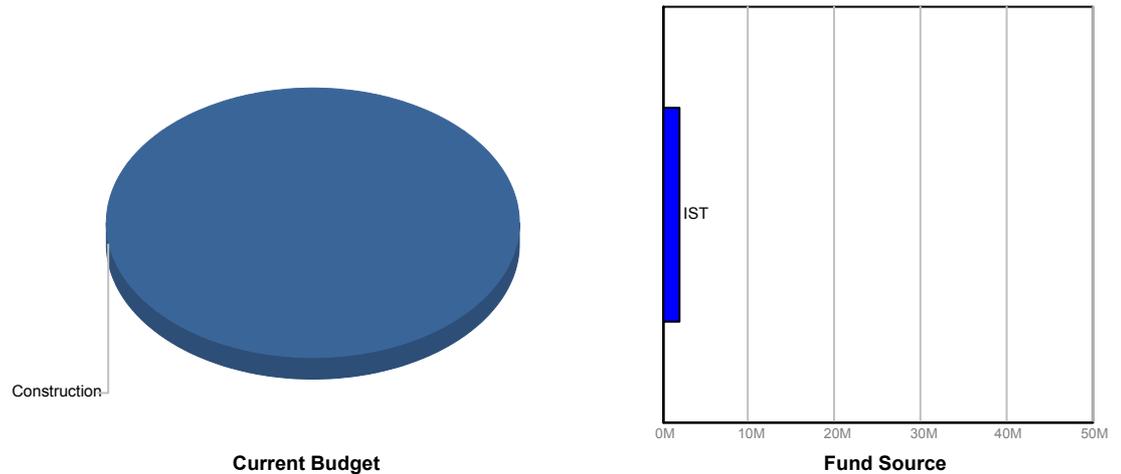

### FINANCIAL SUMMARY

### NOTES

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$0	\$1,515	0.00%	\$1,515
Construction	\$2,000,000	\$995,445	49.77%	\$810,445
Contingency	\$0	\$0	0.00%	\$0
<b>TOTAL</b>	<b>\$2,000,000</b>	<b>\$996,959</b>	<b>49.85%</b>	<b>\$811,959</b>

Brown's Farm Road is approximately 14 miles in length. This project entails resurfacing a portion (\$200,000) of Brown's Farm Road each year. Construction complete for FY2017 thru 2020.

# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects

Data Date: 7/15/2021

Report Date: 8/12/2021

### DESCRIPTION/TEAM

### SCOPE

### PHOTO

**Project Title:** Prosperity Farms Rd. over SFWMD C-17 Canal (934116)  
**Project Number:** 1555  
**BCC District:** 01  
**Delivery Method:** Design CCNA  
**Category:** B08-Bridge Replacements  
**Status:** Design  
**Designer:** Scalar  
**Contractor:** TBD - (bid)  
**Project Manager:** David Young

This project will replace an existing bridge that was built over 60 years ago. The new bridge will improve traffic safety (lane widths, bike lanes, parapets), improve roadway drainage, and enhance pedestrian sidewalk safety. Note the current bridge is weight restricted.



### SCHEDULE SUMMARY

	Original	Actual
Design Contract Notice to Proceed	11/19/2019	11/19/2019
Design Completion	2/1/2022	
Construction Bid Date	6/1/2022	
Construction Start	10/1/2022	
Construction Complete	10/1/2024	

### PARTICIPATION



#### Consultant

SBE 98%  
 Local 100%  
 WBE 0%  
 MBE 0%

#### Contractor

SBE TBD  
 Local TBD  
 WBE TBD  
 MBE TBD

### FUNDING

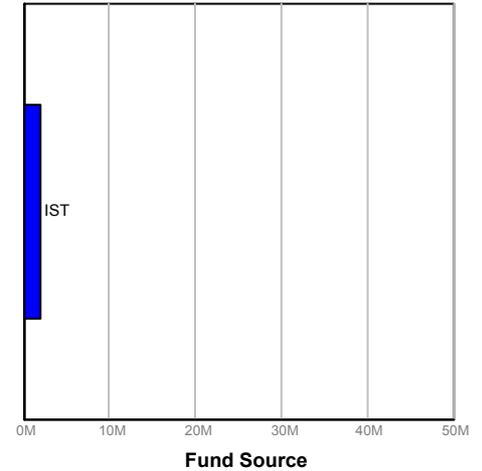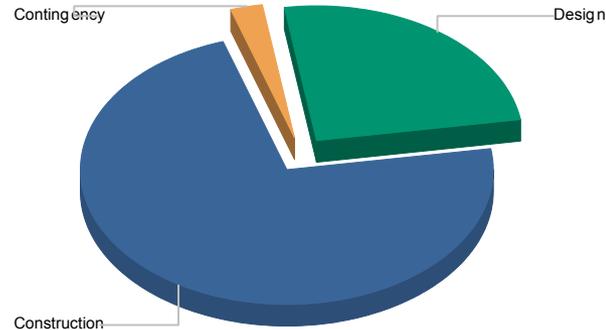

### FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$500,000	\$481,996	96.40%	\$189,622
Construction	\$1,450,000	\$5,003	0.35%	\$5,003
Contingency	\$50,000	\$8,365	16.73%	\$8,365
<b>TOTAL</b>	<b>\$2,000,000</b>	<b>\$495,363</b>	<b>24.77%</b>	<b>\$202,990</b>

### NOTES

This project is under design. Construction is funded in the plan for FY 2021.

# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects

Data Date: 7/15/2021

Report Date: 8/12/2021

### DESCRIPTION/TEAM

### SCOPE

### PHOTO

**Project Title:** Belvedere Rd over E-3 canal (934205 & 934206)  
**Project Number:** 1556  
**BCC District:** 02  
**Delivery Method:** Design CCNA  
**Category:** B08-Bridge Replacements  
**Status:** Design  
**Designer:** Stantec  
**Contractor:** TBD (bid)  
**Project Manager:** Kathleen Farrell

This project will replace the existing bridges that were built over 40 years ago. The new bridge(s) will improve traffic safety (lane widths, bike lanes, parapets), update the guardrail system, improve roadway drainage, restore the slope protection, and enhance pedestrian sidewalk safety.



### SCHEDULE SUMMARY

	Original	Actual
Design Contract Notice to Proceed	10/22/2019	10/22/2019
Design Completion	12/1/2021	
Construction Bid Date	3/1/2022	
Construction Start	8/1/2022	
Construction Complete	3/1/2024	

### PARTICIPATION


#### Consultant

SBE 30%  
 Local 100%  
 WBE 0%  
 MBE 0%


#### Contractor

SBE TBD  
 Local TBD  
 WBE TBD  
 MBE TBD

### FUNDING

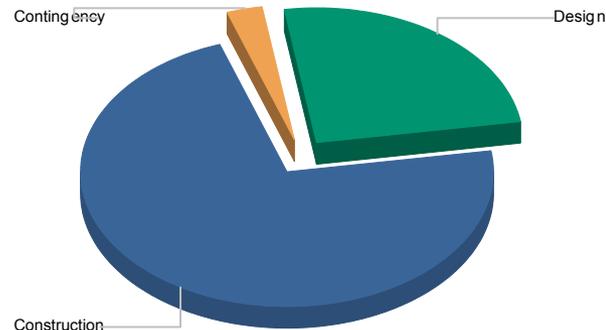

Current Budget

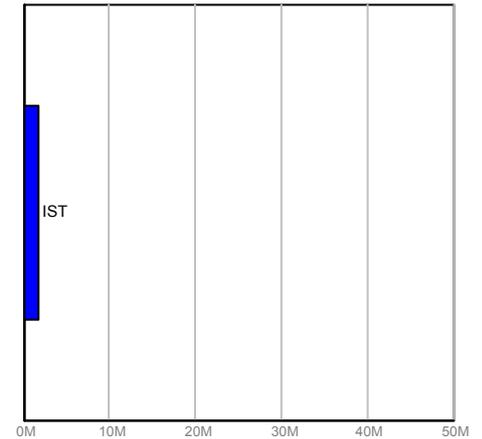

Fund Source

### FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$450,000	\$359,786	79.95%	\$179,298
Construction	\$1,300,000	\$4,192	0.32%	\$4,192
Contingency	\$50,000	\$0	0.00%	\$0
<b>TOTAL</b>	<b>\$1,800,000</b>	<b>\$363,978</b>	<b>20.22%</b>	<b>\$183,490</b>

### NOTES

This project is under design. Construction is funded in the plan for FY 2021.

# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects

Data Date: 7/15/2021

Report Date: 8/12/2021

### DESCRIPTION/TEAM

### SCOPE

### PHOTO

**Project Title:** Various other locations Countywide

Project Number: 1558  
 BCC District: Multiple  
 Delivery Method: Annual Construction Contract  
 Category: D02-Drainage (Pipe Replacements)  
 Status: Construction  
 Designer: N/A  
 Contractor: Hinterland  
 Project Manager: Mark Kroeger

This project will repair and/or replace existing pipe culverts and drainage structures along various roads and canals Countywide. These repairs are needed in order to properly drain and maintain the various roads and canals in a safe operating condition.



### SCHEDULE SUMMARY

### PARTICIPATION

### FUNDING


	Original	Actual
Jupiter Farms (133rd Rd. & 156th St.)	8/1/2018	3/12/2018
1069 Edgehill Road	8/15/2018	6/12/2018
Limestone Creek & Palm Garden St.	8/1/2018	7/17/2018
3261 Atlantic Road	8/15/2018	7/1/2018
Van Buren Road @ E-3 Canal	8/1/2018	6/15/2018
Jupiter Farms (4 locates)	10/15/2018	8/21/2018
6361 Wood Lake Rd./19650 Red Maple F	10/1/2018	10/1/2018
19598 Trails End Terrace	9/15/2018	8/20/2018
19582 Trails End Terrace	9/1/2018	9/1/2018
6558 Wood Lake Road	9/15/2018	9/14/2018
6126 Wood Lake Road	10/15/2018	12/12/2018
6528 Wood Lake Road	11/1/2018	12/12/2018
Whispering Trail Community	6/1/2019	7/9/2019

**Consultant**

SBE N/A  
 Local N/A  
 WBE N/A  
 MBE N/A

**Contractor**

SBE 100%  
 Local 100%  
 WBE 0%  
 MBE 0%

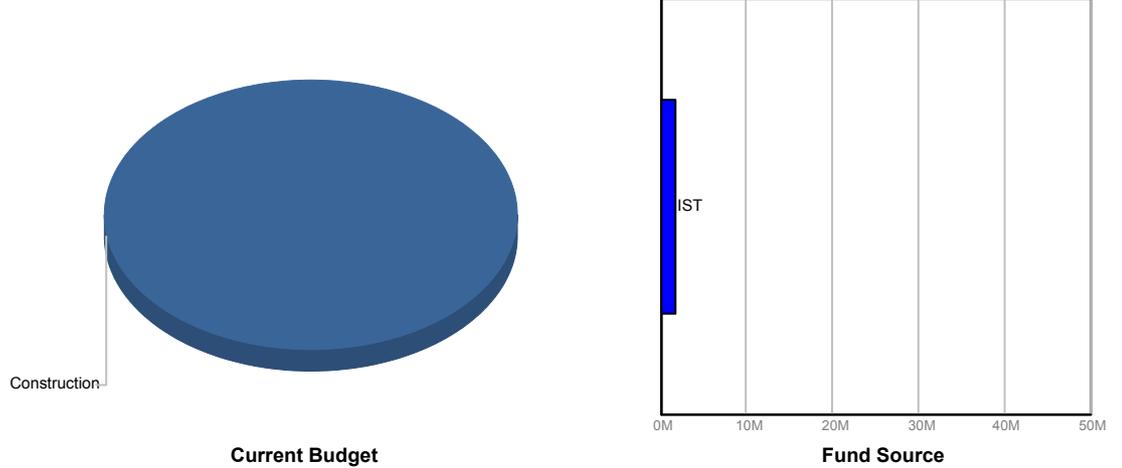

### FINANCIAL SUMMARY

### NOTES

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Construction	\$1,700,000	\$619,125	36.42%	\$619,125
Contingency	\$0	\$0	0.00%	\$0
<b>TOTAL</b>	<b>\$1,700,000</b>	<b>\$619,125</b>	<b>36.42%</b>	<b>\$619,125</b>

This project is funded in:  
 FY 2018 \$500,000, FY 2021 \$500,000, FY 2022 \$200,000  
 FY 2023 \$200,000, FY 2024 \$200,000, FY 2025 \$100,000

The total project is estimated at \$1,700,000.

# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects

Data Date: 7/15/2021

Report Date: 8/12/2021

### DESCRIPTION/TEAM

### SCOPE

### PHOTO

**Project Title:** Video Detection (80 +/- intersection)

This project will replace the traffic detection at numerous signalized intersections from the existing inductive loop system to video detection. The video detection system is more reliable and easier to maintain.



Project Number: 1580  
 BCC District: Multiple  
 Delivery Method: Annual Traffic Signals Contract  
 Category: S08-Signals and Signal Systems  
 Status: Construction  
 Designer: N/A  
 Contractor: Gerelco  
 Project Manager: Fattoush Jafar

### SCHEDULE SUMMARY

	Original	Actual
Woolbright & Hagen Ranch	11/1/2018	4/4/2019
Belvedere & Country Club Road	12/1/2018	4/4/2019
Palm Beach Lakes & Wellesley	1/1/2019	4/4/2019
Military Tr. & Garden Lake	8/1/2018	11/21/2018
Gateway & Renaissance Commons	9/1/2018	4/3/2019
Australian & Turnage	10/1/2018	1/7/2019

### PARTICIPATION


#### Consultant

SBE N/A  
 Local N/A  
 WBE N/A  
 MBE N/A

#### Contractor

SBE 0%  
 Local 23%  
 WBE 0%  
 MBE 0%

### FUNDING

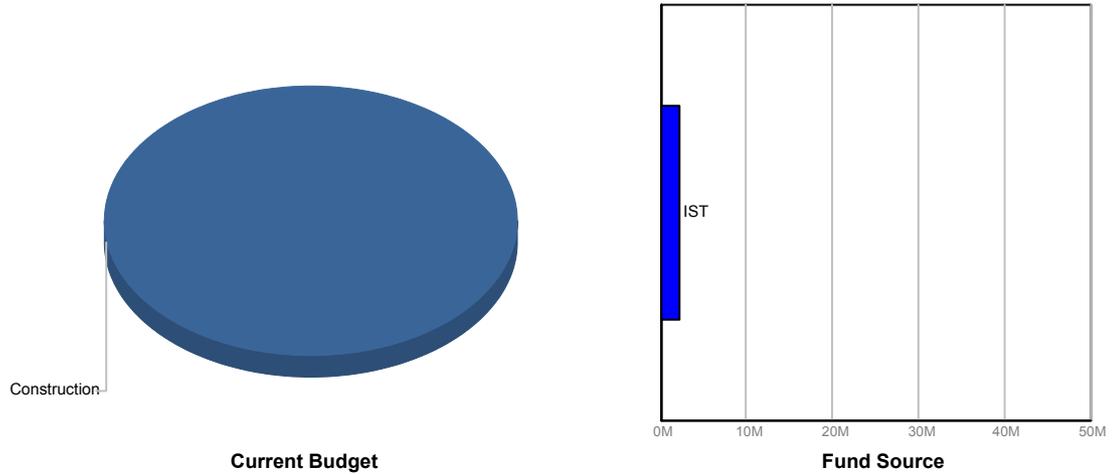

### FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Construction	\$2,200,000	\$199,000	9.05%	\$199,000
Contingency	\$0	\$0	0.00%	\$0
<b>TOTAL</b>	<b>\$2,200,000</b>	<b>\$199,000</b>	<b>9.05%</b>	<b>\$199,000</b>

### NOTES

Work has been completed at six intersections. This project is funded in:  
 FY 2018 \$200,000  
 FY 2023 \$300,000  
 FY 2024 \$800,000  
 FY 2026 \$900,000  
 The total project is estimated at \$2,200,000.

# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects

Data Date: 7/15/2021

Report Date: 8/12/2021

### DESCRIPTION/TEAM

### SCOPE

### PHOTO

**Project Title:** FY 2018 Street Lighting LED Replacements - Countywide  
**Project Number:** 1581  
**BCC District:** CW  
**Delivery Method:** Florida Power and Light  
**Category:** S14-Street Lighting  
**Status:** Construction  
**Designer:** Florida Power and Light  
**Contractor:** Florida Power and Light  
**Project Manager:** May Cheng

These projects will replace the high pressure sodium street lights with LED lights. Many of the street lights along County roads are owned and maintained by Florida Power and Light (FPL) with the County paying all the operation and maintenance costs (including power). FPL will be responsible for the final design and installation to convert the street lighting to the newer LED technology, and the County will reimburse FPL all applicable conversion costs. The result will provide a cost savings, better quality illumination, and a more desirable environmental light source.



### SCHEDULE SUMMARY

### PARTICIPATION

### FUNDING


	Original	Actual
Gun Club Road/Bosque to Congress	8/16/2019	8/16/2019
Congress/Okeechobee to Belvedere	8/16/2019	8/16/2019
10th Avenue North/Haverhill to Kirk	12/11/2019	12/11/2019
Community/Haverhill to Military	8/16/2019	8/16/2019
Haverhill Road/WPB City to Haverhill City		
Glades Road/State Road 7 to Boca Rio		
Boynton Beach Boulevard/Turnpike to Kn		
Jog Road/Belvedere to State Road 80		
Forest Hill/Turnpike to Pinehurst & Jog to		
Haverhill/State Road 80 to Lake Worth		
Congress/Lantana to Hypoluxo & Gun Cl		
Gateway/Military to Windward		
Belvedere Road/RPB City to Haverhill Cit		

#### Consultant

SBE N/A  
 Local N/A  
 WBE N/A  
 MBE N/A

#### Contractor

SBE N/A  
 Local N/A  
 WBE N/A  
 MBE N/A

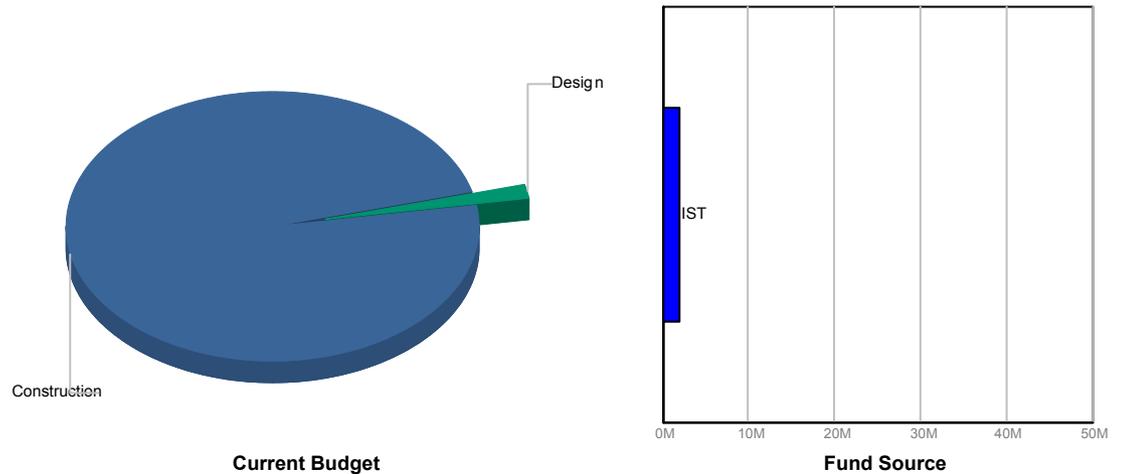

### FINANCIAL SUMMARY

### NOTES

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$30,000	\$25,774	85.91%	\$25,774
Construction	\$1,920,000	\$1,063,409	55.39%	\$475,766
Contingency	\$0	\$0	0.00%	\$0
<b>TOTAL</b>	<b>\$1,950,000</b>	<b>\$1,089,183</b>	<b>55.86%</b>	<b>\$501,541</b>

There are 16 street lighting projects (road segments) funded (\$1,950,000) for conversion in FY 2018. All 16 projects have been forwarded to FPL requesting final design and installation. As of 12/1/20, five projects have been completed, and the street lighting along a portion of the Hypoluxo Road project has also been converted.

# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects

Data Date: 7/15/2021

Report Date: 8/12/2021

### DESCRIPTION/TEAM

### SCOPE

### PHOTO

**Project Title:** CR 880 (Old SR 80) Over C-51 Canal (930940)  
**Project Number:** 1612  
**BCC District:** 06  
**Delivery Method:** Design CCNA  
**Category:** B08-Bridge Replacements  
**Status:** Design  
**Designer:** Alan Gerwig & Assoc.  
**Contractor:** TBD (Bid)  
**Project Manager:** Kathleen Farrell

This project will replace an existing bridge that was built over 80 years ago. The new bridge will improve traffic safety (lane widths and vehicle barrier walls). The current bridge is weight restricted.



### SCHEDULE SUMMARY

	Original	Actual
Design Contract Notice to Proceed	11/9/2018	11/9/2018
Design Completion	10/28/2021	
Construction Bid Date	2/1/2022	
Construction Start	7/1/2022	
Construction Complete	12/1/2023	

### PARTICIPATION


#### Consultant

SBE 94.3%  
 Local 100%  
 WBE 0%  
 MBE 0%

#### Contractor

SBE TBD  
 Local TBD  
 WBE TBD  
 MBE TBD

### FUNDING

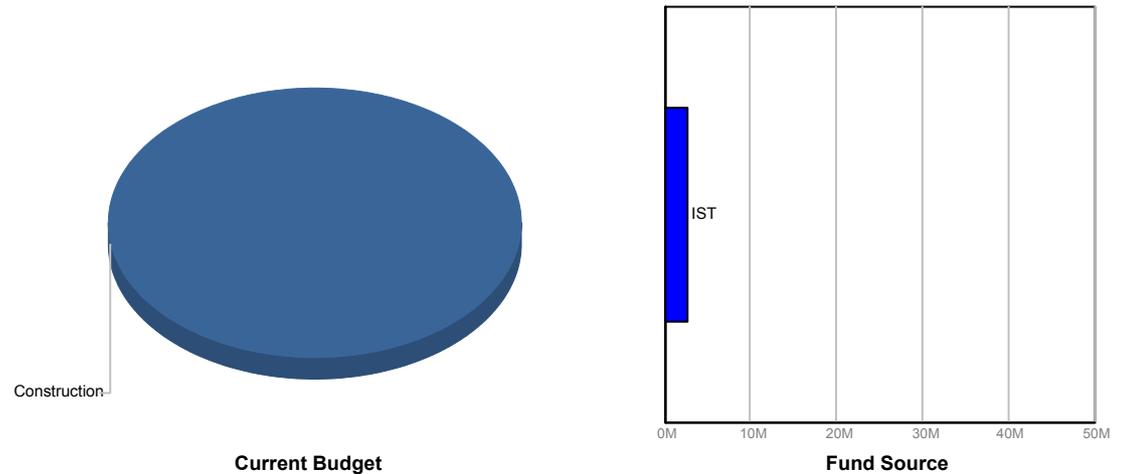

### FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Construction	\$2,700,000	\$0	0.00%	\$0
<b>TOTAL</b>	<b>\$2,700,000</b>	<b>\$0</b>	<b>0.00%</b>	<b>\$0</b>

### NOTES

This project is funded with 5-Year Road Program (RP) funding and IST funding. The project is under design (using 5-Year RP funds). The construction of the project is currently estimated at \$3.5m. The IST partially funds the construction of the project at \$2.7 m in FY 2019. The project is currently scheduled to begin construction in FY22.

# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects

Data Date: 7/15/2021

Report Date: 8/12/2021

### DESCRIPTION/TEAM

### SCOPE

### PHOTO

**Project Title:** Courthouse Electronics System R&R/Command Center  
**Project Number:** 16208  
**BCC District:** 07  
**Delivery Method:** Construction Management  
**Category:** J02-Judicial  
**Status:** Construction  
**Designer:** TLC Engineering  
**Contractor:** Hedrick Brothers Construction Co., Inc.  
**Project Manager:** Rich Avery

Security Systems replacement at the Main County Courthouse including the Security Management System, Access Control System, CCTV system, Duress System, Intercom, Elevator Override, and Fire Alarm. The Project will also include addressing the emergency egress procedures for the facility, as well as build-out for the expansion of the 4th floor Command Center.

Total IST, and Ad Valorem funding for this project is \$16,449,545; Total IST funds are \$12,999,700, which are comprised of FY17 IST funds of \$1,300,000 and FY18 IST funds of \$8,699,700 and FY 19 IST funds of \$3,000,000. Ad Valorem funds are \$3,449,845



### SCHEDULE SUMMARY

	Original	Actual
Project Start	2/19/2016	2/19/2016
Design Start	2/15/2017	2/15/2017
Construction - Start	11/26/2018	1/7/2019
Substantial Completion	2/1/2021	
Project Completion	4/1/2021	

### PARTICIPATION


**Consultant**

- SBE 13.4%
- Local 100%
- WBE N/A
- MBE N/A

**Contractor**

- SBE 25%
- Local 100%
- WBE N/A
- MBE N/A

### FUNDING

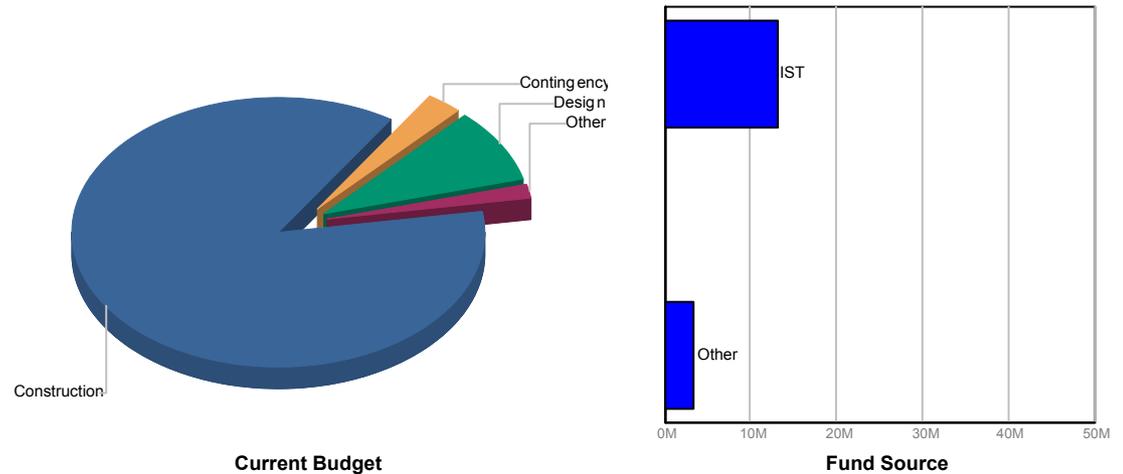

### FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$1,456,336	\$1,367,426	93.89%	\$436,761
Construction	\$14,307,700	\$14,284,827	99.84%	\$12,779,452
Furniture, Fixtures & Equipment	\$0	\$0	0.00%	\$0
Other	\$285,137	\$116,320	40.79%	\$116,320
Contingency	\$465,300	\$0	0.00%	\$0
<b>TOTAL</b>	<b>\$16,514,473</b>	<b>\$15,768,574</b>	<b>95.48%</b>	<b>\$13,332,534</b>

### NOTES

No status change. Project is substantially complete. Currently processing project closeout.

# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects

Data Date: 7/15/2021

Report Date: 8/12/2021

### DESCRIPTION/TEAM

### SCOPE

### PHOTO

**Project Title:** 6th Ave. So. over Lake Osborne (LWDD E-4 Canal)(S Br/ East bound) (934307)

Project Number: 1634

BCC District: 03

Delivery Method: Design CCNA

Category: B08-Bridge Replacements

Status: Construction

Designer: Stantec

Contractor: Ranger

Project Manager: David Young

This project will replace an existing bridge that was built over 50 years ago. The new bridge will improve traffic safety (lane widths, bike lanes and barrier walls), improve roadway drainage, and enhance pedestrian sidewalk safety. The new bridge will also provide greater vertical clearance.



### SCHEDULE SUMMARY

	Original	Actual
Design Contract Notice to Proceed	7/17/2018	7/17/2018
Design Completion	12/1/2020	2/14/2021
Construction Bid Date	3/1/2021	5/4/2021
Construction Start	7/1/2021	
Construction Complete	12/1/2022	

### PARTICIPATION

#### Consultant

SBE 25%

Local 100%

WBE 0%

MBE 0%

#### Contractor


SBE TBD

Local TBD

WBE 0%

MBE 0%

### FUNDING

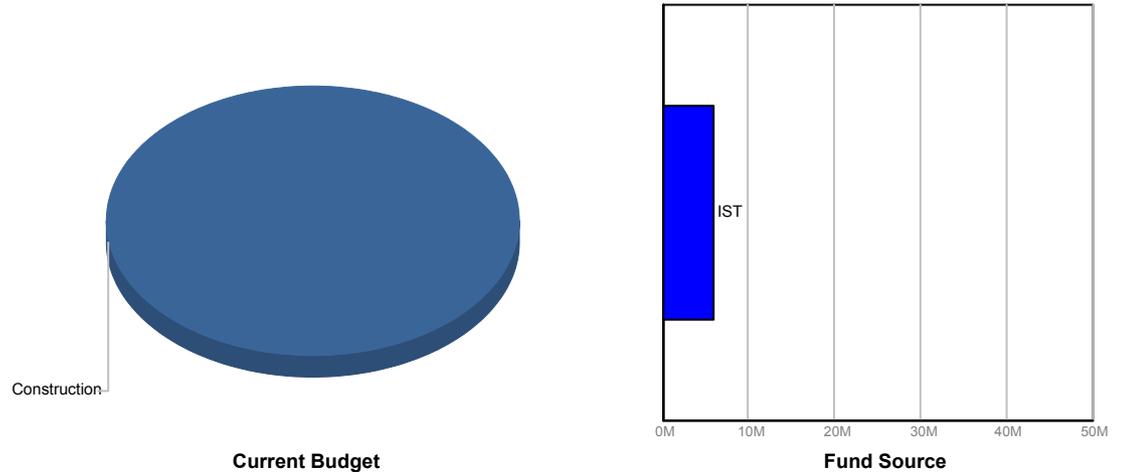

### FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Construction	\$6,000,000	\$0	0.00%	\$0
<b>TOTAL</b>	<b>\$6,000,000</b>	<b>\$0</b>	<b>0.00%</b>	<b>\$0</b>

### NOTES

This project is funded with 5-Year Road Program (RP) funding and IST funding. Design (using RP funds) is complete. The project was bid on 5/4/21 - with apparent low bid of \$ 11.1m The IST partially funds the construction of the project at \$6m in FY 2020. The project is currently scheduled to begin construction in FY21.



# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects

Data Date: 7/15/2021

Report Date: 8/12/2021

DESCRIPTION/TEAM	SCOPE	PHOTO
<p><b>Project Title:</b> Australian Ave. from Banyan St. to 45th St.</p> <p>Project Number: 1658</p> <p>BCC District: BIAF</p> <p>Delivery Method: Design CCNA</p> <p>Category: D04-Drainage Improvements</p> <p>Status: Design</p> <p>Designer: TBD</p> <p>Contractor: TBD (Bid)</p> <p>Project Manager: Kathleen Farrell</p>	<p>The project will include drainage improvements (piped drainage system) and a new paving surface for a 4-lane divided section with new pathways on both sides along Australian Avenue from Banyan Blvd. to 45th Street.</p>	

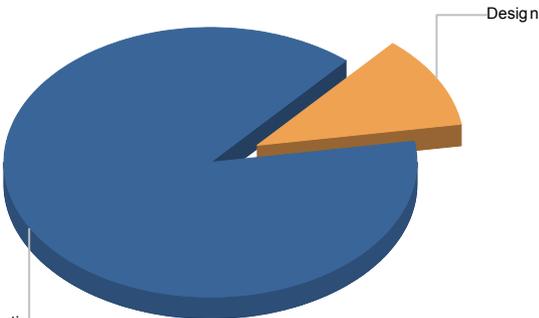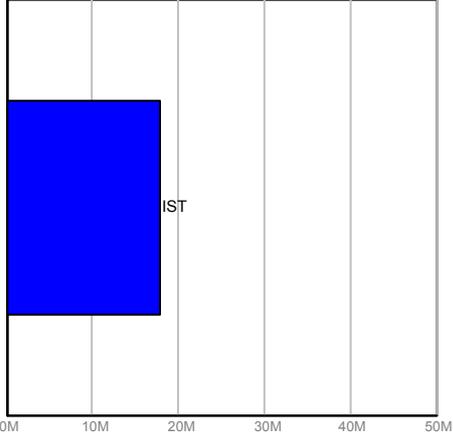SCHEDULE SUMMARY	PARTICIPATION	FUNDING																		
<table border="1"> <thead> <tr> <th></th> <th>Original</th> <th>Actual</th> </tr> </thead> <tbody> <tr> <td>Design Start</td> <td>3/1/2022</td> <td></td> </tr> <tr> <td>Design Complete</td> <td>9/1/2025</td> <td></td> </tr> <tr> <td>Construction Bid Date</td> <td>12/1/2025</td> <td></td> </tr> <tr> <td>Construction Start</td> <td>4/1/2026</td> <td></td> </tr> <tr> <td>Construction Complete</td> <td>4/1/2028</td> <td></td> </tr> </tbody> </table>		Original	Actual	Design Start	3/1/2022		Design Complete	9/1/2025		Construction Bid Date	12/1/2025		Construction Start	4/1/2026		Construction Complete	4/1/2028		<p><b>Consultant</b></p> <p>SBE TBD</p> <p>Local TBD</p> <p>WBE TBD</p> <p>MBE TBD</p> <p><b>Contractor</b></p> <p>SBE TBD</p> <p>Local TBD</p> <p>WBE TBD</p> <p>MBE TBD</p>	<div style="display: flex; justify-content: space-around;"> <div style="text-align: center;">  <p>Current Budget</p> </div> <div style="text-align: center;">  <p>Fund Source</p> </div> </div>
	Original	Actual																		
Design Start	3/1/2022																			
Design Complete	9/1/2025																			
Construction Bid Date	12/1/2025																			
Construction Start	4/1/2026																			
Construction Complete	4/1/2028																			

FINANCIAL SUMMARY				
	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$2,000,000	\$3,203	0.16%	\$3,203
Construction	\$15,800,000	\$2,227	0.01%	\$2,227
<b>TOTAL</b>	<b>\$17,800,000</b>	<b>\$5,429</b>	<b>0.03%</b>	<b>\$5,429</b>

**NOTES**

The project is in the Consultant Selection process. Scope and fee negotiation will follow culminating in a design contract. The project is funded for design (\$2m) in FY21 and for construction (\$15.8m) in FY24 and FY25.

# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects

Data Date: 7/15/2021

Report Date: 8/12/2021

### DESCRIPTION/TEAM

### SCOPE

### PHOTO

**Project Title:** Belvedere Rd canal piping & sidewalk addition (62nd Dr. N. to Haverhill park)

Project Number: 1661  
 BCC District: 02  
 Delivery Method: Design CCNA  
 Category: P04-Pathways  
 Status: Design  
 Designer: Keshavarz  
 Contractor: TBD (Bid)  
 Project Manager: Kathleen Farrell

This project will add a new sidewalk (SW) on the south side of Belvedere Road from 62nd Dr. N. to the Haverhill park (just east of the E-3 Canal) - connecting to the existing south SW at the park's frontage. The SW may require the piping of Lake Worth Drainage District's (LWDD) L-3 Canal.



### SCHEDULE SUMMARY

	Original	Actual
Study Complete	2/1/2022	
Design Complete		
Construction Bid Date		
Construction Start		
Construction Complete		

### PARTICIPATION


#### Consultant

SBE 50%  
 Local 100%  
 WBE 0%  
 MBE 0%

#### Contractor

SBE TBD  
 Local TBD  
 WBE TBD  
 MBE TBD

### FUNDING

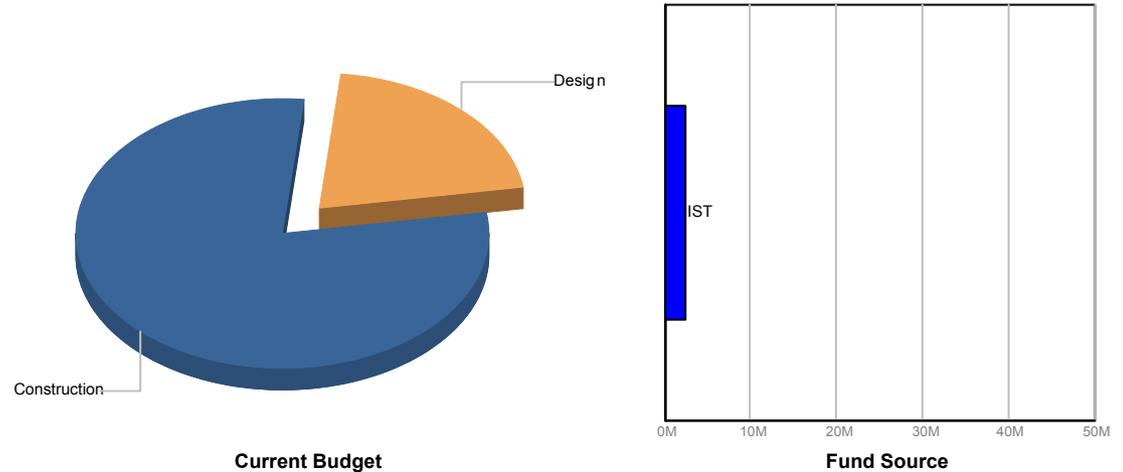

### FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$500,000	\$358	0.07%	\$358
Construction	\$1,900,000	\$0	0.00%	\$0
<b>TOTAL</b>	<b>\$2,400,000</b>	<b>\$358</b>	<b>0.01%</b>	<b>\$358</b>

### NOTES

The project is in the study phase to determine a more precise work scope. The project is funded for design (\$500k) in FY21 and for construction (\$1.9m) in FY23.



# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects

Data Date: 7/15/2021

Report Date: 8/12/2021

DESCRIPTION/TEAM	SCOPE	PHOTO
<p><b>Project Title:</b> Seacrest Blvd from Gulfstream Blvd. to Hypoluxo Rd.</p> <p>Project Number: 1662</p> <p>BCC District: 07</p> <p>Delivery Method: Annual Construction Contract</p> <p>Category: R04-Resurfacing</p> <p>Status: Construction</p> <p>Designer: N/A</p> <p>Contractor: Ranger</p> <p>Project Manager: Thomas Coppini</p>	<p>Resurfacing 5.8 miles (25.3 lane miles) of Seacrest Boulevard from Gulfstream Boulevard to Hypoluxo Road.</p> <p>FY 2021 IST \$2,400,000</p>	

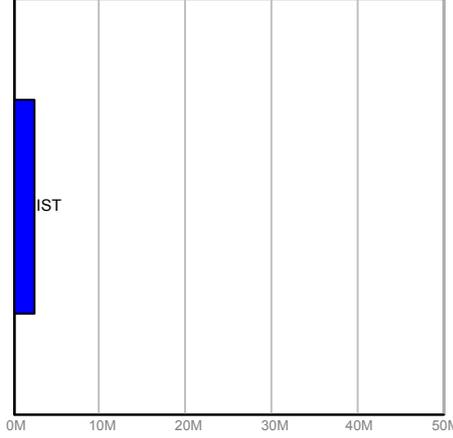SCHEDULE SUMMARY	PARTICIPATION	FUNDING																		
<table border="1"> <thead> <tr> <th></th> <th>Original</th> <th>Actual</th> </tr> </thead> <tbody> <tr> <td>Drainage Repairs</td> <td>11/1/2021</td> <td></td> </tr> <tr> <td>Milling and Pavement Complete</td> <td>2/1/2022</td> <td></td> </tr> <tr> <td>ADA (Curb/Cut Ramps) Complete</td> <td>4/1/2022</td> <td></td> </tr> <tr> <td>Traffic Striping Complete</td> <td>5/1/2022</td> <td></td> </tr> <tr> <td>Traffic Loops Complete</td> <td>7/1/2022</td> <td></td> </tr> </tbody> </table>		Original	Actual	Drainage Repairs	11/1/2021		Milling and Pavement Complete	2/1/2022		ADA (Curb/Cut Ramps) Complete	4/1/2022		Traffic Striping Complete	5/1/2022		Traffic Loops Complete	7/1/2022		<p><b>Consultant</b></p> <p>SBE N/A</p> <p>Local N/A</p> <p>WBE N/A</p> <p>MBE N/A</p> <p><b>Contractor</b></p> <p>SBE 15%</p> <p>Local 100%</p> <p>WBE 0%</p> <p>MBE 0%</p>	<div style="text-align: center;">  <p>Construction</p> <p><b>Current Budget</b></p> </div> <div style="text-align: center;">  <p>IST</p> <p><b>Fund Source</b></p> </div>
	Original	Actual																		
Drainage Repairs	11/1/2021																			
Milling and Pavement Complete	2/1/2022																			
ADA (Curb/Cut Ramps) Complete	4/1/2022																			
Traffic Striping Complete	5/1/2022																			
Traffic Loops Complete	7/1/2022																			

FINANCIAL SUMMARY				
	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Construction	\$2,400,000	\$441,342	18.39%	\$2,117
<b>TOTAL</b>	<b>\$2,400,000</b>	<b>\$441,342</b>	<b>18.39%</b>	<b>\$2,117</b>

**NOTES**

Outstanding work includes drainage repairs, milling and paving, updating ADA ramps, restriping the road, and replacing traffic loops.

# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects

Data Date: 7/15/2021

Report Date: 8/12/2021

### DESCRIPTION/TEAM

### SCOPE

### PHOTO

**Project Title:** Hypoluxo Rd. from Military Trail to U.S. 1

Resurfacing 3.7 miles (21.2 lane miles) of Hypoluxo Road from Military Trail to US 1.

Project Number: 1663  
 BCC District: Multiple  
 Delivery Method: Annual Construction Contract  
 Category: R04-Resurfacing  
 Status: Construction  
 Designer: N/A  
 Contractor: Ranger  
 Project Manager: Thomas Coppini

FY 2021 IST \$1,400,000



### SCHEDULE SUMMARY

### PARTICIPATION

### FUNDING


	Original	Actual
Milling and Pavement Complete	2/1/2021	5/11/2021
ADA (Curb/Cut Ramps) Complete	4/1/2021	
Traffic Striping Complete	5/1/2021	
Traffic Loops Complete	7/1/2021	

#### Consultant

SBE N/A  
 Local N/A  
 WBE N/A  
 MBE N/A

#### Contractor

SBE 5%  
 Local 100%  
 WBE 0%  
 MBE 0%



### FINANCIAL SUMMARY

### NOTES

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Construction	\$1,400,000	\$1,375,354	98.24%	\$1,375,354
<b>TOTAL</b>	<b>\$1,400,000</b>	<b>\$1,375,354</b>	<b>98.24%</b>	<b>\$1,375,354</b>

Outstanding work includes, updating ADA ramps, restriping the road, and replacing traffic loops.


# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects

Data Date: 7/15/2021

Report Date: 8/12/2021

DESCRIPTION/TEAM	SCOPE	PHOTO
<p><b>Project Title:</b> Lake Lytal Aquatic Center Replace Public Aquatic Facility</p> <p>Project Number: 17218</p> <p>BCC District: 02</p> <p>Delivery Method: Construction Management at Risk</p> <p>Category: A02-Aquatic Facility Repair and Replacement</p> <p>Status: Design</p> <p>Designer: Harvard Jolly, Inc.</p> <p>Contractor: Kauffman Lynn</p> <p>Project Manager: Rosalyn Acosta</p>	<p>The project entails constructing a new multi-phase Aquatic Complex mainly on undeveloped land along Kirk Rd. within Lake Lytal Park. The existing Pool Facility is to be demolished once the new aquatic center is opened to the public. The major components of the new Aquatic Complex will be a 70 Meter competition pool with dive well, a family water play area, 6-lane warm-up pool, flow riders, slides and building amenities such as restrooms, lockers, concession stand.</p> <p>FY 2017 IST - \$4,000,000 FY 2018 IST - \$2,000,000</p>	

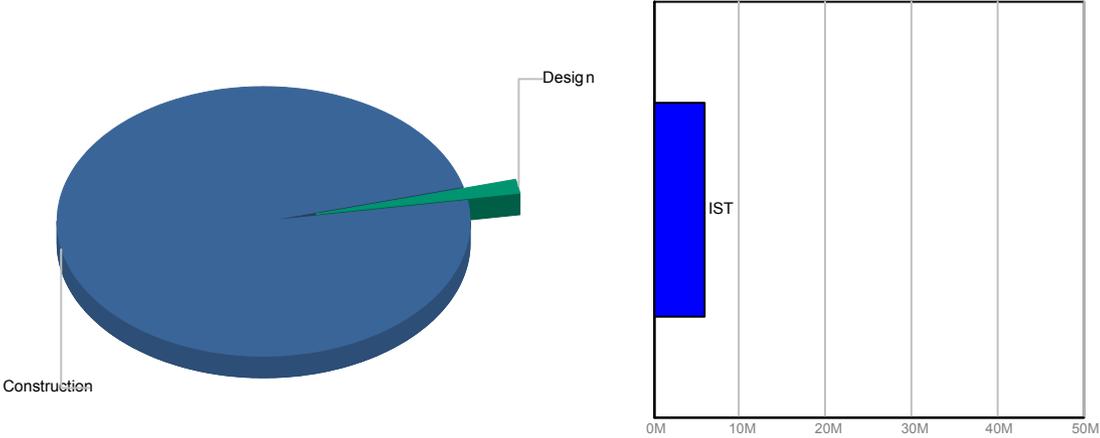SCHEDULE SUMMARY	PARTICIPATION	FUNDING																					
<table border="1"> <thead> <tr> <th></th> <th>Original</th> <th>Actual</th> </tr> </thead> <tbody> <tr> <td>Project Start</td> <td>4/19/2018</td> <td>4/19/2018</td> </tr> <tr> <td>Design Start (Master Plan)</td> <td>7/10/2018</td> <td>7/10/2018</td> </tr> <tr> <td>Design Start (Aquatic Center)</td> <td>11/20/2018</td> <td></td> </tr> <tr> <td>Construction Start</td> <td>7/1/2019</td> <td></td> </tr> <tr> <td>Substantial Completion</td> <td>7/1/2020</td> <td></td> </tr> <tr> <td>Project Completion</td> <td>9/1/2020</td> <td></td> </tr> </tbody> </table>		Original	Actual	Project Start	4/19/2018	4/19/2018	Design Start (Master Plan)	7/10/2018	7/10/2018	Design Start (Aquatic Center)	11/20/2018		Construction Start	7/1/2019		Substantial Completion	7/1/2020		Project Completion	9/1/2020		<p><b>Consultant</b></p> <p>SBE 30%</p> <p>Local 100%</p> <p>WBE N/A</p> <p>MBE N/A</p> <p><b>Contractor</b></p> <p>SBE TBD</p> <p>Local TBD</p> <p>WBE TBD</p> <p>MBE TBD</p>	 <p style="text-align: center;"><b>Current Budget</b></p> <p style="text-align: center;"><b>Fund Source</b></p>
	Original	Actual																					
Project Start	4/19/2018	4/19/2018																					
Design Start (Master Plan)	7/10/2018	7/10/2018																					
Design Start (Aquatic Center)	11/20/2018																						
Construction Start	7/1/2019																						
Substantial Completion	7/1/2020																						
Project Completion	9/1/2020																						

FINANCIAL SUMMARY				
	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$100,000	\$53,801	53.80%	\$53,801
Construction	\$5,900,000	\$86,785	1.47%	\$400
Furniture, Fixtures & Equipment	\$0	\$0	0.00%	\$0
Other	\$0	\$37,316	0.00%	\$37,316
Contingency	\$0	\$0	0.00%	\$0
<b>TOTAL</b>	<b>\$6,000,000</b>	<b>\$177,903</b>	<b>2.97%</b>	<b>\$91,517</b>

**NOTES**

Consultant CSA is going for BCC approval on 8/17.

# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects

Data Date: 7/15/2021

Report Date: 8/12/2021

### DESCRIPTION/TEAM

### SCOPE

### PHOTO

**Project Title:** Community Park - Paulette Burdick Park  
**Project Number:** 18230  
**BCC District:** CW  
**Delivery Method:** TBD  
**Category:** N02-New Park Development  
**Status:** Design  
**Designer:** Urban Design Kilday Studio  
**Contractor:** TBD  
**Project Manager:** Rosalyn Acosta

Construction of a neighborhood park that will service Cam Estates neighborhood, Meadowbrook and Plantation CCRT areas. The Park will mainly feature a walking pathway, children's playground and basketball courts.

IST Funding included in Current FY Budget: \$1,000,000  
 IST Funding included in FY2023 Budget: \$4,900,000



### SCHEDULE SUMMARY

	Original	Actual
Pre-Scope meeting with User	8/7/2018	8/7/2018
Final Concept Drawings (Parks)	8/15/2018	8/15/2018
Pre-Scope with Consultant	8/29/2018	8/29/2018
Project Start (Due Diligence)	11/1/2018	11/28/2018
Design Start	1/7/2019	12/8/2020
Construction Start	4/1/2019	
Substantial Completion	9/1/2019	
Project Completion	10/1/2019	

### PARTICIPATION

#### Consultant

SBE 100%

Local 100%

WBE N/A

MBE N/A

#### Contractor


SBE TBD

Local TBD


WBE TBD

MBE TBD

### FUNDING

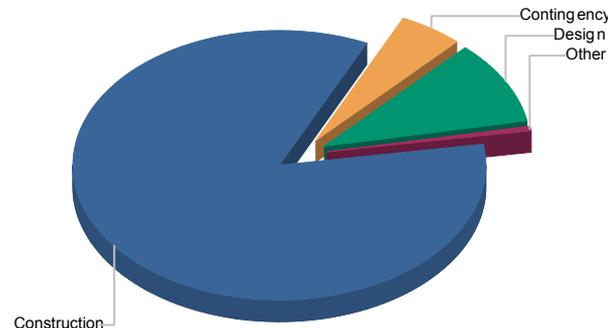

Current Budget

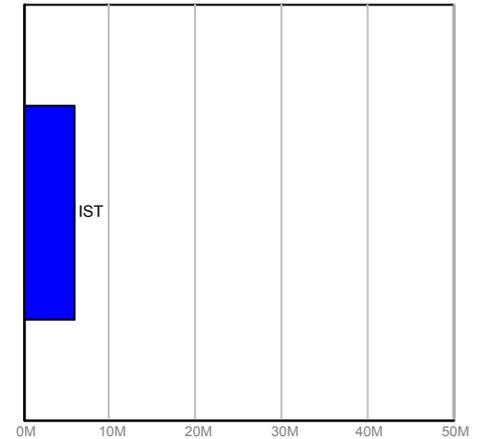

Fund Source

### FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$590,000	\$74,183	12.57%	\$74,183
Construction	\$5,015,000	\$71,236	1.42%	\$71,235
Furniture, Fixtures & Equipment	\$0	\$0	0.00%	\$0
Other	\$32,965	\$33,190	100.68%	\$33,190
Contingency	\$295,000	\$0	0.00%	\$0
<b>TOTAL</b>	<b>\$5,932,965</b>	<b>\$178,608</b>	<b>3.01%</b>	<b>\$178,608</b>

### NOTES

No changes since last report. CID is holding con CSA approval pending resolution of existing encroachment conditions on the site. Terracon is preparing a proposal to abandon testing wells since last set of samples were below levels and acceptable to FDEP.



# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects

Data Date: 7/15/2021

Report Date: 8/12/2021

DESCRIPTION/TEAM	SCOPE	PHOTO
<p><b>Project Title:</b> Lake Worth West Substation</p> <p>Project Number: B607                      BCC District: Multiple                      Delivery Method: Construction Manager at Risk                      Category: S06-Sheriff - FDO                      Status: Design                      Designer: Ohlson Lavoie Collaborative                      Contractor: D Stephenson                      Project Manager: Sunil Jagoo</p>	<p>Provide dedicated office(s) within the HRC2 building (project-19220) for PBSO field personnel's use. Additional interior improvements include a multipurpose room for PBSO training purposes and HRC/community programming, as well as restrooms, circulation area, and other incidental improvements.</p> <p>FY 2019 IST \$1,213,460</p>	

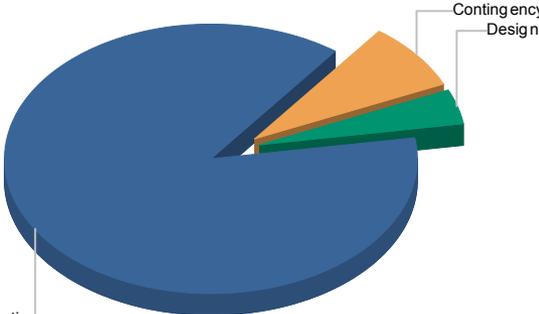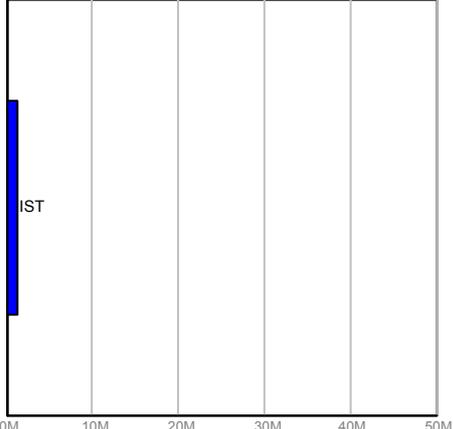SCHEDULE SUMMARY	PARTICIPATION	FUNDING				
<table border="1"> <thead> <tr> <th>Original</th> <th>Actual</th> </tr> </thead> <tbody> <tr> <td colspan="2">Please Refer to Central County Resource</td> </tr> </tbody> </table>	Original	Actual	Please Refer to Central County Resource		<p><b>Consultant</b></p> <p>SBE TBD                      Local TBD                      WBE TBD                      MBE TBD</p> <p><b>Contractor</b></p> <p>SBE TBD                      Local TBD                      WBE TBD                      MBE TBD</p>	 <p style="text-align: center;"><b>Current Budget</b></p>  <p style="text-align: center;"><b>Fund Source</b></p>
Original	Actual					
Please Refer to Central County Resource						

FINANCIAL SUMMARY				
	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$50,000	\$2,227	4.45%	\$2,227
Construction	\$1,063,460	\$4,868	0.46%	\$4,868
Contingency	\$100,000	\$0	0.00%	\$0
<b>TOTAL</b>	<b>\$1,213,460</b>	<b>\$7,095</b>	<b>0.58%</b>	<b>\$7,095</b>

**NOTES**

Please refer to the Central County Resource Center report for current status and material project updates.

# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects

Data Date: 7/15/2021

Report Date: 8/12/2021

### DESCRIPTION/TEAM

### SCOPE

### PHOTO

**Project Title:** Housing Units for Homeless, Extremely Low Income, & Low Income

Project Number: Q001  
 BCC District: CW  
 Delivery Method: TBD  
 Category: H02-Housing  
 Status: Design  
 Designer: TBD  
 Contractor: TBD  
 Project Manager: Eric McClellan

This project involves the acquisition and renovation of older, possibly run down motel properties into efficiency units for use as temporary or longer term affordable housing for homeless and special populations.

This Project is funded in:  
 FY 2017 - FY 2026 for \$2,550,000 each year for a total project estimate at \$25,500,000.



### SCHEDULE SUMMARY

	Original	Actual
Project Start	9/1/2017	9/1/2017
Construction Start		
Substantial Completion		
Project Completion		
Design Start		
RFP Development Start	12/1/2017	12/1/2017
RFP Release	11/26/2018	12/19/2019
RFP Award		

### PARTICIPATION


#### Consultant

SBE TBD  
 Local TBD  
 WBE N/A  
 MBE N/A

#### Contractor

SBE TBD  
 Local TBD  
 WBE TBD  
 MBE TBD

### FUNDING

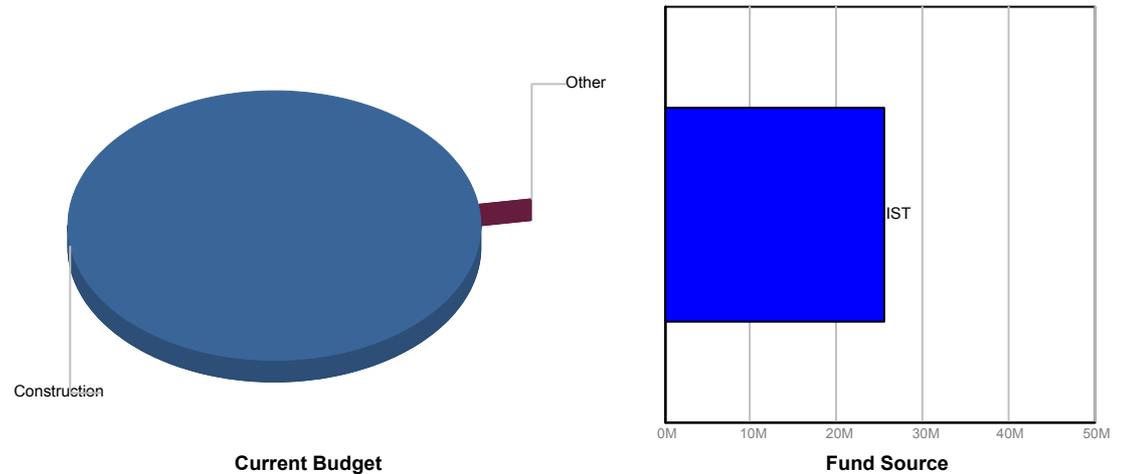

### FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$0	\$11,481	0.00%	\$10,681
Construction	\$25,470,000	\$1,010,805	3.97%	\$578,680
Furniture, Fixtures & Equipment	\$0	\$0	0.00%	\$0
Other	\$30,000	\$44,231	147.44%	\$44,231
Contingency	\$0	\$0	0.00%	\$0
<b>TOTAL</b>	<b>\$25,500,000</b>	<b>\$1,066,517</b>	<b>4.18%</b>	<b>\$633,593</b>

### NOTES

This Project will fund multiple projects over the 10 year period. Direction from the BCC was given on 9/26/2017 to proceed with an affordable housing pilot project. Staff of FD&O, DHES, Community Services, and Administration presented a proposed Project Plan for the remainder of the funding at a BCC Workshop on February 26, 2019 and received direction. The RFP for the Cottage Homes pilot project was awarded by the BCC to the WPB Housing Authority on January 12, 2021. Design by the WPBHA is now in progress. An allocation of \$1M toward renovation of a non-congregate shelter in Pahokee was approved by the BCC on Sept. 15, 2020. Development of a solicitation is now commencing on the next phase of the Project Plan (i.e. Tax Deed Surplus Property Conveyance and Housing Authorities Incentive Funding).

# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects


Data Date: 7/15/2021

Report Date: 8/12/2021

DESCRIPTION/TEAM	SCOPE	PHOTO
<p><b>Project Title:</b> Vehicle Replacement</p> <p>Project Number: Q007                      BCC District: Multiple                      Delivery Method: Direct Purchase                      Category: S04-Sheriff                      Status: Construction                      Designer: N/A                      Contractor: N/A                      Project Manager: Isami Ayala-Collazo</p>	<p>This project funds the replacement of PBSO public safety vehicles and related equipment (other than radios), tools and/or services.</p> <p>FY 18 Funds: \$3,650,513                      FY 19 Funds: \$3,650,513                      FY 20 Funds: \$3,650,514                      FY 24 Funds: \$1,669,963</p>	

SCHEDULE SUMMARY		
	Original	Actual
1 Project Start	10/1/2018	5/1/2018
2 Project Completion	9/30/2024	

PARTICIPATION	
<b>Consultant</b>	
SBE	N/A
Local	N/A
WBE	N/A
MBE	N/A
<b>Contractor</b>	
SBE	N/A
Local	N/A
WBE	N/A
MBE	N/A

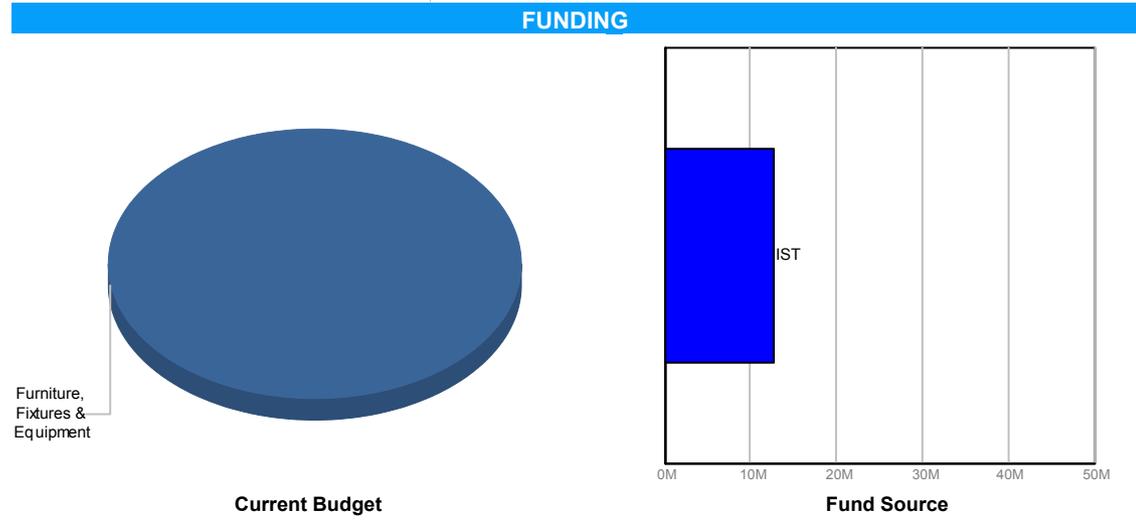

FINANCIAL SUMMARY				
	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Furniture, Fixtures & Equipment	\$12,621,503	\$10,933,034	86.62%	\$10,933,034
Other	\$0	\$0	0.00%	\$0
<b>TOTAL</b>	<b>\$12,621,503</b>	<b>\$10,933,034</b>	<b>86.62%</b>	<b>\$10,933,034</b>

**NOTES**

Prioritization, identification and cost of specific assets are determined by the Sheriff's Office with administration support being performed by FD&O through a Project Funding Agreement with the County.

# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects

Data Date: 7/15/2021

Report Date: 8/12/2021

### DESCRIPTION/TEAM

### SCOPE

### PHOTO

**Project Title:** Animal Care & Control

Project Number: Q008  
 BCC District: CW  
 Delivery Method: Construction Manager at Risk  
 Category: G02-General Government Facilities  
 Status: Design  
 Designer: PGAL  
 Contractor: Wharton-Smith  
 Project Manager: Rich Avery

The Animal Care & Control Renovation & Expansion project for the Belvedere Rd. campus includes: renovations to existing buildings for improved functionality; possible replacement of non-air conditioned kennel buildings with air-conditioned kennel buildings pending evaluation, pricing and approval; and the creation of new spaces necessary to facilitate current and future projected operational needs. The cost of the project includes cost-estimating services necessary in order to validate the project scope, which was derived jointly by FDO & the ACC Division via a needs assessment and programming document, as well as interim arrangements to sustain continuous operations during construction.



### SCHEDULE SUMMARY

	Original	Actual
PROGRAMMING	10/1/2018	10/1/2018
Commence Design Comparative Study	7/24/2019	7/24/2019
Design Start	2/3/2020	12/2/2020
Construction Start	12/1/2020	
Substantial Completion	7/3/2023	

### PARTICIPATION


#### Consultant

SBE 20%  
 Local 100%  
 WBE N/A  
 MBE N/A


#### Contractor

SBE 13.04%  
 Local 13.04%  
 WBE 13.04%  
 MBE 13.04%

### FUNDING

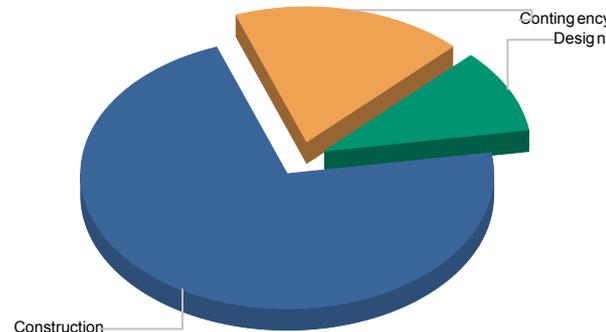

Current Budget

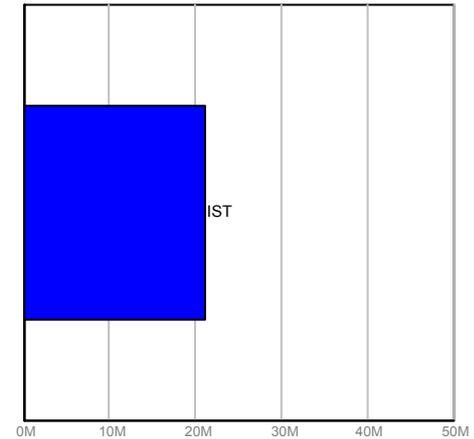

Fund Source

### FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$2,100,000	\$868,205	41.34%	\$361,457
Construction	\$15,120,000	\$213,791	1.41%	\$212,057
Contingency	\$3,780,000	\$0	0.00%	\$0
<b>TOTAL</b>	<b>\$21,000,000</b>	<b>\$1,081,996</b>	<b>5.15%</b>	<b>\$573,514</b>

### NOTES

The architect has completed the gathering of information phase and has commenced with compiling and creating the final schematic design package for submission to the County.

# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects

Data Date: 7/15/2021

Report Date: 8/12/2021

### DESCRIPTION/TEAM

### SCOPE

### PHOTO

**Project Title:** Central County Housing Resource Center  
**Project Number:** Q009  
**BCC District:** CW  
**Delivery Method:** Construction Manager at Risk  
**Category:** H02-Housing  
**Status:** Design  
**Designer:** Ohlson Lavoie Collaborative  
**Contractor:** D Stephenson  
**Project Manager:** Sunil Jagoo

The Homeless Resource Center 2 (HRC 2) is to provide an effective Crisis Response System that provides immediate and easy access to safe and decent temporary shelter to County residents that need it and aims to re-house people as quickly as possible while receiving wrap-around social services. The facility will compliment the County's existing Senator Philip D. Lewis Center in West Palm Beach and will consist of approximately 19,000 square feet to support 74 client beds, dining and service delivery/office areas, restrooms, laundry facilities, an intake lobby, and other incidental interior and exterior improvements. Co-located within the facility will be the improvements identified in the IST Project Plan titled PBSO Lake Worth West Substation.



### SCHEDULE SUMMARY

### PARTICIPATION

### FUNDING


	Original	Actual
Program Development	11/1/2017	11/1/2017
Public Outreach	2/1/2019	2/1/2019
Design Team Solicitation	5/1/2019	9/30/2020
CM Solicitation	9/1/2019	11/26/2019
Schematic Design	11/11/2019	1/31/2020
Design Development	5/1/2020	9/28/2020
Construction Documents	10/1/2020	2/23/2021
Permitting	1/1/2021	
Construction	6/1/2021	
CO/Substantial Completion	9/1/2022	
Occupancy	10/3/2022	

#### Consultant

SBE 0%  
 Local 25%  
 WBE 0%  
 MBE 0%

#### Contractor

SBE TBD  
 Local TBD  
 WBE TBD  
 MBE TBD

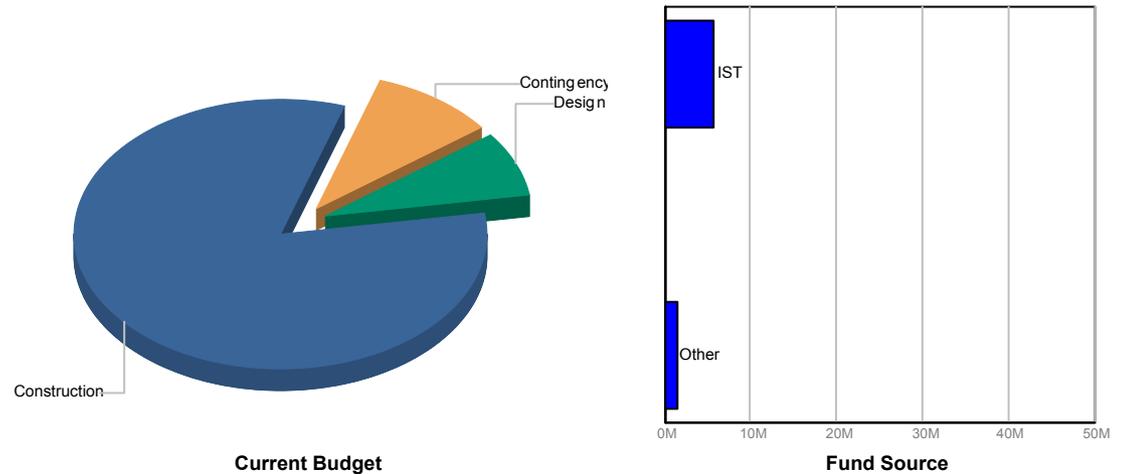

### FINANCIAL SUMMARY

### NOTES

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$550,000	\$76,436	13.90%	\$57,079
Construction	\$5,874,843	\$52,384	0.89%	\$52,384
Contingency	\$700,000	\$0	0.00%	\$0
<b>TOTAL</b>	<b>\$7,124,843</b>	<b>\$128,820</b>	<b>1.81%</b>	<b>\$109,463</b>

Zoning and Building Permit applications remain in progress. A GMP is under review. Funding includes \$5.7 M from IST in FY19 and CDBG funds in the total amount of \$1,424,843

# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects

Data Date: 7/15/2021

Report Date: 8/12/2021

### DESCRIPTION/TEAM

### SCOPE

### PHOTO

**Project Title:** South County Administrative Complex

Project Number: Q010  
 BCC District: 07  
 Delivery Method: Varies  
 Category: G02-General Government Facilities  
 Status: Design  
 Designer: Varies  
 Contractor: Varies  
 Project Manager: Eric McClellan

This project funds essential Renewal and Replacement (R&R) needs to sustain the continuous operation of this 40+ year old complex prior to its future redevelopment. As such there is no defined scope of work. Any funds remaining at such time that redevelopment is funded would be utilized toward professional design services for the redevelopment. Funding includes \$3M each in FY 2020 and FY 2021, for a total of \$6M.



### SCHEDULE SUMMARY

### PARTICIPATION

### FUNDING


Original	Actual
N/A. See notes for current activity.	

#### Consultant

SBE 100%  
 Local 100%  
 WBE 78.6%  
 MBE 0%

#### Contractor

SBE TBD  
 Local TBD  
 WBE TBD  
 MBE TBD

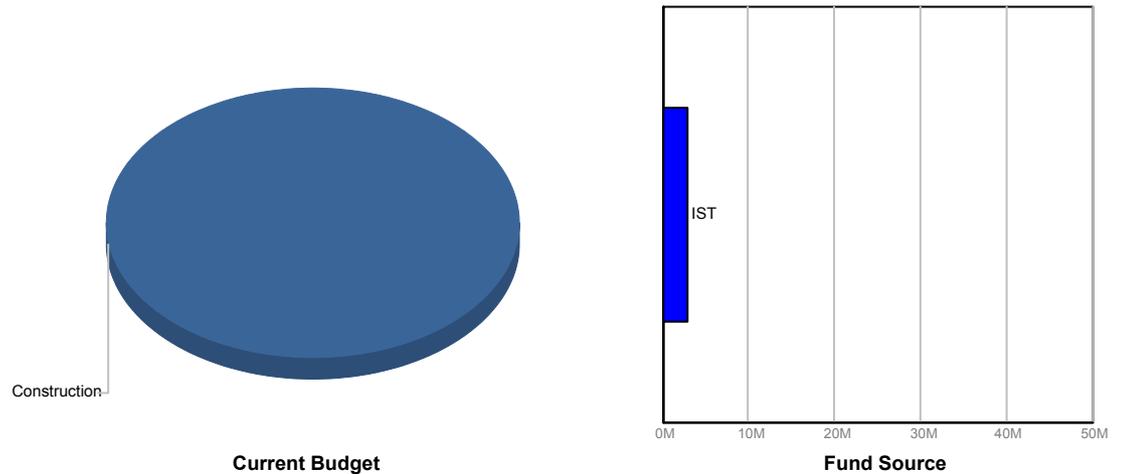

Current Budget

Fund Source

### FINANCIAL SUMMARY

### NOTES

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Construction	\$3,000,000	\$107,564	3.59%	\$56,812
Other	\$0	\$2,784	0.00%	\$1,732
<b>TOTAL</b>	<b>\$3,000,000</b>	<b>\$110,348</b>	<b>3.68%</b>	<b>\$58,544</b>

Paved vehicular surfaces throughout the complex are in need of R&R. Reconfiguration of a driveway for improved circulation, consistency with intended future site development and cross access with an adjacent property will be implemented same time to preclude future duplication of work and lost investment. Planning and design services to permit this scope of work are currently being procured.

A scope of work for other R&R needs is currently under development.

# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects

Data Date: 7/15/2021

Report Date: 8/12/2021

### DESCRIPTION/TEAM

### SCOPE

### PHOTO

**Project Title:** Detention Center Facilities R/R (Phases 3-5)  
**Project Number:** Q019  
**BCC District:** Multiple  
**Delivery Method:** Construction Management  
**Category:** S06-Sheriff - FDO  
**Status:** Construction  
**Designer:** Leo A. Daly  
**Contractor:** Hedrick Brothers Construction  
**Project Manager:** Jeffrey Halverson

Phases 3-5 consist of the East Tower and West Tower which are located at the Main Detention Center. The West Detention Center is located in Belle Glade. The design for both towers and the West Detention Center will require repairing and replacing MEP, Fire Sprinkler System, Low Voltage Systems and interior finishes.  
 Detention Center Facilities R/R (Phases 3-5)  
 FY 2018 IST \$8,500,000  
 FY 2019 IST \$14,700,000  
 FY 2020 IST \$9,800,000



### SCHEDULE SUMMARY

	Original	Actual
East Tower Design Start	11/12/2018	7/11/2019
East Tower Construction Start	10/14/2019	
East Tower Substantial Completion	11/10/2020	

### PARTICIPATION


#### Consultant

SBE 19.88%  
 Local 67%  
 WBE N/A  
 MBE N/A


#### Contractor

SBE 63%  
 Local 84%  
 WBE N/A  
 MBE N/A

### FUNDING

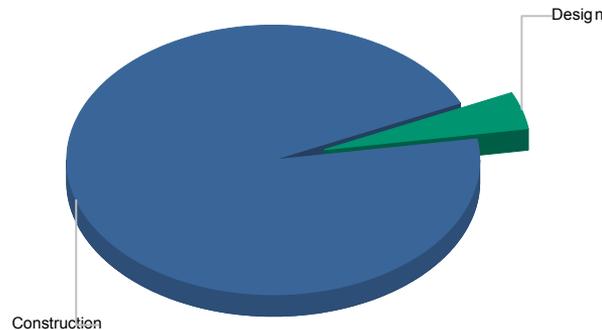

Current Budget

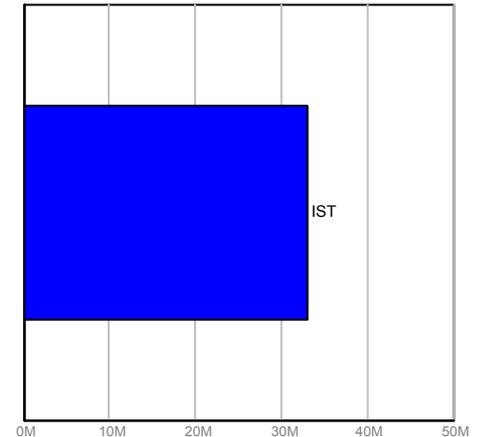

Fund Source

### FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$1,500,000	\$1,973,453	131.56%	\$457,794
Construction	\$31,595,881	\$19,578,878	61.97%	\$10,584,164
Other	\$0	\$1,293,581	0.00%	\$813,240
Contingency	\$0	\$0	0.00%	\$0
<b>TOTAL</b>	<b>\$33,095,881</b>	<b>\$22,845,912</b>	<b>69.03%</b>	<b>\$11,855,198</b>

### NOTES

Main Detention Center South Tower: HVAC units are installed and ducting to the units is underway.  
 Main Detention Center East Tower: New mechanical rooms at 75% complete. All piping for HVAC is in progress. Ductwork still being installed. Roofing material is approximately 90% installed for high roof. Copping cap is being installed. Scaffolding installed to allow construction of ventilation shaft on south side of East Tower.  
 Main Detention Center West Tower: 95% Drawings are in process and are being updated with information learned from East Tower work. Central Energy Plant drawings are being divided out so this work can proceed ahead of other work so the Chiller work can be done during cooler months.

# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects

Data Date: 7/15/2021

Report Date: 8/12/2021

### DESCRIPTION/TEAM

### SCOPE

### PHOTO

**Project Title:** West Boynton Park Athletic Field Renovations Sports Turf  
**Project Number:** T002  
**BCC District:** 03  
**Delivery Method:** TBD  
**Category:** A06-Athletic Field Renovations  
**Status:** Design  
**Designer:** Florida Transportation Engineering  
**Contractor:** TBD  
**Project Manager:** Stuart Patterson

Replacement of existing grass field turf with synthetic turf on multi-purpose field 1 & 2.  
**Funded:**  
 FY 2020 \$1,000,000  
 FY 2023 \$1,000,000



### SCHEDULE SUMMARY

	Original	Actual
Begin Existing Site Surveys	1/29/2020	1/29/2020
Complete Existing Site Surveys	6/30/2020	5/18/2020
Finalization of Existing Site Surveys	8/30/2020	9/18/2020
Design RFP Proposals Due	9/4/2020	9/10/2020
Design RFP Final Selection	10/29/2020	10/29/2020
Consultant Contract Issuance	12/14/2020	4/20/2021
Design Completion	7/2/2021	
Turf Supplier RFP Proposal Due	4/30/2021	

### PARTICIPATION


**Consultant**

- SBE 25%
- Local 25%
- WBE 0%
- MBE 6.13%

**Contractor**

- SBE TBD
- Local TBD
- WBE TBD
- MBE TBD

### FUNDING

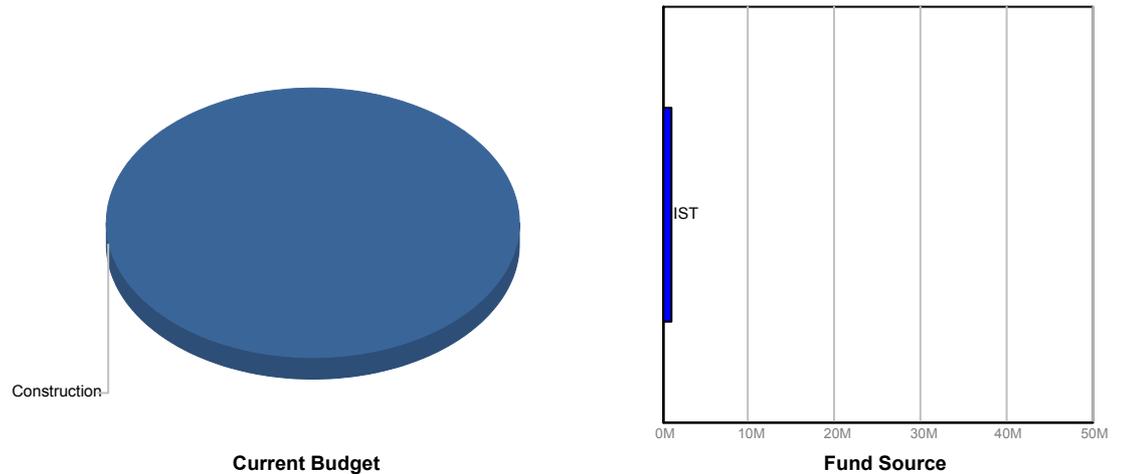

### FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$0	\$174,982	0.00%	\$8,582
Construction	\$1,000,000	\$15,650	1.57%	\$15,650
Furniture, Fixtures & Equipment	\$0	\$0	0.00%	\$0
Other	\$0	\$76	0.00%	\$76
Contingency	\$0	\$0	0.00%	\$0
<b>TOTAL</b>	<b>\$1,000,000</b>	<b>\$190,708</b>	<b>19.07%</b>	<b>\$24,308</b>

### NOTES

DJLA survey complete. Design schedule TBD, but expected to be 100% complete by 12/31/2021. Design and schedule review meeting held 8/6/2021. DD drawings have been complete and review comments have been returned to FTE.



# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects

Data Date: 7/15/2021

Report Date: 8/12/2021

DESCRIPTION/TEAM	SCOPE	PHOTO
<p><b>Project Title: Buttonwood Park</b></p> <p>Project Number: T003                      BCC District: 03                      Delivery Method: TBD                      Category: A06-Athletic Field Renovations                      Status: Design                      Designer: Florida Transportation Engineering                      Contractor: TBD                      Project Manager: Stuart Patterson</p>	<p>Replacement of existing grass field turf with synthetic turf on multi-purpose field 2 &amp; 3</p> <p>Funded:                      FY 2017 \$11,658                      FY 2021 \$900,000                      FY 2023 \$1,488,342</p>	

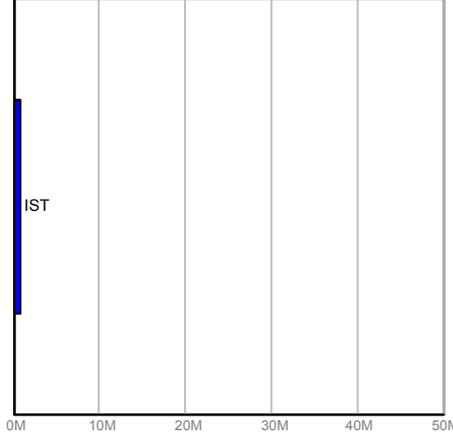SCHEDULE SUMMARY	PARTICIPATION	FUNDING																								
<table border="1"> <thead> <tr> <th></th> <th>Original</th> <th>Actual</th> </tr> </thead> <tbody> <tr> <td>Begin Existing Site Surveys</td> <td>1/29/2020</td> <td>1/29/2020</td> </tr> <tr> <td>Complete Existing Site Surveys</td> <td>8/30/2020</td> <td>5/18/2020</td> </tr> <tr> <td>Finalization of Existing Site Surveys</td> <td>8/30/2020</td> <td>9/18/2020</td> </tr> <tr> <td>Design RFP Proposals Due</td> <td>9/4/2020</td> <td>9/10/2020</td> </tr> <tr> <td>Consultant Contract Issuance</td> <td>12/14/2020</td> <td>4/20/2021</td> </tr> <tr> <td>Design Completion</td> <td>7/22/2001</td> <td></td> </tr> <tr> <td>Turf Supplier RFP Proposal Due</td> <td>4/30/2021</td> <td></td> </tr> </tbody> </table>		Original	Actual	Begin Existing Site Surveys	1/29/2020	1/29/2020	Complete Existing Site Surveys	8/30/2020	5/18/2020	Finalization of Existing Site Surveys	8/30/2020	9/18/2020	Design RFP Proposals Due	9/4/2020	9/10/2020	Consultant Contract Issuance	12/14/2020	4/20/2021	Design Completion	7/22/2001		Turf Supplier RFP Proposal Due	4/30/2021		<p><b>Consultant</b></p> <p>SBE 25%</p> <p>Local 25%</p> <p>WBE 0%</p> <p>MBE 6.13%</p> <p><b>Contractor</b></p> <p>SBE TBD</p> <p>Local TBD</p> <p>WBE TBD</p> <p>MBE TBD</p>	<div style="text-align: center;">  <p>Current Budget</p> </div> <div style="text-align: center;">  <p>Fund Source</p> </div>
	Original	Actual																								
Begin Existing Site Surveys	1/29/2020	1/29/2020																								
Complete Existing Site Surveys	8/30/2020	5/18/2020																								
Finalization of Existing Site Surveys	8/30/2020	9/18/2020																								
Design RFP Proposals Due	9/4/2020	9/10/2020																								
Consultant Contract Issuance	12/14/2020	4/20/2021																								
Design Completion	7/22/2001																									
Turf Supplier RFP Proposal Due	4/30/2021																									

FINANCIAL SUMMARY				
	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$0	\$181,894	0.00%	\$13,895
Construction	\$911,658	\$0	0.00%	\$0
Furniture, Fixtures & Equipment	\$0	\$0	0.00%	\$0
Other	\$0	\$12,458	0.00%	\$12,458
Contingency	\$0	\$0	0.00%	\$0
<b>TOTAL</b>	<b>\$911,658</b>	<b>\$194,353</b>	<b>21.32%</b>	<b>\$26,353</b>

**NOTES**

DJLA survey submitted for PREM review. Design schedule TBD, but expected to be 100% complete by 12/31/2021. Design and schedule review meeting held 8/6/2021. DD drawings have been complete and review comments have been returned to FTE.

# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects

Data Date: 7/15/2021

Report Date: 8/12/2021

### DESCRIPTION/TEAM

### SCOPE

### PHOTO

**Project Title:** FY2017 Sports Field Lighting Replacement  
**Project Number:** T006  
**BCC District:** Multiple  
**Delivery Method:** Sports Field Lighting Annual  
**Category:** S12-Sports Lighting Replacement  
**Status:** Design  
**Designer:** JLRD Engineers  
**Contractor:** Musco  
**Project Manager:** Stuart Patterson

Replacement of Sports Field Lighting at Bert Winters Park, Caloosa Park, Glades Pioneer Park, Juno South Park, Jupiter Farms Park, Okeehelée Park, Pinewoods Park, (Burt Aaronson) South County Regional Park and Westgate Park.  
 IST FY 2017 funds: \$4,100,000.



### SCHEDULE SUMMARY

	Original	Actual
Project Start	6/29/2017	6/29/2017
Procurement (Light Fixture Vendor)	10/16/2018	10/16/2018
Procurement (Installation Contractor)	10/17/2018	5/9/2019
Final Completion	10/2/2020	
Bidding Package 1	11/6/2019	11/6/2019
Construction Phase 1	2/3/2020	2/3/2020
Construction Completion Phase 1	7/2/2020	8/24/2020
Bidding Package 2	2/13/2020	2/13/2020
Construction Start Phase 2	5/11/2020	4/2/2020
Construction Completion Phase 2	7/17/2020	4/2/2021
Bidding Package 3	3/26/2020	3/26/2020
Construction Start Phase 3	6/15/2020	6/1/2020
Construction Completion Phase 3	8/28/2020	

### PARTICIPATION


#### Consultant

SBE 100%  
 Local 100%  
 WBE N/A  
 MBE N/A

#### Contractor

SBE 0%  
 Local 75%  
 WBE 0%  
 MBE 0%

### FUNDING

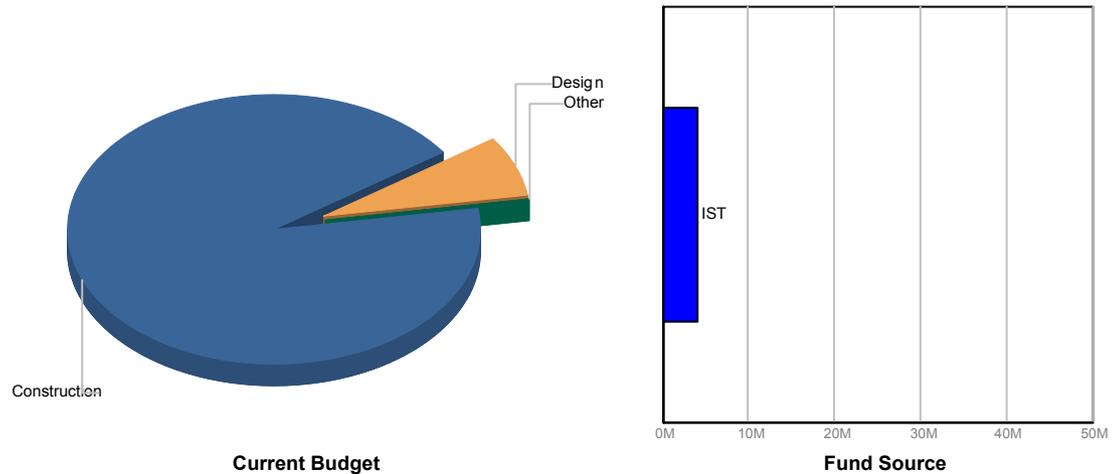

### FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$299,161	\$18,683	6.25%	\$18,683
Construction	\$3,800,000	\$3,777,380	99.40%	\$3,676,059
Other	\$839	\$2,952	351.65%	\$2,952
<b>TOTAL</b>	<b>\$4,100,000</b>	<b>\$3,799,014</b>	<b>92.66%</b>	<b>\$3,697,693</b>

### NOTES

Okeehelée Park Tennis Courts (Package 1), Jupiter Farms Park (Package 1), Caloosa Park (Package 1), Juno Park (Package 2), Westgate Park (Package 2), Bert Winters Park (Package 2), Glades Pioneer Park (Package 2), Pinewoods Park (Package 3), & S County Regional Park (Package 3): Completed

Okeehelée Park Remainder (Package 3) - Project is complete with the exception of added Ski Course pole; expected to be completed mid-August, 2021

# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects


Data Date: 7/15/2021

Report Date: 8/12/2021

DESCRIPTION/TEAM	SCOPE	PHOTO
<p><b>Project Title:</b> FY2018 Sports Field Lighting Replacement</p> <p>Project Number: T007</p> <p>BCC District: Multiple</p> <p>Delivery Method: Sports Field Lighting Annual</p> <p>Category: S12-Sports Lighting Replacement</p> <p>Status: Design</p> <p>Designer: JLRD Engineers</p> <p>Contractor: Musco</p> <p>Project Manager: Stuart Patterson</p>	<p>Replacement of Sports Field Lighting at Dyer Park, Lake Charleston Park and (Burt Aaronson) South County Regional Park.</p> <p>IST FY 2018 funds: \$1,200,000.</p>	

SCHEDULE SUMMARY		
	Original	Actual
Bidding Package 1	11/6/2019	11/6/2019
Construction Start Phase 1	2/3/2020	2/3/2020
Construction Completion Phase 1	7/2/2020	8/24/2020
Bidding Package 2	2/13/2020	2/13/2020
Construction Start Phase 2	5/11/2020	4/2/2020
Construction Completion Phase 2	7/17/2020	4/2/2021
Bidding Package 3	3/26/2020	3/26/2020
Construction Start Phase 3	6/15/2020	6/1/2020
Construction Completion Phase 3		
Project Start	6/29/2017	6/29/2017
Procurement (Light Fixture Vendor)	10/16/2018	10/16/2018
Procurement (Installation Contractor)	10/17/2018	5/9/2019
Final Completion	10/2/2020	

PARTICIPATION	
<b>Consultant</b>	
SBE	100%
Local	100%
WBE	N/A
MBE	N/A
<b>Contractor</b>	
SBE	0%
Local	75%
WBE	0%
MBE	0%

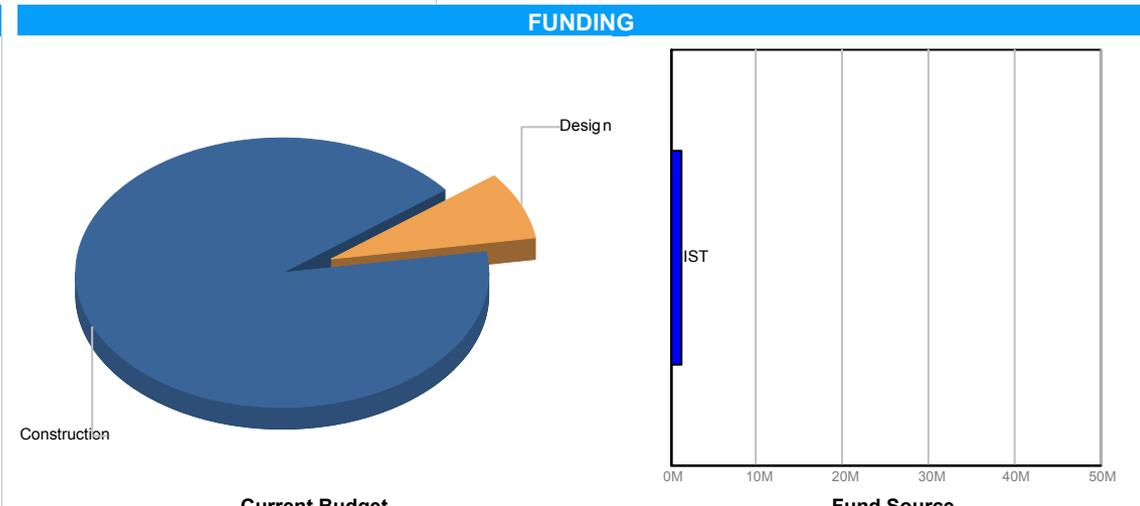

FINANCIAL SUMMARY				
	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$96,000	\$183,041	190.67%	\$183,041
Construction	\$1,104,000	\$193,788	17.55%	\$144,888
<b>TOTAL</b>	<b>\$1,200,000</b>	<b>\$376,829</b>	<b>31.40%</b>	<b>\$327,929</b>

**NOTES**

Lake Charleston Park (Package 1) & S County Regional Park (Package 3): Completed

Dyer Park (Package 3): Construction Complete. Currently in Closeout. Expected completion by end of August.



# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects

Data Date: 7/15/2021

Report Date: 8/12/2021

DESCRIPTION/TEAM	SCOPE	PHOTO
<p><b>Project Title:</b> FY2020 Sports Field Lighting Replacement</p> <p>Project Number: T010</p> <p>BCC District: Multiple</p> <p>Delivery Method: Sports Field Lighting Annual</p> <p>Category: S12-Sports Lighting Replacement</p> <p>Status: Design</p> <p>Designer: JLRD Engineers</p> <p>Contractor: Musco</p> <p>Project Manager: Stuart Patterson</p>	<p>Lake Lytal Athletic Courts, Haverhill Tennis &amp; Racquetball Courts, BASCR Basketball Courts, Duncan Padget Park Raquetball Courts</p> <p>IST Funds = \$1,300,000.</p>	

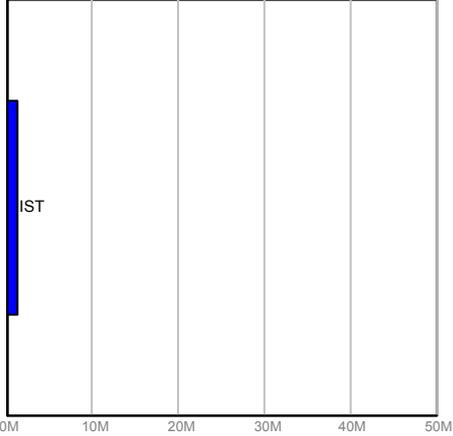SCHEDULE SUMMARY	PARTICIPATION	FUNDING												
<table border="1"> <thead> <tr> <th></th> <th>Original</th> <th>Actual</th> </tr> </thead> <tbody> <tr> <td>Project Start</td> <td>6/29/2017</td> <td>6/29/2017</td> </tr> <tr> <td>Procurement (Light Fixture Vendor)</td> <td>10/16/2018</td> <td>10/16/2018</td> </tr> <tr> <td>Procurement (Installation Contractor)</td> <td>10/17/2018</td> <td></td> </tr> </tbody> </table>		Original	Actual	Project Start	6/29/2017	6/29/2017	Procurement (Light Fixture Vendor)	10/16/2018	10/16/2018	Procurement (Installation Contractor)	10/17/2018		<p><b>Consultant</b></p> <p>SBE 100%</p> <p>Local 100%</p> <p>WBE N/A</p> <p>MBE N/A</p> <p><b>Contractor</b></p> <p>SBE TBD</p> <p>Local TBD</p> <p>WBE TBD</p> <p>MBE TBD</p>	 <p style="text-align: center;"><b>Current Budget</b></p>  <p style="text-align: center;"><b>Fund Source</b></p>
	Original	Actual												
Project Start	6/29/2017	6/29/2017												
Procurement (Light Fixture Vendor)	10/16/2018	10/16/2018												
Procurement (Installation Contractor)	10/17/2018													

FINANCIAL SUMMARY				
	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$130,000	\$452,977	348.44%	\$78,374
Construction	\$1,070,000	\$0	0.00%	\$0
<b>TOTAL</b>	<b>\$1,200,000</b>	<b>\$452,977</b>	<b>37.75%</b>	<b>\$78,374</b>

**NOTES**

Lake Lytal (Package 1) & South County Regional Park (Package 1): Have been sent for advertisement for bid

Haverhill Park (Package 2) & Haverhill Park Racquetball Courts (Package 3): Awaiting advertisement for bid

Duncan Padget Park Raquetball Courts is currently on hold.



# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects

Data Date: 7/15/2021

Report Date: 8/12/2021

DESCRIPTION/TEAM	SCOPE	PHOTO
<p><b>Project Title:</b> FY2021 Sports Lighting Replacement</p> <p>Project Number: T011                      BCC District: Multiple                      Delivery Method: Sports Field Lighting Annual                      Category: S12-Sports Lighting Replacement                      Status: Design                      Designer: JLRD Engineers                      Contractor: Musco                      Project Manager: Stuart Patterson</p>	<p>Caloosa Park Athletic Courts, Seminole Palms BF 1-8 &amp; MPF 9-11, BASCR Tennis Courts, Carlin Park Tennis Courts, Veterans Park Tennis &amp; Bball Courts, Dyer Park Basketball Courts, Lake Lytal Tball Multipurpose Field 5.</p> <p>FY 2021 IST Funds = \$4,050,000.</p>	

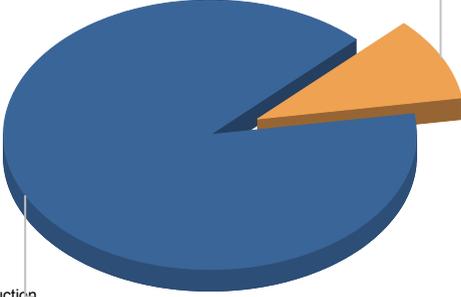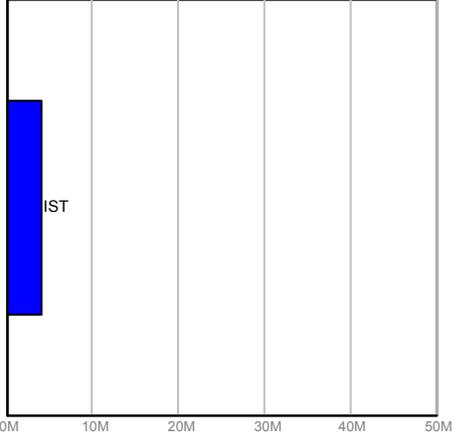SCHEDULE SUMMARY	PARTICIPATION	FUNDING												
<table border="1"> <thead> <tr> <th></th> <th>Original</th> <th>Actual</th> </tr> </thead> <tbody> <tr> <td>Project Start</td> <td>6/29/2017</td> <td>6/29/2017</td> </tr> <tr> <td></td> <td>10/16/2018</td> <td>10/16/2018</td> </tr> <tr> <td></td> <td>10/17/2018</td> <td></td> </tr> </tbody> </table>		Original	Actual	Project Start	6/29/2017	6/29/2017		10/16/2018	10/16/2018		10/17/2018		<p><b>Consultant</b></p> <p>SBE 100%</p> <p>Local 100%</p> <p>WBE N/A</p> <p>MBE N/A</p> <p><b>Contractor</b></p> <p>SBE TBD</p> <p>Local TBD</p> <p>WBE TBD</p> <p>MBE TBD</p>	<div style="display: flex; justify-content: space-around;"> <div style="text-align: center;">  <p><b>Current Budget</b></p> </div> <div style="text-align: center;">  <p><b>Fund Source</b></p> </div> </div>
	Original	Actual												
Project Start	6/29/2017	6/29/2017												
	10/16/2018	10/16/2018												
	10/17/2018													

FINANCIAL SUMMARY				
	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$405,000	\$104,224	25.73%	\$9,728
Construction	\$3,645,000	\$1,795,486	49.26%	\$0
<b>TOTAL</b>	<b>\$4,050,000</b>	<b>\$1,899,710</b>	<b>46.91%</b>	<b>\$9,728</b>

**NOTES**

Carlin Park (Package 1), Seminole Palms Park (Package 1), & South County Regional Park (Package 1): Have been sent for advertisement for bid

Caloosa Park (Package 2), Dyer Park (Package 2), & Veteran's Memorial Park (Package 2): Awaiting Advertisement for Bid

Lake Lytal Park is currently on hold.

# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects

Data Date: 7/15/2021

Report Date: 8/12/2021

### DESCRIPTION/TEAM

### SCOPE

### PHOTO

**Project Title: Bert Winters Park Redevelopment**

Project Number: T041  
 BCC District: 01  
 Delivery Method: Annual Contract  
 Category: E02-Existing Park Redevelopment or Expansion  
 Status: Design  
 Designer: Architecture Green  
 Contractor: TBD  
 Project Manager: Sunil Jagoo

Demolish former PBMI building, tennis courts, and playground. Remove lights and poles servicing Field 2. Renovate Baseball Field 1. Construct new regulation 220' x 360' multipurpose field. Construct new 30' x 60' rental pavilion. Construct new playground area. Renovate existing day use dock for public use. Construct new paved parking, curbing, landscaping, sidewalks and picnic areas. Install new underground infrastructure and site lighting.



The project is funded in:  
 FY 2019 IST \$200,000  
 FY 2021 IST \$1,500,000  
 FY 2021 FIND Grant TBD

### SCHEDULE SUMMARY

	Original	Actual
Project Start	8/22/2019	8/22/2019
Asbestos Report Initiated	8/23/2019	8/23/2019
Asbestos Report Completion	10/1/2019	10/1/2019
Demolition Start	11/12/2019	4/16/2020
Demolition Completion	12/5/2019	8/17/2020
Design Completion	TBD	

### PARTICIPATION


#### Consultant

SBE 89.28%  
 Local 100%  
 WBE N/A  
 MBE N/A


#### Contractor

SBE TBD  
 Local TBD  
 WBE TBD  
 MBE TBD

### FUNDING



Current Budget

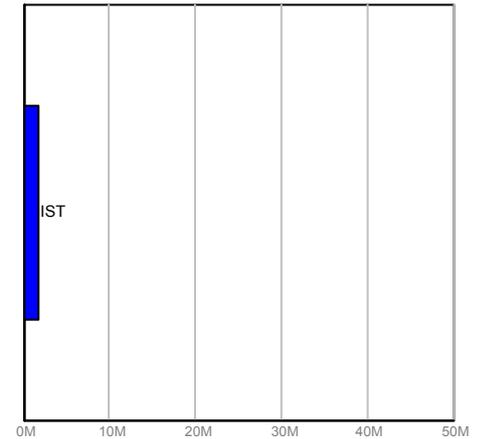

Fund Source

### FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Construction	\$1,700,000	\$103,947	6.11%	\$103,947
Other	\$0	\$3,084	0.00%	\$3,039
Contingency	\$0	\$270	0.00%	\$270
<b>TOTAL</b>	<b>\$1,700,000</b>	<b>\$107,301</b>	<b>6.31%</b>	<b>\$107,256</b>

### NOTES

Parks gave the ok to the consultant to proceed in developing the Master Plan. Awaiting the set of plans for review.

# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects

Data Date: 7/15/2021

Report Date: 8/12/2021

### DESCRIPTION/TEAM


### SCOPE

### PHOTO

**Project Title:** Aqua Crest Pool Facility Replacement

Project Number: T077  
 BCC District: 07  
 Delivery Method: CMR  
 Category: A02-Aquatic Facility Repair and Replacement  
 Status: Design  
 Designer: Ohlson Lavoie Collaborative  
 Contractor: TBD  
 Project Manager: Rosalyn Acosta

The work consist of the design and renovation of the existing Aqua Crest pool facility. The scope includes but is not limited to: pool improvements such as leak detection, re-surface, lane marker replacement, filtration system replacement; pool deck renovations; demolition of wadding pool; new splash pad; relocation of ticketing booth, admin offices, guards room and weight's room; bathroom renovations; new shade structures and Marquee sign.

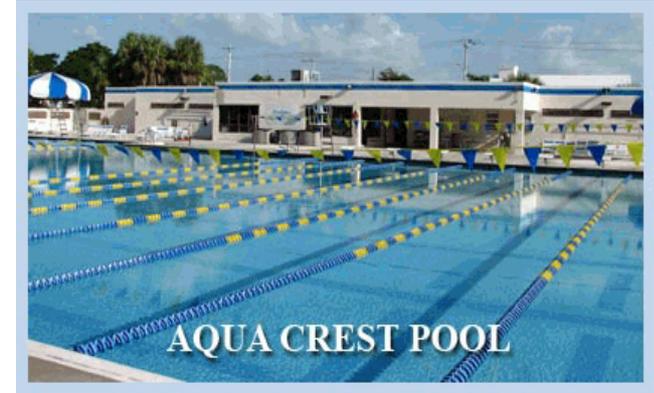

### SCHEDULE SUMMARY

	Original	Actual
Pre-Scope meeting	2/20/2019	2/20/2019
Design Services Advertisement	6/17/2019	8/4/2019
Consultant BCC Approval	1/14/2020	
Design Start	1/21/2020	
Construction Start	3/9/2021	
Substantial Completion	3/8/2022	
Project Close-out	5/3/2022	

### PARTICIPATION


#### Consultant

SBE TBD  
 Local TBD  
 WBE N/A  
 MBE N/A


#### Contractor

SBE TBD  
 Local TBD  
 WBE TBD  
 MBE TBD

### FUNDING

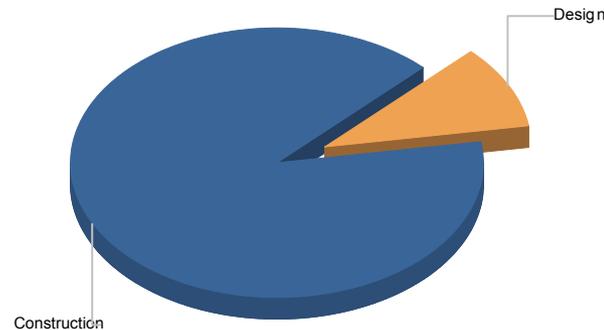

Current Budget

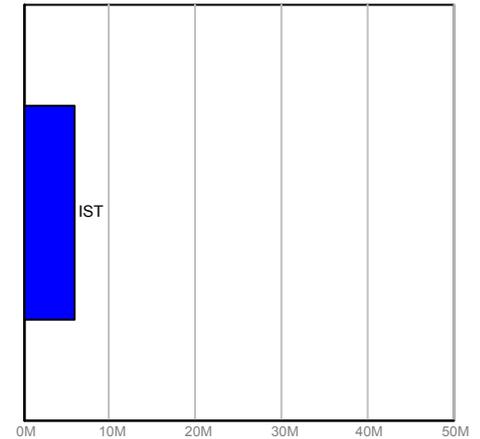

Fund Source

### FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$600,000	\$123,092	20.52%	\$105,826
Construction	\$5,400,000	\$14,058	0.26%	\$14,058
<b>TOTAL</b>	<b>\$6,000,000</b>	<b>\$137,150</b>	<b>2.29%</b>	<b>\$119,884</b>

### NOTES

No status change. Re-estimation workshop was postponed until after the budget is reviewed and approved by the BCC.

# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects

Data Date: 7/15/2021

Report Date: 8/12/2021

### DESCRIPTION/TEAM

### SCOPE

### PHOTO

**Project Title:** Dyer Park Athletic Field Renovation

Replacement of existing grass field turf with synthetic turf on multi-purpose field 3, 4, & 5 as well as additional damaged area.  
Funded: FY 2020 \$6,000,000



Project Number: T099  
BCC District: 07  
Delivery Method: TBD  
Category: A06-Athletic Field Renovations  
Status: Design  
Designer: Florida Transportation Engineering  
Contractor: TBD  
Project Manager: Stuart Patterson

### SCHEDULE SUMMARY

	Original	Actual
Begin Existing Site Surveys	1/29/2020	1/29/2020
Complete Existing Site Surveys	6/30/2020	5/18/2020
Consultant Contract Issuance	12/14/2020	4/20/2021
Design Completion	7/2/2021	
Turf Supplier RFP Proposal Due	4/30/2021	
Design RFP Final Selection	10/29/2020	10/29/2020
Finalization of Existing Site Surveys	8/30/2020	9/18/2020
Design RFP Proposals Due	9/4/2020	9/10/2020

### PARTICIPATION


#### Consultant

SBE 25%  
Local 25%  
WBE 0%  
MBE 6.13%


#### Contractor

SBE TBD  
Local TBD  
WBE TBD  
MBE TBD

### FUNDING

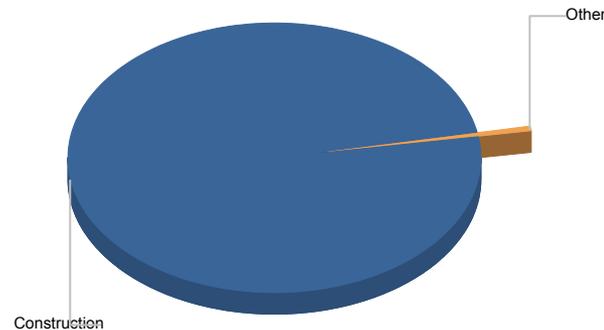

Current Budget

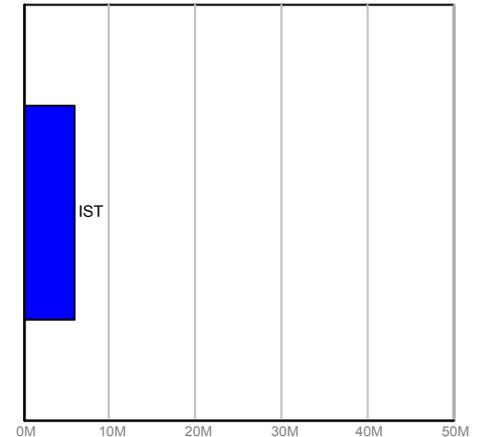

Fund Source

### FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Construction	\$5,970,000	\$17,250	0.29%	\$17,250
Other	\$30,000	\$226,792	755.97%	\$19,979
<b>TOTAL</b>	<b>\$6,000,000</b>	<b>\$244,042</b>	<b>4.07%</b>	<b>\$37,229</b>

### NOTES

Additional DJLA survey to be completed. Design schedule TBD, but expected to be 100% complete by 12/31/2021. Design and schedule review meeting held 8/6/2021. DD drawings have been complete and review comments have been returned to FTE.

# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects

Data Date: 7/15/2021

Report Date: 8/12/2021

### DESCRIPTION/TEAM

### SCOPE

### PHOTO

**Project Title:** Caloosa Park Athletic Field Renovation

Replacement of existing grass field turf with synthetic turf on multi-purpose field 1 & 3 as well as softball field 4.  
Funded: FY 2020 \$4,000,000



Project Number: T100  
BCC District: 04  
Delivery Method: TBD  
Category: A06-Athletic Field Renovations  
Status: Design  
Designer: Florida Transportation Engineering  
Contractor: TBD  
Project Manager: Stuart Patterson

### SCHEDULE SUMMARY

	Original	Actual
Begin Existing Site Surveys	1/29/2020	1/29/2020
Complete Existing Site Surveys	6/30/2020	5/18/2020
Consultant Contract Issuance	12/14/2020	4/20/2021
Design Completion	7/2/2021	
Turf Supplier RFP Proposal Due	4/30/2021	
Finalization of Existing Site Surveys	8/30/2020	9/18/2020
Design RFP Proposals Due	9/4/2020	9/10/2020
Design RFP Final Selection	10/29/2020	10/29/2020

### PARTICIPATION


#### Consultant

SBE 25%  
Local 25%  
WBE 0%  
MBE 6.13%


#### Contractor

SBE TBD  
Local TBD  
WBE TBD  
MBE TBD

### FUNDING

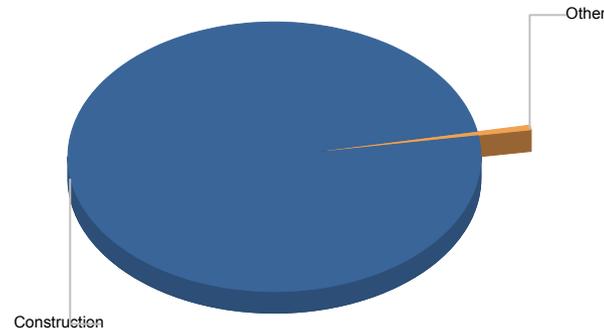

Current Budget

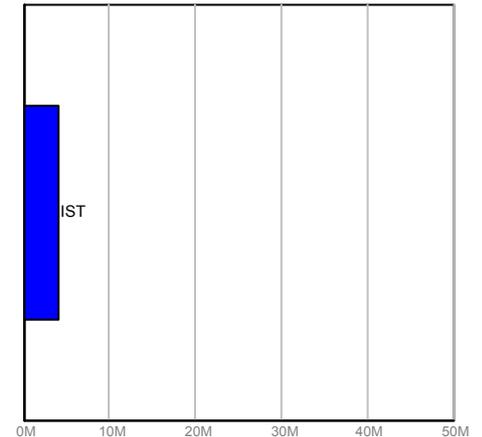

Fund Source

### FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Construction	\$3,980,000	\$227,501	5.72%	\$22,215
Other	\$20,000	\$11,755	58.78%	\$11,755
<b>TOTAL</b>	<b>\$4,000,000</b>	<b>\$239,257</b>	<b>5.98%</b>	<b>\$33,971</b>

### NOTES

DJLA survey complete. Design schedule TBD, but expected to be 100% complete by 12/31/2021. Design and schedule review meeting held 8/6/2021. DD drawings have been complete and review comments have been returned to FTE.

# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects

Data Date: 7/15/2021

Report Date: 8/12/2021

### DESCRIPTION/TEAM

### SCOPE

### PHOTO

**Project Title:** JPP Athletic Field Renovation

Replacement of existing grass field turf with synthetic turf on the Miracle League Field as well as softball fields 2 & 3.  
Funded: FY 2020 \$3,222,000



Project Number: T101  
BCC District: 03  
Delivery Method: TBD  
Category: A06-Athletic Field Renovations  
Status: Design  
Designer: Florida Transportation Engineering  
Contractor: TBD  
Project Manager: Stuart Patterson

### SCHEDULE SUMMARY

	Original	Actual
Design RFP Final Selection	10/29/2020	10/29/2020
Finalization of Existing Site Surveys	8/30/2020	9/18/2020
Design RFP Proposals Due	9/4/2020	9/10/2020
Consultant Contract Issuance	12/14/2020	4/20/2021
Design Completion	7/2/2021	
Turf Supplier RFP Proposal Due	4/30/2021	
Begin Existing Site Surveys	1/29/2020	1/29/2020
Complete Existing Site Surveys	6/30/2020	5/18/2020

### PARTICIPATION


#### Consultant

SBE 25%  
Local 25%  
WBE 0%  
MBE 6.13%

#### Contractor

SBE TBD  
Local TBD  
WBE TBD  
MBE TBD

### FUNDING

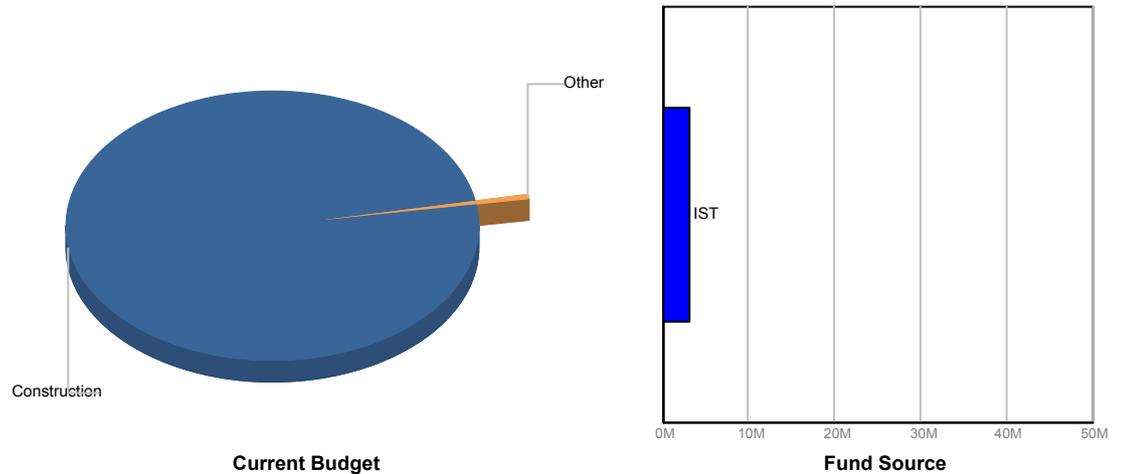

### FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Construction	\$3,204,000	\$183,827	5.74%	\$16,860
Other	\$16,000	\$11,332	70.83%	\$11,332
<b>TOTAL</b>	<b>\$3,220,000</b>	<b>\$195,159</b>	<b>6.06%</b>	<b>\$28,192</b>

### NOTES

DJLA survey complete. Design schedule TBD, but expected to be 100% complete by 12/31/2021. Design and schedule review meeting held 8/6/2021. DD drawings have been complete and review comments have been returned to FTE.

# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects

Data Date: 7/15/2021

Report Date: 8/12/2021

### DESCRIPTION/TEAM

### SCOPE

### PHOTO

**Project Title:** Loggers Run Park Athletic Field Renovation  
**Project Number:** T102  
**BCC District:** 05  
**Delivery Method:** TBD  
**Category:** A06-Athletic Field Renovations  
**Status:** Design  
**Designer:** TBD  
**Contractor:** TBD  
**Project Manager:** Stuart Patterson

Replacement of existing grass field turf with synthetic turf on multi-purpose field 1 & 2.  
 Funded: FY 2020 \$3,200,000



### SCHEDULE SUMMARY

	Original	Actual
Begin Existing Site Surveys	1/29/2020	1/29/2020
Complete Existing Site Surveys	6/30/2020	5/18/2020
Consultant Contract Issuance	12/14/2020	4/20/2021
Design Completion	7/2/2021	
Turf Supplier RFP Proposal Due	4/30/2021	
Finalization of Existing Site Surveys	8/30/2020	9/18/2020
Design RFP Proposals Due	9/4/2020	9/10/2020
Design RFP Final Selection	10/29/2020	10/29/2020

### PARTICIPATION


**Consultant**

- SBE 25%
- Local 25%
- WBE 0%
- MBE 6.13%

**Contractor**

- SBE TBD
- Local TBD
- WBE TBD
- MBE TBD

### FUNDING

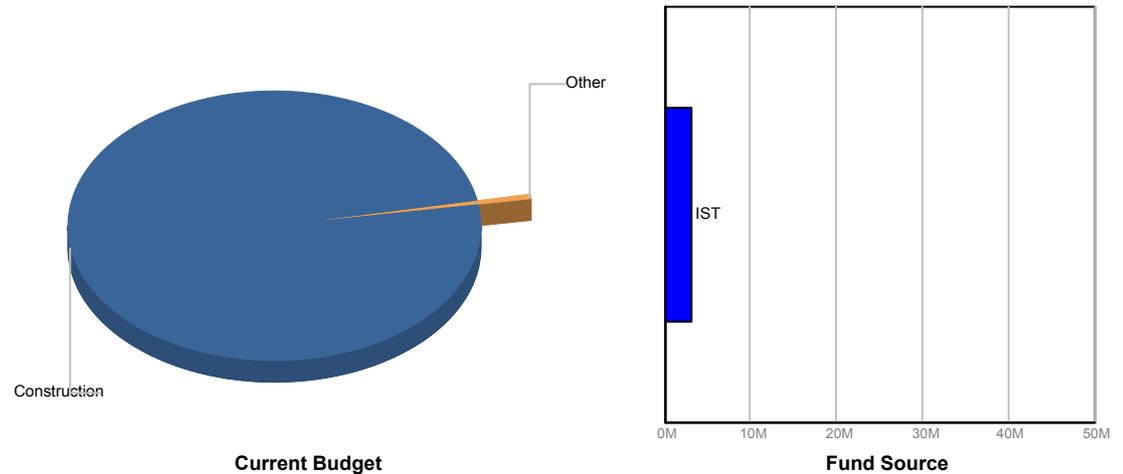

### FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Construction	\$3,184,000	\$180,380	5.67%	\$13,750
Other	\$16,000	\$14,281	89.26%	\$14,281
<b>TOTAL</b>	<b>\$3,200,000</b>	<b>\$194,661</b>	<b>6.08%</b>	<b>\$28,031</b>

### NOTES

DJLA survey complete. Design schedule TBD, but expected to be 100% complete by 12/31/2021. Design and schedule review meeting held 8/6/2021. DD drawings have been complete and review comments have been returned to FTE.

# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects

Data Date: 7/15/2021

Report Date: 8/12/2021

### DESCRIPTION/TEAM

### SCOPE

### PHOTO

**Project Title:** Samuel Friedland District Park Expansion  
**Project Number:** T103  
**BCC District:** 06  
**Delivery Method:** TBD  
**Category:** A06-Athletic Field Renovations  
**Status:** Design  
**Designer:** Florida Transportation Engineering  
**Contractor:** TBD  
**Project Manager:** Stuart Patterson

Replacement of existing grass field turf with synthetic turf on multi-purpose field 9 & 10 as well as the open play field.  
 Funded: FY 2020 \$3,000,000



### SCHEDULE SUMMARY

### PARTICIPATION

### FUNDING



	Original	Actual
Design RFP Final Selection	10/29/2020	10/29/2020
Finalization of Existing Site Surveys	8/30/2020	9/18/2020
Design RFP Proposals Due	9/4/2020	9/10/2020
Consultant Contract Issuance	12/14/2020	4/20/2021
Design Completion	7/2/2021	
Turf Supplier RFP Proposal Due	4/30/2021	
Begin Existing Site Surveys	1/20/2020	1/29/2020
Complete Existing Site Surveys	6/30/2020	5/18/2020

#### Consultant

SBE TBD  
 Local TBD  
 WBE TBD  
 MBE TBD

#### Contractor

SBE TBD  
 Local TBD  
 WBE TBD  
 MBE TBD

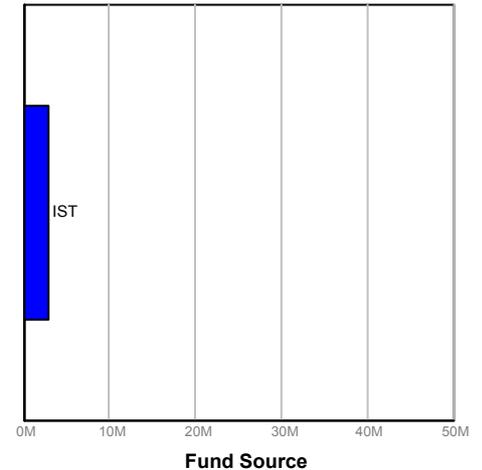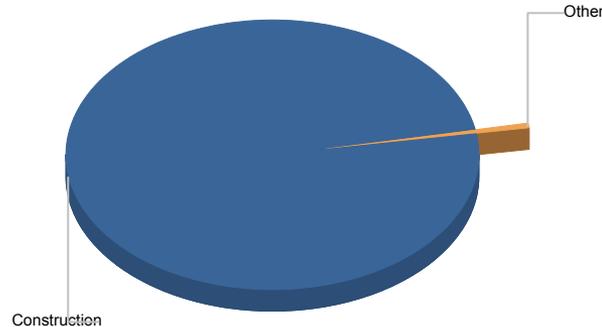

### FINANCIAL SUMMARY

### NOTES

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Construction	\$2,985,000	\$179,985	6.03%	\$12,967
Other	\$15,000	\$8,061	53.74%	\$8,061
<b>TOTAL</b>	<b>\$3,000,000</b>	<b>\$188,046</b>	<b>6.27%</b>	<b>\$21,028</b>

DJLA survey complete. Design schedule TBD, but expected to be 100% complete by 12/31/2021. Design and schedule review meeting held 8/6/2021. DD drawings have been complete and review comments have been returned to FTE.

# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects

Data Date: 7/15/2021

Report Date: 8/12/2021

DESCRIPTION/TEAM	SCOPE	PHOTO
<p><b>Project Title:</b> Westgate Park Restroom and Athletic Field Renovation</p> <p>Project Number: T110</p> <p>BCC District: 07</p> <p>Delivery Method: TBD</p> <p>Category: E02-Existing Park Redevelopment or Expansion</p> <p>Status: Design</p> <p>Designer: Florida Transportation Engineering</p> <p>Contractor: TBD</p> <p>Project Manager: Stuart Patterson</p>	<p>Replacement of existing grass field turf with synthetic turf on multi-purpose field 1.</p> <p>Funded:</p> <p>FY 2020 \$250,000</p> <p>FY 2023 \$1,750,000</p>	

SCHEDULE SUMMARY	PARTICIPATION	FUNDING																											
<table border="1"> <thead> <tr> <th></th> <th>Original</th> <th>Actual</th> </tr> </thead> <tbody> <tr> <td>Begin Existing Site Surveys</td> <td>1/29/2020</td> <td>1/29/2020</td> </tr> <tr> <td>Complete Existing Site Surveys</td> <td>6/30/2020</td> <td>5/18/2020</td> </tr> <tr> <td>Finalization of Existing Site Surveys</td> <td>8/30/2020</td> <td>9/18/2020</td> </tr> <tr> <td>Design RFP Proposals Due</td> <td>9/4/2020</td> <td>9/10/2020</td> </tr> <tr> <td>Design RFP Final Selection</td> <td>10/29/2020</td> <td>10/29/2020</td> </tr> <tr> <td>Consultant Contract Issuance</td> <td>12/14/2020</td> <td>4/20/2021</td> </tr> <tr> <td>Design Completion</td> <td>7/2/2021</td> <td></td> </tr> <tr> <td>Turf Supplier RFP Proposal Due</td> <td>4/30/2021</td> <td></td> </tr> </tbody> </table>		Original	Actual	Begin Existing Site Surveys	1/29/2020	1/29/2020	Complete Existing Site Surveys	6/30/2020	5/18/2020	Finalization of Existing Site Surveys	8/30/2020	9/18/2020	Design RFP Proposals Due	9/4/2020	9/10/2020	Design RFP Final Selection	10/29/2020	10/29/2020	Consultant Contract Issuance	12/14/2020	4/20/2021	Design Completion	7/2/2021		Turf Supplier RFP Proposal Due	4/30/2021		<p><b>Consultant</b></p> <p>SBE 25%</p> <p>Local 25%</p> <p>WBE 0%</p> <p>MBE 6.13%</p> <p><b>Contractor</b></p> <p>SBE TBD</p> <p>Local TBD</p> <p>WBE TBD</p> <p>MBE TBD</p>	<div style="text-align: center;"> <p><b>Current Budget</b></p> </div> <div style="text-align: center;"> <p><b>Fund Source</b></p> </div>
	Original	Actual																											
Begin Existing Site Surveys	1/29/2020	1/29/2020																											
Complete Existing Site Surveys	6/30/2020	5/18/2020																											
Finalization of Existing Site Surveys	8/30/2020	9/18/2020																											
Design RFP Proposals Due	9/4/2020	9/10/2020																											
Design RFP Final Selection	10/29/2020	10/29/2020																											
Consultant Contract Issuance	12/14/2020	4/20/2021																											
Design Completion	7/2/2021																												
Turf Supplier RFP Proposal Due	4/30/2021																												

FINANCIAL SUMMARY				
	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Construction	\$248,750	\$136,854	55.02%	\$0
Other	\$1,250	\$16,766	1,341.28%	\$16,143
<b>TOTAL</b>	<b>\$250,000</b>	<b>\$153,620</b>	<b>61.45%</b>	<b>\$16,143</b>

**NOTES**

DJLA survey complete. Design schedule TBD, but expected to be 100% complete by 12/31/2021. Design and schedule review meeting held 8/6/2021. DD drawings have been complete and review comments have been returned to FTE.



# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects

Data Date: 7/15/2021

Report Date: 8/12/2021

DESCRIPTION/TEAM	SCOPE	PHOTO
<p><b>Project Title:</b> Dubois Park Var Historic Building Repair and Renovation</p> <p>Project Number: T111</p> <p>BCC District: 01</p> <p>Delivery Method: Annual Contract</p> <p>Category: P08-Public Building Repair Replacement &amp; Expans</p> <p>Status: Construction</p> <p>Designer: N/A</p> <p>Contractor: Robling Architecture Construction</p> <p>Project Manager: Ben Carroll</p>	<p>The project consists of relocating the Pineapple Packing House structure, wood framing repairs, roof replacement and new windows, doors, electrical and HVAC</p> <p>IST FY 2020 - \$250,000</p> <p>IST FY 2021 - \$250,000</p> <p>IST FY 2022 - \$250,000</p> <p>IST FY 2023 - \$250,000</p> <p>IST FY 2024 - \$400,585</p> <p>IST FY 2025 - \$599,415</p>	

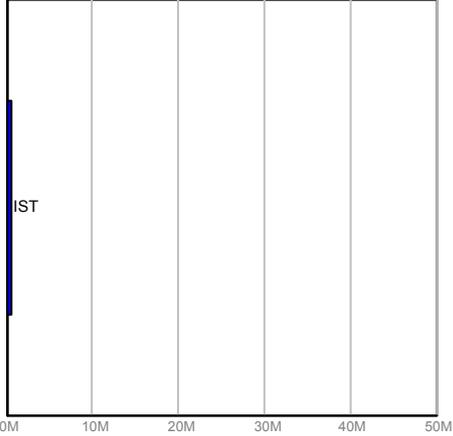SCHEDULE SUMMARY	PARTICIPATION	FUNDING									
<table border="1"> <thead> <tr> <th></th> <th style="text-align: center;">Original</th> <th style="text-align: center;">Actual</th> </tr> </thead> <tbody> <tr> <td>Project Start</td> <td style="text-align: center;">4/12/2021</td> <td style="text-align: center;">4/12/2021</td> </tr> <tr> <td>Project Completion</td> <td style="text-align: center;">12/13/2021</td> <td></td> </tr> </tbody> </table>		Original	Actual	Project Start	4/12/2021	4/12/2021	Project Completion	12/13/2021		<p><b>Consultant</b></p> <p>SBE N/A</p> <p>Local N/A</p> <p>WBE N/A</p> <p>MBE N/A</p> <p><b>Contractor</b></p> <p>SBE 10.46%</p> <p>Local 100%</p> <p>WBE 0%</p> <p>MBE 0%</p>	<div style="display: flex; justify-content: space-around;"> <div style="text-align: center;">  <p>Construction</p> </div> <div style="text-align: center;">  <p>IST</p> </div> </div> <p style="text-align: center;"><b>Current Budget</b>      <b>Fund Source</b></p>
	Original	Actual									
Project Start	4/12/2021	4/12/2021									
Project Completion	12/13/2021										

FINANCIAL SUMMARY				
	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Construction	\$498,750	\$216,668	43.44%	\$27,661
Other	\$1,250	\$583	46.67%	\$583
<b>TOTAL</b>	<b>\$500,000</b>	<b>\$217,251</b>	<b>43.45%</b>	<b>\$28,245</b>

**NOTES**

No status change. Dimensional lumber has 5-6 month lead time. Contractor will complete underground work, foundation until lumber arrives.

# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects

Data Date: 7/15/2021

Report Date: 8/12/2021

### DESCRIPTION/TEAM

### SCOPE

### PHOTO

**Project Title:** Canyon's District Park New Park Development  
**Project Number:** T122  
**BCC District:** 05  
**Delivery Method:** Construction Manager at Risk  
**Category:** N02-New Park Development  
**Status:** Design  
**Designer:** Architecture Green  
**Contractor:** Kaufman Lynn  
**Project Manager:** Rosalyn Acosta

The project consists of the construction of a 52 acre Park south of Boynton Beach Blvd, along the west side of Acme Dairy Rd. with the Canyon Lakes Communities bordering the south and west limits of the site. The park will be constructed in two phases. Phase I will need to be completed in order to transfer the multi-purpose activities that currently take place on two existing soccer fields located to the west of the park. Once transferred the old soccer fields site will become the site of the new Canyon District Library.

FT2021 IST \$12,000,000



### SCHEDULE SUMMARY

### PARTICIPATION

### FUNDING


	Original	Actual
GMP Approval	1/14/2021	5/4/2021
Construction Start	1/27/2021	
Construction Completion	1/27/2022	
Project Completion	3/27/2022	

**Consultant**

- SBE 75.93%
- Local 100%
- WBE 21.41%
- MBE 0%

**Contractor**

- SBE 22.32%
- Local 100%
- WBE 22.32%
- MBE 22.32%

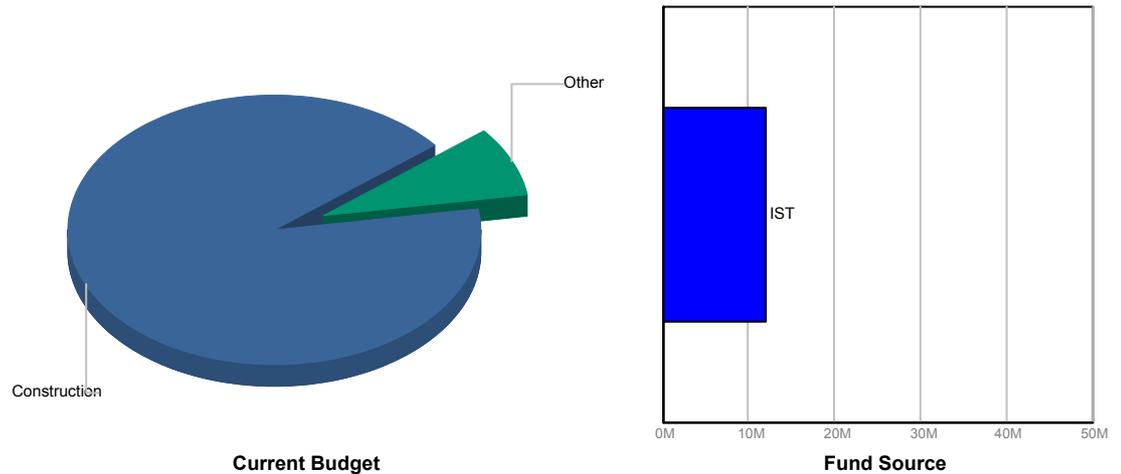

### FINANCIAL SUMMARY

### NOTES

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$0	\$0	0.00%	\$0
Construction	\$11,000,000	\$11,470,763	104.28%	\$2,904,791
Other	\$1,000,000	\$13,424	1.34%	\$13,424
<b>TOTAL</b>	<b>\$12,000,000</b>	<b>\$11,484,187</b>	<b>95.70%</b>	<b>\$2,918,215</b>

First lift of asphalt has been completed on part of the roadways and parking lots. First lift for fitness trail planned for the first week of August. Installation of roadway drainage structures and irrigation lines is ongoing. Maintenance and Concessions buildings activities are also ongoing.



# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects

Data Date: 7/15/2021

Report Date: 8/12/2021

DESCRIPTION/TEAM	SCOPE	PHOTO
<p><b>Project Title:</b> Glades Pioneer Park Athletic Field Renovation</p> <p>Project Number: T175</p> <p>BCC District: 07</p> <p>Delivery Method: TBD</p> <p>Category: A06-Athletic Field Renovations</p> <p>Status: Design</p> <p>Designer: Florida Transportation Engineering</p> <p>Contractor: TBD</p> <p>Project Manager: Stuart Patterson</p>	<p>Replacement of existing grass field turf with synthetic turf on multi-purpose field 1.</p> <p>Funded:</p> <p>FY 2021 \$210,000</p> <p>FY 2023 \$2,000,000</p>	

SCHEDULE SUMMARY	PARTICIPATION	FUNDING																								
<table border="1"> <thead> <tr> <th></th> <th>Original</th> <th>Actual</th> </tr> </thead> <tbody> <tr> <td>Begin Existing Site Surveys</td> <td>1/29/2020</td> <td>1/29/2020</td> </tr> <tr> <td>Complete Existing Site Surveys</td> <td>6/30/2020</td> <td>5/18/2020</td> </tr> <tr> <td>Finalization of Existing Site Surveys</td> <td>8/30/2020</td> <td>9/18/2020</td> </tr> <tr> <td>Design RFP Final Selection</td> <td>10/29/2020</td> <td>10/29/2020</td> </tr> <tr> <td>Consultant Contract Issuance</td> <td>12/14/2020</td> <td></td> </tr> <tr> <td>Design Completion</td> <td>7/2/2021</td> <td></td> </tr> <tr> <td>Turf Supplier RFP Proposal Due</td> <td>4/30/2021</td> <td></td> </tr> </tbody> </table>		Original	Actual	Begin Existing Site Surveys	1/29/2020	1/29/2020	Complete Existing Site Surveys	6/30/2020	5/18/2020	Finalization of Existing Site Surveys	8/30/2020	9/18/2020	Design RFP Final Selection	10/29/2020	10/29/2020	Consultant Contract Issuance	12/14/2020		Design Completion	7/2/2021		Turf Supplier RFP Proposal Due	4/30/2021		<p><b>Consultant</b></p> <p>SBE 25%</p> <p>Local 25%</p> <p>WBE 0%</p> <p>MBE 6.13%</p> <p><b>Contractor</b></p> <p>SBE TBD</p> <p>Local TBD</p> <p>WBE TBD</p> <p>MBE TBD</p>	<div style="text-align: center;">  <p>Design</p> <p><b>Current Budget</b></p> </div> <div style="text-align: center;">  <p>IST</p> <p><b>Fund Source</b></p> </div>
	Original	Actual																								
Begin Existing Site Surveys	1/29/2020	1/29/2020																								
Complete Existing Site Surveys	6/30/2020	5/18/2020																								
Finalization of Existing Site Surveys	8/30/2020	9/18/2020																								
Design RFP Final Selection	10/29/2020	10/29/2020																								
Consultant Contract Issuance	12/14/2020																									
Design Completion	7/2/2021																									
Turf Supplier RFP Proposal Due	4/30/2021																									

FINANCIAL SUMMARY				
	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$210,000	\$156,214	74.39%	\$3,283
<b>TOTAL</b>	<b>\$210,000</b>	<b>\$156,214</b>	<b>74.39%</b>	<b>\$3,283</b>

**NOTES**

Title report received from PREM. DJLA survey in progress. Design schedule TBD, but expected to be 100% complete by 12/31/2021. Design and schedule review meeting held on 8/6/2021. DD drawings have been completed and comments have been returned to FTE.
